This project is funded by the European Union

REPUBLIKA E SHQIPËRISË
KËSHILLI I MINISTRAVE
MINISTËR SHTETI PËR RINDËRTIMIN

The Annual Report

November 4, 2020 to November 3, 2021

Project Title:	EU4Schools

Project Details:

Contract No:	*CTR 2020/417-701 (amended July 5th, 2021)*
Date of Contract Signature:	*03-November-2020*
Implementation period:	*42 months*
Total Cost of Action (Euro)	*60,000,000.00*
Contracting Authority max financing (Euro %):	*98.93 %*
Project Reference No.:	*ALB10/00123296*
International UN Organization:	*United Nations Development Programme (UNDP)*

TABLE OF CONTENTS

MAP OF PROGRAMME IMPLEMENTATION AREA 4

ACRONYMS 5

EXECUTIVE SUMMARY 7

.1. SUMMARY AND CONTEXT OF THE ACTION 8

.1.1. Project background/Situation Analysis 8

.1.2. Strategy and Objectives of the Action 8

.1.3. Relevance of the Action 9

.1.4. Results Framework/Logical Framework 11

.1.5. Management Arrangements 13

.2.OUTPUTS, ACTIVITIES CARRIED OUT DURING REPORTING PERIOD AND RESULTS/ACHIEVEMENTS 14

.2.1. Work-Plan Planning and Implementation 14

.2.2. "Build Back Better" (BBB) 20

.2.3."Build Back Together" (BBT) 23

.2.4. Annual work-plan for the reporting period 24

.3. IMPACT 24

.4. RISKS, ASSUMPTIONS AND DIFFICULTIES ENCOUNTERED AND MEASURES TAKEN 26

.5. STRUCTURE OF THE ACTION'S BUDGET 29

.5.1. Correction within the budget 29

.5.2. Staff and other inputs 30

.5.3. Sources of funding 31

.5.4. Procurement Activity and Progress 31

.6. COORDINATION AND COLLORATION 36

.7. HANDOVER/SUSTAINABILITY 38

.8. CHANGES INTRODUCED IN IMPLEMENTATION 39

.9. LESSONS LEARNED AND CHALLENGES 40

.10. VISIBILITY, TRANSPARENCCY AND COMMUNICATION 41

LIST OF TABLES 42

LIST OF ANNEXES 43

MAP OF PROGRAMME IMPLEMENTATION AREA

List of 41 Education Facilities in EU4Schools Programme	
Mirditë Municipality	
1	Kindergarten, Crèche Nr. 1, Rubik
Lezhë Municipality	
1	9-year school "Gjergj Kastrioti"
2	Kindergarten, 9-year school "Fran Ivanaj"
Kurbin Municipality	
1	Kindergarten Nr. 1
Krujë Municipality	
1	Kindergarten Varosh
2	Kindergarten, 9-year school Bilaj
Durrës Municipality	
1	High school "Naim Frashëri"
2	High school "Gjergj Kastrioti"
3	High school "Olsi Lasko"
4	Kindergarten, 9-year school "Eftali Koçi"
5	Crèche Nr. 3
6	Kindergarten Bizë
7	Professional high school "Bernardina Qerraxhi"
8	Dormitory "Bernardina Qerraxhi"
9	Crèche Nr. 2
10	Kindergarten Manëz
11	9-year school "14 Nëntori"
12	Dormitory "Beqir Çela"
Vorë Municipality	
1	9-year school Vorë
2	9-year school Bërxullë
Kamëz Municipality	
1	Crèche Kamëz
2	Kindergarten "Jashar Hoxha"
3	Kindergarten "Azem Hajdari"
4	9-year school "Ibrahim Basha"
Shijak Municipality	
1	Kindergarten Nr. 2
2	Kindergarten, 9-year school "Rilindja"
Tiranë Municipality	
1	Kindergarten Nr. 41
2	9-year school "Musine Kokalari"
3	9-year school "26 Nëntori"
4	9-year school "Emin Duraku"
5	9-year school "Xhezmi Delli"
6	Professional high school "Asim Vokshi"
7	High school "Myslym Keta"
Kavajë Municipality	
1	9-year school "3 Dëshmorët"
2	9-year school Karpen
3	Professional high school "Charles Telford Erickson"
Rrogozhinë Municipality	
1	Kindergarten Okshtun
2	Kindergarten, 9-year school Kryevidh
3	Kindergarten, 9-year school Rreth-Greth
4	Kindergarten, 9-year school Vilë Bashtovë
5	9-year school "Xhorxh Soros"

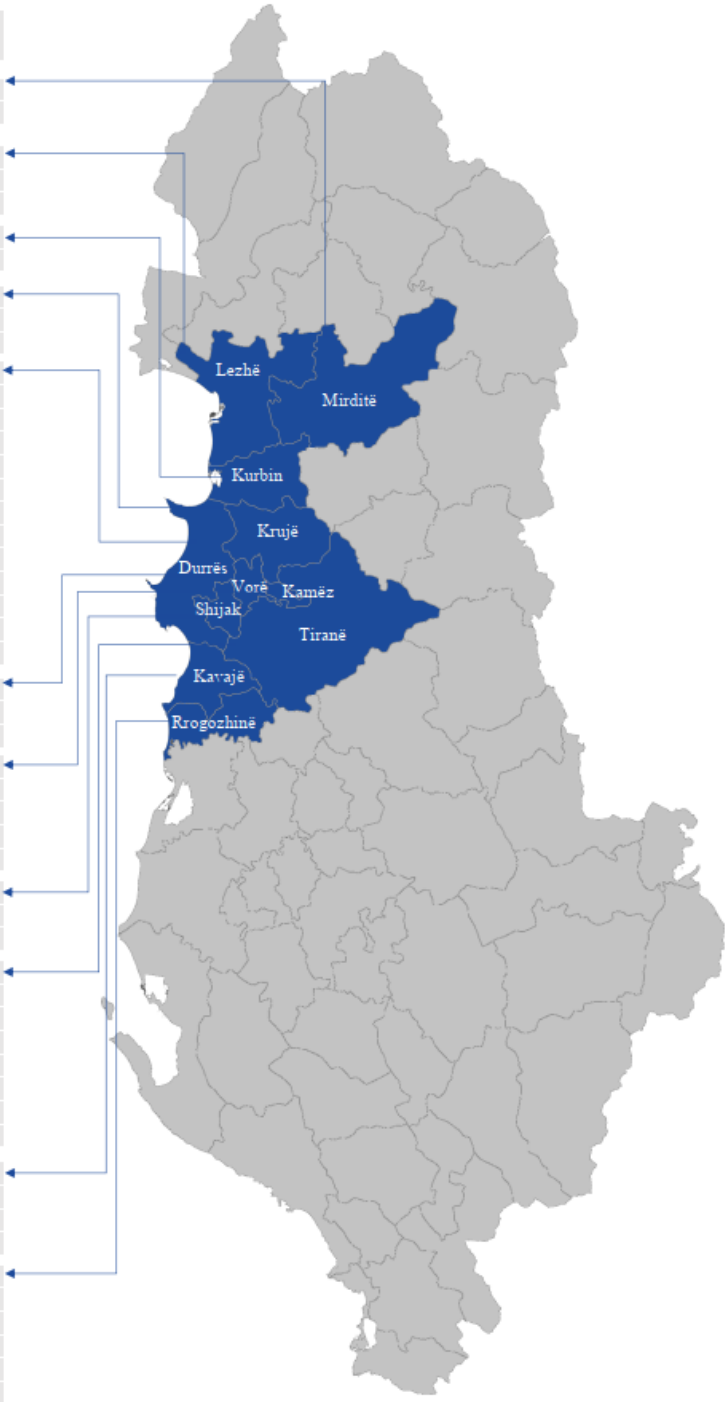


Figure 1: Map of the Municipalities where EU4Schools Programme is implemented

ACRONYMS

AWP	Annual Work plan
BBB	Build Back Better
BBT	Build Back Together
CCTV	Closed-Circuit Television
CoP	Coefficient of Performance
DCM	Decision of Council of Ministers
DLP	Defects Liability Period
DoA	Description of Action
DPMSRP	Deputy Prime Minister and Minister of State for Reconstruction and Reforms' Program
EU	European Union
EUD	Delegation of European Union
FEED	Front to End Engineering Design
HSE	Health, Safety and Environment
HVAC	Highly Ventilated & Air Conditioning System
IC	Individual Contracts
ICT	Information and Communication Technology
IoC	Institute of Construction
ITB	Invitation to Bid
ITP	Invitation to Pre-Qualify
JCT	Joint Technical Group
LED	Light Emitting Diode
LTA	Long-Term Agreement
MoESY	Ministry of Education and Sports

MoU	Memorandum of Understanding
PDNA	Post Disaster Need Assessment
PSC	Programme Steering Committee
RFP	Request for proposal
RFQ	Request for Quotation
SDG	Sustainable Development Goals
TAG	Technical Assurance Group
ToR	Terms of References
UN	United Nations
UNDP	United Nations Development Programme
UNGM	United Nations Global Marketplace
VAT	Value Added Tax

EXECUTIVE SUMMARY

This report presents the activity of EU4Schools programme, Phase II, for the period November 4, 2020, up to November 3, 2021. The programme, funded by European Union (EU) and implemented by United Nations Development Programme (UNDP) in collaboration with Albanian Government, supports the recovery process caused by the earthquake that hit Albania on November 26, 2019, and was build based on Phase I of the EU4Schools programme. Though the Programme has two Phases, EU4Schools is conceptualised as a unified initiative, where Phase I and II are implemented consecutively.

The programme has been operating in the complex situation created by COVID-19 pandemic and respective restrictive measures. Despite all, the programme managed to initiate and implement the activities as planned.

During this period, EU4Schools expanded its scope of work in 11 Municipalities, namely: (i) Durrës, (ii) Kruja, (iii) Kurbin, (iv) Kavaja (v) Kamza, (vi) Lezhë, (vii) Mirditë, (viii) Rrogozhinë, (ix) Tiranë, (x) Shijak and (xi) Vorë and is impacting indirectly about 1 million citizens overall and directly about 24 000 students, children, and teachers. Initially 36 education facilities (either to be repaired or to be reconstructed) were part of the programme's scope for the reporting period. Later the number extended to 41, with 5 more education facilities added through the Addendum of the contribution agreement signed with the EU Delegation in Tirana on July 5, 2021. As such, this annual report, and the consecutive ones, will report for on the repair/reconstruction of 41 educational facilities. The expected results are updated accordingly to reflect this modification.

Building upon the Phase I experience, during the reporting period, the following achievements are noteworthy: (i) technical evaluation prepared for 41 education facilities; (ii) procurement procedures were carried to contract 7 design and supervision and 7 construction companies; (iii) detailed designs for 19 educational facilities were completed, (iv) 40 consultation meetings were organized in 36 education facilities in the 11 Municipalities; (v) civil works have initiated in 7 education facilities; (vi) furnishing of 10 education facilities. On the other side, 11 Memorandum of Understandings (MoU) are signed with all impacted Municipalities to enable a solid partnership and efficient implementation of the programme.

As established, the recovery process is aligned with two important principles: "*Build Back Better*" and "*Build Back Together*". They transform this recovery process into an opportunity: EU4Schools aims to not only reconstruct and repair education facilities, but to restore trust and create hope for communities in the impacted areas.

Based on the communication and visibility plan of the programme, the interventions are promoted through EU4Schools portal (www.eu4schoolsportal.al). During the reporting period, the portal had 70 75 visits with a total 181 577 clicks in total. As per visibility and communication plan, the activity of EU4Schools was reflected in 504 posts in social media (Facebook, Twitter, and Instagram) and 18 publications on national media online. A travelling exhibition to inform the wider public in 11 Municipalities was organised and visited by approximately 5000 visitors.

On the same time, EU4Schools initiated two initiatives: (i) "*I love my school because…*" and (i) "*Name my school…"* with the goal to increase inclusiveness, participation between children/students, institutions, and communities as well gender-awareness.

Considered this initiative as a unified Programme, some of the costs of civil works and furniture for education facilities part of Phase I are budgeted in the budget of Phase II as agreed with the EU Delegation. These changes are reflected in the financial report for the reporting period.

.1. SUMMARY AND CONTEXT OF THE ACTION

.1.1. Project background/Situation Analysis

The Phase II started implementation on November 4, 2020 when COVID-19 pandemic had already impacted the Albania society for more than nine months. The Government imposed preventive and precautionary measures succeeding in avoiding the overstretching of the health system and keeping the parameters of the pandemic to relatively low levels compared to many other countries.[*] With all schools nationwide closed, and although alternative online learning options were adopted, the closures of educational facilities, had an impact on the quality of learning, especially on most of the vulnerable groups who lack connectivity and adequate equipment for online options. Around 572 000 children and students were impacted from the COVID-19 lockdown only few months after the earthquake. In the 11 impacted Municipalities, the education suffered from two consecutive crises, causing impatience to return into classes and raising expectations on the speed and quality of the post-earthquake recovery process.

It also coincided with the post-earthquake reconstruction process initiated from the Albanian Development Fund through dedicated governmental funds, thus increasing the demand for qualified construction companies to be contracted.

The Post Disaster Need Assessment (PDNA) indicated that a total of 321 public Crèches, Pre-Schools, Basic Schools and Secondary Schools were fully destroyed, partially damaged or lightly damaged in the 11 municipalities. 60% of destroyed and damaged schools are in rural areas. Facilities which have been lightly or partially damaged are subject of repairs. Facilities that have been severely damaged or fully destroyed are being rebuilt.

.1.2. Strategy and Objectives of the Action

The overall objective of EU4Schools is to further support central and local governments in reducing social and economic losses from the earthquake, and to accelerate the recovery process through educational facility repairs and reconstruction, as a continuation of the “EU4Schools” Phase I.

The specific objectives are:

[*] UN ALBANIA COVID-19 Socio-Economic Recovery and Response Plan July 8, 2020; https://www.un.org.al/sites/default/files/Socio%20Economic%20Plan%20Albania_0.pdf

1. To support repairing and reconstruction, including basic furnishing, of education facilities in municipalities affected by the earthquake according to the EU standards.

2. To provide increased transparency, accountability, and inclusiveness to the recovery process and,

3. To improve capacities of central and local governments in accelerating the recovery processes according to the highest EU International standards.

Same as in Phase I, the Programme is continuing to address issues of transparency and inclusiveness by organising various activities, such as: consultancy meetings and place checks (with main beneficiaries), including students, teachers, student's government, local community, local and central institutions etc. Through the MoUs signed with each of 11 Municipalities where the interventions are taking place, and the collaboration thereof, the EU4Schools is supporting capacity improvements of the local governments by (i) urging for prompt and reliable information; (ii) accelerate institutional decision-making; and (iii) increase internal capacities for adequate operation and maintenance of the repaired/reconstructed education facilities.

To track the progress of the Programme, the EU4Schools portal was launched and being promoted to urge beneficiaries and interested parties to access online our business intelligence platform so that they can be informed on the EU4Schools progress. Visibility of the action is ensured based on a joint EU-UNDP communication and visibility strategy, aiming to promote and highlight the support of the European Union to the education sector recovery.

.1.3. Relevance of the Action

The 6.3 magnitude earthquake that hit Albania on 26 November 2019 left 51 people dead and at least, 913 others injured. Eleven municipalities situated in three prefectures (Tirana, Durrës and Lezha), with an approximate population of 1,185,286 persons, have suffered to varying degrees from the earthquake with 202,291 people affected directly or indirectly. According to government sources, around 17,090 affected inhabitants had to vacate their homes. For the first time in recent history, the Government of Albania announced a State of Natural Emergency in the three prefectures. According to the findings of the PDNA, the total effect of the disaster in the 11 municipalities amounts to 985.1 million EUR (121.21 billion ALL). Most of the damages are recorded in the Housing sector (78.5%), followed by the Productive sector (8.4%) and the Education (7.5%) sector.

According to the PDNA, damages were reported to 321 educational institutions (including crèches, pre-schools, basic schools, secondary schools, vocational and education training schools, high education schools and dormitories) in the 11 municipalities, representing 24% of all educational establishments. About 90% of damaged institutions are in the public sector. The municipalities of Tirana and Durrës have the highest share of damage, with 55% and 21%, respectively. Schools were also damaged in smaller municipalities such as Vora, where half of all education facilities were either fully or partially destroyed.

In addition to infrastructure, the earthquake also damaged physical assets such as furniture, labs, ICT equipment, libraries, textbooks, and other learning materials. The physical infrastructure of education

facilities, especially in rural areas, did not meet standards (as per current regulations) on safety and accessibility.

The Programme is contributing to address the recommendations of the 2021 EC report to Albania, which stated that "*The budget in 2021, expected to drop at 3.5% of the GDP, should be enhanced to support the efforts to modernise the educational system and ensure quality and inclusiveness in education for all pupils. The expected school financial autonomy has not progressed in 2020 as the sublegal acts and provisions for providing actual financial autonomy in the school were not developed despite the existing legislation.*"

By delivering its objectives, the Programme will contribute to achievement of the targets set within the Sustainable Development Agenda 2030, more specifically:

- SDG 4 "Quality education",
- SDG 9 "Industry, Innovation and Infrastructure",
- SDG 10 "Reduced Inequalities",
- SDG 16 "Peace, justice and strong institutions" and
- SDG 17 "Partnership for the Goals".

EU4Schools is in line with 2030 Sustainable Development Agenda and 2018 -2021 UNDP's Strategic Plan: Development Setting C. Build resilience to shocks, crisis, and Signature Solution 3: Enhance prevention and recovery for resilient societies.

This Programme is intervening in 41 education facilities affected by the earthquake that are approved by the State Reconstruction Committee through the proposal of the Deputy PM and Minister of State for Reconstruction and Reforms' Program (DPMSRP) as the institution in charge of coordinating government and donor funded recovery programs. 17 of the targeted education facilities are in the rural areas and 24 in the urban ones. The majority of education facilities part of the EU4Schools' scope are 9 - year schools (as per figure below).

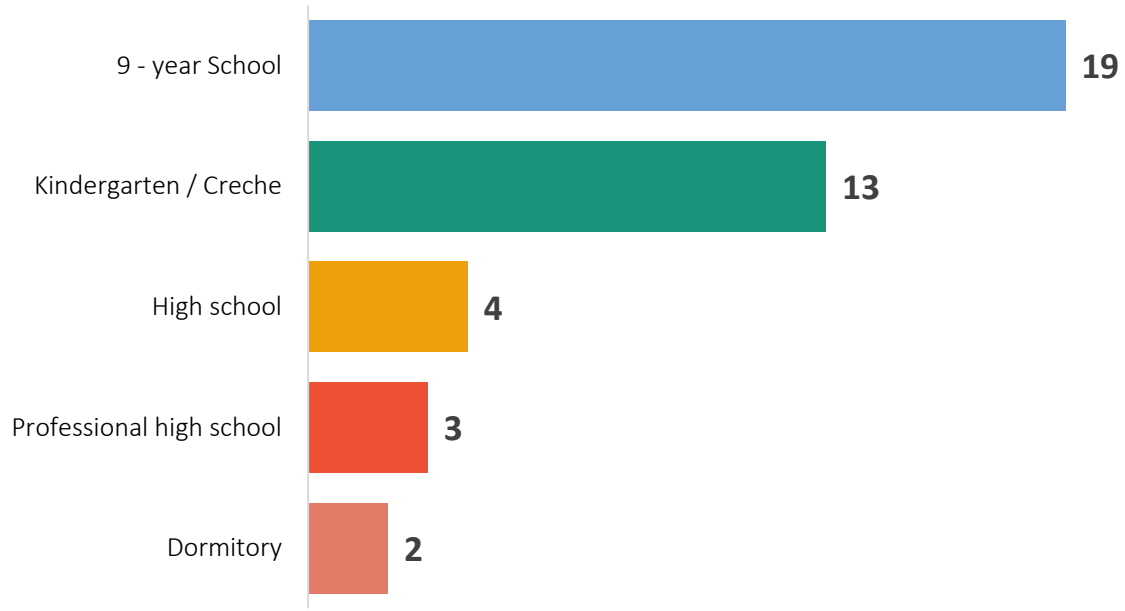


Figure 2: Typology of education facilities for Phase II EU4Schools

Information on all education facilities to be targeted by this Programme are attached as ***Annex I***.

.1.4. Results Framework/Logical Framework

Progress is made in achieving the results for all interventions. During the reporting period, detailed designs for 19 educational facilities were completed, including preparation of project ideas and approval from the Institute of Construction. All detailed designs were prepared based on "*Build Back Better*" and "*Build Back Together*" principles. Construction works started in 7 educational facilities, while a prequalification process for construction companies was launched and completed. To increase transparency and inclusiveness, the EU4Schools portal (launched on January 27, 2021) continues to be promoted and used by interested parties as an information tool on the progress of EU4Schools programme. As foreseen in the intervention logic, state of play for results indicators, during the reporting period is as follows:

R1: Indicatively 41 technical designs in place for repair and/or reconstruction – ***on going***. Design and supervision contracts signed for 36 education facilities, and contracted companies are working on respective designs. ToRs have been prepared for 5 education facilities part of the amendment agreement Technical designs approved for 19 education facilities.

R1: Indicatively 41 reports for testing and commissioning finalised and approved – ***not started***. No education facility is delivered during the reporting period.

R1: Indicatively 60 inspections of works at the end of defects notification periods in indicatively 41 educational facilities – ***not started***. The first education facility started construction work on April 26th, 2021.

R2: Up to 26 IT laboratory in place – ***ongoing***. Construction work has started in 5 education facilities.

R2: Up to 41 health rooms created and equipped – ***ongoing***. Construction work has started in 5 education facilities.

R2: Up to 41 psychosocial rooms finalized to serve the needs of the teachers and students – ***ongoing***. Construction work has started in 5 education facilities.

R2: 1 Manual on operations prepared and shared – ***completed***.

R3: 11 MoUs signed with targeted municipalities – ***completed***. 11 MoUs signed during the reporting period including renewal of MoUs for five Municipalities EU4Schools signed during Phase I.

R3: Up to 80 consultative meetings organised – ***on going***. 40 consultative meetings organized during the reporting period.

R3: Around 2000 people participating in consultative processes – ***on going***. 946 participants gave their opinions on consultative meetings and one Place Check organized during reporting period.

R3: Up to 20 short stories videos prepared – ***not started***. Promotion of the EU4Schools programme is carried according to the completion of education facilities or other topics as occurring. Initiation of the short video stories will initiate for Phase II as progress continues.

R3: Up to 10 events organised - ***ongoing***. In May 2021, EU4Schools organized an awareness-raising travelling exhibition in coordination with the European Weeks' events. It was displayed in the main squares of 9 targeted municipalities, namely Tirana, Durrës, Kruja, Kavaja, Rrogozhina, Kurbin, Vora, Kamza, and Shijak.

R3: Up to 10.000 visibility elements produced – ***on going***. 13 019 visibility materials produced during reporting period. This includes T-Shirts, caps, masks, EU4Schools bags, branded safety helmets, branded high-vis vests, pencils, roll-up banners, stand-up flags, branded classrooms tags for completed schools.

Assumptions presented in the Logical Framework during programme formulation phase have been scrutinized. After one year of programme implementation, the initial assumptions still stand; explanations are provided for each assumption to clarify their current status.

Assumptions to achieve the Specific Objectives 1, 2 and 3 include:

Table 1: List of EU4Schools assumptions as per Log Frame

Nr.	Assumption	Explanation
1	*Coordination and complementarity with recovery assistance interventions delivered by governments and international community*	The post-earthquake recovery has been a top priority for all partners involved, despite the implications of the COVID-19 pandemic. Coordination between all stakeholders was streamlined once the Programme Steering Committee was formalized in June 2020, working as the same structure for both phases. Its role is to inform, coordinate and lead decision making for all EU4Schools related matters. Periodically, Joint Coordination Meetings are organized with the main partnership for the EU4schools partnership.
2	*Central government is committed to collaborate in sharing information*	The collaboration with the Central Government is mostly organized by two institutions: The Ministry of Education, Sports and Youth (MoESY) the Deputy Prime Minister and

		Minister of State for Reconstruction and Reforms' Program (DPMSRP). Their partnership is important in moving forward the activities of the programme. Collaboration is also established with Institute of Construction (IoC) as the organization in charge of technical review and approval for all proposed project designs. In addition, ever since the start of Phase I, collaborating with General Directorate of Taxation has been a programme necessity.
3	*Target municipalities cooperate effectively and engage in all relevant action activities by providing relevant documentation*	Information has been shared and presented (when available) by the respective Municipalities and their Education Departments. One of the main Municipalities' responsibilities is to demolish damaged buildings, remove the demolition' debris, clear and make construction sites ready for civil works to start. Some delays have been noticed which has stretched the timelines and postponed deadlines for construction works. These delays are impacting mostly the education facilities to be reconstructed as they require demolition and transport of all debris to dedicated waste areas.
4	*Weather conditions are conducive of construction works*	Weather conditions have not been extreme therefore, they have not been a matter of concern for the reporting period.

For achieving the Results 1, 2 and 3 these have been the following assumptions:

1-*Target municipalities are committed to provide necessary documents*: As stated above, despite the willingness to collaborate, the Municipalities have had their share of delays in providing documentation to sustain the ownership of construction lands, consultation process, the technical design or issuing the construction permits. On some occasions, data provided to establish the future teaching capacities of new education facilities were inaccurate or inconsistent.

2-*Availability of qualified construction companies*: Based on the phase I, a prequalification process for selection of qualified construction companies was conducted, and 56 companies were selected (more information is provided in point 5.4 of this report). They have proof of long and positive work experience and sufficient capacities to perform such type of contracts. However, due to the engagement in other contracts, mainly part of other earthquake reconstruction processes, the number of applications for different bids could have been higher yet not being an impediment to complete works.

3- *Procurement procedures are implemented in due time:* The EU4Schools team has strived to expedite all procurement processes in line with UNDP rules and procedures for the unified EU4Schools Programme.

A detailed description of the Logical Framework results so far, is found on ***Annex 2.***

.1.5. Management Arrangements

The scope of the programme involves 11 Municipalities, thus reinforcing the necessity to streamline stakeholders' collaboration, crucial to minimize overlap and maximize complementarity. Other than MoUs

and periodic meetings with each Municipality, existing coordination mechanisms are used to promote the action but also regularly disseminate information to key national and international stakeholders.

In the beginning of Phase II (January 2021), the Programme Steering Committee (PSC), which was established during Phase I and will function as one, for the unified Programme, to oversee and coordinate the operations of the Programme, was enlarged with representatives of six other Municipalities.

The PSC continues to oversee the project's implementation and to take all necessary strategic decisions based on the project's initial plan and budget as well as on monitoring data. It provides policy guidance and recommendation regarding the EU4Schools strategy and objectives, receives and comments semi-annual reports, approve annual plans of operation and reports.

As stated, the PSC is composed of representatives from the European Union Delegation to Albania (as the donor), UNDP Albania, (the implementing Agency), a Representative of the Deputy Prime Minister and Minister of State for Reconstruction and Reforms' Program, and the Ministry of Education, Sports and Youth, UN Resident coordinator and one representative from each of the eleven beneficiary municipalities.

Joint Coordination Team (JCT) meeting are organized periodically between the three main partners of the programme: EU Delegation in Albania, UNDP Albania, and representative of DPMSRP. The scope of this meeting is to update on the progress of EU4Schools and coordinate on various implementation issues. So far, the JCT meetings are held monthly.

Technical Assurance Group (TAG) meeting are organized frequently to discuss technical aspects of the projects designs prior to the finalisation of each technical project. TAG is formed by representatives of EU4Schools, the contracted design company, representatives of the respective Municipalities, representative of the Institute of Construction and management of the education facility to repaired/reconstructed. There have been six TAG meeting, where the technical designs are discussed among representatives of municipalities, Institute of Construction, Ministry of Education and Sports, design company and EU4Schools Programme.

.2.OUTPUTS, ACTIVITIES CARRIED OUT DURING REPORTING PERIOD AND RESULTS/ACHIEVEMENTS

.2.1. Work-Plan Planning and Implementation

The implementation of the work-plan is reported below as per each activity. The scope of Phase II I was initially limited to 36 education facilities. It was later expanded to 41 ones through a contract signed with the EU Delegation in Tirana on July 5, 2021.

Result 1: Educational facilities repaired and/or reconstructed, with a strong emphasis on sustainability, inclusiveness, and environmental protection.

Activity 1.1: Technical assessment for education facilities and identification of the needs for infrastructure intervention.

Initially 36 education facilities in 11 Municipalities have been assessed during the reporting period. Due to the amendment of the agreement, 5 more education facilities were added to the list, thus in total 41 technical assessments are carried as planned.

All education facilities identified for repairs and/or reconstruction by the Programme has gone through a technical survey to assess the extent of the intervention needed to make them fully operational. This process was based on site visits of UNDP Albania's engineers and technical review of assessment reports prepared by the Institute of Construction and other relevant documents made available by municipalities and educational departments.

As in Phase I, during this process the project team in collaboration with local authorities gathered data on the exact number of students impacted as well as the current status of education services, to determine whether teaching to the students is provided in the damaged school or the students have been temporarily transferred to another educational facility. This activity resulted in the preparation of Terms of Reference (ToRs) and technical specifications for the design and supervision of 41 education facilities.

Activity 1.2: Contracting of companies for the preparation of detailed technical design (FEED) and supervision services for educational facilities to repair or reconstruct.

These activities include procurement of services for the preparation of the technical designs and provision of supervision for the repair and reconstruction of education facilities in line with specifications foreseen in the ToRs.

19 technical designs are completed and approved by the IoC, and 17 others are on the process of being completed into December 2021. The procurement process for the technical designs of 5 education facilities part of the amendment agreement will commence in the first ten of days of November. More information on how the procurement process for this activity is provided in point 5.4 of the report.

Activity 1.3: Contracting construction companies and implementation of the civil, mechanical, and electrical works for repair and reconstruction

Under this activity a competitive procurement process for the selection of service providers to implement the reconstruction and repairs works was launched in March 2021. Eligible providers were invited to submit their offers within April 6, 2021. The aim was to refresh the list of highly qualified contractors who are technically, financially, and administratively capable of providing excellent implementation of construction projects for 36 education facilities, falling in four predefined groups:

1. Group 1: works up to 300,000 USD,
2. Group 2: works up to 600,000 USD,
3. Group 3: up to 1,000,000 USD and
4. Group 4: works over 1,000,000 USD.

Considering the capacities required, the applicants could be prequalified for one, two, three or four the above groups.

The pre-qualified Applicants (selected under the process of Phase I) were continuously invited, to submit bids through several processes of Invitation to Bid (ITB) for the construction works for reconstruction

and/or repair of education facilities. Invitations to bid are only sent to the pre-qualified applicants of the predefined groups. More information is provided on section 5.4 of the report.

Before starting the civil works the municipalities, as foreseen in the MoUs, must issue the construction permit and make available the objects/land for repair and/or reconstruction. During the reporting period, construction companies have been contracted for 7 educational facilities tendered, namely Kindergarten No. 2 and 9-year school "Rilindja" in Shijak, Kindergarten/ 9-year school "Eftali Koçi" in Durrës, Kindergarten Varosh and 9-year school Bilaj in Krujë, Kindergarten "Jashar Hoxha" in Kamëz and Kindergarten No. 1 in Kurbin. In total, seven civil works' contracts are signed for seven education facilities. In two education facilities civil works will commence in the first ten days of November. The table below, provides information on contract signature for each of above-mentioned education facilities.

Table 2: List of education facilities where civil works have commenced

No.	Education facility	Municipality	Contract signature
1.	Kindergarten No. 2	Shijak	28-Oct-2021
2.	9-year school "Rilindja"	Shijak	29-Oct-2021
3.	Kindergarten, 9-year school "Eftali Koçi"	Durrës	04-May-2021
4.	Kindergarten Varosh	Krujë	19-Apr-2021
5.	9-year school Bilaj	Krujë	04-May-2021
6.	Kindergarten "Jashar Hoxha"	Kamëz	19-Apr-2021
7.	Kindergarten No. 1	Kurbin	08-Jun-2021

While the focus is on high quality implementation of the civil works, the contracted companies are expected to deliver swiftly in order to restore normal conditions in the teaching process in the affected education facilities as soon as possible. An operation manual and another one dedicated to Health and Safety at Work are prepared and share with contracting companies. Training of staff will continue based on a calendar in each construction sites. The companies contracted for the technical designs of the facilities to be repaired/reconstructed, are also engaged for the supervision of the civil works conducted under this activity.

Activity 1.4: Testing and commissioning for repaired and reconstructed facilities

Based on the experience gathered during Phase I, after the civil works are completed, testing and commissioning of all repaired /reconstructed education facilities will be performed for 41 education facilities. As per legal national requirements, it will be done by a group of contracted experts, including representatives of the municipality and other responsible institutions. This process is carried in line with specifications and contracts provisions. A work schedule is prepared based on the progress of construction works and the process will be performed by a team of dedicated engineers. During the reporting period, the terms of reference are being prepared as to initiate the procurement process.

Activity 1.5: Formal handover of repaired and reconstructed education facilities

All facilities repaired and reconstructed as part of theEU4Schools, Phase ll will be formally handed over to the relevant beneficiaries following a satisfactory assessment of the works done by a quality assurance body. Based on the experience of Phase I, adequate time will be allocated to design and administer a comprehensive quality assurance regime across all components, ensuring that commitments by all

stakeholders are met in full, while handing-over knowledge and tools to relevant domestic authorities. The procedure for formal handover and final inspection is already prepared and tested during Phase I of the programme.

Activity 1.6: Final inspection of works at the end of defects notification period

The construction works for the repair of "Jashar Hoxha" Kindergarten in Kamëz has started on April 2021 and is expected to be handed over on mid-November 2021. The other education facility, Varosh Kindergarten in Kruja, which has commenced later in May 2021, is expected to be completed in beginning 2022.

Result 2: Quality of learning environment, including technical capacities of central and local level institutions improved

Activity 2.1: Preparation of technical specifications for furniture and equipment for repaired and reconstructed facilities

Based on the EU4Schols procurement strategy, the team has prepared technical specifications and Terms of References (ToR) for procuring the preparation, delivery and installation of basic furniture and equipment in the respective education facilities part of Phase I (10 education facilities) and Phase II. Five companies are selected, and Long Term Agreements (LTAs) are signed with them.

Activity 2.2: Purchase and delivery of furniture and equipment for each repaired and reconstructed educational facility

The furniture and equipment will be delivered after the completion of the civil works in all education facilities part of Phase II. As agreed with Delegation of EU in Albania, the budget for furniture and equipment of 10 education facilities, part of Phase I, will be covered by the budget of Phase II. A detailed schedule is prepared to ensure the furniture in due time based also on lessons learned during the furnishing of the facilities in Phase I. Close collaboration and consultations were carried with Education Departments of respective Municipalities for the preparation and delivery of the furniture to guarantee that furniture is designed and prepared as per needs of each education facility and accommodate the needs of teachers and children/students.

Activity 2.3: Conducting a training needs assessment of the teachers of primary and basic education in IT and digital literacy to identify gaps and upgrading strategies

The assessment will be carried by an independent and contracted third party. During the reporting period, the evaluation process for this requirement has been completed and the contract is expected to be signed in the second week of November 2021. This assignment is expected to assess the needs of teachers/staff of educational facilities, targeted by EU4Schools programme. A detailed methodology will be prepared by awarded company, on how to conduct this assessment.

Activity 2.4: Strengthen local capacities in Operations and Maintenance and health and safety in school environment.

The Operation and Maintenance training will be carried in each education facility where the beneficiaries will be learning the know-how and requirements necessary for a long and sustainable use of the

repaired/reconstructed education facilities. The training will be custom-made based on the type of equipment installed in each education facility.

In the meantime, a series of guidelines (six of them) are prepared on health and safety issues, that will be used to train teachers, staff and children on safety, transport and road safety, prevention and protection from fire, earthquake response, flooding response, and first aid.

Result 3: Transparency, accountability, and inclusiveness in recovering processes strengthened

Activity 3.1: Signature of Memorandum of Understanding (MoU) with municipalities and specific dialogue and interventions to ensure their full commitment during the Action implementation and at the end for the maintenance of the facilities

To outline the roles and responsibilities of partner institutions in the implementation of the Action, MoU between UNDP and targeted municipalities representatives were signed. MoU amendments were signed with the five (5) Municipalities part of Phase I, whereas six (6) new MoUs were signed other Municipalities. The purpose of the MOUs is to provide a framework of cooperation and facilitate and strengthen collaboration between UNDP and partners municipalities for successful implementation of the EU4Schools objectives.

UNDP has the overall responsibility to repair and reconstruct the educational facilities damaged by the earthquake of 26th of November 2019, while each partner municipality will:

(i) coordinate with all local actors and make available the relevant documentation for the repair and reconstruction of education facilities,

(ii) deal with any liability that may arise from land ownership and assets property or any other property related issue,

(iii) follow the necessary procedures and issue the relevant construction permit in a very short period of time,

(iv) make available the objects that will be repaired and lands for those that will be reconstructed to the UNDP contractor to start works as per the agreed time schedule and

(v) ensure regular maintenance of the educational facilities repaired and reconstructed after their handover.

To better define the roles and responsibilities several meetings of program representatives with mayors and interested departments in the municipality are organised. Targeted municipalities have also appointed a high-level representative as a permanent member of the Programme Steering Committee and nominated a focal point, who is in close contact with the EU4Schools team and coordinate all local level activities.

As the five new education facilities are added to the list of Phase II, no new MoUs were needed to be signed as the added education facilities are within the same geographic scope of the EU4Schools programme.

Activity 3.2: Organisation of community led local consultations on the interventions

Into the reporting period, 39 consultation meetings and one Place Check have been organised with the stakeholders, direct and indirect beneficiaries such as teachers, students, parents, and other representatives from the community in total of 950 persons. Representatives from the municipalities, from the regional directorate education office and from urban planning office in each municipality have been invited and have participated.

Data collected during the consultation process and site visits were shared with the project team, mostly with data management department and were inputted on the programme transparency portal ensuring integration into the action components, developing community awareness and close monitoring by the beneficiaries.

Participation data are showed in the point 2.4 of this report.

Adequate representation of community views is enabled during consultative meetings and the final technical design plans are being developed considering at a large extend the community expressed needs, opinions, and feedback. As per stablished procedure in Phase I, a stakeholders' mapping and identification of community leaders and local government focal points is conducted; a list is prepared containing information about their contact details.

In addition to the planned activities, EU4Schools has originated another initiative which contributes to the involvement of the community with the children of the newly repaired or reconstructed facilities. "*I love my school because…*" is a project of EU4Schools which in line with of "*Building Back Together"* aims to engage students, teachers, and pupils to appreciate their new schools. The project suggests a set of activities to be discussed with the teachers and students of the recently completed education facilities and once agreed upon, implement them thereafter. As a start, this activity will be organized in four municipalities, Kavajë, Krujë, Kamëz and Kurbin, in education facilities completed.

With the purpose to promote the gender-balance and respect for women personalities of Albania, EU4Schools has generated anther initiative which is under implementation. "*Name my school…"* is a project which encourages respective communities and local governments to name education facilities currently without a name. The suggested names are of female personalities who are important for the country or the regions where the education facilities are located.

Activity 3.3: Updating the online, publicly accessible BI (Business Intelligence) dashboard available to all partners and the public through web technologies, for showing Action progress.

Transparency, accountability, and participation are key principles of this programme. In that context, a web-based accessible platform/portal is prepared and launched on 27 January 2021. The transparency portal www.eu4schoolsportal.al (prepared both in Albanian and English) is the main tool to communicate the results of the programme and inform and update stakeholders and the public on action progress. The portal encompasses information for both Phases, I and II.

Every subcategory has comprehensive details that will be updated on a regular basis by the respective members of the project team. This platform improves accountability and serves as an effective tool for tracking. During the reporting period, and from the launch of the portal, the portal is visited by 7 075 users, which have visited 20 373 pages and have had 181 577 user interactions with Power BI dashboard embedded in the portal. More statistics on the portal are provided on ***Annex 3.*** The portal has been praised as good practice by Faktoje.al an independent online media which checks the accuracy and transparency of the information provided to the public.

Activity 3.4: Communicate the results through visibility actions

The response to the 26th of November 2019 earthquake has a special importance to the Albanian public. It can be considered as a "test of maturity" for public institutions, and everyone involved in the recovery process. In this context and considering the scale of the programme, the EU4Schools plays an important part in providing information in the most adequate form possible to the public. The Albanian audience must be aware on the quality of work carried, the participatory approach and the integrity of internal processes done in the EU4Schools programme.

The team has communicated progress and provided information for the wider public through 504 posts in social media, 18 articles in online national media, a major press trip organised with the outstanding presence of the President of the EU Commission, Ursula von Der Leyen and the Prime Minister of Albania, Edi Rama. All posts have been prepared by following the UNDP and EU respective guidelines. More information is provided in ***Annex 4*** of the report.

Another tangible and more interactive method of communication was to "take" EU4Schools in the public squares of the municipalities where EU4Schools is reconstructing, starting from the capital, Tirana. As such during the reporting period, the team worked to conceptualize, approve, and implement a travelling exhibition which was launched in May along with and in coordination with the European Weeks organized by the Delegation of EU in Albania. The exhibition was visited by about 5000 people which discussed with EU4Schools engineers and team members.

This unique initiative aimed to bring the construction process in the piazzas and squares of the Albanian towns where the programme operates. Children had the opportunity to enjoy their visit by engaging themselves as engineers, use the dedicated photo-frames or check the knowledge gained by answering questions.

.2.2. "Build Back Better" (BBB)

As established from the very start of the EU4Schools Phase I, the BBB framework gives the impacted communities a unique opportunity to sustainably reduce current and future risks. BBB offers the opportunity to rebuild stronger, safer, more disaster-resilient infrastructure and systems and with higher standards.

Based on this approach, the Eurocode 8 standards are adopted in all designs and construction works as the best current technical model. This provides a uniform approach for the design of new buildings, and seismic retrofitting of the existing buildings. Hazardous construction materials (e.g., asbestos, POP containing sealants) are banned and environmentally friendly furnishings and equipment (e.g., LED lights instead of mercury containing fluorescent light bulbs) are promoted.

The BBB principle also includes the application of accessible construction principles, e.g., building ramps for wheelchairs (EU 6° incline), accessible door sills, stairs, doors, hygienic facilities, among others. Hygienic facilities are complying with EU standards, taking hygiene, child protection and gender into account. Chemistry and physics labs will be equipped according to EU safety standards and include e.g. fume hoods in chemistry cabinets/labs, secure and safe storage rooms for chemicals, etc. To quantify the impact of BBB, an internal monitoring tool was developed and put in place. The BBB framework is developed based on the criteria listed below:

1. *Implementation while considering Eurocode 8 standards*: To ensure the application of the requirements of Eurocode 8 and specific measures required on the seismic design especially for educational facilities, the structures are being designed and constructed to withstand the most extreme seismic activity. Great attention is paid on respecting all technical design requirements during the civil works implementation.

2. *Energy efficiency and environmental protection:* To guarantee that the energy efficiency requirements are met in the repair and reconstruction of the education facilities, several criteria are considered, namely: (i) High quality thermal insulated façade and terrace in an envelope system which prevents heat loss in the winter and heat gain in the summer, (ii) Solar hot water collectors especially applied in kindergartens, (iii) Efficient lighting system as well as (iv) Efficient heating systems (chiller or VRF systems) among others. In several education facilities, part of Phase II, ready- made installations for installing later a photovoltaic system are considered. In few others, installing photovoltaic systems is being designed.

3. *Health and Safety:* To adapt to the COVID- 19 health emergency conditions, design companies have been requested to introduce new measures, so hygienic conditions are further improved and complying, when possible, to EU standards. Medical and psychological rooms have been introduced in the new schools.

4. *Accessibility:* The design of new schools and improvements to existing ones, take into consideration the accessibility requirements of all users: students, teachers and administration staff, parents, and visitors. However, the focus is on the special needs of children/students with disabilities. The education facilities external environment, entrances, internal circulation, evacuation, other facilities, and classrooms are given attention when designing for accessibility. Particular attention is paid to entrances, corridors, pathways, staircases, etc, with elevators and ramps included in all schools.

5. *IT and smart solution:* to adopt with the new situation, especially after COVID-19, it is necessary to provide the necessary tools to teachers and students. In that context, internet installation and other smart solution instruments are introduced to educational facilities, including IT laboratories.

For each of these categories, several parameters were established since Phase I, which measure the situation before and after the intervention of EU4Schools programme. Baseline data was collected for the situation before earthquake for each parameter (when available). The parameters for after EU4Schoools intervention are based on works completed or as planned in the approved project design and Bill of Quantities. The table below, provides data for 19 education facilities, for which the designs are approved.

Based on this comparison, only in nineteen education facilities, the total square meters of construction area have increased with 4685 square meters, or about 22% increase compared to the pre-earthquake situation. In all nineteen education facilities are added ramps, elevators, and toilets for people with disabilities whereas there were none before. Regarding Health and Safety, important to note the improvements in exist stairs, signs, and fire alarms planned to be installed in all of the nineteen education facilities. Complete information will be provided in the future reports when all designs are completed and approved.

Table 3: List of BBB indicators as per established framework

Main Category	Indicator	Unit	Baseline	2021	Improvement
General improvements	Total square meter of construction after EU4Education Facility intervention	M^2	21,015	25,700	4,685
	Nr. of classrooms / kindergarten groups	Rooms	174	187	13
	Nr. of laboratories	Laboratories	17	27	10
	Education Facility with Gym Access	Piece	4	8	4
	Medical room	Room	2	12	10
	Psychological room	Room	6	13	7
Accessibility	Has the design considered accessibility for people with specific needs/disabilities?	Education Facility	N/A	19	
	Ramps	Education Facility	1	19	18
	Elevator	Education Facility	0	10	10
	Toilets accessible for people with disability	Education Facility	0	18	18
Energy Efficiency	Energy efficiency measures on building envelope thermal and hydro-insulation	Education Facility	0	19	19
	Is the lighting of the building foreseen with LED light?	Education Facility	1	19	18
	Are the main equipment of the building Energy Efficient (CoP of HVAC systems, smart pumps, etc)	Education Facility	0	19	19
	Is there any Heating/Cooling System for the building?	Education Facility	3	19	16
	Is there a hot water system in place?	Education Facility	2	19	17
	Is the hot water system foreseen with a Solar Thermal System?	Education Facility	0	7	7
	Is there a photovoltaic system installed?	Education Facility	0	4	4
It and smart solution	Is there any readymade Internet installation?	Education Facility	4	16	12
	Is there any IT Laboratory?	Education Facility	6	11	5
Seismic	Have project designers considered Eurocode 8 during modelling/calculations for education facilities (including partial/specific factors recommended)?	Education Facility	N/A	19	
	Have supervision confirmed all educational facilities have been constructed according to project	Education Facility	N/A	19	

	design, especially on Eurocode related features?				
Health and Safety	Is there any Emergency Exit?	Education Facility	2	19	17
	Is there Emergency signs?	Education Facility	0	19	19
	Is there Emergency stairs?	Education Facility	0	12	12
	Is there any Fire alarm and firefighting system?	Education Facility	1	19	18
	Is there any CCTV system?	Education Facility	3	19	16
	Is there anti-theft system?	Education Facility	3	19	16
	Is there safe electrical installations and earthing?	Education Facility	10	19	19
	Is there emergency illumination?	Education Facility	0	19	19
	Is there fencing?	Education Facility	16	19	3

.2.3.“Build Back Together” (BBT)

In addition to the “Build Back Better” the programme strongly relies in the implementation of the “Build Back Together” approach. This implies inclusiveness and transparency throughout all the cycles of programme implementation. Working together with local governments, local public institutions, and communities to design and implement recovery activities rapidly with a participatory approach and a transparent and accountable system, is core to EU4Schools programme. Involvement of main stakeholders is crucial to identify and address the needs for adequate education facilities in line with the international standards. In that context, during the reporting period, 39 consultation processes are organised and one Place Check, with participation of around 950 people, representatives of community, teachers, students, kids, local authorities, etc. They are integral part of discussions and all the project designs address the needs articulated during the consultation processes. The Place Check is another tool to ensure that this approach is implemented in all phases of EU4Schools implementation

The one Place Check organised during the reporting period was in the Kindergarten “Jashar Hoxha”, Kamëz, aiming to check if all the standards displayed in the design are implemented during the construction works.

To increase transparency and inclusiveness, the online transparency portal was introduced at each consultation meeting, inviting the public to stay informed on programme milestone and progress, but also to provide their feedback on how different processes can be improved.

At the start of the reporting period, due to Covid – 19 restrictions, consultation meetings were organized with a limit of 10 participants per each consultation meeting. This impacted the community involvement in number of participants, but also the length of the discussions during the consultation meetings. To

mitigate this, prior to the consultation meeting, a video presentation was shared with selected community members via whatsup or other digital tools, to get to know better the two proposed technical designs.

This was considered useful by the participants in the consultation meeting; it simplified the process of understanding the technical designs proposed and it enabled the gathering of opinions and suggestions. In addition, it helped to select the best version according to the needs of the beneficiaries and do different changes as per their suggestions. The contracted design company, under the supervision of the programme engineers, implemented these changes on the selected proposal by the participants during the consultation process.

Consultation meetings were mostly organized in open air, at the education facilities' yards, in order to have as much participants as possible in respect of Covid-19 protocols. Listed below is presented a table of the participants by category:

Table 4: List of participation in the consultation meetings

	Female	Male	Total
Teachers	349	81	430
Students	75	58	133
Community	172	84	256
LG Reps.	53	61	114
Total	**649**	**284**	**933**

.2.4. Annual work-plan for the reporting period

The initial work plan is presented in ***Annex 5***: as changes occurred during the implementation, the updated work plan is presented in ***Annex 6***. The rationale for the changes occurred in the work-plan are presented in the section 2.2 of the report.

.3. IMPACT

The progress of the unified EU4Schools Programme implementation is already providing successful examples and is encouraging respective communities to trust it. As per data provided from the Place Checks satisfaction questionaries, 88.9% of the interviewed are very satisfied with the EU4Schools interventions. By intervention, the interviewers recognize both the quality of works and the participatory approach, guaranteed by the BBB and BBT principles.

The programme is directly impacting positively by:

a. restoring normal academic routines, child-care, and social play,

b. providing safe, inclusive, welcoming environments for all children leading not only to better learning and academic growth, but also to wellbeing, emotional and psychosocial development,

c. providing enabling learning environments for all students, including accommodating children with disabilities,

d. building a sense of community and belonging within the school,

e. cultivating connectedness between the school and its community and providing the community with a meaningful role in their children's education,

f. harmonizing buildings, school playgrounds and environment as children interact with them,

g. equipping the facilities to deal with (post) COVID-19 situation.

The EU4Schools unified Programme, is having an impact in the improvement of learning outcomes of students and teachers frequenting the new or improved education facilities and it is enabling teaching activities in one shift.

Investments in Information and Communication Technologies (ICT) in the new or rehabilitated facilities is creating the basic infrastructure for modern teaching methods, providing benefits for both teachers and students, improved teaching and learning processes that boost learning outcomes, increased students' engagement and more robust opportunities that ICT offers for enrolment in higher education or joining the labor force.

The EU4Schools impact is also noticed by improving fairness and equity in the system of education, with quality education facilities rehabilitated or rebuilt in urban, semi urban, and rural areas with students living either in the cities or villages, are attending similar high quality education schools. The new or repaired educational facilities in urban areas, provide space for more students to attend pre-schools and schools in their neighborhood without the need to travel or walk a distance.

The improved and expanded education infrastructure will better facilitate implementation of inclusive education approaches encouraging better participation of vulnerable children from Roma or Egyptian communities or children with disabilities to attend mainstream education.

The data collected on digital literacy by EU4Schools will be made available to educational authorities at national and local level to be used in the future endeavors and the evidence base related to the impact of learning environments on academic outcomes. Follow up analysis should be undertaken to show the correlation of investments in education infrastructure and improvement of learning outcome or how physical school design affects the health, safety, and learning processes of children.

EU4Schools unified Programme, marks a distinct contribution to the Sustainable Development Agenda. It contributes directly to Sustainable Development Goal 4: *"Ensure inclusive and equitable quality education and promote lifelong learning opportunities for all"* as well as other SDGs as reported on point 1.3 of this report.

The most relevant target and indicator of EU4Schools is:

Build and upgrade education facilities that are child, disability and gender sensitive and provide safe, nonviolent, inclusive, and effective learning environments for all. This target addresses the need for adequate physical infrastructure and safe, inclusive environments that nurture learning for all, regardless of background or disability status.

Indicator 1: Proportion of schools offering basic services, by type of service. Portion of schools with access to: (a) electricity, (b) the Internet for pedagogical purposes, (c) computers for pedagogical purposes, (d)

adapted infrastructure and materials for students with disabilities, (e) basic drinking water, (f) single-sex basic sanitation facilities and (g) basic handwashing facilities (as per the WASH indicator definitions).

The EU4Schools programme objective and expected results are supportive of the country's progress in achieving other SDG 4 targets such as:

(i) By 2030, ensure that all girls and boys complete free, equitable and quality primary and secondary education leading to relevant and Goal 4 effective learning outcomes.

(ii) By 2030, ensure that all girls and boys have access to quality early childhood development, care and pre-primary education so that they are ready for primary education.

(iii) By 2030, ensure equal access for all women and men to affordable and quality technical, vocational, and tertiary education, including university.

(iv) By 2030, substantially increase the number of youth and adults who have relevant skills, including technical and vocational skills, for employment, decent jobs and entrepreneurship.

(v) By 2030, eliminate gender disparities in education and ensure equal access to all levels of education and vocational training for the vulnerable, including persons with disabilities, indigenous people, and children in vulnerable situation.

.4. RISKS, ASSUMPTIONS AND DIFFICULTIES ENCOUNTERED AND MEASURES TAKEN

During the reporting period, the Risk Log specified in the DoA was closely monitored and assessed. All risks assessed during the preparation of the project proposal are mitigated. Some of the risks were more impactful than planned. These changes are reflected in the following table:

Table 5: Table of risks

Nr.	Type or risks	Probability	Lightly impact	Mitigation measures and contingency plan	Mitigation measures undertaken during the reporting period
1	Low level of coordination of central and local actors to make information available, share data and cooperate expediently during the process of Action implementation.	Likely	Major	UNDP is taking a facilitator role in engaging different stakeholders, including governmental authorities in all the steps of planning, implementing, and monitoring of COVID19 Action interventions.	Main institutions, in central and local level are part of the Programme Steering Committee. All interventions are coordinated by the Deputy Prime Minister and Minister of State for Reconstruction and Reforms' Program, and targeted municipalities handled the process in

					due time, despite shortage of staff due to COVID-19.
2	Extended countermeasures at national and international level to prevent the pandemic outspread limit workers mobility and risk to jeopardise project implementation.	Possible	High	Reassessment of the work plan to consider the measures that the Government is taking on COVID-19 pandemic. As required, the EU4Schools' team is preparing the technical specifications and launch procurement processes online (e-procurement). At the same time, the team designed and adopted virtual communication and consultation methodologies.	Delay in design preparation and design approval processes, starting of construction works and evaluation processes due to ongoing pandemic situation. However, a coordination plan to divide the works within the staff has been prepared and implemented. All protocols approved by the government on COVID-19 protective measures are ensured. Masks and sanitizers are procured and distributed to all participants in consultation meetings, respecting the distance and organisation of meetings in open space is promoted. Video presentation have been prepared to ensure maximization and input from the beneficiaries and to cope with the actual conditions. During the reporting period, main works are performed in the office or from home as per established UNDP Albania internal regulations. Virtual communication and consultation methodologies are prepared and used.
3	Lack of capacity of Municipalities to provide construction permits expediently.	Possible	Major	Several consultation meetings are taking place with various offices of the Municipalities to receive appropriate guidance for an expedited process for obtaining the relevant construction permits.	Procedures for issuing the construction permit are extended to all targeted municipalities, right after the signature of the MoUs. Several consultation meetings took place with various offices of the Municipalities to receive appropriate guidance for an expedited process for obtaining the relevant construction permits. Municipalities shared the procedures for issuing the permits

					though in some cases the procedures have not been clearly defined causing delays, DPMSRP has facilitated the process.
4	Limited number of service providers available to deliver the services to a satisfactory level, while several reconstruction and recovery interventions are taking place in the country.	Possible	Moderate	UNDP is using all instruments to attract a considerable number of companies in the competitive processes and use diligent evaluation processes to select the best service providers.	UNDP used all instruments to attract a considerable number of companies in the competitive processes and use diligent evaluation processes to select the best service providers. UNDP launched an invitation for prequalification for Phase II which has added to existing pool of companies as to increase the competitiveness.
5	Municipalities do not have proper documentation of property titles of some rural education facilities that have been damaged by the earthquake	High	Major	The EU4schools team is planning its intervention in stages. It is engaging in dialogue with the relevant central institutions to settle all pending issues and equip Municipalities with due documentation on the education sector assets.	The EU4Schools team is communicating daily with the relevant central institutions to settle all pending issues and equip Municipalities with due documentation on the education sector assets.
6	Quality of reconstructed/ repaired facilities	Possible	Moderate	The Action is using the recovery efforts as an opportunity for improving access to enhanced quality education through improved design of learning spaces, teacher development, and by strengthening the capacity of education authorities at all levels in the planning and implementation of the education system's recovery.	The EU4Schools used the recovery efforts as an opportunity for improving access to enhanced quality education through improved design of learning spaces, teacher development, and by strengthening the capacity of education authorities at all levels in the planning and implementation of the education system's recovery. In that context, all the designs are in line with best standards.

A risk worth to mention, which is not part of the initial Risk-Log, is the increase in the prices of construction material, a phenomenon which is impacting European and worldwide markets. In addition, there is also a shortage of construction materials supply, which might be more impactful considering most construction materials are imported in Albania. This risk is being monitored and more will be reported in the next periodic reports.

.5. STRUCTURE OF THE ACTION'S BUDGET

Even if the EU4Schools Programme is conceptualized as a unified Programme, the budget is clearly divided for each of the phases. Alterations are made only in specific cases, as agreed with the EU Delegation to Albania, mainly to cover costs arise from the Phase I.

.5.1. Correction within the budget

The tables below show budget alterations made in the budget for the reporting period. Justifications and comments for each of the alterations are provided in the financial report.

Table 6: Alterations made through the first year of project implementation - Initial budget

2. Equipment, supplies and Project Office	Unit	Number of units	Unit rate	Total
2.1 Furnitures				
2.1.1 Tables	Per piece	17	260.00	4,420.00
2.1.2 Drawers / Cabinets	Per piece	14	200.00	2,800.00
2.1.3 Chairs	Per piece	25	100.00	2,500.00
2.1.4 Closets	Per piece	14	400.00	5,600.00
2.2 Equipment				
2.2.1 Computers	Per piece	14	1,500.00	21,000.00
2.2.2 Printers/photocopies/scanner	Per piece	4	2,000.00	8,000.00
2.2.3 Cameras	Per piece	1	800.00	800.00
2.2.4 Projectors	Per piece	2	500.00	1,000.00
2.3 Project office				
2.3.1 Vehicles costs (4 vehicles rented + driver + fuel)	Per month	124	2,100.00	260,400.00

Below are presented the proposed adjustments:

Table 7: Alterations made through the first year of project implementation - Proposed adjustments

2. Equipment, supplies and Project Office	Unit	Number of units	Unit rate	Total
2.1 Furnitures				
2.1.1 Tables	Per piece	17	217.79	3,702.40
2.1.2 Drawers / Cabinets	Per piece	14	86.35	1,208.87
2.1.3 Chairs	Per piece	25	68.65	1,716.16
2.1.4 Closets	Per piece	14	207.23	2,901.29
2.2 Equipment				
2.2.1 Computers	Per piece	14	1,433.25	20,065.46
2.2.2 Printers/photocopies/scanner	Per piece	4	786.90	3,147.61
2.2.3 Cameras	Per piece	1	866.29	866.29
2.2.4 Projectors	Per piece	2	630.82	1,261.63
2.3 Project office				

2.3.1 Vehicles costs (6 vehicles rented + driver + fuel)	Per month	164	1,656.40	271,650.28

The rationale for the corrections within the budget are presented below:

Position title for budget lines 1.1.5 and 1.1.11 are revised as per the service contracts. The total cost and their respective unit rates have changed for the budget line 2.1.1; 2.1.2; 2.1.3; 2.1.4; 2.2.1; 2.2.2; 2.2.3 and 2.2.4, as per the actual expenses incurred. The number of units, their respective unit rates and total costs have changed for the budget line 2.3.1.

The total budget remains the same regardless of the proposed changes.

.5.2. Staff and other inputs

Within the reporting period, the EU4Schools has fulfilled the following positions in line with the Programme's organigramme.

Table 8: Job positions filled during the Phase II

No.	Position	Entry on Duty
1	International Programme Manager	10 Aug 2021
2	Monitoring and Reporting Officer	05 Jan 2021
3	Contract Management Officer	15 Feb 2021
4	Community Coordinator	11 Nov 2020
	Community Coordinator	01 Mar 2021
5	Hydrotechnical Engineer	15 Feb 2021
6	National Civil Engineer	07 Dec 2020
	National Civil Engineer	11 Nov 2020
	National Civil Engineer	11 Nov 2020
7	Civil Engineer	24 Mar 2020
	Civil Engineer	10 Jul 2021
8	Finance Officer	01 Mar 2021
9	Procurement Officer	01 Dec 2020
10	Cleaner	01 Jan 2021

By the end of the reporting period all positions were filled, with the exception of the position of Communication Officer.

The position of the Cleaning person will be overlapping with Phase I (11 months) and will be covered by Phase II only after overlapping period (20 months).

One of the National Civil Engineer of EU4Schools Programme has resigned and the last day of his service was 31 October 2021. The hiring process has started for the replacement of this position.

Additionally, the EU4Schools has fulfilled the following positions in line with the EU4Schools's organigramme under Phase I to continue on Phase II:

- 1.1.2 Programme Manager (continuation from Phase I)

- 1.1.5 Civil Engineer (3) (continuation from Phase I)
- 1.1.8 Quality Assurance and Data Management Officer (continuation from Phase I)
- 1.1.11 Procurement Assistant (continuation from Phase I)
- 1.1.13 Administrative and Finance Assistant (continuation from Phase I)
- 1.1.14 Cleaning person 1.1.14.1 Overlapping period with Phase I (11 months)

Two position titles are revised as per the Service Contracts as below:

- One Civil Engineer (point 1.1.5 of the budget) revised into the Senior Civil Engineer.
- The position Procurement assistant (point 1.1.11 of the budget) revised into Procurement Officer.

During the reporting period additional expert support was secured through outsourcing and engagement of the consultants in area such as: Wood technology, energy efficiency in buildings, health and safety, archaeology, architecture, and electrical systems.

.5.3. Sources of funding

Sources of funding are indicated in the Actions Budget (for details please see third tab of *Annex 7*, Budget for Phase II).

.5.4. Procurement Activity and Progress

Procurement is one of the main activities carried out during the EU4Schools Programme with several procurement processes planned to be implemented as foreseen in the annual Procurement Plan. The main processes are related to design and supervision, construction works, equipment and furniture and testing and commissioning. Contracting a number of consultants was foreseen to support the implementation of the programme. During the reporting period, UNDP has carried out several processes for the repair and reconstruction of 41 educational facilities.

Due to the complex nature of the procurement processes included in the programme, a Procurement Strategy is prepared, which outlines in detail all the implemented procurement actions related to works, goods and services. It also provides a clear view on every process, procurement methods applied, how contracts are managed, risks and mitigation measures, as well as the tools that EU4Schools Programme have created to ensure a smooth implementation of each activity. All related procurement actions are governed by UNDP Financial Regulations, Rules and Procedures.

The main principles which guide UNDP procurement in general and for extension apply to procurement of EU4Schools Programme are as follows:

(i) Best Value for Money,

(ii) Fairness, Integrity and Transparency,

(iii) Effective International Competition, and

(iv) In the best interest of UNDP.

In addition, activities are following principles of sustainable development by using designs, methodologies, and technical requirements that make efficient use of resources and energy, protect people and ecological systems, maintain and improve the quality of educational facilities of the communities in 11 targeted municipalities.

Integrity, as demonstrating the core values of UN in daily activities and behaviors: act without consideration of personal gain; resist undue political pressure in decision-making and actions. As part of its commitment to the environment and sustainable management of natural resources, UNDP actively promotes and implements green procurement, taking into consideration the effects of energy consumption, toxicity, ozone depletions, radiations, and the use of recycled materials.

Further to the above core principles, during technical designs, supervision and civil works conducted under the EU4Schools Programme some fundamental principles, such as Build Back Better, Build Back Together, Accessibility for Persons with Disabilities, Inclusion, Gender Equality, Environmental Sustainability, Energy Efficiency, Safety and Security, Seismic Preparedness, are taken into consideration.

Main procurement activities and progress for the reporting period is presented in detail below.

Procurement for Design and Supervision Services

A process of technical assessment of the first 36 educational facilities was conducted in November – December 2020 leading to the preparation of the Terms of Reference (ToR) for the technical design and supervision for all the identified objects, divided in 7 lots. Due to the large volume of works it is decided to launch tenders, where the bidders will be responsible for both, the design and the supervision of the works, in batches of 4-5 educational facilities. Request for Proposals (hereinafter: RFPs) for the preparation of technical designs and supervisions of 36 educational facilities were launched for the 7 lots and the recommended bidders were awarded contracts for preparing the technical designs and the full technical documentation for launching the competitive process for the civil works for each of the identified educational facilities. The same approach will be used for the design and supervision of five educational facilities, part of the agreement amendment.

Table 9: Table with information on the procurement processes

No.	Procurement Process	Contract start date	Contract end date
1	LOT 1 - Designs and Supervision of 3 LOTs Lot 1 includes: 1. Reconstruction of Shijak Kindergarten No 2 – Shijak Municipality 2. Reconstruction of 9-Year School "Rilindja" Sallmone – Shijak Municipality 3. Reconstruction of 9-Year School Vore – Vorë Municipality 4. Reconstruction of 9-Year School Bërxull – Vorë Municipality	19-Mar-21	28-Feb-23
2	LOT 2 - Designs and Supervision of 3 LOTs Lot 2 includes: 1. Reconstruction of High School Naim Frasheri – Durrës Municipality	20-Mar-21	29-Sep-23

	2. Reconstruction of High School Gjergj Kastrioti – Durrës Municipality 3. Repair and retrofitting of 9-Year School Karpen – Kavajë Municipality 4. Repair and retrofitting of Professional School "Charles Telford Erickson" – Golem, Kavajë Municipality 5. Repair and retrofitting of 9-Year School "3 Dëshmorët" - Kavajë Municipality		
3	LOT 3 - Designs and Supervision of 3 LOTs Lot 3 includes: 1. Reconstruction of Professional School "Bernardina Qerraxhi" – Durrës Municipality 2. Reconstruction of Dormitory (campus) of Professional School "Bernardina Qerraxhi" – Durrës Municipality 3. Reconstruction of High School "Olsi Lasko" – Shkozet, Durrës Municipality 4. Repair and retrofitting of Creche No 3 – Durrës Municipality	19-Mar-21	21-Jul-23
4	LOT 4 Design and Supervision for Reconstruction and Repair/Retrofitting of educational facilities located in Tirana Municipality. Lot 4 includes: 1. Repair and retrofitting of 9-year school "Musine Kokalari", Tiranë; 2. Repair and retrofitting of 9-year school "Emin Duraku", Tiranë; 3. Reconstruction of 9-year school "Xhezmi Delli", Tiranë; 4. Repair and retrofitting of professional school "Asim Vokshi", Tiranë.	6-Apr-21	14-Jul-23
5	LOT 5 Design and Supervision for Reconstruction and Repair/Retrofitting of educational facilities, located in Rrogozhina Municipality Lot 5 includes: 1. Reconstruction of 9-year school Kryevidh, Rrogozhinë; 2. Reconstruction of 9-year school Rreth-Greth, Rrogozhinë; 3. Reconstruction of kindergarten Okshtun, Rrogozhinë; 4. Reconstruction of 9-year school and kindergarten Vile Bashtovë, Rrogozhinë; 5. Repair and retrofitting of 9-year school "Xhorxh Sorros", Rrogozhinë.	22-Apr-21	28-Apr-23
6	LOT 6 Design and Supervision for Reconstruction and Repair/Retrofitting of educational facilities, located in Kamza and Tirana Municipalities 1. Reconstruction of Crèche, Kamza Municipality; 2. Repair and retrofitting of "Azem Hajdari" kindergarten, Paskuqan, Kamza Municipality; 3. Repair and retrofitting of "Ibrahim Basha" 9-year school, Bulqesh, Kamza municipality; 4. Repair and retrofitting of Kindergarten No. 41, Tirana municipality; 5. Repair and retrofitting of "26 Nëntori" 9-year school, Tirana municipality.	22-Apr-21	21-Aug-23
7	LOT 7 Design and Supervision for Reconstruction and Repair/Retrofitting of educational facilities, located in Mirdita, Lezha and Durrës Municipalities 1. Repair and retrofitting of Kindergarten No. 1, Mirdita municipality; 2. Reconstruction of "Gjergj Kastrioti" 9-year school, Lezha municipality; 3. Reconstruction and Repair / retrofitting of "Fran Ivanaj" 9-year school and kindergarten, Ishull Shëngjin, Lezha municipality; 4. Reconstruction of Kindergarten in Bizë village, Ishëm, Durrës municipality.	5-May-21	09-May-23

Procurement of civil works

Due to the considerable number of reconstruction/repairs works and the limited timeframe, UNDP Albania issued an open international two-stage tender procedure. This process was used to ensure that bidders selected to provide an offer, had the necessary experience, financial and personnel capacities to successfully complete the works. Timewise, the two-stage process did not delay the process, since it was conducted in parallel with the development of the project designs for the construction works.

The first stage of the tender procedure was an Invitation to Pre-Qualify (hereinafter: ITP). The ITP was advertised internationally for a period of three weeks. The solicitation documents were advertised in UNDP PSO website, e-Tendering, Newspapers and social media. The process resulted in the establishment of a pool of 34 technically qualified bidders in terms of experience, financial and personnel capacities, whereas the other 11 bidders were deemed not qualified. As the list of targeted educational facilities expanded, the need for additional qualified bidders led to the launching of another pre-qualification exercise. The new pre-qualification process allowed companies, which had been previously qualified to upgrade their presence in the four groups described in the ITP.

If it was determined that the bidder had the relevant capacities, it was included in higher groups. Considering learned lessons from the first pre-qualification exercise and based on preliminary estimated values of the upcoming interventions, it was decided to introduce another band to the new ITP. The newly established Group 4 includes companies capable of performing works valued over $1,000,000.

The ITP exercises provided a list of highly qualified contractors, who could provide construction services for educational facilities falling in the four pre-defined groups. Only companies qualified in one of the pre-defined groups are receiving, through the second stage process, the Invitation to Bid (hereinafter: ITB) respective to its value. Thus, if the estimated value of the facility to be reconstructed/ repaired was below $300,000, companies in Groups 1, 2, 3 and 4 received the ITB. If the estimated value of the facility to be reconstructed/repaired was between $300,000 - $600,000, only companies qualified in Group 2, 3 and received the ITB. If the estimated value of the facility to be reconstructed/repaired was between $600,000 - $1,000,000, only companies qualified in Groups 3 and 4 received the ITB. If the estimated value of the facility to be reconstructed/repaired was over $1,000,000, only companies qualified in Groups 4 received the ITB.

As of the second pre-qualification exercise, the Programme has a pool of 56 qualified bidders, that will receive Invitations to Bid according to their assessed capacities. In this regard, prequalified companies are structured in groups as below:

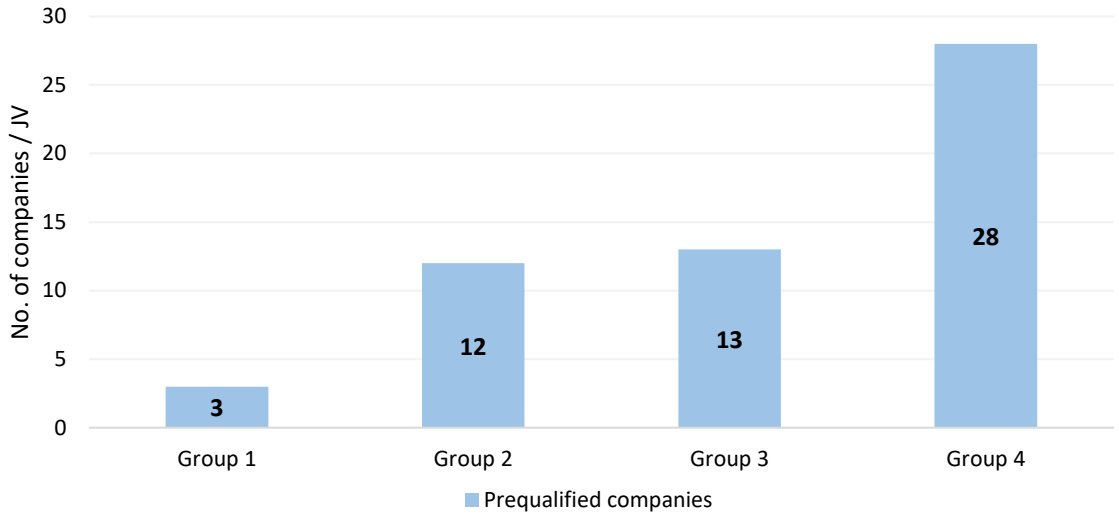


Figure 3: Groups of prequalified companies

The second stage of the procurement process consists of a competitive bidding process aimed at inviting bids from the pre-qualified companies.

EU4Schools launched a series of 17 ITBs from February to November 2021. After receipt of offers through e-Tendering module, the bids are preliminary exanimated in terms of properly submitted forms and documentation and, after passing the preliminary examination, they are evaluated in terms of their technical and financial submission. The technical evaluation is based on the submitted Method statement, Quality assurance review mechanism, Work schedule, Health, Safety and Environmental (HSE) programs, as well as their provided prices, bid security, staff, machineries, ongoing works, legal and financial documentation and equipment to be installed in the facilities. Project engineers conduct a price analysis of the financial offers making sure that there is no significant price deviation from the internal estimated amounts, prepared in the project design phase, in the Bill of Quantities (BoQ).

In addition, the pre-qualified bidders are requested to provide an overview of all their works in progress (with UNDP or through contracts not with UNDP) and cash flow information. This contributed to the capacity assessment carried out for the bidders and determined whether they had enough resources to deliver two or more projects simultaneously.

UNDP reviewed ongoing projects, cash flow, and made sure teams/engineers proposed for an ITB were not involved in other projects. When applying for several ITBs simultaneously, UNDP made sure that bidders proposed different and dedicated staff to each project. Reference checks are conducted at the end of each evaluation process, with previous employers. EU4Schools used this practice for 17 tender processes, awarding Contract for Works to 7 different bidders, as of the date of the reporting period while the rest of the processes are still under evaluation.

Procurement of Furniture and Equipment

Based on the identified needs, procurement processes were carried out to supply with furniture and equipment all the repaired or reconstructed educational facilities. An Invitation to Bid was issued aiming at establishing Long-Term Agreement (LTA) with multiple suppliers for indicatively 58 educational facilities.

The selected procurement approach reduced transaction costs and identified potential qualified companies able to deliver furniture as per the forecasted volume and with the best value for money. In that context, a market research was conducted to assess the capacities of local vendors in producing and providing the required furniture. As per market research, it resulted that none of the local vendors had the capacities to produce and deliver the entire list of items/furniture for all educational facilities within the appropriate timeframe. In this regard, the appropriate option was to divide the requirement into LOTs

The approach enables vendors to timely deliver all the necessary furniture, while also mitigating the risk of non-performance. No additional competitive bidding process or any other bidding between the LTA contractors will be requested. Goods will be supplied based on vendor availability and capacities, in order to mitigate the risk for timely delivery of all furniture at the respective educational facilities. The Invitation to Bid resulted in the establishment of 5 Long-Term Agreements with the most qualified companies in the market. The LTAs have been established for an initial period of one year, with the option of extending them for an additional two years.

Procurement of IT Equipment

Based on the identified needs, educational facilities will also be furnished with IT equipment, such as computers, printers, copiers, routers and switches. The requirement aims at providing IT equipment for indicatively 47 educational facilities (phase I and phase 2). Due to the complexity and volume of the requirement, a request to submit an offer was sent to the One-UN Long-Term Agreements IT Consolidators. These companies are contracted by the United Nations to provide IT goods and services and have ongoing LTAs with UNDP Globally. The request for offer was sent to all four LTA Holders. The process is currently under evaluation and the contract is expected to be awarded by end year 2021.

Procurement of Services for Consultants/Technical Experts

In the framework of programme activities, several consultants/technical experts are contracted, as they are deemed necessary for the proper implementation of the programme. These experts are contracted via Individual Contracts (IC). The types of services performed, consist of specialized knowledge or expertise, that could not be provided by the internal staff of the programme. Some of the expertise engaged include reviewing and evaluating the detailed architectural designs in compliance with Albanian Legislation and European Standards; communication visibility of the programme, providing professional photos and videos; monitoring the implementation of the civil works at the site in compliance with the EU and national standards on health and safety works; training at the construction site on health and safety principles; consultancy on implementing of highly energy efficient social building standard and supporting the preparation of specifications for furniture and equipment.

.6. COORDINATION AND COLLABORATION

The main mechanism established to oversee and coordinate the operations of the EU4Schools is the Programme Steering Committee. It takes all necessary strategic decisions and provide policy guidance and recommendation regarding the EU4Schools strategy and objectives, receives and comment semi-annual reports, approve annual plans of operation and reports. The PSC is composed of representatives from the European Union Delegation to Albania, (as the donor), UNDP, (as the implementing Agency), a

Representative of the Government of Albania (Deputy Prime Minister and Minister of State for Reconstruction and Reforms' Program or the Ministry of Education and Sports), UN Resident Coordinator and one representative from each of beneficiary municipalities. It summons at least twice a year, and upon necessity.

In that context, during the reporting period are prepared and approved the terms of reference for functioning of the Programme Steering Committee. All the institutions represented in the committee appointed one high level person as member of the PSC. The meeting was organized on January 21, 2021 and this was the first PSC meeting with representative of 11 Municipalities. The main result of the first PSC meeting was the approval of the annual work plan for 2021 and the review and approval of the transparency portal of "EU4Schools".

Strong coordination is ensured with state institutions, not only central institutions/members of the Programme Steering Committee, but also with other institutions such as Institute of Construction, General Directorate of Taxation, etc. The cooperation was already set up during Phase I and it will be enforced during the implementation of the rest of the EU4Schools programme. In this context, a MoU is singed between UNDP and Institute of Construction to clarify roles and responsibilities of parties during implementation of the Action. On the other side, local education offices, part of the Ministry of Education, Sports and Youth have contributed to the consultation meetings especially on issues related to the standards of design/civil works for each educational facility.

In order to facilitate technical level coordination work and expedite work processes, a Joint Coordination Team is established, including representative of UNDP, EUD, Deputy Prime Minister and Minister of State for Reconstruction and Reforms' Program and Ministry of Education Sports and Youth. It aims to discuss issues such as:

- Progress update of all programme activities.
- Status of implementation of various works and objects.
- Address all challenges and bottlenecks in programme and construction implementation, especially those mentioned above as a priority.
- Progress update of other reconstruction programs as relevant for EU4Schools implementation.
- Follow up on the Calendar of consultations.
- Any other issue as guided by the Programme Steering Committee or as requested by the Joint Co-ordination Team members.

During the reporting period were organized four JCT meetings.

The Technical Assistance Group is an addition to the Programme Steering Committee and the Joint Coordination Team, thanks to which coordination on a technical level is established. More information on TAG was provided on the section 1.5 of the report. The Terms of Reference for the functioning of the Technical Assistance Group are found in *Annex 8*.

.7. HANDOVER/SUSTAINABILITY

From the very start of the Programme, UNDP signed a Memorandum of Understanding with each of the Municipalities to outline the long-term obligations of partner institutions in the implementation of the EU4Schools as well as their roles and responsibilities when it comes to the operation and maintenance of the newly refurbished facilities. The Municipalities agreed to adhere to the new established standards in education infrastructure facilities and allocate funding for the appropriate maintenance of the repaired and reconstructed facilities.

The EU4Schools promoted that the new models of consultative processes with the interested stakeholders, students, teachers, and parents' communities are adopted by the Municipalities as a new standard for public consultation and stakeholder's engagement. In that context, the meetings are organized in close coordination with local authorities and representative offices of the Ministry of Education, Sports and Youth at the local level.

Based on the lessons learnt from the Phase I, intensive communication and meetings are organised with relevant central and local authorities to ensure that the relevant procedures for construction permits are done in due time. Experience to date with the municipalities has shown that when local governments are involved in the process from its inception, and when obligations are clear, detailed and discussed between the parties, local governments are more responsible and more willing to collaborate, get the ownership of rebuilding process and ensure sustainability of the investment and the Action in the longer run.

In its overall efforts to achieve sustained results, the Programme has also adopted new approaches to increase the capacities of Action partners to be able to engage in programme activities and to deliver qualitatively. Training have been conducted with construction companies to introduce to procurement procedures and construction standards foreseen in the Action. A training on rules and regulations on safety at the workplace and COVID 19 protocols has been prepared and will be delivered to all contractors' workers.

A manual on education facilities maintenance is prepared and shared for each education facility completed with municipalities along with a dedicated training for all educational facilities staff. A manual on health and safety at works is prepared and trainings on the issue are ongoing in each construction sites, including staff of construction and supervision companies.

During this reporting period, several facilities were completed and handed over to local authorities.

The handing over process went through several steps:

- Completing the documentation of the project
- Ensure that the utilities are connected (Power, Water and Sewage)
- Testing and commissioning
- Training of nominated Operation and Maintenance staff by the municipality

To achieve the above, and due to delays in connecting the facilities to the utilities, the process was amended into the following:

- Substantial Completion
- Complete Testing and Commissioning
- Nominating and training of maintenance staff: Municipalities were found to be in shortage of the required resources (Human and Financial) and thus require support to enable them to maintain those new facilities and secure the sustainability of the facilities.
- Final Handover

.8. CHANGES INTRODUCED IN IMPLEMENTATION

As stated, on July 5, 2021 an amendment to the cooperation agreement was signed between the Delegation of EU in Albania and UNDP Albania. Through this amendment, 5 more education facilities were added to the scope of EU4schools, (thus the total number of education facilities to be repaired/reconstructed is now 41 for Phase II). Respectively, the budget, funded by European Union, was increased with 10 million Euro. Through this amendment, the unified EU4Schools Programme will repair/reconstruct 63 education facilities in 11 municipalities.

Other than the amendment, no major changes to the activities and results of the programme are introduced during the reporting period. However, after preparation of detailed designs, in line with the national standards as stated in the Decision of Council of Ministers (DCM) no. 319, dated 12.04.2017 "On approval of standards for the design of schools" and DCM no. 159, dated 01.03.2017 “On approval of standards for the design of kindergartens” and following the “Build Back Better” principles, some changes are proposed and agreed among UNDP, EUD in Albania and DPMSP representatives. The main changes introduced are as follow:

A- Changes in the type or scale of intervention as per list of education facilities below:

1. “Musine Kokalari” 9-year school in Tirana Municipality: A new section was designed to be added to the existence structure. This was a requirement to accommodate the needs of the education facility management and the community requirements.
2. “Emin Duraku” 9-year school in Tirana Municipality: Located in the heart of the country’s capital, Tirana, this education facility welcomes 1300 children impacting a considerable community. The school was considered for repair and retrofitting, however a further decision from the institute of Construction was issued to demolish and reconstruct the school so it can accommodate all requests gathered from the community consultations and the other legal requirements.
3. “Asim Vokshi” high school in Tirana Municipality: The existing gym of the education facility was planned to be repaired. After the design and consultation process, it was agreed to reconstruct the gym so it can accommodate the requirements of the students and teachers at the school.
4. Kindergarten and creche in Rubik, Mirditë Municipality: This education facility was initially foreseen to be repaired. From the evaluation carried prior to the design process, it was found that

the building was structurally unstable thus "forcing" the decision to change its intervention into reconstruction.

B- Changes/delays related to land plots

1. The land plot of "Eftali Koçi's" 9-year school Durrës and kindergarten (as provided by the Durrës Municipality) overlaps with an archaeological zone. Rescue archeology works were undertaken, and the findings are being cataloged and recorded. Archeological ruins within construction plot have an impact on cost and timeline.

2. "Gjergj Kastrioti" 9-year school in Lezha Municipality: To accommodate the requests of the teachers, students and the community for a gym where sports activity can be carried, the Lezha Municipality provided a land plot where the gym is planned to be designed and to constructed.

C- Changes related to the number of students

The terms of references for the preparation of the technical designs, must include the number of students/children; any changes in the number of students is reflected in the technical design. Such is the case of the "Bernardina Qerraxhiu" Professional High School in Durrës and "Bernardina Qerraxhiu" dormitory. The initial data provided by the local government, was 150 students for the dormitory and 250 students for the High School. Based on the consultation process with the management team of the education facility as well as the education department in the Municipality of Durrës, and to reflect the growing number of students, the ToR were changed to create a technical design which accommodates 200 students for the dormitory and 300 students for the High School.

.9. LESSONS LEARNED AND CHALLENGES

Throughout the reporting period, lessons were learned which have impacted the EU4Schools programme implementation. These lessons provide both confirmation of positive steps taken, and solution provided, as well as issues to address and improve. The lessons are listed as below:

- Application for building permits should foresee longer period than the anticipated construction period, to avoid redoing the application for permit extension in case delays happen during the project implementation.

- Demolition of existing facilities by the municipalities is never good enough for the contractors to start working. An additional demolition and debris removal process is often needed in all sites where new schools are to be built.

- The need to arrange with municipalities to complete the needed procedures for electrical, water and sewer connections much in advance, so that no delays happen because of missing electricity or water connection

- Attending Site visits and pre-bid conference by the bidders prior to submission of bids should be encouraged to enable them to get more realistic estimation of the anticipated costs.

- During the consultation process there was noticed a high interest for participation on the part of students and teachers though Covid 19 limitations do not allow for big group gatherings. A video presentation was prepared and shared prior to the consultation meeting with all parties invited in the meeting. This allowed for the participants (children, students, teachers, parents and local authorities) review the project proposals better, get the views of many more interested individuals and provide insightful feed-back in the consultation events.

The challenges stated for the reporting mostly relate to the capacities of the local governments to address the obligations of the EU4Schools as stipulated in the respective MoUs. A detailed explanation is provided below:

1. Durrës Municipality has requested an in-depth and extended analysis of the interventions previously agreed, with the special request to have the final opinion and approval from the Institute of Construction. The time requested to carry this procedure by this Municipality took 4 months to be completed, causing delays and postponement in the annual plan.

2. Municipalities have faced challenges in collecting and delivering ownership documents which are crucial for all the design and approval phases of the technical project designs. A special case was the Municipality of Lezha which had very specific requests for two education facilities part of the EU4Schools scope of work. After negotiations, the Municipality of Lezha provided extra plots of land which enables designs and construction of education facilities as per their needs.

3. Permits issuing continues to be a challenge; this process has taken a lot more time and efforts as expected due to limited capacities to handle the number of requests for construction permits.

.10. VISIBILITY, TRANSPARENCCY AND COMMUNICATION

As part of the Communication and Visibility Plan, during the reporting period, the EU4Schools has managed to provide prolific information communicated through many posts in the social media. Communication and visibility of the unified programme, are done based on the Action plan, agreed with EU Delegation to Albania. Action plan has been revised to address challenges due to measures taken to prevent COVID-19. In that context, main communications are done through social media. All content was created to reflect the progress of the unified EU4Schools Programme and was approved by the Delegation of EU in Albania prior to be published. The content reflected the implementation of Build Back Better, Build Back Together, and the lives of children, teachers and parents positively impacted by the programme.

More specifically

- 231 posts were posted on Facebook;
- 137 posts on Instagram;
- 141 tweets on Twitter and
- 18 publications in national online media.

The chart below shows the monthly number of posts for the reporting period:




Figure 4: Monthly number of posts

Though budgeted in Phase I, they have informed and disseminated information on the work of EU4Schools programme generally.

All content was created to reflect the progress of the EU4Schools and was approved by the Delegation of EU in Albania prior to be published. The content reflected the implementation of Build Back Better, Build Back Together, and the lives of children, teachers and parents positively impacted by the programme.

Five press trips are organized in education facilities, targeted by the EU4Schools unified programme, aiming to inform journalists on the progress of the programme. High representatives of EU Delegation to Albania, Albanian Government and UNDP, participated in these trips providing detailed information on two main principles where the unified Programme is based: (i) Build back better and (ii) Build back together.

In addition, a travelling exhibition was organized in May 2021 in the context of the European Weeks. The exhibition featured movable panels for each municipality where EU4Schools is working on. The exhibition was displayed entirely in Scanderbeg Square in Tirana, (for 4 days) and two days in Durres, with a total of 9 Municipalities displayed totally or partially. The exhibition was visited by about 5000 citizens and children.

A questionnaire was prepared, and 120 people were interviewed after visiting the exhibition. After the information provided in the exhibition and the questions and answers with the programme team present in the exhibition, 90% of the interviewed visitors were confident that all education facilities the EU4Schools is repairing, or reconstructing will be up to the standards required.

Visibility materials, such as T-shirts, caps, masks, pens etc... are produced and distributed to enhance the visibility of the Programme. During the reporting period, are prepared and shared 8 video stories, showing the real impact of the unified EU4Schools Programme.

On the other side, EU4Schools transparency portal, has been an important tool tool to improve accountability and serves as an effective tool for tracking of the Programme. Launched on 27 January 2021, the transparency portal is the main tool to communicate the results of the programme and inform and update stakeholders and the general public on action progress.

The transparency portal structure includes information presented in various categories of content including the following elements: (i) home, (ii) about the portal, (iii) progress update, (iii) questions and answers, (iv) gallery, (v) programme data and (vi) feedback. All educational facility's subcategories include information about the municipality, educational facility, geo-location, type of intervention, type of facilities, building status prior to intervention, start and completion dates, contract values, and so on.

Comprehensive information is provided for education facilities targeted by the unified Programme. information is updated on a regular basis by the respective members of the project team. During the reporting period, the portal is visited by 7 075 users, which have visited 20 373 pages and have had 181 577 user interactions with Power BI dashboard embedded in the portal.

Use of the portal was promoted during EU4Schools travelling exhibition, whereby through a touch screen wide TV, the visitor could learn how to navigate the portal and access information. The portal was also used to request information using the contact us option provided in the portal. It is also promoted during consultation meetings and place checks organized. Journalists participating in press trips are informed in detail about the portal and are encouraged to use it.

LIST OF TABLES

Table 1: List of EU4Schools assumptions as per Log Frame 12
Table 2: List of education facilities where civil works have commenced 16
Table 3: List of BBB indicators as per established framework 22
Table 4: List of participation in the consultation meetings 24
Table 5: Table of risks 26
Table 6: Alterations made through the first year of project implementation - Initial budget 29
Table 7: Alterations made through the first year of project implementation - Proposed adjustments 29
Table 8: Job positions filled during the Phase II 30
Table 9: Table with information on the procurement processes 32

LIST OF ANNEXES

ANNEX 1 – LIST OF EDUCATION FACILITIES TARGETED BY EU4SCHOOLS PROGRAMME
ANNEX 2 – LOGICAL FRAMEWORK
ANNEX 3 – PORTAL VISIBILITY STATISTICS
ANNEX 4 – COMMUNICATION AND VISIBILITY REPORTS
ANNEX 5 – PLANNED EU4SCHOOLS PROGRAMME ANNUAL WORK PLAN – Year 1
ANNEX 6 – UPDATED EU4SCHOOLS PROGRAMME ANNUAL WORK PLAN – Year 1
ANNEX 7 – BUDGET OF THE PROGRAMME
ANNEX 8 – TECHNICAL ASSURANCE GROUP TERMS OF REFERENCE

This project is funded by the European Union

REPUBLIKA E SHQIPËRISË
KËSHILLI I MINISTRAVE
MINISTËR SHTETI PËR RINDËRTIMIN

Annexes



ANNEX 1 – LIST OF EDUCATION FACILITIES TARGETED BY EU4SCHOOLS PROGRAMME..... 3

ANNEX 2 – LOGICAL FRAMEWORK 5

ANNEX 3 – PORTAL VISIBILITY STATISTICS.....15

ANNEX 4 – COMMUNICATION AND VISIBILITY REPORTS.....17

ANNEX 5 – PLANNED EU4SCHOOLS PROGRAMME ANNUAL WORK PLAN – YEAR 1.....86

ANNEX 6 – UPDATED EU4SCHOOLS PROGRAMME ANNUAL WORK PLAN – YEAR 1.....90

ANNEX 7 – BUDGET OF THE PROGRAMME.....94

ANNEX 8 – TECHNICAL ASSURANCE GROUP TERMS OF REFERENCE.....95

This project is funded by the European Union

REPUBLIKA E SHQIPËRISË
KËSHILLI I MINISTRAVE
MINISTËR SHTETI PËR RINDËRTIMIN

ANNEX 1 – LIST OF EDUCATION FACILITIES TARGETED BY EU4SCHOOLS PROGRAMME

No	Municipality	Educational facility
1	Durrës	High school “Naim Frashëri”
2		High school “Gjergj Kastrioti”
3		High school “Olsi Lasko”, Shkozet
4		Kindergarten, 9-year school “Eftali Koçi”
5		Crèche No.3
6		Kindergarten Bizë, Ishëm
7		Professional School “Bernardina Qerraxhi”
8		Dormitory “Bernardina Qerraxhi”
9		Crèche No.2
10		Kindergarten Manëz
11		9-year school “14 Nëntori”
12		Dormitory “Beqir Çela”
13	Kavajë	9-year school Karpen
14		9-year school “3 Dëshmorët”
15		Professional high school “Charles Teleford Erikson”, Golem
16	Kamëz	Crèche Kamëz
17		Kindergarten “Azem Hajdari”, Paskuqan
18		Kindergarten “Jashar Hoxha”, Paskuqan
19		9-year school “Ibrahim Basha”, Bulqesh
20	Kurbin	Kindergarten No. 1 Mamurras
21	Krujë	Kindergarten Varosh
22		Kindergarten, 9-year school Bilaj
23	Rrogozhinë	Kindergarten, 9-year school Kryevidh
24		Kindergarten, 9-year school Rreth-Greth
25		9-year school “Xhorxh Sorros”
26		Kindergarten Okshtun
27		Kindergarten, 9-year school Vilë Bashtovë
28	Lezhë	9-year school “Gjergj Kastrioti”
29		9-year school “Fran Ivanaj”, Ishull Shëngjin
30	Tiranë	Kindergarten No. 41

No	Municipality	Educational facility
31		9-year school “Musine Kokalari”
32		9-year school “26 Nëntori”
33		9-year school “Emin Duraku”
34		9-year school “Xhezmi Delli”
35		Professional high school “Asim Vokshi”
36		High school “Myslym Keta”
37	Mirditë	Kindergarten, Crèche No. 1, Rubik
38	Shijak	Kindergarten No. 2
39		Kindergarten, 9-year school “Rilindja”, Sallmone
40	Vorë	9-year school Bërxullë
41		9-year school Vorë

This project is funded by the European Union

REPUBLIKA E SHQIPËRISË
KËSHILLI I MINISTRAVE
MINISTËR SHTETI PËR RINDËRTIMIN

ANNEX 2 – LOGICAL FRAMEWORK

	Results chain	Indicators	Baseline (incl. reference year)	Current value November 3, 2021	Targets (incl. reference year)	Sources and means of verification	Assumptions
Overall objective: Impact	To further support central and local governments in reducing social and economic losses from the earthquake, and to accelerate the recovery process through educational facility repairs and reconstruction, as a continuation of the "EU4Schools" Phase I.	Number of people in affected areas benefiting from improved education facilities	Baseline: 0 (2020)	Total: **0** indirect beneficiaries (community) ***101,432*** *people benefiting from* ***5*** *education facilities under construction work*	Target: Up to **800,000** people benefiting from improved education facilities (2023)	Official related reports from affected municipalities Official related reports from central institutions Official related reports from the international community. Action reports	
Specific objective(s): Outcome(s)	SO1: To support repairing and reconstruction, including basic furnishing, of education facilities in municipalities affected by the earthquake according to the EU standards;	SO1: Indicatively 41 education facilities repaired and reconstructed according to the EU standards	Baseline: 0 (2020)	Total: **0** education facilities repaired and reconstructed ***5*** *education facilities under*	Target: **41** education facilities repaired and reconstructed (2023)	Action reports and relevant technical/tender documentation Education facilities work/equipment	Coordination and complementarity with recovery assistance interventions delivered by governments

	according to international standards			*construction work*		delivery protocols signed by beneficiaries Official documentation and reports from target municipalities Equipment/goods delivery protocols signed by beneficiaries Memorandum of Understanding with municipalities	and international community Central government is committed to collaborate in sharing information Target municipalities cooperate effectively and engage in all relevant action activities by providing relevant documentation Weather conditions are
		SO1: Indicatively 41 of education facilities with basic furniture and equipment	Baseline: 0 (2020)	Total: **0** education facilities with basic furniture and equipment ***1*** *education facility under furnish and equipment process*	Target: **41** education facilities with basic furniture and equipment (2023)		
		SO1: Around 14.500 children and students (boys and girls) benefiting from improved education facilities	Baseline: 0 (2020)	Total: **0** children and students benefiting from improved education facilities ***1,156*** *children and students benefiting from* ***5*** *education facilities under*	Target: **Around 14.500** children and students (boys and girls) benefiting from improved education facilities (2023)		

				construction work			conducive of construction works
		SO1: Around 700 teachers and professional staff (women and men) benefiting from the new education facilities	Baseline: 0 (2020)	Total: **69** teachers benefiting from the new education facilities ***574*** *teachers benefiting from* ***5*** *education facilities under construction work*	Target: **Around 700** teachers and professional staff (women and men) benefiting from the new education facilities (2023)		
		SO1: Indicatively 41 education facilities with increased energy efficiency	Baseline: 0 (2020)	Total: **0** education facilities ***5 e****ducation facilities under construction work*	Target: **41** education facilities with increased energy efficiency (2023)		

		SO1: Indicatively 41 education facilities with improved accessibility	Baseline: 0 (2020)	Total: **0** education facilities ***5 e****ducation facilities under construction work*	Target: **41** education facilities with improved accessibility (2023)		
		SO1: Indicatively 41 educational facilities adopted to address the exigencies of pandemic situation	Baseline: 0 (2020)	Total: **0** education facilities ***5 e****ducation facilities under construction work*	Target: **41** education facilities adopted to address the exigencies of pandemic situation (2023)		
	SO2: To provide increased transparency, accountability and inclusiveness to the recovery process	SO2: Up to 80 consultative forums organised	Baseline: 0 (2020)	Total: **40** consultative forums organised in **36** education facilities	Target: **Up to 80** consultative forums organised (2023)		
		SO2: Up to 11 municipalities accepting new standards for maintenance of education facilities	Baseline: 0 (2020)	Total: **11** municipalities accepting new standards for maintenance of	**Target achieved**		

				education facilities			
	SO3: To improve capacities of central and local governments in accelerating the recovery processes according to the highest international standards	SO3: Around 100 local staff trained to apply international standards during operations and maintenance	Baseline: 0 (2020)	Total: **0** staff trained to apply international standards during operations and maintenance	Target: **Around 100** local staff trained to apply international standards during operations and maintenance (2023)		
Results	Result 1: Educational facilities repaired and/or reconstructed, with a strong emphasis on sustainability, inclusiveness, and environmental protection.	R1: Indicatively 41 technical designs in place for repair and/or reconstruction	Baseline: 0 (2020)	Total: **19** technical designs approved	Target: **41** technical designs in place for repair and/or reconstruction (2023)	Action reports and relevant technical documentation Contracts signed with service providers Official documentation and reports from target municipalities	Target municipalities are committed to provide necessary documents Availability of qualified construction companies
		R1: Indicatively 41 reports for testing and commissioning finalised and approved	Baseline: 0 (2020)	Total: **0** reports for testing and commissioning finalised and approved	Target: **41** reports for testing and commissioning finalised and approved (2023)		
		R1: Indicatively 60 inspections of works at	Baseline: 0 (2020)	Total: **0** inspections of	Target: **41** inspections of		

		the end of defects notification periods in indicatively 41 educational facilities		works at the end of defects notification periods	works at the end of defects notification periods (2024)	Monitoring reports provided by businesses intelligence database Minutes of meetings for consultative forums Participant lists Photos	Procurement procedures are implemented in due time
	Result 2: Quality of learning environment, including technical capacities of central and local level institutions improved	R2: Up to 26 IT laboratories in place	Baseline: 0 (2020)	Total: **0** IT laboratories in place *Construction works in progress in 2 education facilities that includes IT laboratory*	Target: **Up to 26** IT laboratories in place (2023)		
		R2: Up to 41 health rooms created and equipped	Baseline: 0 (2020)	Total: **0** health rooms created and equipped ***5 e**ducation facilities under construction work*	Target: **Up to 41** health rooms created and equipped (2023)		
		R2: Up to 41 psychosocial rooms finalized to serve the	Baseline: 0 (2020)	Total: **0** psychosocial rooms finalized	Target: **Up to 41** psychosocial rooms finalized (2023)		

		needs of the teachers and students		*5 education facilities under construction work*			
		R2: 1 Manual on operations prepared and shared	Baseline: 0 (2020)	Total: Manual of operations prepared	Target: 1 Manual on operations prepared and shared (2023)		
	Result 3: Transparency, accountability and inclusiveness in recovery processes strengthened	R3: 11 MoUs signed with targeted municipalities	Baseline: 0 (2020)	Total: **11** MoUs signed with municipalities	Target achieved		
		R3: Up to 80 consultative meetings organised	Baseline: 0 (2020)	Total: **40** consultative forums organised in **36** education facilities	Target: **Up to 80** consultative forums organised (2023)		
		R3: Around 2000 people participating in consultative processes	Baseline: 0 (2020)	Total: **946** people participating in consultative processes	Target: **Around 2000** people participating in consultative processes (2023)		

		R3: Up to 20 short stories videos prepared	Baseline: 0 (2020)	Total: 0*	Target: **Up to 20** short stories videos prepared (2024)		
		R3: Up to 10 events organised	Baseline: 0 (2020)	Total: **1** event organised	R3: **Up to 10** events organized (2024)		
		R3: Up to 10.000 visibility elements produced (masks, T-shirts, pens, caps etc.)	Baseline: 0 (2020)	Total: **13.019** visibility elements produced	**Target achieved**		
		R3: Number of Visitors on EU4Schools portal	Baseline: 0 (2020)	Total: **7,075** Visits on EU4Schools Portal	Target: Raising awareness of EU4Schools Portal via different tools and activities		
		R3: Number of Pages Visited on EU4Schools portal	Baseline: 0 (2020)	Total: **20,373** Pages Visited on EU4Schools Portal			
		R3: Number of User Interactions on EU4Schools portal	Baseline: 0 (2020)	Total: **181,577** User Interactions on EU4Schools Portal			

* During the reporting period, all video materials are prepared under the communication budget of Phase I.

Activities	*Activities relevant for Result 1:* Activity 1.1: Technical assessment of education facilities and identification of the needs for infrastructure intervention. Activity 1.2: Contracting of companies for the preparation of detailed technical design (FEED)[†] and supervision services for educational facilities to repair or reconstructed. Activity 1.3: Contracting construction companies and implementation of the civil, mechanical and electrical works for repair and reconstruction Activity 1.4: Testing and commissioning for repaired and reconstructed facilities Activity 1.5: Formal handover of repaired and reconstructed education facilities Activity 1.6: Final inspection of works at the end of defects notification period *Activities related with Result 2:* Activity 2.1: Preparation of technical specifications for furniture and equipment for repaired and reconstructed facilities Activity 2.2: Purchase and delivery of furniture and equipment for each repaired and reconstructed educational facility	Human Resources Equipment, supplies & local office Visibility actions Other costs, services Indirect Costs TOTAL BUDGET EUROPEAN UNION UNDP and local governments	1,735,250.00 604,120.00 238,700.00 54,146,696.35 3,925,233.65 60,650,000.00 60,000,000.00 650,000.00	Preliminary pool of potential service providers (construction works/delivery of equipment/other services) is created. Strong motivation for participation and engagement on behalf of target municipalities Motivation and participation from teachers, students and local community with concrete ideas

[†] FEED: Front to End Engineering Design




	Activity 2.3: Conducting a training needs assessment of the teachers of primary and basic education in IT and digital literacy to identify gaps and upgrading strategies and implement the recommendations. Activity 2.4: Strengthen local capacities in Operations and Maintenance and health and safety in school environment. *Activities related with Result 3:* Activity 3.1: Signature of Memorandum of Understanding (MoU) with municipalities and specific dialogue and interventions to ensure their full commitment during the Action implementation and at the end for the maintenance of the facilities Activity 3.2: Community led local consultations on the interventions Activity 3.3: Updating the online, publicly accessible BI (Business Intelligence) dashboard available to all partners and the public through web technologies, for showing Action progress. Activity 3.4: Communicate the results through visibility actions		


This project is funded by the European Union


REPUBLIKA E SHQIPËRISË
KËSHILLI I MINISTRAVE
MINISTËR SHTETI PËR RINDËRTIMIN


ANNEX 3 – PORTAL VISIBILITY STATISTICS

7075	20373	2.88	181577	25.66
Total Visits	Pages	Pages / Visit	Clicks	Clicks / Visit

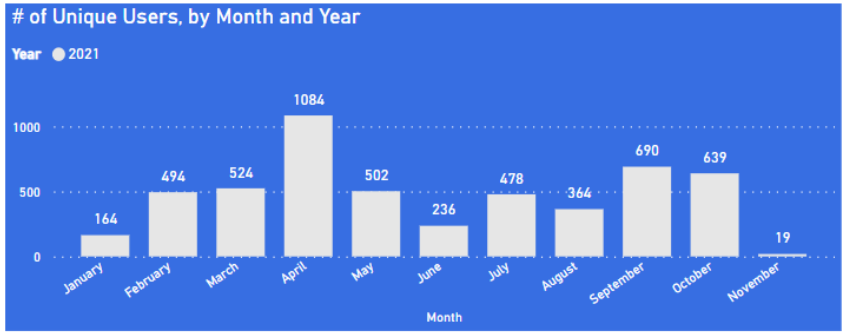

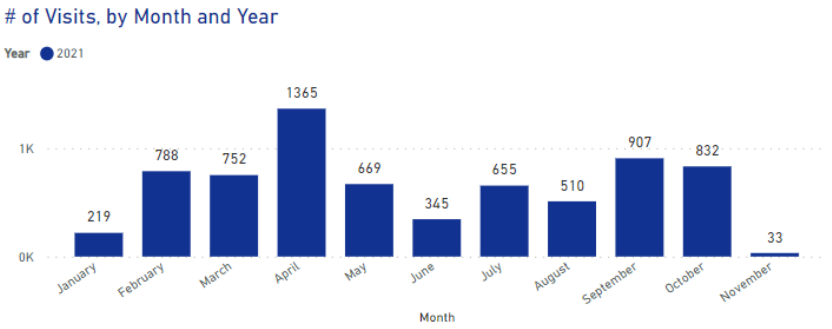



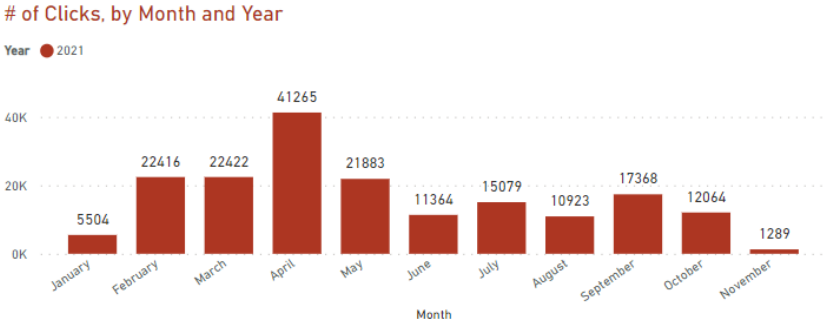


This project is funded by the European Union

REPUBLIKA E SHQIPËRISË
KËSHILLI I MINISTRAVE
MINISTËR SHTETI PËR RINDËRTIMIN


EU4SCHOOLS

7075	20373	2.88	181577	25.66
Total Visits	Pages	Pages / Visit	Clicks	Clicks / Visit


of Visits by weekday




Visits / Visitor, by Month and Year

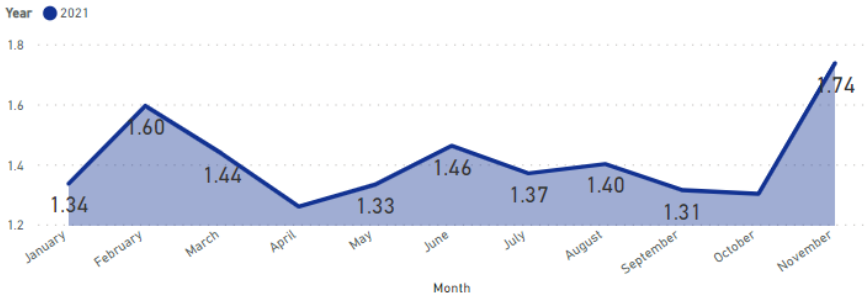

Pages / Visit, by Month and Year

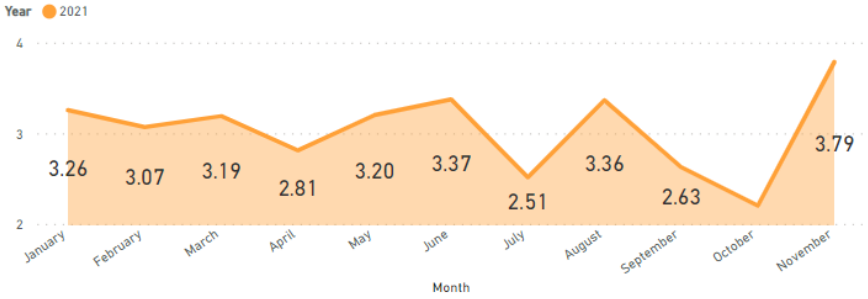

Clicks / Visit, by Month and Year

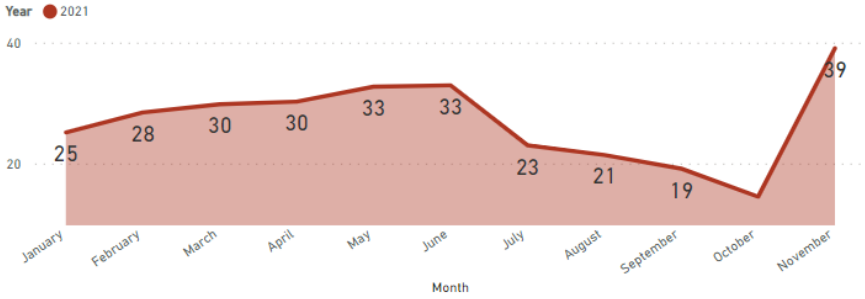

This project is funded by the European Union

REPUBLIKA E SHQIPËRISË
KËSHILLI I MINISTRAVE
MINISTËR SHTETI PËR RINDËRTIMIN

ANNEX 4 – COMMUNICATION AND VISIBILITY REPORTS OF INTEGRATED EU4SCHOOLS PROGRAMME

No.	Description	Date	Link	Social Media
NOVEMBER 2020				
1	UNDP in Albania on EU4Schools Testimony from a student in "Sherif Dervishi" school, Budull, Kruja Municipality	4 November 2020	https://www.instagram.com/p/CHLTIXfnGbs/	Instagram
2	UNDP in Albania on EU4Schools Testimony from a student in school "Sherif Dervishi", Budull, Kruja Municipality	4 November 2020	https://www.facebook.com/PNUDSHQIPERI/posts/3588469067878510	Facebook
3	Mayor of Shijak Mr. Elton Arbana on EU4Schools Meeting with UNDP Albania representatives	5 November 2020	https://www.facebook.com/permalink.php?story_fbid=1521164341421878&id=1085717774966539	Facebook
4	Mayor of Shijak Mr. Elton Arbana on EU4Schools Meeting with UNDP Albania representatives	5 November 2020	https://www.instagram.com/p/CHNkhvfgvhn/	Instagram
5	Kurbin Municipality on EU4Schools Info for the project, declaration	5 November 2020	https://www.instagram.com/p/CHNiFrRAcqm/	Instagram
6	Kruja Municipality on EU4Schools Starting reconstruction of "Korb Muca" school	6 November 2020	https://www.instagram.com/p/CHQm-5whZb5/	Instagram
7	Mayor of Kruja Mr. Artur Bushi on EU4Schools Starting reconstruction of "Korb Muca" school	6 November 2020	https://www.facebook.com/BashkiaKruje/videos/826633638096537	Facebook
8	Mayor of Lezha Mr. Pjerin Ndreu on EU4Schools Meeting about the reconstruction process of school "Gjergj Kastrioti" and "Fran Ivanaj"	6 November 2020	https://www.facebook.com/permalink.php?story_fbid=1280123805656466&id=100009765763688	Facebook

No.	Description	Date	Link	Social Media
9	School "Korb Muca" on EU4Schools Starting reconstruction of "Korb Muca" school	6 November 2020	https://www.facebook.com/NxenesitQereke/posts/2746493638922213	Facebook
10	UNDP in Albania on EU4Schools Starting reconstruction of "Korb Muca" school	9 November 2020	https://www.facebook.com/PNUDSHQIPERI/posts/3602072383184845	Facebook
11	UNDP in Albania on EU4Schools Reconstruction "Korb Muca" school	9 November 2020	https://www.instagram.com/p/CHYH4Edna_e/	Instagram
12	UNDP in Albania on EU4Schools Starting reconstruction of "Korb Muca" school	9 November 2020	https://twitter.com/UNDPAlbania/status/1325868328313819137	Twitter
13	School "Korb Muca" on EU4Schools Opening of the reconstruction site in "Krob Muca" school	9 November 2020	https://www.facebook.com/NxenesitQereke/posts/2749635995274644	Facebook
14	UNDP in Albania on EU4Schools About the reconstruction process of "Fiqiri Kurti" school	10 November 2020	https://www.facebook.com/PNUDSHQIPERI/posts/3604889852903098	Facebook
15	UNDP in Albania on EU4Schools About the reconstruction process of "Fiqiri Kurti" school	10 November 2020	https://www.instagram.com/p/CHa08R9HlLb/	Instagram
16	Director for WB at the EU Commission Ms.Calavera retweets UNDP in Albania post on EU4Schools	10 November 2020	https://twitter.com/CalaveraRuiz/status/1326088438769201152	Twitter
17	School "Korb Muca" on EU4Schools Starting reconstruction of "KorbMuca" school	10 November 2020	https://www.facebook.com/NxenesitQereke/posts/2749941895244054	Facebook
18	UNDP in Albania on EU4Schools About the reconstruction process of "Dom Nikolle Kacorri" school	11 November 2020	https://www.facebook.com/PNUDSHQIPERI/posts/3607583329300417	Facebook

No.	Description	Date	Link	Social Media
19	UNDP in Albania on EU4Schools About the reconstruction process of "Dom Nikolle Kacorri" school	11 November 2020	https://www.instagram.com/p/CHdXui-Hjz6/	Instagram
20	UNDP in Albania on EU4Schools About the reconstruction process of "Dom Nikolle Kacorri" school	12 November 2020	https://www.linkedin.com/posts/undp-albania-6436b2170_eu4schools-be-pnud-activity-6732341595040960513-SbNX	Linkedin
21	PM Edi Rama on EU4Schools Inspection during the reconstruction of school "Jashar Hoxha"	13 November 2020	https://www.facebook.com/watch/live/?v=1511405965735560&ref=watch_permalink	Facebook
22	Mayor of Kamza, Mr. Suli on EU4Schools Inspection during the reconstruction of school "Jashar Hoxha"	13 November 2020	https://www.facebook.com/permalink.php?story_fbid=3408693295846351&id=153971977985182	Facebook
23	UNDP in Albania on EU4Schools Training about safety at work organized in Durres Municipality	17 November 2020	https://www.facebook.com/PNUDSHQIPERI/posts/3624528507605899	Facebook
24	UNDP in Albania on EU4Schools Training about safety at work organized in Durres Municipality	17 November 2020	https://www.instagram.com/p/CHs--cLH-yR/	Instagram
25	UNDP in Albania on EU4Schools About the reconstruction process of "Korb Muca" School, Kruja Municipality	22 November 2020	https://www.facebook.com/PNUDSHQIPERI/posts/3637525862972830	Facebook
26	UNDP in Albania on EU4Schools Article about the reconstruction of "Korb Muca" School, Kruja Municipality	22 November 2020	https://albania-undp.medium.com/eu4schools-nj%C3%AB-arsim-cil%C3%ABsor-p%C3%ABr-brezat-e-sot%C3%ABm-dhe-t%C3%AB-ardhsh%C3%ABm-72b68141b5cb	UNDP online media

No.	Description	Date	Link	Social Media
27	UNDP in Albania on EU4Schools About the reconstruction of "Korb Muca" School, Kruja Municipality	22 November 2020	https://twitter.com/UNDPAlbania/status/1330576571074289664	Twitter
28	UNDP in Albania on EU4Schools Completion of the reconstruction process for "Hysen Cela" school, Durres Municipality	24 November 2020	https://www.facebook.com/PNUDSHQIPERI/posts/3721830037875745	Facebook
29	EU in Albania on EU4Schools About the reconstruction process one year after the earthquake	25 November 2020	https://www.facebook.com/eu.delegation.albania/posts/3434560519947060	Facebook
30	EU in Albania on EU4Schools About the reconstruction process one year after the earthquake	25 November 2020	https://www.instagram.com/p/CIA2VRfqtq8/	Instagram
31	UNDP in Albania on EU4Schools About the reconstruction process one year after the earthquake	25 November 2020	https://www.facebook.com/PNUDSHQIPERI/posts/3645104872214929	Facebook
32	UNDP in Albania on EU4Schools About the reconstruction process one year after the earthquake	25 November 2020	https://www.instagram.com/p/CIA6arLnVs9/	Instagram
33	EU Neighborhood & Enlargement on EU4Schools About the EU support on the reconstruction process one year after the earthquake	26 November 2020	https://www.instagram.com/p/CIDRq_UnAfy/	Instagram
34	EU Neighborhood & Enlargement on EU4Schools About the EU support on the reconstruction process one year after the earthquake	26 November 2020	https://twitter.com/eu_near/status/1331903321842593792	Twitter

No.	Description	Date	Link	Social Media
34	EU in Albania on EU4Schools Info about the EU4Schools project implementation	26 November 2020	https://www.instagram.com/p/CIDhTTCHOdO/	Instagram
35	EU in Albania on EU4Schools Info about the EU4Schools project implementation	26 November 2020	https://twitter.com/EUinAlbania/status/1331944786052456448	Twitter
36	EU in Albania on EU4Schools Info about the EU4Schools project implementation	26 November 2020	https://www.facebook.com/eu.delegation.albania/posts/3437379616331817	Facebook
37	School "Korb Muca" on EU4Schools Photos and statements of EU Ambassador Mr. Soreca and UNDP Representative Mrs. Eltayed, during their visit in the reconstruction sites of "Korb Muca" School in Kruja Municipality and "Hysen Cela" School in Durres Municipality	26 November 2020	https://www.facebook.com/NxenesitQereke/posts/2765412107030366	Facebook
38	UNDP in Albania on EU4Schools EU Ambassador Mr. Soreca and UNDP Representative Mrs. Eltayed, visit the reconstruction sites of "Korb Muca" School in Kruja Municipality and "Hysen Cela" School in Durres Municipality	26 November 2020	https://www.facebook.com/PNUDSHQIPERI/posts/3648014451923971	Facebook
39	EU in Albania on EU4Schools EU Ambassador Mr. Soreca visits the reconstruction sites of "Korb Muca" School in Kruja Municipality and "Hysen Cela" School in Durres Municipality	27 November 2020	https://www.instagram.com/p/CIFt-BwgBLH/	Instagram
40	EU in Albania on EU4Schools EU Ambassador Mr. Soreca visits the reconstruction sites of "Korb Muca" School in Kruja Municipality and "Hysen Cela" School in Durres Municipality	27 November 2020	https://www.facebook.com/eu.delegation.albania/posts/3439748816094897	Facebook

No.	Description	Date	Link	Social Media
41	EU in Albania on EU4Schools EU Ambassador Mr. Soreca visits the reconstruction sites of "Korb Muca" School in Kruja Municipality and "Hysen Cela" School in Durres Municipality	27 November 2020	https://twitter.com/EUinAlbania/status/1332250061842112513	Twitter
42	EU in Albania on EU4Schools EU Ambassador Mr. Soreca post after its visit in the reconstruction sites of "Korb Muca" and "Hysen Cela" school	27 November 2020	https://twitter.com/EUinAlbania/status/1332255051612639232	Twitter
43	UNDP in Albania on EU4Schools EU Ambassador Mr. Soreca and UNDP Representative Mrs. Eltayed, visit the reconstruction sites of "Korb Muca" School in Kruja Municipality and "Hysen Cela" School in Durres Municipality	27 November 2020	https://www.instagram.com/p/CIF2idVg9nM/	Instagram
44	UNDP in Albania on EU4Schools EU Ambassador Mr. Soreca and UNDP Representative Mrs. Eltayed, visit the reconstruction sites of "Korb Muca" School in Kruja Municipality and "Hysen Cela" School in Durres Municipality	27 November 2020	https://www.facebook.com/PNUDSHQIPERI/posts/3650254655033284	Facebook
45	UNDP in Albania on EU4Schools EU Ambassador Mr. Soreca and UNDP Representative Mrs. Eltayed, visit the reconstruction sites of "Korb Muca" School in Kruja Municipality and "Hysen Cela" School in Durres Municipality	27 November 2020	https://twitter.com/UNDPAlbania/status/1332293687062228993	Twitter
46	School "Hysen Cela" on EU4Schools	27 November 2020	https://www.facebook.com/hysencela/posts/3686888088028103	Facebook

No.	Description	Date	Link	Social Media
	EU Ambassador Mr. Soreca and UNDP Representative Mrs. Eltayed, visit the reconstruction sites of "Korb Muca" School in Kruja Municipality and "Hysen Cela" School in Durres Municipality			
47	EU Ambassador in Albania Mr. Soreca on EU4Schools Visit in reconstruction sites of "Korb Muca" and "Hysen Cela" school	27 November 2020	https://twitter.com/LSorecaEU/status/1332252535206391809	Twitter
DECEMBER 2020				
48	UNDP at EU on EU4Schools Promotion of EU4School Programme in Albania	7 December 2020	https://twitter.com/UNDPEU/status/1335874216688758785	Twitter
49	Mayor of Kamza Mr. Suli on EU4Schools Starting of the reconstruction of "Dom Nikolle Kacorri" school	10 December 2020	https://www.facebook.com/permalink.php?story_fbid=3480430538672626&id=153971977985182	Facebook
50	School "Dom Nikolle Kacorri" on EU4Schools Starting of the reconstruction of "Dom Nikolle Kacorri" school	10 December 2020	https://www.facebook.com/permalink.php?story_fbid=1029584894218862&id=293816884462337	Facebook
51	Kamez Municipality of EU4Schools Starting of the reconstruction of "Dom Nikolle Kacorri" school	10 December 2020	https://www.facebook.com/permalink.php?story_fbid=433558771356085&id=108419860536646	Facebook
52	Minister of State for Reconstruction Mr. Ahmetaj on EU4Schools About the reconstruction process of "Korb Muca" school, Kruja Municipality	10 December 2020	https://www.facebook.com/arben.ahmetaj.al/videos/1022744504895012	Facebook
53	Kruja Municipality on EU4Schools	15 December 2020	https://www.instagram.com/p/CI1DdrlBWZb/	Instagram

No.	Description	Date	Link	Social Media
	Starting of consultations for a 9-year school in Bilaj and a kindergarten in Varosh, Kruja Municipality			
54	Mayor of Kruja Mr. Bushi on EU4Schools Starting of consultations for a 9-year school in Bilaj and a kindergarten in Varosh, Kruja Municipality	15 December 2020	https://www.facebook.com/BashkiaKruje/posts/3762381437145349	Facebook
55	UNDP in Albania on EU4Schools Starting of consultations for 9-year school in Bilaj, Kruja Municipality	16 December 2020	https://www.instagram.com/p/CI3YWRCh2lq/	Instagram
56	UNDP in Albania on EU4Schools Starting of consultations for 9-year school in Bilaj, Kruja Municipality	16 December 2020	https://www.facebook.com/PNUDSHQIPERI/posts/3701714269887322	Facebook
57	Kamez Municipality on EU4Schools Presentation of project options for the reconstruction of "Jashar Hoxha" kindergarten, Kamez Municipality	17 December 2020	https://www.facebook.com/permalink.php?story_fbid=438446264200669&id=108419860536646	Facebook
58	Mayor of Kamza on EU4Schools Presentation of project options for the reconstruction of "Jashar Hoxha" kindergarten, Kamez Municipality	17 December 2020	https://www.facebook.com/153971977985182/videos/422064892309526	Facebook
59	Mayor of Kurbin Mrs. Cara on EU4Schools Starting of the reconstruction process in "Gjok Elezi" school, Kurbin Municipality	17 December 2020	https://www.facebook.com/MajlindaShqalsiCara/posts/754932048455008	Facebook
60	Kurbin Municipality on EU4Schools Starting of the reconstruction process in "Gjok Elezi" school, Kurbin Municipality	17 December 2020	https://www.instagram.com/p/CI5YlA8gpzl/	Instagram
61	UNDP in Albania on EU4Schools About the EU4Schools Programme	18 December 2020	https://twitter.com/UNDPAlbania/status/1339893040778010627	Twitter

No.	Description	Date	Link	Social Media
62	UNDP in Albania on EU4Schools Project consultations about the reconstruction of "Jashar Hoxha" kindergarten, Kamez Municipality	18 December 2020	https://www.facebook.com/PNUDSHQIPERI/posts/3706332409425508	Facebook
63	UNDP in Albania on EU4Schools Project consultations about the reconstruction of "Jashar Hoxha" kindergarten, Kamez Municipality	18 December 2020	https://www.instagram.com/p/CI8PbXGBHVZ/	Instagram
64	Mayor of Kurbin Mrs. Cara on EU4Schools Starting of the reconstruction process in "Demokracia" school, Kurbin Municipality	19 December 2020	https://www.facebook.com/MajlindaShqalsiCara/posts/756959598252253	Facebook
65	Kurbin Municipality on EU4Schools Starting of the reconstruction process in "Demokracia" school, Kurbin Municipality	19 December 2020	https://www.instagram.com/p/CI-yJi7AWla/	Instagram
66	UNDP in Albania on EU4Schools Completion of the reconstruction process of "Hysen Cela" school, Durres Municipality	24 December 2020	https://www.facebook.com/PNUDSHQIPERI/posts/3721830037875745	Facebook
67	UNDP in Albania on EU4Schools Completion of the reconstruction process of "Hysen Cela" school, Durres Municipality	24 December 2020	https://www.instagram.com/p/CJL3F02BBzI/	Instagram
68	UNDP in Albania on EU4Schools Starting of consultations for kindergarten no. 1, Kurbin Municipality	30 December 2020	https://www.facebook.com/PNUDSHQIPERI/posts/3736054433119972	Facebook
69	UNDP in Albania on EU4Schools Starting of consultations for kindergarten no. 1, Kurbin Municipality	30 December 2020	https://www.instagram.com/p/CJbC8xzBaCK/	Instagram
JANUARY 2021				

No.	Description	Date	Link	Social Media
70	Mayor of Kavaja Mr. Krali on EU4Schools Inspection at the construction site in "Fiqiri Kurti" school, Kavaja Municipality	11 January 2021	https://www.facebook.com/RedjanKrali/posts/743922492995807	Facebook
71	Mayor of Kavaja Mr. Krali on EU4Schools Inspection at the construction site in "Fiqiri Kurti" school, Kavaja Municipality	11 January 2021	https://www.instagram.com/p/CJ6rYWEsayU/	Instagram
72	Mayor of Kavaja Mr. Krali on EU4Schools Inspection at the construction site in "Mehmet Babamusta" school, Kavaja Municipality	12 January 2021	https://www.facebook.com/RedjanKrali/posts/744427072945349	Facebook
73	Mayor of Kavaja Mr. Krali on EU4Schools Inspection at the construction site in "Mehmet Babamusta" school, Kavaja Municipality	12 January 2021	https://www.instagram.com/p/CJ9PLN5MLJp/	Instagram
74	Director for WB European Neighborhood Policy & Enlargement Mrs. Calavera on EU4School Interview about the EU4Schools & EU4Culture programs with UNDP	13 January 2021	https://twitter.com/CalaveraRuiz/status/1349385371067555840	Twitter
75	Mayor of Kruja Mr. Bushi on EU4Schools Starting of the reconstruction process in kindergarten in Varosh, Kruja Municipality	20 January 2021	https://www.facebook.com/permalink.php?story_fbid=3855129491203876&id=550157205034471	Facebook
76	EU in Albania on EU4Schools 2nd steering committee of EU4Schools laying out the reconstruction work for 2021 with UNDP Albania	20 January 2021	https://www.facebook.com/eu.delegation.albania/posts/3577536702316107	Facebook
77	EU in Albania on EU4Schools 2nd steering committee of EU4Schools laying out the reconstruction work for 2021 with UNDP Albania	20 January 2021	https://www.instagram.com/p/CKR25LOBsDs/	Instagram

No.	Description	Date	Link	Social Media
78	UNDP in Albania on EU4Schools 2nd steering committee of EU4Schools laying out the reconstruction work for 2021 with UNDP Albania	20 January 2021	https://twitter.com/UNDPAlbania/status/1351903721156960256	Twitter
79	EU in Albania on EU4Schools 2nd steering committee of EU4Schools laying out the reconstruction work for 2021 with UNDP Albania	20 January 2021	https://twitter.com/EUinAlbania/status/1351900055402405889	Twitter
80	Minister of Education Mrs. Kushi on EU4Schools Online meeting with the steering committee of EU4Schools program	21 January 2021	https://www.facebook.com/kushievis/posts/198273971988045	Facebook
81	Minister of Education Mrs. Kushi on EU4Schools Online meeting with the steering committee of EU4Schools program	21 January 2021	https://www.instagram.com/p/CKTSYqmhMVv/	Instagram
82	Minister of Reconstruction Mr. Ahmetaj on EU4Schools Completion of the reconstruction of "Hysen Cela" school, Durres Municipality	21 January 2021	https://www.facebook.com/arben.ahmetaj.al/posts/3497031020416497	Facebook
83	Durres Municipality on EU4Schools Completion of the reconstruction of "Hysen Cela" school, Durres Municipality	21 January 2021	https://www.facebook.com/durres.gov.al/posts/10159249233101119	Facebook
84	Minister of Education Mrs. Kushi on EU4Schools Online meeting with the steering committee of EU4Schools program	21 January 2021	https://twitter.com/EvisKushi/status/1352182715731337216	Twitter
85	Deputy Mayor of Tirana Mrs. Ristani on EU4Schools 5 fully reconstructed and 1 school in Tirana under the EU4Schools Program	21 January 2021	https://twitter.com/Anuela/status/1352034414830772225	Twitter

No.	Description	Date	Link	Social Media
86	Ministry of Education and Sports on EU4Schools Online meeting with the steering committee of EU4Schools program	22 January 2021	https://www.instagram.com/p/CKV0_W5ABOf/	Instagram
87	UNDP Eurasia on EU4Schools The EU4Schools program contribution in the educational system in Albania	24 January 2021	https://twitter.com/UNDPEurasia/status/1353313096845111303	Twitter
88	UNDP in Albania on EU4Schools About the reconstruction process of "Hysen Cela" High School, Durres Municipality	25 January 2021	https://albania-undp.medium.com/supporting-skills4life-vet-schools-benefit-from-eu4schools-programme-e96aa610da7f	UNDP online media
89	UNDP in Albania on EU4Schools Article on the importance of VET and the reconstruction process in "Hysen Cela" vocational school, Durres Municipality	25 January 2021	https://albania-undp.medium.com/supporting-skills4life-vet-schools-benefit-from-eu4schools-programme-e96aa610da7f	UNDP online media
90	UNDP in Albania on EU4Schools About the reconstruction process of "Hysen Cela" High School, Durres Municipality	26 January 2021	https://www.facebook.com/PNUDSHQIPERI/posts/3807317272660354	Facebook
91	UNDP in Albania on EU4Schools About the vocational schools benefiting from the EU4School Program	26 January 2021	https://www.instagram.com/p/CKg-p0sBWFW/	Instagram
92	UNDP in Albania on EU4Schools About the vocational schools benefiting from the EU4School Program	26 January 2021	https://twitter.com/UNDPAlbania/status/1354096434778406912	Twitter
93	EU in Albania on EU4Schools About the reconstruction process of "Hysen Cela" High School, Durres Municipality	26 January 2021	https://twitter.com/EUinAlbania/status/1354138206963425281	Twitter

No.	Description	Date	Link	Social Media
94	UNDP in Albania on EU4Schools The EU4Schools Program Transparency Portal	27 January 2021	https://www.facebook.com/PNUDSHQIPERI/posts/3810035339055214	Facebook
95	UNDP in Albania on EU4Schools The EU4Schools Program Transparency Portal	27 January 2021	https://www.instagram.com/p/CKj_5r8hL7j/	Instagram
96	EU in Albania on EU4Schools The EU4Schools Program Transparency Portal	27 January 2021	https://www.instagram.com/p/CKjhuKQKWxk/	Instagram
97	UNDP in Albania on EU4Schools The EU4Schools Program Transparency Portal goes live	27 January 2021	https://twitter.com/UNDPAlbania/status/1354532106739843087	Twitter
98	UNDP in Albania on EU4Schools The EU4Schools Program Transparency Portal	27 January 2021	https://twitter.com/UNDPAlbania/status/1354530315985973252	Twitter
99	Euronews Albania on EU4Schools The EU4Schools Program Transparency Portal	27 January 2021	https://twitter.com/EuronewsAlbania/status/1354527913505394694	Twitter
100	EU in Albania EU4Schools The EU4Schools Program Transparency Portal	27 January 2021	https://twitter.com/EUinAlbania/status/1354461077422092290	Twitter
101	EU Ambassador in Albania Mr. Soreca on EU4Schools The EU4Schools Program Transparency Portal	27 January 2021	https://twitter.com/LSorecaEU/status/1354453234639904769	Twitter
102	EU in Albania on EU4Schools The EU4Schools Program Transparency Portal goes live	27 January 2021	https://twitter.com/EUinAlbania/status/1354451224897204226	Twitter
103	Mayor of Kruja Mr. Bushi on EU4Schools Video and images of the reconstruction process in "Korb Muca" school, Kruja Municipality	29 January 2021	https://www.facebook.com/permalink.php?story_fbid=3880351115348380&id=550157205034471	Facebook
104	MP Ms. Rraja on EU4Schools	29 January 2021	https://www.facebook.com/rraja.rrahman/posts/2292936355275 89	Facebook

No.	Description	Date	Link	Social Media
	About the reconstruction process in "Korb Muca" school, Kruja Municipality			
		FEBRUARY 2021		
105	UNDP in Albania on EU4Schools Testimonials about the finalization of the reconstruction process in "Hysen Cela" school, Durres Municipality	1 February 2021	https://www.facebook.com/PNUDSHQIPERI/posts/3822209341171147	Facebook
106	UNDP in Albania on EU4Schools Testimonials about the finalization of the reconstruction process in "Hysen Cela" school, Durres Municipality	1 February 2021	https://www.instagram.com/p/CKv4A9CgZg_/	Instagram
107	EU in Albania on EU4Schools Video and images of the reconstruction site in "Korb Muca" school, Kruja Municipality	1 February 2021	https://www.instagram.com/p/CKv1gKCAQgS/	Instagram
108	UNDP Eurasia on EU4Schools About the vocational schools benefiting from the EU4School Program	3 February 2021	https://twitter.com/UNDPEurasia/status/1356976568623579140	Twitter
109	EU in Albania on EU4Schools Completion of the reconstruction process in "Hysen Cela" High School, Durres Municipality	4 February 2021	https://www.facebook.com/eu.delegation.albania/posts/3616148021788308	Facebook
110	EU in Albania on EU4Schools Completion of the reconstruction process in "Hysen Cela" High School, Durres Municipality	4 February 2021	https://www.instagram.com/p/CK35M0NqRkG/	Instagram
111	Kindergarten "1 Qershori" on EU4Schools	4 February 2021	https://www.facebook.com/www.kop.1Qershori.Dr/posts/4118302731536061	Facebook

No.	Description	Date	Link	Social Media
	EU4School team visit at the construction site in "1 Qershori" kindergarten, Durres Municipality			
112	UNDP in Albania on EU4Schools EU4School team visit at the construction site in "1 Qershori" kindergarten, Durres Municipality	4 February 2021	https://www.facebook.com/PNUDSHQIPERI/posts/3830200540372027	Facebook
113	UNDP in Albania on EU4Schools EU4School team visit at the construction site in "1 Qershori" kindergarten, Durres Municipality	4 February 2021	https://www.instagram.com/p/CK4HyjIBbOz/	Instagram
114	Representative of UNDP in Albania Mrs. Eltayeb on EU4Schools The EU4Schools Program Transparency Portal	5 February 2021	https://twitter.com/EltayebLimya/status/1357708261399658501	Twitter
115	UNDP in Albania on EU4Schools EU4School team, teachers and parents visit the construction site in "1 Qershori" kindergarten, Durres Municipality	6 February 2021	https://twitter.com/UNDPAlbania/status/1357944429928185858	Twitter
116	Mayor of Kruja Mr. Bushi on EU4Schools Approval of the reconstruction project of a 9-year school in Kruja Municipality	8 February 2021	https://www.facebook.com/BashkiaKruje/posts/261101432049329	Facebook
117	Kruja Municipality on EU4Schools Approval of the reconstruction project of a 9-year school in Kruja Municipality	8 February 2021	https://www.instagram.com/p/CLCweKjBOdK/	Instagram
118	Kindergarten "1 Qershori" on EU4Schools Images of the reconstruction process in "1 Qershori" kindergarten, Durres Municipality	10 February 2021	https://www.facebook.com/www.kop.1Qershori.Dr/posts/4110483698984631	Facebook

No.	Description	Date	Link	Social Media
119	EU in Albania on EU4Schools EU4Schools team visit in "1 Qershori" kindergarten, Durres Municipality	12 February 2021	https://www.facebook.com/eu.delegation.albania/posts/3635838429819267	Facebook
120	EU in Albania on EU4Schools EU4Schools team visit in "1 Qershori" kindergarten, Durres Municipality	12 February 2021	https://www.instagram.com/p/CLMOWesKjqq/	Instagram
121	EU in Albania on EU4Schools EU4Schools team visit in "1 Qershori" kindergarten, Durres Municipality	12 February 2021	https://twitter.com/EUinAlbania/status/1360191647263436802	Twitter
122	Mayor of Durres Mrs. Sako on EU4Schools EU4Schools team visit in "1 Qershori" kindergarten, Durres Municipality	13 February 2021	https://www.instagram.com/p/CLPr6WMhA7C/	Instagram
123	UNDP in Albania on EU4Schools EU4Schools Transparency Portal	13 February 2021	https://twitter.com/UNDPAlbania/status/1360650746140758020	Twitter
124	EU in Albania on EU4Schools About the reconstruction of "Korb Muca" school, Kruja Municipality	15 February 2021	https://www.facebook.com/eu.delegation.albania/posts/3644334795636297	Facebook
125	EU in Albania on EU4Schools Video about the reconstruction of "Korb Muca" school, Kruja Municipality	15 February 2021	https://www.instagram.com/p/CLU05gMAMbT/	Instagram
126	EU Neighborhood and Enlargement on EU4Schools About the reconstruction of "Korb Muca" school, Kruja Municipality	16 February 2021	https://www.facebook.com/EUnear/posts/5078538945553386	Facebook
127	EU Neighborhood and Enlargement on EU4Schools	16 February 2021	https://www.instagram.com/p/CLWxKLBHyVl/	Instagram

No.	Description	Date	Link	Social Media
	About the reconstruction of "Korb Muca" school, Kruja Municipality			
128	EU in Albania on EU4Schools Video and images of the newly reconstructed school "Hysen Cela", Durres Municipality	16 February 2021	https://www.facebook.com/eu.delegation.albania/posts/3646065525463224	Facebook
129	EU in Albania on EU4Schools Video and images of the newly reconstructed school "Hysen Cela", Durres Municipality	16 February 2021	https://twitter.com/EUinAlbania/status/1361676477847252999	Twitter
130	EU in Albania on EU4Schools Video and images of the reconstructed school "Hysen Cela", Durres Municipality	16 February 2021	https://www.instagram.com/p/CLWw-tiK_Ry/	Instagram
131	UNDP in Albania on EU4Schools Video and images about the implementation of EU4School Project	17 February 2021	https://www.facebook.com/watch/?v=432029648068895	Facebook
132	UNDP in Albania on EU4Schools About the implementation of EU4School Program one year after the Donors Conference in Brussels	17 February 2021	https://www.instagram.com/p/CLZBo8BA9VX/	Instagram
133	UNDP in Albania on EU4Schools About the implementation of EU4School Program one year after the Donors Conference in Brussels	17 February 2021	https://www.facebook.com/PNUDSHQIPERI/posts/3862296077162473	Facebook
134	UNDP in Albania on EU4Schools One year after the Donors Conference in Brussels, info about the reconstruction process	17 February 2021	https://www.facebook.com/PNUDSHQIPERI/posts/3862027493855998	Facebook
135	UNDP in Albania on EU4Schools	17 February 2021	https://www.instagram.com/p/CLZe7zxA0j9/	Instagram

No.	Description	Date	Link	Social Media
	One year after the Donors Conference in Brussels, info about the reconstruction process			
136	UNDP in Albania on EU4Schools Video testimonial on EU4School Program	17 February 2021	https://www.facebook.com/PNUDSHQIPERI/posts/3862444017147679	Facebook
137	UNDP in Albania on EU4Schools Testimonial on EU4School Program, info about the reconstruction process	17 February 2021	https://www.instagram.com/p/CLZTKs0AXyN/	Instagram
138	UNDP Communication Manager Mrs. Kushti on EU4Schools Reporters visit in 2 schools &1 kindergarten	17 February 2021	https://twitter.com/norakushti/status/1362072198178037762	Twitter
139	UNDP in Albania on EU4Schools Deputy Rep of UNDP in Albania, EU in Albania team and journalists visit in 2 schools & 1 kindergarten part of the EU4Schools program	17 February 2021	https://twitter.com/UNDPAlbania/status/1362056659846238208	Twitter
140	EU in Albania on EU4School Journalists visit the construction site of “1 Qershori”, Durres Municiaplity	17 February 2021	https://twitter.com/EUinAlbania/status/1362024085669240834	Twitter
141	EU in Albania on EU4School Journalists visit the construction site of the new “Korb Muça”, Kruja Municiaplity	17 February 2021	https://twitter.com/EUinAlbania/status/1361999517239894016	Twitter
142	UNDP in Albania on EU4School About the implementation of EU4School Program one year after the Donors Conference in Brussels	17 February 2021	https://twitter.com/UNDPAlbania/status/1362012986345484292	Twitter
143	EU in Albania on EU4School	17 February 2021	https://twitter.com/EUinAlbania/status/1362002046753382413	Twitter

No.	Description	Date	Link	Social Media
	About the reconstruction process in "Democracia" school, Kruja Municipality			
144	UNDP in Albania on EU4School Reporters visit in reconstruction sites one year after the Donors Conference	17 February 2021	https://twitter.com/UNDPAlbania/status/1361979326229577731	Twitter
145	UNDP in Albania on EU4Schools EU4School media coverage-Ballkan Web	18 February 2021	https://www.facebook.com/PNUDSHQIPERI/posts/3865214013537346	Facebook
146	UNDP in Albania on EU4Schools EU4School media coverage-Euronews Albania	18 February 2021	https://www.facebook.com/PNUDSHQIPERI/posts/3864734443585303	Facebook
147	Kindergarten "1 Qershori" on EU4Schools Images of the reconstruction process in "1 Qershori" kindergarten, Durres Municipality	18 February 2021	https://www.facebook.com/www.kop.1Qershori.Dr/posts/4131373473562320	Facebook
148	Kindergarten "1 Qershori" on EU4Schools EU4Schools team visit in "1 Qershori" kindergarten, Durres Municipality	18 February 2021	https://www.facebook.com/www.kop.1Qershori.Dr/posts/4131363960229938	Facebook
149	EU in Albania on EU4School EU4School media coverage-Ballkan Web	18 February 2021	https://twitter.com/EUinAlbania/status/1362399928811728899	Twitter
150	EU in Albania on EU4School EU4School media coverage-Euronews Albania	19 February 2021	https://www.facebook.com/eu.delegation.albania/posts/3653664311370012	Facebook
151	EU in Albania on EU4School EU4School media coverage-Euronews Albania	19 February 2021	https://twitter.com/EUinAlbania/status/1362809176376885251	Twitter
152	Mayor of Kurbin Mrs. Cara on EU4Schools About the reconstruction process in "Cub Capani" school, Kurbin Municipality	19 February 2021	https://www.facebook.com/MajlindaShqalsiCara/posts/800983843849828	Facebook

No.	Description	Date	Link	Social Media
153	Kurbin Municipality on EU4Schools About the reconstruction process in "Cub Capani" school, Kurbin Municipality	19 February 2021	https://www.facebook.com/permalink.php?story_fbid=467744527942968&id=115227253194699	Facebook
154	Kurbin Municipality on EU4Schools About the reconstruction process in "Cub Capani" school, Kurbin Municipality	19 February 2021	https://www.instagram.com/p/CLfbxflASax/	Instagram
155	UNDP Eurasia on EU4Schools About the EU4Schools Program implementation in Albania	20 February 2021	https://twitter.com/UNDPEurasia/status/1363209808653000711	Twitter
156	Representative of UNDP in Albania Mrs. Eltayeb on EU4Schools EU4schools project implementation one year after the Donors Conference	20 February 2021	https://twitter.com/EltayebLimya/status/1363070639217729540	Twitter
157	EU in Albania on EU4School Finalization of the reconstruction process in "1 Qershori" kindergarten, Durres Municipality	22 February 2021	https://www.facebook.com/eu.delegation.albania/posts/3659503674119409	Facebook
158	Kindergarten "1 Qershori" on EU4Schools Testimonials and images for the reconstruction process of " 1 Qershori" kindergarten, Durres Municipality	22 February 2021	https://www.facebook.com/www.kop.1Qershori.Dr/posts/4141122965920704	Facebook
159	EU in Albania on EU4School Video and images about the finalization of the reconstruction process in "1 Qershori" kindergarten, Durres Municipality	22 February 2021	https://www.instagram.com/p/CLlrP6KAMj_/	Instagram

No.	Description	Date	Link	Social Media
160	EU in Albania on EU4School Video and images about the finalization of the reconstruction process in "1 Qershori" kindergarten, Durres Municipality	22 February 2021	https://twitter.com/EUinAlbania/status/1363775543015972864	Twitter
161	UNDP in Albania on EU4Schools Testimonials for the reconstruction of "1 Qershori" kindergarten, Durres Municipality	23 February 2021	https://www.facebook.com/PNUDSHQIPERI/posts/3877682842290463	Facebook
162	UNDP in Albania on EU4Schools Testimonials for the reconstruction of "1 Qershori" kindergarten, Durres Municipality	23 February 2021	https://www.instagram.com/p/CLoxIiPgVhT/	Instagram
163	Kindergarten "1 Qershori" on EU4Schools Testimonials for the reconstruction of "1 Qershori" kindergarten, Durres Municipality	23 February 2021	https://www.facebook.com/www.kop.1Qershori.Dr/posts/4143862142313453	Facebook
164	UNDP Communication Manager Mrs. Kushti on EU4Schools EU4School media coverage-RTSH	23 February 2021	https://twitter.com/norakushti/status/1364318264898297862	Twitter
165	UNDP in Albania on EU4Schools EU4School media coverage-RTSH	24 February 2021	https://www.facebook.com/PNUDSHQIPERI/posts/3881408121917935	Facebook
166	UNDP in Albania on EU4Schools EU4School media coverage-RTSH	24 February 2021	https://www.instagram.com/p/CLrHBMSnMz3/	Instagram
167	Mayor of Kamza Mr. Suli on EU4School About the reconstruction process in "Nikolle Kacorri" school, Kamez Municipality	25 February 2021	https://www.facebook.com/permalink.php?story_fbid=3680127395369605&id=153971977985182	Facebook

No.	Description	Date	Link	Social Media
168	UNDP in Albania on EU4Schools Article about the importance of the EU4Schools Program in educational system and society	26 February 2021	https://albania-undp.medium.com/eu4schools-early-education-investment-for-children-and-the-society-ade1636f50de	UNDP online media
	MARCH 2021			
169	Mayor of Kavaja Mr. Krali on EU4Schools Visit in the reconstruction site of "Fiqiri Kurti" school, Kruja Municipality	1 March 2021	https://www.facebook.com/RedjanKrali/videos/771080853831291	Facebook
170	"1 Qeshori Kindergarten" on EU4schools Journalists visit in "1 Qershori Kindergarten", Durres Municipality	1 March 2021	https://www.facebook.com/www.kop.1Qershori.Dr/posts/4168422499857417	Facebook
171	Mayor of Kavaja Mr. Krali on EU4Schools Images from the visit in the reconstruction site of "Fiqiri Kurti" school, Kruja Municipality	1 March 2021	https://www.facebook.com/RedjanKrali/posts/769510177103705	Facebook
172	Mayor of Kavaja Mr. Krali on EU4Schools Images from the visit in the reconstruction site of "Fiqiri Kurti" school, Kruja Municipality	1 March 2021	https://www.instagram.com/p/CL44yu-Mv_w/	Instagram
173	UNDP in Albania on EU4Schools Video about the implementation and reconstruction sites	1 March 2021	https://twitter.com/UNDPAlbania/status/1366490909047676934	Twitter
174	UNDP in Albania on EU4Schools Congratulations on the teachers' day and the contribution of the EUSchools program	7 March 2021	https://www.facebook.com/PNUDSHQIPERI/posts/3916008571791223	Facebook
175	EU in Albania on EU4Schools Congratulations on the teachers' day and the contribution of the EUSchools program	7 March 2021	https://www.facebook.com/permalink.php?story_fbid=3699167940152982&id=304579276278549	Facebook

No.	Description	Date	Link	Social Media
176	UNDP in Albania on EU4Schools Congratulations on the teachers' day and the contribution of the EUSchools program	7 March 2021	https://twitter.com/UNDPAlbania/status/1368494838132408320	Twitter
177	UNDP in Albania on EU4Schools EUSchools program- Investing in early education for children and society	7 March 2021	https://albania-undp.medium.com/eu4schools-investim-n%C3%AB-arsimin-e-hersh%C3%ABm-p%C3%ABr-f%C3%ABmij%C3%ABt-dhe-shoq%C3%ABrin%C3%AB-12222c05fcaa	UNDP online media
178	MP Ms. Rraja on EU4Schools About the reconstruction process in "Gjergj Kastrioti Skenderbeu" school, Kruja Municipality	9 March 2021	https://www.facebook.com/rraja.rrahman/posts/2535548796435406	Facebook
179	MP Ms. Rraja on EU4Schools About the reconstruction process in "Gjergj Kastrioti Skenderbeu" school, Kruja Municipality	9 March 2021	https://www.instagram.com/p/CMNmJ5WgMXT/	Instagram
180	Mayor of Kruja Ms. Bushi on EU4Schools Start of the reconstruction process in "Gjergj Kastrioti Skenderbeu" school, Kruja Municipality	9 March 2021	https://www.facebook.com/BashkiaKruje/posts/2780594336868 62	Facebook
181	Kruja Municipality on EU4Schools Start of the reconstruction process in "Gjergj Kastrioti Skenderbeu" school	9 March 2021	https://www.instagram.com/p/CMNfBtnBzHG/	Instagram
182	"1 Qeshori Kindergarten" on EU4schools Completion of the reconstruction of "1 Qershori Kindergarten", Durres Municipality	11 March 2021	https://www.facebook.com/www.kop.1Qershori.Dr/posts/4194364463929887	Facebook
183	EU in Albania on EU4Schools	11 March 2021	https://www.facebook.com/permalink.php?story_fbid=3712259542177155&id=304579276278549	Facebook

No.	Description	Date	Link	Social Media
	Ambassador Soreca & UNDP Representative Mrs. Eltayeb visit the reconstruction sites of 3 schools in Laknas and Durres			
184	EU in Albania on EU4Schools Ambassador Soreca & UNDP Representative Mrs. Eltayeb visit the reconstruction sites of "Dom Nikolle Kacorri" school and "1 Qershori" kindergarten	11 March 2021	https://www.instagram.com/p/CMSSs7GgqJH/	Instagram
185	Faktoje.al on EU4Schools About the reconstruction process and the importance of transparency and data publication	11 March 2021	https://faktoje.al/rindertimi-i-shkollave-nga-be-dhe-undp-standard-tjeter-transparence/?fbclid=IwAR2Ui8QOpB5ZAWBHOmQijOGeLJH3aO_WNIm9by_Txr50RmQMaKpkSODSiwc	Faktoje.al portal
186	Faktoje.al on EU4Schools About the reconstruction process and the importance of transparency and data publication	11 March 2021	https://www.instagram.com/p/CMSvGDEheZR/	Instagram
187	UNDP in Albania on EU4Schools Ambassador Soreca & UNDP Representative Mrs. Eltayeb visit the reconstruction sites of "Dom Nikolle Kacorri" school and "1 Qershori" kindergarten	11 March 2021	https://www.facebook.com/PNUDSHQIPERI/posts/3926948257363921	Facebook
188	UNDP in Albania on EU4Schools Ambassador Soreca & UNDP Representative Mrs. Eltayeb visit in "1 Qershori Kindergarten", Durres Municipality	11 March 2021	https://www.instagram.com/p/CMSwvsoh6H3/	Instagram
189	UNDP in Albania on EU4Schools	11 March 2021	https://www.instagram.com/p/CMSNFGxgPdY/	Instagram

No.	Description	Date	Link	Social Media
	Ambassador Soreca & UNDP Representative Mrs. Eltayeb visit the reconstruction sites of "Dom Nikolle Kacorri" school and "1 Qershori" kindergarten			
190	EU Ambassador on EU4Schools Visit in "1 Qershori" kindergarten, Durres Municipality	11 March 2021	https://twitter.com/LSorecaEU/status/1370074401396383756	Twitter
191	EU in Albania on EU4Schools Ambassador Soreca & UNDP Representative Mrs. Eltayeb visit the reconstruction sites of 3 schools in Laknas and Durres	11 March 2021	https://twitter.com/EUinAlbania/status/1370053435979137028	Twitter
192	EU in Albania on EU4Schools Promoting the transparency portal for more info on the progress made	11 March 2021	https://twitter.com/EUinAlbania/status/1370053452978601990	Twitter
193	UNDP Albania Representative Mrs. Eltayeb on EU4Schools Visit in the reconstruction sites of 3 schools in Laknas and Durres	11 March 2021	https://twitter.com/EltayebLimya/status/1370111112428060672	Twitter
194	Mayor of Kurbin Mrs. Cara on EU4Schools About the reconstruction process of "Demokracia" school, Krubin Municipality	14 March 2021	https://www.facebook.com/MajlindaShqalsiCara/posts/814529602495252	Facebook
195	Kurbin Municipality of EU4Schools About the reconstruction process of "Demokracia" school, Krubin Municipality	14 March 2021	https://www.facebook.com/permalink.php?story_fbid=482391896478231&id=115227253194699	Facebook
196	Kurbin Municipality of EU4Schools About the reconstruction process of "Demokracia" school, Krubin Municipality	14 March 2021	https://www.instagram.com/p/CMaUkszgmbq/	Instagram

No.	Description	Date	Link	Social Media
197	EU in Albania on EU4Schools Online media "Faktoje.al" accompanied Mr. Soreca during his visit. The newly open media provides info on EU4Schools program	15 March 2021	https://www.facebook.com/eu.delegation.albania/posts/113433454142966	Facebook
198	EU in Albania on EU4Schools Media Coverage-TVKlan together with Ambassador Soreca visit the reconstruction sites in Laknas and Durres	15 March 2021	https://www.facebook.com/eu.delegation.albania/posts/113434154142896	Facebook
199	UNDP in Albania on EU4Schools Media coverage for the EU4School program-Top Channel	15 March 2021	https://www.facebook.com/PNUDSHQIPERI/posts/3936867526371994	Facebook
200	EU in Albania on EU4Schools Online media "Faktoje.al" accompanied Mr. Soreca during his visit. The newly open media provides info on EU4Schools program	15 March 2021	https://twitter.com/EUinAlbania/status/1371436013135007745	Twitter
201	EU in Albania on EU4Schools Media coverage-TVKlan together with Ambassador Soreca visit the reconstruction sites in Laknas and Durres	15 March 2021	https://twitter.com/EUinAlbania/status/1371461183341883399	Twitter
202	EU in Albania on EU4Schools About the EU funded programs helping Albania to recover from the earthquake	16 March 2021	https://www.facebook.com/eu.delegation.albania/posts/113803684105943	Facebook
203	EU in Albania on EU4Schools About the EU funded programs helping Albania to recover from the earthquake	16 March 2021	https://www.instagram.com/p/CMeW46nL5Ho/	Instagram

No.	Description	Date	Link	Social Media
204	EU in Albania on EU4Schools About the EU funded programs helping Albania to recover from the earthquake	16 March 2021	https://twitter.com/EUinAlbania/status/1371751596057620485	Twitter
205	Mayor of Kamza Mr. Suli on EU4Schools About the schools and kindergartens under reconstruction in Kamez Municipality	18 March 2021	https://www.facebook.com/watch/?v=2788435671199906	Facebook
206	Mayor of Kamza Mr. Suli on EU4Schools About the schools and kindergartens under reconstruction in Kamez Municipality	18 March 2021	https://www.instagram.com/p/CMkMXb7Cy3C/	Instagram
207	"1 Qeshori Kindergarten" on EU4schools Images on the new and reconstructed building of "1 Qershori Kindergarten", Durres Municipality	19 March 2021	https://www.facebook.com/www.kop.1Qershori.Dr/posts/4216209491745384	Facebook
208	Mayor of Kamza Mr. Suli on EU4Schools Images of the reconstruction site of "Dom Nikolle Kacorri" school, Kamez Municipality	19 March 2021	https://www.facebook.com/watch/?v=706542553356576	Facebook
209	UNDP in Albania on EU4Schools Completion of the reconstruction process in "1 Qershori Kindergarten", Durres Municipality	19 March 2021	https://www.facebook.com/PNUDSHQIPERI/posts/3948091088582971	Facebook
210	UNDP in Albania on EU4Schools Completion of the reconstruction process in "1 Qershori Kindergarten", Durres Municipality	19 March 2021	https://www.instagram.com/p/CMmR8Bvhuf_/	Instagram
211	Mayor of Kamza Mr. Suli on EU4Schools Images of the reconstruction site of "Dom Nikolle Kacorri" school, Kamez Municipality	20 March 2021	https://www.instagram.com/p/CMo7V-zCUQn/	Instagram

No.	Description	Date	Link	Social Media
212	MP Ms. Rraja on EU4Schools About the reconstruction process in 9-year old school in Bushnesh, Kruja Municipality	26 March 2021	https://www.facebook.com/rraja.rrahman/posts/264072862049666	Facebook
213	Kruja Municipality on EU4Schools About the reconstruction process in 9-year old school in Bushnesh,	26 March 2021	https://www.instagram.com/p/CM36ycnrgM8/	Instagram
214	"1 Qeshori Kindergarten" on EU4schools Children return in their renovated kindergarten	26 March 2021	https://www.facebook.com/www.kop.1Qershori.Dr/posts/4235639723135694	Facebook
215	Mayor of Kruja Ms. Bushi on EU4Schools About the reconstruction process in 9-year old school in Bushnesh, Kruja Municipality	26 March 2021	https://www.facebook.com/BashkiaKruje/posts/287672376058901	Facebook
216	UNDP in Albania on EU4Schools Children return in their renovated kindergarten "1 Qershori", Durres Municipality	26 March 2021	https://www.facebook.com/PNUDSHQIPERI/posts/3967154776676602	Facebook
217	UNDP in Albania on EU4Schools Children return in their renovated kindergarten "1 Qershori", Durres Municipality	26 March 2021	https://www.instagram.com/p/CM4sBO-hBDV/	Instagram
218	UNDP in Albania on EU4Schools Children return in their renovated kindergarten "1 Qershori", Durres Municipality	26 March 2021	https://twitter.com/UNDPAlbania/status/1375448765251862532	Twitter
219	UNDP Communication Manager Mrs. Kushti on EU4Schools Children return in their renovated kindergarten "1 Qershori", Durres Municipality	26 March 2021	https://twitter.com/norakushti/status/1375530024934203396	Twitter

No.	Description	Date	Link	Social Media
220	Mayor of Kamza Mr. Suli on EU4Schools Images of the reconstruction site of "Dom Nikolle Kacorri" school, Kamez Municipality	30 March 2021	https://www.facebook.com/permalink.php?story_fbid=3775129442536066&id=153971977985182	Facebook
221	Mayor of Kamza Mr. Suli on EU4Schools Images of the reconstruction site of "Dom Nikolle Kacorri" school, Kamez Municipality	30 March 2021	https://www.instagram.com/p/CNDQRsJCLna/	Instagram
		APRIL 2021		
222	UNDP in Albania on EU4Schools Video about the EU4Schools program reconstruction process	1 April 2021	https://twitter.com/UNDPAlbania/status/1377627210815799312	Twitter
223	UNDP Communication Manager Mrs. Kushti on EU4Schools The contribution of the EU4Schools program in quality education for present and future generations	1 April 2021	https://twitter.com/norakushti/status/1377717245019848712	Twitter
224	EU Neighbourhood & Enlargement on EU4Schools About the newly reconstructed kindergarten facilities in Durres Municipality	2 April 2021	https://www.instagram.com/p/CNJ_XXBIeeZ/	Instagram
225	EU Neighbourhood & Enlargement on EU4Schools About the newly reconstructed kindergarten facilities in Durres Municipality	2 April 2021	https://twitter.com/eu_near/status/1377893564936413185	Twitter
226	Mayor of Kamza Mr. Suli on EU4Schools Video on the reconstruction process in "Tahir Sinani" 9-year school	3 April 2021	https://www.facebook.com/permalink.php?story_fbid=3785003448215332&id=153971977985182	Facebook
227	Mayor of Kamza Mr. Suli on EU4Schools	3 April 2021	https://www.instagram.com/p/CNMgSrliJBc/	Instagram

No.	Description	Date	Link	Social Media
	Video on the reconstruction process in "Tahir Sinani" 9-year school			
228	UNDP Communication Manager Mrs. Kushti on EU4Schools The EU4Schools Program Transparency Portal	6 April 2021	https://twitter.com/norakushti/status/1379502510340198408	Twitter
229	UNDP in Albania on EU4Schools About the reconstruction of "Bernardina Qerraxhia" school and dormitory, Durres Municipality	7 April 2021	https://www.facebook.com/PNUDSHQIPERI/posts/4007348602657219	Facebook
230	UNDP in Albania on EU4Schools Testimonials from the article about the importance of the EU4School program to quality education for present and future generations	12 April 2021	https://twitter.com/UNDPAlbania/status/1381671767425568768	Twitter
231	Mayor of Shijak Mr. Arbana on EU4Schools Consultations about the reconstruction project of Kindergarten No.2 and "Rilindja" 9-year school	19 April 2021	https://www.facebook.com/permalink.php?story_fbid=1648323652039279&id=1085717774966539	Facebook
232	Shijak Municipality on EU4Schools Consultations about the reconstruction project of Kindergarten No.2 and "Rilindja" 9-year school	19 April 2021	https://www.facebook.com/permalink.php?story_fbid=295904482105801&id=107332337629684	Facebook
233	UNDP in Albania on EU4Schools About the reconstruction process of "Fiqiri Kuri" 9-year school, Kavaja Municipality	19 April 2021	https://www.facebook.com/PNUDSHQIPERI/posts/4042189095839836	Facebook
234	UNDP in Albania on EU4Schools About the reconstruction process of "Fiqiri Kuri" 9-year school, Kavaja Municipality	19 April 2021	https://www.instagram.com/p/CN2WahzBIVE/	Instagram

No.	Description	Date	Link	Social Media
235	UNDP in Albania on EU4Schools About the reconstruction process of "Fiqiri Kuri" 9-year school, Kavaja Municipality	19 April 2021	https://twitter.com/UNDPAlbania/status/1384097570130071564	Twitter
236	Kindergarten No.2 on EU4Schools Consultations about the reconstruction project of Kindergarten No.2	20 April 2021	https://www.facebook.com/permalink.php?story_fbid=2932579000396575&id=100009335116532	Facebook
237	UNDP in Albania on EU4Schools The EU4Schools Program Transparency Portal	21 April 2021	https://www.facebook.com/PNUDSHQIPERI/posts/4047799058612173	Facebook
238	UNDP in Albania on EU4Schools One year after the signature of the EU4School program	29 April 2021	https://twitter.com/UNDPAlbania/status/1387730112695750662	Twitter
239	UNDP in Albania on EU4Schools Images from the visit in the newly reconstructed "1 Qershori" kindergarten, Durres Municipality	30 April 2021	https://www.facebook.com/PNUDSHQIPERI/posts/4074339535958125	Facebook
240	UNDP in Albania on EU4Schools Images from the visit in the newly reconstructed "1 Qershori" kindergarten, Durres Municipality	30 April 2021	https://www.instagram.com/p/COSxBsThmA-/	Instagram
241	UNDP in Albania on EU4Schools Images from the visit in the newly reconstructed "1 Qershori" kindergarten, Durres Municipality	30 April 2021	https://twitter.com/UNDPAlbania/status/1388133276955598855	Twitter
MAY 2021				
242	EU Ambassador Mr. Soreca on EU4Schools Images from the visit in the newly reconstructed "1 Qershori" kindergarten, Durres Municipality	1 May 2021	https://twitter.com/LSorecaEU/status/1388391965931282437	Twitter

No.	Description	Date	Link	Social Media
243	EU in Albania on EU4Schools Images from the visit in the newly reconstructed "1 Qershori" kindergarten, Durres Municipality	1 May 2021	https://twitter.com/EUinAlbania/status/1388410372948910083	Twitter
244	Mayor of Kruja Mr. Bushi on EU4Schools Prime minister Mr. Rama and EU Ambassador Mr. Soreca inspect the progress made from the EU4School program implementation in Budulla	3 May 2021	https://www.facebook.com/BashkiaKruje/posts/310371230455682	Facebook
245	Kruja Municipality on EU4Schools Prime minister Mr. Rama and EU Ambassador Mr. Soreca inspect the progress made from the EU4School program implementation in Budulla	3 May 2021	https://www.instagram.com/p/COa0YzGrmRG/	Instagram
246	EU in Albania on EU4Schools Prime minister Mr. Rama and EU Ambassador Mr. Soreca inspect the progress made from the EU4School program implementation	3 May 2021	https://www.facebook.com/eu.delegation.albania/posts/3863399330396508	Facebook
247	EU in Albania on EU4Schools Prime minister Mr. Rama and EU Ambassador Mr. Soreca inspect the progress made from the EU4School program implementation	3 May 2021	https://twitter.com/EUinAlbania/status/1389186257700495360	Twitter
248	EU in Albania on EU4Schools Prime minister Mr. Rama and EU Ambassador Mr. Soreca inspect the progress made from the EU4School program implementation	3 May 2021	https://www.instagram.com/p/COaVLs2hNnr/	Instagram
249	Mayor of Kamza Mr. Suli on EU4Schools	5 May 2021	https://www.facebook.com/permalink.php?story_fbid=3875536205828722&id=153971977985182	Facebook

No.	Description	Date	Link	Social Media
	Video and images from the reconstruction site in Babrru			
250	Mayor of Kamza Mr. Suli on EU4Schools Video and images from the reconstruction site in Babrru	5 May 2021	https://www.instagram.com/p/COf4DQ8iKQ4/	Instagram
251	UNDP in Albania on EU4Schools Consultation about "Rilindja" school project, Shijak Municipality	5 May 2021	https://www.facebook.com/PNUDSHQIPERI/posts/4088896881169057	Facebook
252	UNDP in Albania on EU4Schools Consultation about "Rilindja" school project, Shijak Municipality	5 May 2021	https://twitter.com/UNDPAlbania/status/1390025288130650119	Twitter
253	UNDP in Albania on EU4Schools Consultation about "Rilindja" school project, Shijak Municipality	5 May 2021	https://www.instagram.com/p/COgMayMBMlb/	Instagram
254	UNDP in Albania on EU4Schools EU-UNDP partnership projects	9 May 2021	https://www.instagram.com/p/COqDo-zhi5d/	Instagram
255	UNDP in Albania on EU4Schools EU-UNDP partnership projects	9 May 2021	https://twitter.com/UNDPAlbania/status/1391299019671052288	Twitter
256	UNDP in Albania on EU4Schools About the reconstruction process in "Fiqiri Kurti" school, Kavaja Municipality	10 May 2021	https://www.facebook.com/PNUDSHQIPERI/posts/4104248546300557	Facebook
257	Minister of State Mrs. Spiropali on EU4Schools About the reconstruction process in Babrru, Kamza Municipality	10 May 2021	https://www.facebook.com/espiropali/posts/10160853799537926	Facebook

No.	Description	Date	Link	Social Media
258	Minister of State Mrs. Spiropali on EU4Schools About the reconstruction process in Babrru, Kamza Municipality	10 May 2021	https://www.instagram.com/p/COs7wTDBrS6/	Instagram
259	UNDP in Albania on EU4Schools Video and images after the finalization of the reconstruction process for "1 Qershori" kindergarten, Durres Municipality	11 May 2021	https://www.facebook.com/PNUDSHQIPERI/posts/4106037952788283	Facebook
260	UNDP in Albania on EU4Schools Video and images after the finalization of the reconstruction process for "1 Qershori" kindergarten, Durres Municipality	11 May 2021	https://www.instagram.com/p/COvJ8kRBdyU/	Instagram
261	UNDP Representative Mrs. Eltayeb on EU4Schools Images from the visit in the reconstruction site of "1 Qershori" kindergarten, Durres Municipality	11 May 2021	https://twitter.com/EltayebLimya/status/1370111112428060672	Twitter
262	Mayor of Shijak Mr. Arbana on EU4Schools About the reconstruction process of a 9-year old school	12 May 2021	https://www.instagram.com/p/COxdJLyLFjZ/	Instagram
263	Mayor of Durres Mrs. Sako on EU4Schools Video and images after the finalization of the reconstruction process for "1 Qershori" kindergarten, Durres Municipality	13 May 2021	https://www.instagram.com/p/CO0Xs2cBW8N/	Instagram
264	EU in Albania on EU4Schools Visit in the reconstruction site of "Skenderbeu" school in Kruja Municipality	14 May 2021	https://www.facebook.com/eu.delegation.albania/posts/3897382116998229	Facebook

No.	Description	Date	Link	Social Media
265	UNDP in Albania on EU4Schools Visit in the reconstruction site of "Skenderbeu" school in Kruja Municipality	14 May 2021	https://twitter.com/UNDPAlbania/status/1393232847444586502	Twitter
266	UNDP in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Kurbin and Kruje	14 May 2021	https://www.facebook.com/PNUDSHQIPERI/posts/4115736091818469	Facebook
267	UNDP in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Kurbin and Kruje	14 May 2021	https://www.instagram.com/p/CO26lE5HQgP/	Instagram
268	UNDP in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Kurbin and Kruje	14 May 2021	https://twitter.com/UNDPAlbania/status/1393229170059190273	Twitter
269	Mayor of Kamza Mr. Suli on EU4Schools Video and images of the reconstruction site of "Tahir Sinani" school	14 May 2021	https://www.facebook.com/watch/?v=318686826496433	Facebook
270	Mayor of Kamza Mr. Suli on EU4Schools Video and images of the reconstruction site of "Tahir Sinani" school	14 May 2021	https://www.instagram.com/p/CO3JoeRilLP/	Instagram
271	Mayor of Shijak Mr. Arbana on EU4Schools Starting of the reconstruction process for the "Kindergarten No. 2"	14 May 2021	https://www.instagram.com/p/CO3PNq6Lvts/	Instagram
272	EU in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Tirana	14 May 2021	https://www.instagram.com/p/CO3CqpIL9Wv/	Instagram

No.	Description	Date	Link	Social Media
273	EU in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Tirana	15 May 2021	https://www.facebook.com/eu.delegation.albania/posts/3899504046786036	Facebook
274	EU in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Tirana	15 May 2021	https://www.instagram.com/p/CO5fzeXHw05/	Instagram
275	EU in Albania on EU4Schools Europe Weeks 2021 - Video and images from the EU4School program exhibition in Kruja	15 May 2021	https://www.facebook.com/eu.delegation.albania/posts/3900260306710410	Facebook
276	EU in Albania on EU4Schools Europe Weeks 2021 - Video and images from the EU4School program exhibition in Kruja	15 May 2021	https://twitter.com/EUinAlbania/status/1393670872716779525	Twitter
277	EU Ambassador Mr. Soreca on EU4School Europe Weeks 2021 - Video and images from the EU4School program exhibition in Kruja	15 May 2021	https://twitter.com/LSorecaEU/status/1393673472371474437	Twitter
278	EU in Albania on EU4Schools Europe Weeks 2021 - Video and images from the EU4School program exhibition in Kruja	15 May 2021	https://www.instagram.com/p/CO6G01CBYoE/	Instagram
279	Mayor of Kruja Mr. Bushi on EU4Schools EU Ambassador Mr. Soreca visit in “Skenderbeu” school reconstruction site	15 May 2021	https://www.facebook.com/BashkiaKruje/posts/3173388839758921	Facebook
280	EU Ambassador Mr. Soreca on EU4School Europe Weeks 2021 - Video and images from the EU4School program exhibition in Kruja	15 May 2021	https://www.instagram.com/p/CO6HnPqB__5/	Instagram

No.	Description	Date	Link	Social Media
281	Kruja Municipality on EU4Schools Visit in the reconstruction site of "Skenderbeu" school	15 May 2021	https://www.instagram.com/p/CO5bGYOBna8/	Instagram
282	Kruja Municipality on EU4Schools Europe Weeks 2021 – Video and images from the EU4School program exhibition in Kruja	16 May 2021	https://www.instagram.com/p/CO7QVRRBvJN/	Instagram
283	UNDP in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Tirana	16 May 2021	https://www.facebook.com/PNUDSHQIPERI/posts/4120965301295548	Facebook
284	UNDP in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Tirana	16 May 2021	https://twitter.com/UNDPAlbania/status/1393959140079329284	Twitter
285	UNDP in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Tirana	16 May 2021	https://twitter.com/UNDPAlbania/status/1393841940605591559	Twitter
286	UNDP in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Tirana	16 May 2021	https://twitter.com/UNDPAlbania/status/1393889200894791681	Twitter
287	UNDP in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Tirana	16 May 2021	https://twitter.com/UNDPAlbania/status/1393965276174209026	Twitter
288	UNDP in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Tirana	16 May 2021	https://www.instagram.com/p/CO8PPwShBAr/	Instagram
289	UNDP in Albania on EU4Schools	16 May 2021	https://www.instagram.com/p/CO7UGdsHyTX/	Instagram

No.	Description	Date	Link	Social Media
	Europe Weeks 2021 - EU4School program exhibition in Tirana			
290	EU in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Tirana	16 May 2021	https://www.instagram.com/p/CO8R4YfBchr/	Instagram
291	EU in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Tirana	16 May 2021	https://www.facebook.com/eu.delegation.albania/posts/3902751406461300	Facebook
292	Deputy Mayor of Tirana Mrs. Ristani on EU4Schools Europe Weeks 2021 – Video and images from the EU4School program exhibition in Tirana	16 May 2021	https://www.instagram.com/p/CO79s4sHJR0/	Instagram
293	Deputy Mayor of Tirana Mrs. Ristani on EU4Schools Europe Weeks 2021 – EU4School program exhibition in Tirana	16 May 2021	https://www.instagram.com/p/CO8RLAYhfyL/	Instagram
294	Deputy Mayor of Tirana Mr. Mazniku on EU4Schools Europe Weeks 2021 – Video and images from the EU4School program exhibition in Tirana	16 May 2021	https://www.instagram.com/p/CO7YjyhHvkl/	Instagram
295	EU in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Tirana	16 May 2021	https://twitter.com/EUinAlbania/status/1393975768175235078	Twitter
296	UNDP in Albania on EU4Schools Europe Weeks 2021 – Video and images from the EU4School program exhibition in Tirana	17 May 2021	https://www.facebook.com/PNUDSHQIPERI/posts/4123875787671166	Facebook
297	UNDP in Albania on EU4Schools	17 May 2021	https://www.instagram.com/p/CO-UvNghSyM/	Instagram

No.	Description	Date	Link	Social Media
	Europe Weeks 2021 – Video and images from the EU4School program exhibition in Tirana			
298	UNDP in Albania on EU4Schools Europe Weeks 2021 – Video and images from the EU4School program exhibition in Tirana	17 May 2021	https://twitter.com/UNDPAlbania/status/1394241283267473412	Twitter
299	EU in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Tirana	17 May 2021	https://www.instagram.com/p/CO-zROnLocp/	Instagram
300	UNDP Representative Mrs. Eltayeb on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Tirana	17 May 2021	https://twitter.com/EltayebLimya/status/1394192573565214720	Twitter
301	Mayor of Kamza Mr. Suli on EU4Schools Europe Weeks 2021 - EU Ambassadors Mr. Soreca visit in Kamza	18 May 2021	https://www.facebook.com/permalink.php?story_fbid=3914408465274829&id=153971977985182	Facebook
302	UNDP in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Shijak, Kamza and Vora	18 May 2021	https://www.facebook.com/PNUDSHQIPERI/posts/4129260823799329	Facebook
303	EU in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Kamza	18 May 2021	https://www.facebook.com/eu.delegation.albania/posts/3908312365905204	Facebook
304	EU in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Kamza	18 May 2021	https://www.instagram.com/p/CPAprtQB22i/	Instagram
305	EU in Albania on EU4Schools	18 May 2021	https://twitter.com/EUinAlbania/status/1394591097557553156	Twitter

No.	Description	Date	Link	Social Media
	Europe Weeks 2021 - EU4School program exhibition in Kamza			
306	EU Ambassador Mr. Soreca on EU4School Europe Weeks 2021 - EU4School program exhibition in Kamza	18 May 2021	https://www.instagram.com/p/CPAzSGnByMf/	Instagram
307	EU Ambassador Mr. Soreca on EU4School Europe Weeks 2021 - EU4School program exhibition in Kamza	18 May 2021	https://twitter.com/LSorecaEU/status/1394592060733329408	Twitter
308	UNDP in Albania on EU4Schools Consultation prior to reconstructing the 9- year school in Vora	18 May 2021	https://twitter.com/UNDPAlbania/status/1394558166365507584	Twitter
309	UNDP in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Shijak, Kamza and Vora	19 May 2021	https://twitter.com/UNDPAlbania/status/1394907613947736066	Twitter
310	Durres Municipality on EU4Schools Europe Weeks 2021 - EU Ambassador Mr. Soreca visit in Durres	19 May 2021	https://www.facebook.com/durres.gov.al/posts/10159636984331119	Facebook
311	Mayor of Durres Mrs. Sako on EU4Schools Europe Weeks 2021 - EU Ambassador Mr. Soreca visit in Durres	19 May 2021	https://www.facebook.com/emiriana.sako/posts/2484899973735048	Facebook
312	Mayor of Durres Mrs. Sako on EU4Schools Europe Weeks 2021 - EU Ambassador Mr. Soreca visit in Durres	19 May 2021	https://www.instagram.com/p/CPDfBGdh4vI/	Instagram
313	Mayor of Durres Mrs. Sako on EU4Schools	19 May 2021	https://www.facebook.com/emiriana.sako/posts/2486612570389455	Facebook

No.	Description	Date	Link	Social Media
	Europe Weeks 2021 - Inspection in the reconstruction site of "Ismet Nanushi" high school, with EU Ambassador Mr. Soreca			
314	UNDP in Albania on EU4Schools Europe Weeks 2021 - Inspection in the reconstruction site of "Ismet Nanushi" school	19 May 2021	https://www.facebook.com/PNUDSHQIPERI/posts/4132098670182211	Facebook
315	UNDP in Albania on EU4Schools Europe Weeks 2021 - Inspection in the reconstruction site of "Ismet Nanushi" school	19 May 2021	https://twitter.com/UNDPAlbania/status/1395083741568114690	Twitter
316	UNDP in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Durres	19 May 2021	https://www.facebook.com/PNUDSHQIPERI/posts/4130724960319582	Facebook
317	UNDP in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Durres	19 May 2021	https://www.instagram.com/p/CPDMqhfn5vX/	Instagram
318	UNDP in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Durres	19 May 2021	https://twitter.com/UNDPAlbania/status/1394915587323740161	Twitter
319	UNDP in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Durres	19 May 2021	https://twitter.com/UNDPAlbania/status/1394953018848776193	Twitter
320	EU in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Durres	19 May 2021	https://www.facebook.com/eu.delegation.albania/posts/3911306238939150	Facebook

No.	Description	Date	Link	Social Media
321	EU in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Durres	19 May 2021	https://www.instagram.com/p/CPDN9pWnHUO/	Instagram
322	EU Neighbourhood & Enlargement on EU4Schools About the EU4Schools project implementation	19 May 2021	https://www.instagram.com/p/CPDAuqPrS4n/	Instagram
323	EU in Albania on EU4Schools EU Ambassador Mr. Soreca visit in Durres	19 May 2021	https://twitter.com/EUinAlbania/status/1394954212044382208	Twitter
324	Mayor of Kavaja Mr. Krali on EU4Schools Europe Weeks 2021 - Head of Cooperation at the EU Delegation Mr. Mariani visit in Kavaja	20 May 2021	https://www.facebook.com/RedjanKrali/posts/813762232678499	Facebook
325	EU in Albania on EU4Schools Europe Weeks 2021 – Visit in the reconstruction site of “Fiqiri Kurti” school, Kavaja Municipality	20 May 2021	https://www.facebook.com/eu.delegation.albania/posts/3915415228528251	Facebook
326	UNDP in Albania on EU4Schools Europe Weeks 2021 - EU4School program exhibition in Kavaja	20 May 2021	https://www.facebook.com/PNUDSHQIPERI/posts/4134064636636652381	Facebook
327	EU in Albania on EU4Schools Images from the visit in the reconstruction site of “Fiqiri Kurti” school, Kavaja Municipality	20 May 2021	https://www.facebook.com/eu.delegation.albania/posts/3914203218649452	Facebook
328	EU in Albania on EU4Schools Images from the visit in the reconstruction site of “Fiqiri Kurti” school, Kavaja Municipality	20 May 2021	https://twitter.com/EUinAlbania/status/1395329083597332481	Twitter
329	UNDP in Albania on EU4Schools Visit in the reconstruction site of “Fiqiri Kurti” school, Kavaja Municipality	20 May 2021	https://twitter.com/UNDPAlbania/status/1395359340119351297	Twitter

No.	Description	Date	Link	Social Media
330	EU in Albania on EU4Schools Images from the visit in the reconstruction site of "Fiqiri Kurti" school, Kavaja Municipality	20 May 2021	https://www.instagram.com/p/CPF46PaLOUo/	Instagram
331	EU in Albania on EU4Schools About the reconstruction process in "Ismet Nanushi" school, Durres Municipality	20 May 2021	https://www.facebook.com/eu.delegation.albania/posts/3914623145274126	Facebook
332	EU in Albania on EU4Schools About the reconstruction process in "Ismet Nanushi" school, Durres Municipality	20 May 2021	https://twitter.com/EUinAlbania/status/1395394684915232775	Twitter
333	EU Ambassador Mr. Soreca on EU4Schools About the reconstruction process in "Ismet Nanushi" school, Durres Municipality	20 May 2021	https://twitter.com/LSorecaEU/status/1395398167819083776	Twitter
334	EU in Albania on EU4Schools About the reconstruction process in "Ismet Nanushi" school, Durres Municipality	20 May 2021	https://www.instagram.com/p/CPGWPkoq0Cy/	Instagram
335	EU in Albania on EU4Schools About the reconstruction process in "Ismet Nanushi" school, Durres Municipality	20 May 2021	https://twitter.com/EUinAlbania/status/1395329092329762832	Twitter
336	Mayor of Kavaja Mr. Krali on EU4Schools Inspection in the reconstruction site of "Fiqiri Kurti" school with Head of Cooperation at the EU Delegation Mr. Mariani	21 May 2021	https://www.facebook.com/groups/fiqirikurti/permalink/10158073495142327/	Facebook
337	Prime minister Edi Rama on EU4Schools Inspection in the reconstruction site of "Ismet Nanushi" school, with Minister for Reconstruction Mr.	24 May 2021	https://www.facebook.com/edirama.al/videos/331676444960452	Facebook

No.	Description	Date	Link	Social Media
	Ahmetaj, Mayor of Durres Mrs. Sako and UNDP Representative Mrs. Eltayeb			
338	Mayor of Durres Mrs. Sako on EU4Schools Inspection in the reconstruction site of "Ismet Nanushi" school, with prime minister Mr. Rama, Minister for Reconstruction Mr. Ahmetaj and UNDP Representative Mrs. Eltayeb	24 May 2021	https://www.facebook.com/emiriana.sako/posts/2520005703383475	Facebook
339	Minister for Reconstruction Mr. Ahmetaj on EU4Schools Inspection in the reconstruction site of "Ismet Nanushi" school, with prime minister Mr. Rama, Mayor of Durres Mrs. Sako and UNDP Representative Mrs. Eltayeb	24 May 2021	https://www.facebook.com/arben.ahmetaj.al/videos/331677464960350	Facebook
340	UNDP in Albania on EU4Schools Prime minister Mr. Rama, Minister for Reconstruction Mr. Ahmetaj, Mayor of Durres Mrs. Sako and UNDP Representative Mrs. Eltayeb inspect the reconstruction site of "Ismet Nanushi" school, Durres Municipality	24 May 2021	https://www.facebook.com/PNUDSHQIPERI/posts/4145705795488165	Facebook
341	UNDP in Albania on EU4Schools Prime minister Mr. Rama, Minister for Reconstruction Mr. Ahmetaj, Mayor of Durres Mrs. Sako and UNDP Representative Mrs. Eltayeb inspect the reconstruction site of "Ismet Nanushi" school, Durres Municipality	24 May 2021	https://www.instagram.com/p/CPQP3Y1ni9W/	Instagram

No.	Description	Date	Link	Social Media
342	EU in Albania on EU4Schools Europe Weeks 2021 – Video about the EU4School program exhibition in Durres	24 May 2021	https://www.facebook.com/eu.delegation.albania/posts/3927028647366909	Facebook
343	EU in Albania on EU4Schools Europe Weeks 2021 – Video about the EU4School program exhibition in Durres	24 May 2021	https://www.instagram.com/p/CPQ33u9rfH-/	Instagram
344	EU in Albania on EU4Schools Europe Weeks 2021 – Video about the EU4School program exhibition in Durres	24 May 2021	https://twitter.com/EUinAlbania/status/1396878676403294211	Twitter
345	UNDP Representative Mrs. Eltayeb on EU4Schools Prime minister Mr. Rama, Minister for Reconstruction Mr. Ahmetaj, Mayor of Durres Mrs. Sako and UNDP Representative Mrs. Eltayeb inspect the reconstruction site of "Ismet Nanushi" school, Durres Municipality	24 May 2021	https://twitter.com/EltayebLimya/status/1396763338709872640	Twitter
346	UNDP in Albania on EU4Schools Europe Weeks 2021 – About the EU4Schools project implementation	24 May 2021	https://twitter.com/UNDPAlbania/status/1397539699229609989	Twitter
347	Mayor of Kamza Mr. Suli on EU4Schools Video and images from the reconstruction site of "Dom Nikolle Kacorri" school	31 May 2021	https://www.facebook.com/permalink.php?story_fbid=3953399601375715&id=153971977985182	Facebook
348	Mayor of Kamza Mr. Suli on EU4Schools Video and images from the reconstruction site of "Dom Nikolle Kacorri" school	31 May 2021	https://www.instagram.com/p/CPjHTkXCRld/	Instagram

No.	Description	Date	Link	Social Media
		JUNE 2021		
349	PM Edi Rama on EU4Schools PM Edi Rama, Minister of State for Reconstruction Mr. Ahmetaj, EU Ambassador Mr. Soreca and UNDP Representative Mrs. Eltayeb, visit in "Gjoke Elezi" and "Demokracia" school and kindergarten in Kurbin Municipality	1 June 2021	https://www.facebook.com/edirama.al/videos/1849377525222993	Facebook
350	UNDP in Albania on EU4Schools PM Edi Rama, Minister of State for Reconstruction Mr. Ahmetaj, EU Ambassador Mr. Soreca and UNDP Representative Mrs. Eltayeb, visit in "Gjoke Elezi" and "Demokracia" school and kindergarten in Kurbin Municipality	1 June 2021	https://www.facebook.com/PNUDSHQIPERI/posts/4170372796354798	Facebook
351	UNDP in Albania on EU4Schools PM Edi Rama, Minister of State for Reconstruction Mr. Ahmetaj, EU Ambassador Mr. Soreca and UNDP Representative Mrs. Eltayeb, visit in "Gjoke Elezi" and "Demokracia" school and kindergarten in Kurbin Municipality	1 June 2021	https://www.instagram.com/p/CPlW7KAhwbt/	Instagram
352	UNDP in Albania on EU4Schools PM Edi Rama, Minister of State for Reconstruction Mr. Ahmetaj, EU Ambassador Mr. Soreca and UNDP Representative Mrs. Eltayeb, visit in "Gjoke Elezi" school in Kurbin Municipality	1 June 2021	https://twitter.com/UNDPAlbania/status/1399693553987620870	Twitter

No.	Description	Date	Link	Social Media
353	UNDP in Albania on EU4Schools PM Edi Rama, Minister of State for Reconstruction Mr. Ahmetaj, EU Ambassador Mr. Soreca and UNDP Representative Mrs. Eltayeb, visit in "Demokracia" 9-year school and kindergarten in Kurbin Municipality	1 June 2021	https://twitter.com/UNDPAlbania/status/1399756649607356421	Twitter
354	EU in Albania on EU4Schools PM Edi Rama, Minister of State for Reconstruction Mr. Ahmetaj, EU Ambassador Mr. Soreca and UNDP Representative Mrs. Eltayeb, visit in "Gjoke Elezi" and "Demokracia" school and kindergarten in Kurbin Municipality	1 June 2021	https://www.facebook.com/eu.delegation.albania/posts/3949592555110518	Facebook
355	EU in Albania on EU4Schools PM Edi Rama, Minister of State for Reconstruction Mr. Ahmetaj, EU Ambassador Mr. Soreca and UNDP Representative Mrs. Eltayeb, visit in "Gjoke Elezi" and "Demokracia" school and kindergarten in Kurbin Municipality	1 June 2021	https://www.instagram.com/p/CPkzpGvrDk6/	Instagram
356	EU in Albania on EU4Schools PM Edi Rama, Minister of State for Reconstruction Mr. Ahmetaj, EU Ambassador Mr. Soreca and UNDP Representative Mrs. Eltayeb, visit in "Gjoke Elezi" and "Demokracia" school and kindergarten in Kurbin Municipality	1 June 2021	https://twitter.com/EUinAlbania/status/1399679423004151808	Twitter
357	EU Ambassador Mr. Soreca on EU4Schools	1 June 2021	https://twitter.com/LSorecaEU/status/1399669590762926081	Twitter

No.	Description	Date	Link	Social Media
	PM Edi Rama, Minister of State for Reconstruction Mr. Ahmetaj, EU Ambassador Mr. Soreca and UNDP Representative Mrs. Eltayeb, visit in "Gjoke Elezi" and "Demokracia" school and kindergarten in Kurbin Municipality			
358	UNDP Representative Mrs. Eltayeb on EU4Schools PM Edi Rama, Minister of State for Reconstruction Mr. Ahmetaj, EU Ambassador Mr. Soreca and UNDP Representative Mrs. Eltayeb, visit in "Gjoke Elezi" and "Demokracia" school and kindergarten in Kurbin Municipality	1 June 2021	https://twitter.com/EltayebLimya/status/1399656740380200962	Twitter
359	UN Resident Coordinator Mrs. McCluney on EU4Schools About the UNDP work delivering and officials visit in reconstruction sites in Kurbin Municipality	1 June 2021	https://twitter.com/FionaMcCluney/status/1399811979989159944	Twitter
360	Kurbin Municipality on EU4Schools PM Edi Rama, Minister of State for Reconstruction Mr. Ahmetaj, EU Ambassador Mr. Soreca and UNDP Representative Mrs. Eltayeb, visit in "Gjoke Elezi" and "Demokracia" school and kindergarten in Kurbin Municipality	1 June 2021	https://www.facebook.com/permalink.php?story_fbid=534877734562980&id=115227253194699	Facebook
361	Mayor of Kamza Mr. Suli on EU4Schools Video and images from the reconstruction site of childcare in Babrru	3 June 2021	https://www.facebook.com/permalink.php?story_fbid=3962063970509278&id=153971977985182	Facebook

No.	Description	Date	Link	Social Media
362	Mayor of Kamza Mr. Suli on EU4Schools Video and images from the reconstruction site of childcare in Babrru	3 June 2021	https://www.instagram.com/p/CPqpVQ0i1m4/	Instagram
363	Local Educational Office in Kamza on EU4Schools Video and images from the reconstruction site of "Dom Nikolle Kacorri" school in Laknas	7 June 2021	https://www.facebook.com/ZyraVendoreArsimoreKamez/posts/1066162227123681	Facebook
364	Mayor of Kamza Mr. Suli on EU4Schools Video and images from the reconstruction site of "Dom Nikolle Kacorri" school in Laknas	7 June 2021	https://www.facebook.com/permalink.php?story_fbid=3972062132842795&id=153971977985182	Facebook
365	Mayor of Kamza Mr. Suli on EU4Schools Video and images from the reconstruction site of "Dom Nikolle Kacorri" school in Laknas	7 June 2021	https://www.instagram.com/p/CPz3oYhCdi1/	Instagram
366	"Benardina Qerraxhia" Sports School on EU4Schools Presentation of the reconstruction project for "Bernardina Qerraxhia" school	9 June 2021	https://www.facebook.com/shkollasportive.benardinaqerraxhia/posts/4203854069635981	Facebook
367	Mayor of Kavaja Mr. Krali on EU4Schools Images from the reconstruction site of "Fiqiri Kurti" school	15 June 2021	https://www.facebook.com/RedjanKrali/posts/827988497922539	Facebook
368	Mayor of Kamza Mr. Suli on EU4Schools Video and images from the reconstruction site of "Jashar Hoxha" kindergarten	15 June 2021	https://www.facebook.com/permalink.php?story_fbid=3994357510613257&id=153971977985182	Facebook
369	Mayor of Kamza Mr. Suli on EU4Schools Video and images from the reconstruction site of "Jashar Hoxha" kindergarten	15 June 2021	https://www.instagram.com/p/CQJDHflCR1Y/	Instagram

No.	Description	Date	Link	Social Media
370	Mayor of Kavaja Mr. Krali on EU4Schools Images from the reconstruction site of "Mehmet Babamusta" school	16 June 2021	https://www.facebook.com/RedjanKrali/posts/828516617869727	Facebook
371	UNDP in Albania on EU4Schools Consultation about the reconstruction project of "Gjergj Kastrioti" school, Lezha Municipality	17 June 2021	https://www.facebook.com/PNUDSHQIPERI/posts/4214598608598883	Facebook
372	Mayor of Kruja Mr. Bushi on EU4Schools Images from the reconstruction site of Derede" kindergarten	18 June 2021	https://www.facebook.com/BashkiaKruje/posts/339722600853878	Facebook
373	Kruja Municipality on EU4Schools Images from the reconstruction site of Derede" kindergarten	18 June 2021	https://www.instagram.com/p/CQROwS1L4gX/	Instagram
374	UNDP in Albania on EU4Schools Images from public consultations	23 June 2021	https://twitter.com/UNDPAlbania/status/1407674660595044358	Twitter
375	Mayor of Kamza Mr. Suli on EU4Schools Video of the two variants proposed for the construction of the child care in Paskuqan	24 June 2021	https://www.facebook.com/permalink.php?story_fbid=4019136391468702&id=153971977985182	Facebook
376	Mayor of Kamza Mr. Suli on EU4Schools Video of the two variants proposed for the construction of the child care in Paskuqan	24 June 2021	https://www.instagram.com/p/CQhFeYgizKG/	Instagram
377	Mayor of Kamza Mr. Suli on EU4Schools Video of the two variants proposed for the construction of "Azem Hajdari" kindergarten	25 June 2021	https://www.facebook.com/permalink.php?story_fbid=4021843017864706&id=153971977985182	Facebook
378	Mayor of Kamza Mr. Suli on EU4Schools	25 June 2021	https://www.instagram.com/p/CQjRKKgCwey/	Instagram

No.	Description	Date	Link	Social Media
	Video of the two variants proposed for the construction of "Azem Hajdari" kindergarten			
379	EU in Albania on EU4Schools Europe Weeks 2021 – EU4School program in Kavaje and Rrogozhine Municipality	29 June 2021	https://www.facebook.com/eu.delegation.albania/posts/4026210467448726	Facebook
380	EU in Albania on EU4Schools Europe Weeks 2021 – EU4School program in Kavaje and Rrogozhine Municipality	29 June 2021	https://www.instagram.com/p/CQthJN_LelJ/	Instagram
381	EU in Albania on EU4Schools Europe Weeks 2021 – EU4School program in Kavaje and Rrogozhine Municipality	29 June 2021	https://twitter.com/EUinAlbania/status/1409911449560944642	Twitter
		JULY 2021		
382	Mayor of Kamza Mr. Suli on EU4Schools Proposed variants for the reconstruction of "Ibrahim Basha" school and kindergarten	1 July 2021	https://www.facebook.com/permalink.php?story_fbid=4038103916238616&id=153971977985182	Facebook
383	Local Educational Office in Kamza on EU4Schools Proposed variants for the reconstruction of "Ibrahim Basha" school and kindergarten	1 July 2021	https://www.facebook.com/ZyraVendoreArsimoreKamez/posts/1081340388939198	Facebook
384	UNDP in Albania on EU4Schools Public consultations for "Ibrahim Basha" school and kindergarten, "26 Nentori" school and kindergarten no. 41	5 July 2021	https://www.facebook.com/PNUDSHQIPERI/posts/4262345823824161	Facebook

No.	Description	Date	Link	Social Media
385	UNDP in Albania on EU4Schools Public consultations for "Ibrahim Basha" school and kindergarten, "26 Nentori" school and kindergarten no. 41	5 July 2021	https://twitter.com/UNDPAlbania/status/1412010730161856516	Twitter
386	UNDP in Albania on EU4Schools Public consultations for "Ibrahim Basha" school and kindergarten, "26 Nentori" school and kindergarten no. 41	5 July 2021	https://www.instagram.com/p/CQ8HUq8DJiP/	Instagram
387	UNDP in Albania on EU4Schools Article about the first 15 education facilities ready for the new school year	7 July 2021	https://albania-undp.medium.com/eu4schools-brings-childrens-dreams-to-life-e30977e572f9	UNDP online media
388	UNDP Communication Manager Mrs. Kushti on EU4Schools Article about the importance of the EU4School program for children and the society	7 July 2021	https://twitter.com/norakushti/status/1412864988314836997	Twitter
389	Mayor of Kurbin Mrs. Cara on EU4Schools About the reconstruction process of "Gjoke Elezi" 9-year school	13 July 2021	https://www.facebook.com/MajlindaShqalsiCara/posts/886315625316649	Facebook
390	UNDP in Albania on EU4Schools Article about the first 15 education facilities ready for the new school year	13 July 2021	https://twitter.com/UNDPAlbania/status/1414931670470258692	Twitter
391	UNDP in Albania on EU4Schools EU4Schools Transparency Portal	13 July 2021	https://twitter.com/UNDPAlbania/status/1414923866800107522	Twitter
392	Kurbin Municipality on EU4School	14 July 2021	https://www.facebook.com/permalink.php?story_fbid=562422781808475&id=115227253194699	Facebook

No.	Description	Date	Link	Social Media
	Completion of the reconstruction process in "Gjoke Elezi" 9-year school			
393	Kurbin Municipality on EU4School Completion of the reconstruction process in "Gjoke Elezi" 9-year school	14 July 2021	https://www.instagram.com/p/CRUpdflriy3/	Instagram
394	Mayor of Durres Mrs. Sako on EU4Schools Inspection in the reconstruction site of "Ismet Nanushi" school and kindergarten	14 July 2021	https://www.instagram.com/p/CRUcKOmDb08/	Instagram
395	Mayor of Kamza Mr. Suli on EU4Schools Towards completion of the reconstruction process in "Dom Nikolle Kacorri" school	22 July 2021	https://www.facebook.com/permalink.php?story_fbid=4096905120358495&id=153971977985182	Facebook
396	Local Educational Office in Kamza on EU4Schools Towards completion of the reconstruction process in "Dom Nikolle Kacorri" school	22 July 2021	https://www.facebook.com/ZyraVendoreArsimoreKamez/posts/1094268724313031	Facebook
397	Director of Local Educational Office in Kamza Mr. Murataj on EU4Schools Towards completion of the reconstruction process in "Dom Nikolle Kacorri" school	22 July 2021	https://www.facebook.com/geri.murataj.3/posts/540263650451454	Facebook
398	UNDP Eurasia on EU4Schools About the EU4School project	22 July 2021	https://twitter.com/UNDPEurasia/status/1418116186617823232	Twitter
399	Mayor of Kamza Mr. Suli on EU4Schools Towards completion of the reconstruction process in "Dom Nikolle Kacorri" kindergarten	23 July 2021	https://www.facebook.com/permalink.php?story_fbid=4099681403414200&id=153971977985182	Facebook
400	Mayor of Kamza Mr. Suli on EU4Schools	24 July 2021	https://www.facebook.com/permalink.php?story_fbid=4101828376532836&id=153971977985182	Facebook

No.	Description	Date	Link	Social Media
	Towards completion of the reconstruction process in "Tahir Sinani" school			
401	Local Educational Office in Kamza on EU4Schools Towards completion of the reconstruction process in "Tahir Sinani" school	24 July 2021	https://www.facebook.com/ZyraVendoreArsimoreKamez/posts/1095311727542064	Facebook
402	Mayor of Kavaja Mr. Krali on EU4Schools Public consultation for "Charles Telford Erickson" high school	26 July 2021	https://www.facebook.com/RedjanKrali/posts/2340821285372 09	Facebook
403	"Charles Telford Erickson" high school on EU4Schools Public consultation about project ideas and variants	27 July 2021	https://www.instagram.com/p/CR09FkVs4uO/	Instagram
404	Mayor of Kamza Mr. Suli on EU4Schools Towards completion of the reconstruction process in "Jashar Hoxha" kindergarten	30 July 2021	https://www.facebook.com/watch/?v=2991959286251 33	Facebook
	AUGUST 2021			
405	Minister of Education, Mrs. Kushi on EU4Schools About the reconstruction process of "28 Nentori" 9-year school and kindergarten	5 August 2021	https://www.facebook.com/kushievis/posts/324387966043311	Facebook
406	Minister of Education, Mrs. Kushi on EU4Schools About the reconstruction process of "28 Nentori" 9-year school and kindergarten	5 August 2021	https://www.instagram.com/p/CSMaDfxMXOY/	Instagram
407	Minister of Education, Mrs. Kushi on EU4Schools About the reconstruction process of "28 Nentori" 9-year school and kindergarten	5 August 2021	https://twitter.com/EvisKushi/status/1423271424660283394	Twitter

No.	Description	Date	Link	Social Media
408	Ministry of Education on EU4Schools About the reconstruction process of "28 Nentori" 9-year school and kindergarten	5 August 2021	https://www.instagram.com/p/CSMa-KsspM8/	Instagram
409	UNDP in Albania on EU4Schools About the newly reconstructed "1 Qershori" kindergarten in Durres Municipality	5 August 2021	https://twitter.com/UNDPAlbania/status/1423261656864460803	Twitter
410	Mayor of Kruja Mr. Bushi on EU4Schools Towards completion of the reconstruction process in a facility in Budull	12 August 2021	https://www.facebook.com/BashkiaKruje/posts/374641974028607	Facebook
411	Mayor of Kavaja Mr. Krali on EU4Schools Completion of the reconstruction process in "Mehmet Babamusta" school	17 August 2021	https://www.facebook.com/RedjanKrali/posts/2473394005448 15	Facebook
412	Mayor of Kavaja Mr. Krali on EU4Schools Completion of the reconstruction process in "Mehmet Babamusta" school	17 August 2021	https://www.instagram.com/p/CSrt7CfsuLL/	Instagram
413	"Dom Nikolle Kacorri" school on EU4Schools Towards completion of the reconstruction process in "Dom Nikolle Kacorri" school	19 August 2021	https://www.facebook.com/permalink.php?story_fbid=1191109441399739&id=293816884462337	Facebook
414	Local Educational Office in Kamza on EU4Schools Towards completion of the reconstruction process in "Dom Nikolle Kacorri" school	19 August 2021	https://www.facebook.com/ZyraVendoreArsimoreKamez/posts/1111342875938949	Facebook
415	Director of Local Educational Office in Kamza Mr. Murataj on EU4Schools Towards completion of the reconstruction process in "Dom Nikolle Kacorri" school	19 August 2021	https://www.facebook.com/geri.murataj.3/posts/556986355445850	Facebook

No.	Description	Date	Link	Social Media
416	EU in Albania on EU4Schools Visits in some of the educational facilities during Europe Weeks 2021	19 August 2021	https://www.facebook.com/eu.delegation.albania/posts/4157127251023713	Facebook
417	EU in Albania on EU4Schools Visits in some of the educational facilities during Europe Weeks 2021	19 August 2021	https://www.instagram.com/p/CSv53rjLe3J/	Instagram
418	EU in Albania on EU4Schools Visits in some of the educational facilities during Europe Weeks 2021	19 August 2021	https://twitter.com/EUinAlbania/status/1428265478049472513	Twitter
419	Mayor of Kruja Mr. Bushi on EU4Schools Start of the reconstruction process of a 9-year school in Bilaj village	20 August 2021	https://www.facebook.com/BashkiaKruje/posts/379715286854609	Facebook
420	Kruja Municipality on EU4Schools Start of the reconstruction process of a 9-year school in Bilaj village	20 August 2021	https://www.instagram.com/p/CSzjB9Lr0p3/	Instagram
421	Mayor of Kamza Mr. Suli on EU4Schools Video and images of the newly reconstructed “Dom Nikolle Kacorri” school	21 August 2021	https://www.facebook.com/153971977985182/videos/573640123817073	Facebook
422	Mayor of Kamza Mr. Suli on EU4Schools Video and images of the newly reconstructed “Dom Nikolle Kacorri” school	21 August 2021	https://www.instagram.com/p/CS1GEGOiU6l/	Instagram
423	“Dom Nikolle Kacorri” school on EU4Schools Video and images of the completed reconstruction of “Dom Nikolle Kacorri” school	21 August 2021	https://www.facebook.com/permalink.php?story_fbid=1192263807950969&id=293816884462337	Facebook

No.	Description	Date	Link	Social Media
424	Mayor of Kamza Mr. Suli on EU4Schools Video and images of the completed reconstruction of "Dom Nikolle Kacorri" school	23 August 2021	https://www.facebook.com/permalink.php?story_fbid=4189929797722693&id=153971977985182	Facebook
425	UNDP in Albania on EU4Schools The list of educational facilities for which the reconstruction process has been completed	23 August 2021	https://www.facebook.com/PNUDSHQIPERI/posts/4405523776173031	Facebook
426	UNDP in Albania on EU4Schools About the EU4School project progress so far	23 August 2021	https://www.instagram.com/p/CS6wjupDXdP/	Instagram
427	UNDP in Albania on EU4Schools About the EU4School project progress so far	23 August 2021	https://twitter.com/UNDPAlbania/status/1429792226251509761	Twitter
428	UNDP in Albania on EU4Schools EU4Schools Transparency Portal	24 August 2021	https://twitter.com/UNDPAlbania/status/1430159221207797778	Twitter
429	Mayor of Kavaja Mr. Krali on EU4Schools Completion of the reconstruction process in "Fiqiri Kurti" school	27 August 2021	https://www.facebook.com/RedjanKrali/posts/2533242279946327	Facebook
430	Mayor of Kavaja Mr. Krali on EU4Schools Completion of the reconstruction process in "Fiqiri Kurti" school	27 August 2021	https://www.instagram.com/p/CTFpFqTsaES/	Instagram
431	Mayor of Kamza Mr. Suli on EU4Schools Video and images from the reconstruction site and project of "Jashar Hoxha" kindergarten	28 August 2021	https://www.facebook.com/permalink.php?story_fbid=4205251496190523&id=153971977985182	Facebook
432	Mayor of Kurbin Mrs. Cara on EU4Schools Completion of the reconstruction process in "Demokracia" 9-year school	28 August 2021	https://www.facebook.com/MajlindaShqalsiCara/posts/914911249123753	Facebook

No.	Description	Date	Link	Social Media
433	Kurbin Municipality on EU4Schools Completion of the reconstruction process in "Demokracia" 9-year school	28 August 2021	https://www.facebook.com/permalink.php?story_fbid=591687655548654&id=115227253194699	Facebook
434	Kruja Municipality on EU4Schools Start of the reconstruction process in a kindergarten in Varosh	31 August 2021	https://www.instagram.com/p/CTPz23_LoGM/	Instagram
435	UNDP in Albania on EU4Schools Monitoring visit at one of the 63 education facilities which are being reconstructed/repaired	31 August 2021	https://twitter.com/UNDPAlbania/status/1432642991995375616	Twitter
436	UNDP in Albania on EU4Schools Article about the first 15 education facilities ready or the new school year	31 August 2021	https://albania-undp.medium.com/eu4schools-the-first-13-education-institutions-to-welcome-children-for-the-new-school-year-c9ac0e7a8f0d	UNDP online media
SEPTEMBER 2021				
437	Nuno Queiros, Dep. Rep. of UNDP in Albania on EU4Schools: 3 education facilities to welcome children for the new school year	1 September 2021	https://twitter.com/ndequeiros/status/1433079543154282496?t=K7t0Y-M8qLdhcZ6BgSUI6w&s=19	Twitter
438	UNDP in Albania on EU4Schools: 13 new repaired/reconstructed educational facilities ready for the new academic year	1 September 2021	https://www.facebook.com/302120716513378/posts/4431778763547532/	Facebook
439	Mayor of Kamza on EU4Schools: inspection to "Dom Nikollë Kaçorri" 9-year school	10 September 2021	https://m.facebook.com/story.php?story_fbid=4244245862291086&id=153971977985182	Facebook
440	Mayor of Kamza on EU4Schools: inspection to thoroughly reconstructed "Dom Nikollë Kaçorri" 9-year school & kindergarten	10 September 2021	https://www.instagram.com/p/CTpt8jKqq_r/?utm_medium=copy_link	Instagram

No.	Description	Date	Link	Social Media
441	Kamza Educational Office Director on EU4Schools: inspection in the newly reconstructed "Dom Nikollë Kaçorri" 9-year school & kindergarten	10 September 2021	https://www.facebook.com/100034034721573/posts/570233600787792/	Facebook
442	Mayor of Kurbin on EU4Schools: Works at "28 Nëntori" & "Cub Çapani" schools are at the final phases	13 September 2021	https://m.facebook.com/story.php?story_fbid=924978831450328&id=376016303013253	Facebook
443	Mayor of Kamza on EU4Schools: "Tahir Sinani" 9-year school & kindergarten, ready to welcome children and teachers	14 September 2021	https://m.facebook.com/story.php?story_fbid=4258068720908800&id=153971977985182	Facebook
444	Mayor of Kamza on EU4Schools: "Tahir Sinani" 9-year school & kindergarten ready with modern contemporary standards	14 September 2021	https://www.facebook.com/153971977985182/posts/4258068720908800/	Facebook
445	"Tahir Sinani" 9-year school in Kamza on "EU4Schools": The school today offers the highest standards	14 September 2021	https://www.facebook.com/141893092840843/posts/1523128961383909/	Facebook
446	Mayor of Kurbin on EU4Schools: inspection during the reconstruction process of "Gjokë Elezi" high school	15 September 2021	https://m.facebook.com/story.php?story_fbid=926261334655411&id=376016303013253	Facebook
447	UNDP in Albania on EU4Schools: images from the thoroughly renovated “1 Qershori” Kindergarten in Durrës	16 September 2021	https://twitter.com/UNDPAlbania/status/1438510252580687886?t=MeIxWalZyZyQU-vHX5yKTg&s=19	Twitter
448	Deputy Prime Minister on EU4Schools: "Demokracia" school reconstructed. Standards for 130 children	20 September 2021	https://ata.gov.al/2021/09/20/rikonstruktohet-shkolla-demokracia-ne-kurbin-ahmetaj-standarde-per-130-femije/	Online Media
449	Deputy Prime Minister on EU4Schools: "Demokracia" 9-year school & kindergarten, thoroughly	20 September 2021	https://www.instagram.com/p/CUCrvvHo_Px/?utm_medium=copy_link	Instagram

No.	Description	Date	Link	Social Media
	reconstructed through the principles of "Building Back Better"			
450	Deputy Prime Minister on EU4Schools: "Demokracia" 9-year school & kindergarten, thoroughly reconstructed through the principles of "Building Back Better"	20 September 2021	https://www.facebook.com/100044420739861/posts/407673287390026/	Facebook
451	UNDP in Albania on EU4Schools: facts provided on the Programme	21 September 2021	https://twitter.com/UNDPAlbania/status/1440266726797574152?t=DqxeRT5wVMAyzqWvI6f-DQ&s=19	Twitter
452	UNDP in Albania on EU4Schools: facts on the programme	21 September 2021	https://www.instagram.com/p/CUFys9bgIi0/?utm_medium=copy_link	Instagram
453	UNDP in Albania on EU4Schools: video on “Build Back Together” principle	24 September 2021	https://twitter.com/UNDPAlbania/status/1441358771268120576?t=8qOWXKFS0JwX1f6atyCD6g&s=19	Twitter
454	EU Ambassador to Albania on EU4Schools: retweet on the UNDP Albania’s video on “Build Back Together” principle	24 September 2021	https://twitter.com/LSorecaEU/status/1441374342651150338?t=mTh6gyD1xt3AZ2iJ-ZPBGA&s=19	Twitter
455	UNDP in Albania on EU4Schools: video on the partnership between EU & UNDP	24 September 2021	https://www.facebook.com/watch/?v=386147349847750	Facebook
456	UNDP in Albania on EU4Schools: video on “Build Back Together”	24 September 2021	https://www.instagram.com/tv/CUM9kVhIMtU/?utm_medium=copy_link	Instagram
457	Mayor of Kamza on EU4Schools: Meeting and conversation with students, teachers, parents and citizens after the reconstruction of "Dom Nikollë Kaçorri" 9-year school & kindergarten	24 September 2021	https://m.facebook.com/story.php?story_fbid=429074492097451 3&id=153971977985182	Facebook
458	EU in Albania on EU4Schools: Build Back Together and Build Back Better, EU is reconstructing 63 educational	24 September 2021	https://twitter.com/EUinAlbania/status/1441356747197882368?t=jt7jnFdTr2emBlNIggxszg&s=19	Twitter

No.	Description	Date	Link	Social Media
	institutions together with local communities and UNDP			
459	EUD in Albania on EU4Schools: Build Back Together and Build Back Better, EU is reconstructing 63 educational institutions together with local communities and UNDP	24 September 2021	https://m.facebook.com/story.php?story_fbid=4281247461945024&id=304579276278549	Facebook
460	EUD in Albania on EU4Schools: Build Back Together and Build Back Better, EU is reconstructing 63 educational institutions together with local communities and UNDP	24 September 2021	https://www.instagram.com/tv/CUNCqcwLYou/?utm_medium=copy_link	Instagram
461	Ambassador Soreca on EU4Schools: Building Back Together is a basic principle of the reconstruction work under EU4Schools programme	24 September 2021	https://twitter.com/LSorecaEU/status/1441374342651150338?t=y9-XJAc5iFWvxWE2SYoxcw&s=19	Twitter
462	EU in Albania on EU4Schools: video on the traveling exhibition of the #EU4Schools	26 September 2021	https://twitter.com/EUinAlbania/status/1442081518201966599?t=KFPWTBU2KxVgoRLf4IfSHw&s=19	Twitter
463	UNDP in Albania on EU4Schools: video on the partnership between EU & UNDP	26 September 2021	https://www.instagram.com/tv/CUSEtbLgeqV/?utm_medium=copy_link	Instagram
464	UNDP in Albania on EU4Schools: stories from beneficiaries of the programme	26 September 2021	https://www.facebook.com/watch/?v=449480889724813	Facebook
465	UNDP in Albania on EU4Schools: video on the partnership between EU & UNDP	26 September 2021	https://twitter.com/UNDPAlbania/status/1442082761263747075?t=wvZ1KBBPCwqfGT7V_nf4-g&s=19	Twitter
466	EUD in Albania on EU4Schools: video on traveling exhibition EU4Schools during Europe Weeks 2021	26 September 2021	https://m.facebook.com/story.php?story_fbid=4281262128610224&id=304579276278549	Facebook

No.	Description	Date	Link	Social Media
467	Ambassador Soreca on EU4Schools: Building Back Together, video from traveling exhibition during Europe Weeks 2021	26 September 2021	https://twitter.com/LSorecaEU/status/1442091901100851206?t=1IZff8LPmGTzdv2Oh1s7bA&s=19	Twitter
468	Mayor of Kurbin on EU4Schools: visit to "Demokracia" 9-year school, contemporary standards	27 September 2021	https://m.facebook.com/story.php?story_fbid=9340114205470 69&id=376016303013253	Facebook
469	Ambassasor Soreca on EU4Schools: President VDL will attend the inauguration of "Korb Muça" 9-year school & "Evropa" kindergarten in Qereke, Kruja	27 September 2021	https://twitter.com/LSorecaEU/status/1442483767784792069?t=5YubfZgGWb_bXqlICJTKxA&s=19	Twitter
470	UNDP in Albania on EU4Schools: inauguration of “Korb Muça” 9-year school & kindergarten. Presence of the President of European Commission Ursula Von Der Leyen, PM Edi Rama, D/PM Arben Ahmetaj, Minister of Sports & Youth Evis Kushi, UN Resident Coodinator Fiona McCluney, UNDP Permanent Representative Limya Eltayeb.	28 September 2021	https://www.instagram.com/p/CUXisDxoSzi/?utm_medium=copy_link	Instagram
471	UNDP in Albania on EU4Schools: inauguration of “Korb Muça” 9-year school & kindergarten. Presence of the President of European Commission Ursula von der Leyen, PM Edi Rama, D/PM Arben Ahmetaj, Minister of Sports & Youth Evis Kushi, UN Resident Coodinator Fiona McCluney, UNDP Permanent Representative Limya Eltayeb.	28 September 2021	https://www.facebook.com/302120716513378/posts/4517428128315928/	Facebook
472	Prime Minister Edi Rama on EU4Schools: Inauguration of “Korb Muça” 9-year school & kindergarten in	28 September 2021	https://www.facebook.com/ediramaal/videos/3031315000479713	Facebook

No.	Description	Date	Link	Social Media
	Qereke, Kruja. Participation of President of European Commission Ursula von der Leyen & other actors			
473	Prime Minister Edi Rama on EU4Schools: Inauguration of "Korb Muça" 9-year school & kindergarten in Qereke, Kruja. Participation of President of European Commission Ursula von der Leyen & other actors	28 September 2021	https://www.youtube.com/watch?v=6qBod9maVhU	Online Media
474	President VDL on EU4Schools: inauguration of "Korb Muça" 9-year school & kindergarten in Qereke, Kruja	28 September 2021	https://twitter.com/vonderleyen/status/1442796084426944520?t=gHT7jNtMq6Kk4UudCcEzaQ&s=19	Twitter
475	UNDP Eurasia on EU4Schools: facts about the newly reconstructed "Korb Muça" 9-year school & kindergarten in Qereke, Kruja	28 September 2021	https://twitter.com/UNDPEurasia/status/1442851415387512835?t=oTpD2OORsfWcYX_JVYrQ1g&s=19	Twitter
476	UNDP in Albania on EU4Schools: 160 children start the new academic year in the newly reconstructed "Korb Muça" 9-year school	28 September 2021	https://twitter.com/UNDPAlbania/status/1442900215812399107?t=cHKlqANoA0z3a-aMerTI6w&s=19	Twitter
477	EU in Albania on EU4Schools: retweet of President VDL for the newly reconstructed "Korb Muça" 9-year school & kindergarten	28 September 2021	https://twitter.com/EUinAlbania/status/1442800794630299652?t=0OdAtXhDSmQPYE1Fr8IHcA&s=19	Twitter
478	UNDP in Albania on EU4Schools: enthusiasm in Qereke village, Kruja. Inauguration of "Korb Muça" 9-year school & kindergarten. Presence of President VDL, PM Rama & other actors	28 September 2021	https://twitter.com/UNDPAlbania/status/1442847677411172362?t=lS9HuYBqZTTHryrTT9w7Dw&s=19	Twitter
479	EU Near on EU4Schools: visit of President VDL, inauguration of "Korb Muça" 9-year school & kindergarten in Qereke, Kruja.	28 September 2021	https://twitter.com/eu_near/status/1442833708881530880	Twitter

No.	Description	Date	Link	Social Media
480	Limya Eltayeb on EU4School: visit of President VDL, inauguration of “Korb Muça” 9-year school & kindergarten in Qereke, Kruja	28 September 2021	https://twitter.com/EltayebLimya/status/1442836478325927941?t=nFmqM-ArevqkYr6izJODyA&s=19	Twitter
481	UNDP in Albania on EU4Schools: 160 children in Qereke start the new academic year in brand new facilities	28 September 2021	https://www.al.undp.org/content/albania/en/home/presscenter/articles/2021/eu4schools-160-children-in-Qereke.html	UNDP Albania’s Website
482	UNDP Albania's Communication Manager Nora Kushti on EU4Schools: 15 educational facilities have welcomed children in the new academic year	28 September 2021	https://twitter.com/norakushti/status/1442933332938002434?t=ig85qliZKXT4sBLJIKYKPg&s=19	Twitter
483	Minister of Education and Sports on EU4Schools: Inauguration of "Korb Muça" 9-year school & "Evropa" kindergarten in Qereke, Kruja	28 September 2021	https://www.facebook.com/100057450729783/posts/327509752507380/	Facebook
484	Deputy Prime Minister on EU4Schools: Inauguration of "Korb Muça" 9-year school & "Evropa" kindergarten in Qereke, Kruja	28 September 2021	https://www.instagram.com/p/CUX09h9opn9/?utm_medium=copy_link	Instagram
485	Deputy Prime Minister on EU4Schools: Inauguration of "Korb Muça" 9-year school & "Evropa" kindergarten in Qereke, Kruja	28 September 2021	https://m.facebook.com/story.php?story_fbid=413140950176593&id=100044420739861	Facebook
486	Deputy Prime Minister on EU4Schools: Inauguration of "Korb Muça" 9-year school & kindergarten in Qereke, Kruja	28 September 2021	https://m.facebook.com/story.php?story_fbid=396529378732622&id=100044420739861	Facebook
487	EU Delegation in Albania on EU4Schools: pledged support of European Commission for the recovering of Albania after the earthquake, and reconstruction of	28 September 2021	https://m.facebook.com/story.php?story_fbid=2274640006073243&id=100064289365748	Facebook

No.	Description	Date	Link	Social Media
	"Korb Muça" 9-year school & "Evropa" kindergarten in Qereke, Kruja			
488	EU Near on EU4chools: on her visit to Albania, President of European Commission VDL inaugurated "Korb Muça" 9-year school & "Evropa" kindergarten	28 September 2021	https://twitter.com/eu_near/status/1442833708881530880?t=0L20F-33NC-LCkFAqZOxxA&s=19	Twitter
489	Ursula von der Leyen on EU4Schools: Glad to inaugurate Korb Muça" 9-year school & "Evropa" kindergarten	28 September 2021	https://twitter.com/vonderleyen/status/1442796084426944520?t=-_DMVYJDUmq92uRR7srb0A&s=19	Twitter
490	Online Media on EU4Schools: Visit of European Commission Ursula von der Leyen, Korb Muça" 9-year school & "Evropa" kindergarten inaugurated	28 September 2021	https://ata.gov.al/2021/09/28/perurohet-shkolla-dhe-kopshti-ne-qereke-von-der-leyen-simbol-i-miqesise-be-shqiperi/	Online Media
491	Online Media on EU4Schools: Visit of European Commission Ursula von der Leyen, Korb Muça" 9-year school & "Evropa" kindergarten inaugurated	28 September 2021	https://diasporashqiptare.al/2021/09/28/presidentja-e-ke-ne-shkollen-e-krujes-simbol-i-miqesise-mes-be-dhe-shqiperise/	Online Media
492	Online Media on EU4Schools: Visit of European Commission Ursula von der Leyen, Korb Muça" 9-year school & "Evropa" kindergarten inaugurated	28 September 2021	https://www.oranews.tv/vendi/peruron-shkollen-dhe-kopshtin-ne-kruje-presidentja-e-ke-se-pritet-me-lule--i1010496	Online Media
493	Online Media on EU4Schools: Visit of European Commission Ursula von der Leyen, Korb Muça" 9-year school & "Evropa" kindergarten inaugurated	28 September 2021	https://newsbomb.al/e-ndertuar-nga-fondet-e-be-ursula-von-der-leyen-peruron-shkollen-ne-fushe-kruje-ulet-mes-femijeve-ne-kopesht/	Online Media
494	Online Media on EU4Schools: Visit of European Commission Ursula von der Leyen, Korb Muça" 9-year school & "Evropa" kindergarten inaugurated	28 September 2021	https://opinion.al/von-der-leyen-mberrin-ne-krujeshkolla-simbol-miqesie-mes-be-e-shqiperise/	Online Media

No.	Description	Date	Link	Social Media
495	Online Media on EU4Schools: Visit of European Commission Ursula von der Leyen, Korb Muça" 9-year school & "Evropa" kindergarten inaugurated	28 September 2021	https://lexo.com.al/2021/09/ursula-von-der-leyen-ne-shqiperi-ulet-mes-femijeve-ne-nje-shkolle-ne-fushe-kruje/	Online Media
496	Online Media on EU4Schools: Visit of European Commission Ursula von der Leyen, Korb Muça" 9-year school & "Evropa" kindergarten inaugurated	28 September 2021	https://abcnews.al/ursula-von-der-leyen-ne-shqiperi-ulet-mes-femijeve-ne-nje-shkolle-ne-fushe-kruje/	Online Media
497	Online Media on EU4Schools: Visit of European Commission Ursula von der Leyen, Korb Muça" 9-year school & "Evropa" kindergarten inaugurated	28 September 2021	https://www.youtube.com/watch?v=SoCmimre0Eo	Online Media
498	Online Media on EU4Schools: Visit of European Commission Ursula von der Leyen, Korb Muça" 9-year school & "Evropa" kindergarten inaugurated	28 September 2021	https://www.vizionplus.tv/presidentja-e-ke-se-ne-fushe-kruje-ulet-mes-femijeve-ne-nje-shkolle/	Online Media
499	Online Media on EU4Schools: Visit of European Commission Ursula von der Leyen, Korb Muça" 9-year school & "Evropa" kindergarten inaugurated	28 September 2021	https://top-channel.tv/2021/09/28/presidentja-e-ke-ne-fushe-kruje-ulet-prane-femijeve-dhe-nxenesve-gjenka-e-mrekullueshme/	Online Media
500	Online Media on EU4Schools: Visit of European Commission Ursula von der Leyen, Korb Muça" 9-year school & "Evropa" kindergarten inaugurated	28 September 2021	https://www.youtube.com/watch?v=PE2mwwAYWWY	Online Media
501	EU in Albania on EU4Schools: President of European Commission VDL inaugurated yesterday "Korb Muça" 9-year school & "Evropa" kindergarten	29 September 2021	https://twitter.com/EUinAlbania/status/1443134236618276864?t=WcMWXVecJUUVx63emJ3d6A&s=19	Twitter
502	UNDP in Albania on EU4Schools: share of live video from PM Edi Rama. Inauguration process of “Korb Muça” 9-year school & kindergarten in Qereke, Kruja	29 September 2021	https://www.facebook.com/302120716513378/posts/4518895604835847/	Facebook

No.	Description	Date	Link	Social Media
503	UN Resident Coordinator in Albania on EU4Schools: inauguration of "Korb Muça" 9-year school & kindergarten in Qereke, Kruja	29 September 2021	https://twitter.com/FionaMcCluney/status/1443296793278693385?t=o0Sj6gpk4FYXmuwHJglJ6Q&s=19	Twitter
504	UNDP in Albania on EU4Schools: President of the European Commission Ursula von der Leyen inaugurates Evropa Kindergarten and Korb Muca School	29 September 2021	https://www.al.undp.org/content/albania/en/home/presscenter/pressreleases/-eu4schools--president-of-the-european-commission-ursula-von-der.html	UNDP Albania's website
505	Mayor of Kruja on EU4schools: Newly reconstructed "Korb Muça" 9-year school & "Evropa" kindergarten, a modern space for children like in Europe	30 September 2021	https://www.facebook.com/100044484217378/posts/405554707604000/	Facebook
506	Mayor of Kruja on EU4schools: Newly reconstructed "Korb Muça" 9-year school & "Evropa" kindergarten, a modern space for children like in Europe	30 September 2021	https://www.facebook.com/100044484217378/posts/405814207578050/	Facebook
OCTOBER 2021				
507	UNDP in Albania on EU4Schools: images & happy faces of children from different repaired/reconstructed educational facilities	1 October 2021	https://twitter.com/UNDPAlbania/status/1443907115865808913?t=fldq4lZ-baveJlsGpydPoA&s=19	Twitter
508	EUD in Albania on EU4Schools: hightlight of President VDL to Albania, inauguration of "Korb Muça" 9-year school & "Evropa" kindergarten in Qereke, Kruja	3 October 2021	https://www.instagram.com/reel/CUkujBbI2Er/?utm_medium=copy_link	Instagram
509	Mayor of Kavaja on EU4schools: visit to new "Fiqiri Kurti" school. Gratitude to EU & expression of responsibility to properly maintain the new facilities	5 October 2021	https://www.facebook.com/100058062699883/posts/276589780953110/	Facebook
510	UNDP in Albania on EU4Schools: facts on the programme	7 October 2021	https://twitter.com/UNDPAlbania/status/1446021223163514880?t=jbFA21LHTGHTbX8rWo5xvw&s=19	Twitter

No.	Description	Date	Link	Social Media
511	Mayor of Durrës on EU4Schools, public consultations for educational facilities to be repaired/reconstructed: "Eftali Koçi", "Bernardina Qerraxhia", "Olsi Lasko", Crèche Nr. 3	8 October 2021	https://www.facebook.com/100063824615403/posts/25207633359 6519/	Facebook
512	Mayor of Durrës on EU4Schools, public consultations for educational facilities to be repaired/reconstructed: "Eftali Koçi", "Bernardina Qerraxhia", "Olsi Lasko", Crèche Nr. 3	8 October 2021	https://www.instagram.com/p/CUxEA-YIHas/?utm_medium=copy_link	Instagram
513	Mayor of Durrës on EU4Schools: "Eftali Koçi" 9-year school & kindergarten will be reconstructed more modern for its 500 children	16 October 2021	https://www.instagram.com/p/CVFwARNogCb/?utm_medium=copy_link	Instagram
514	Mayor of Durrës on EU4Schools: "Eftali Koçi" 9-year school & kindergarten will be reconstructed more modern for its 500 children	16 October 2021	https://m.facebook.com/story.php?story_fbid=2577740696934 12&id=100063824615403	Facebook
515	Mayor of Kurbin on EU4Schools: visit in the new "Gjokë Elezi" 9-year school & kindergarten	18 October 2021	https://www.instagram.com/p/CVKm5F5A9ay/?utm_medium=copy_link	Instagram
516	Mayor of Kurbin on EU4Schools: visit in the new "Gjokë Elezi" 9-year school & kindergarten	18 October 2021	https://www.facebook.com/100063954780029/posts/261024932705998/	Facebook
517	Mayor of Kurbin on EU4Schools: visit in the first day of opening to the newly reconstructed "28 Nëntori" 9-year school & kindergarten in Fushë-Milot	19 October 2021	https://www.facebook.com/100063954780029/posts/261906152617876/	Facebook
518	Kamza Educational Directorate on EU4Schools: "Tahir Sinani", model educational facility like in the best schools & kindergartens in Europe	21 October 2021	https://www.facebook.com/577114826028426/posts/1151238455282724/	Facebook

No.	Description	Date	Link	Social Media
519	Mayor of Kurbin on EU4Schools: "Cub Çapani" 9-year school & kindergarte in Malbardhë, Kurbin, is reconstructed	21 October 2021	https://www.facebook.com/100063954780029/posts/263055772502914/	Facebook
520	Mayor of Kamza on EU4Schools: "Tahir Sinani", model educational facility like in the best schools & kindergartens in Europe	21 October 2021	https://www.facebook.com/100044332874482/posts/414450500042709/	Facebook
521	Kruja Educational Office Director on EU4Schools: Newly reconstructed "Sherif Dervishi" 9-year school & kindergarten welcomes its students	25 October 2021	https://m.facebook.com/story.php?story_fbid=10224489525299847&id=1658831251	Facebook
522	Minister of Education and Sports on EU4Schools: Opening session of "Europe is here" campaign, importance of partnership with EU	27 October 2021	https://www.facebook.com/100057450729783/posts/346339370624418/	Facebook
523	UNDP in Albania on EU4Schools: Public consultation process for “Emin Duraku” 9-year school in Tirana	28 October 2021	https://www.instagram.com/p/CVk9rMrNgvK/?utm_medium=copy_link	Instagram
524	UNDP in Albania on EU4Schools: Public consultation process for “Emin Duraku” 9-year school in Tirana	28 October 2021	https://www.facebook.com/302120716513378/posts/4610559795669427/	Facebook
525	UNDP in Albania on EU4Schools: Public consultation process for “Emin Duraku” 9-year school in Tirana	28 October 2021	https://twitter.com/UNDPAlbania/status/1453749999926484994?t=Z-p4I_H44XKUXfOWgaa40A&s=19	Twitter
526	Mayor of Kavaja on EU4Schools: EU friends continue being our main partners through EU4Schools programme	28 October 2021	https://m.facebook.com/story.php?story_fbid=2913487097477217&id=100058062699883	
527	Mayor of Durrës on EU4Schools: public consultion for schools "Naim Frashëri", "Gjergj Kastrioti", "Dhosi Liperi" and "Biza" kindergarten	29 October 2021	https://m.facebook.com/story.php?story_fbid=2665784921463038&id=100063824615403	

This project is funded by the European Union

REPUBLIKA E SHQIPËRISË
KËSHILLI I MINISTRAVE
MINISTËR SHTETI PËR RINDËRTIMIN

ANNEX 5 – PLANNED EU4SCHOOLS PROGRAMME ANNUAL WORK PLAN – YEAR 1

Activity	2020		2021										Implementing Body
	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	
Inception phase													UNDP
Activity 1.1: Technical assessment for education facilities and identification of the needs for infrastructure intervention.													UNDP, Municipalities
Activity 1.2: Contracting of companies for the preparation of detailed technical design (FEED) and supervision services for educational facilities to repair or reconstructed													UNDP
Activity 1.3: Contracting construction companies and implementation of the civil, mechanical and electrical works for repair and reconstruction													UNDP

Activity	2020		2021										Implementing Body
	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	
Activity 1.4: Testing and commissioning for repaired /reconstructed facilities													UNDP, Municipalities
Activity 1.5: Formal handover of repaired and reconstructed education facilities													UNDP, Municipalities
Activity 1.6: Final inspection of works at the end of defects notification period													UNDP
Activity 2.1: Preparation of technical specifications for furniture and equipment for repaired /reconstructed facilities													UNDP, Municipalities
Activity 2.2: Purchase and delivery of furniture and equipment for each repaired and reconstructed educational facility													UNDP
Activity 2.3: Conducting a training needs assessment of the teachers of primary and basic education in IT and digital													UNDP, Relevant authorities

Activity	2020		2021										Implementing Body
	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	
literacy to identify gaps and upgrading strategies													
Activity 2.4: Strengthen local capacities in Operations and Maintenance and health and safety in school environment													UNDP
Activity 3.1: Signature of Memorandum of Understanding (MoU) with municipalities and specific dialogue and interventions to ensure their full commitment during the Action implementation and at the end for the maintenance of the facilities													UNDP, Municipalities
Activity 3.2: Organisation of community led local consultations on the interventions													UNDP, Municipalities, Relevant authorities, Communities
Activity 3.3: Updating the online, publicly accessible BI (Business Intelligence)													UNDP, Municipalities

Activity	2020		2021										Implementing Body
	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	
dashboard available to all partners and the public through web technologies, for showing Action progress													
Activity 3.4: Communicate the results through visibility actions													UNDP

This project is funded by the European Union

REPUBLIKA E SHQIPËRISË
KËSHILLI I MINISTRAVE
MINISTËR SHTETI PËR RINDËRTIMIN

ANNEX 6 – UPDATED EU4SCHOOLS PROGRAMME ANNUAL WORK PLAN – YEAR 1

Activity	2020		2021										Implementing Body
	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	
Inception phase													UNDP
Activity 1.1: Technical assessment for education facilities and identification of the needs for infrastructure intervention.													UNDP, Municipalities
Activity 1.2: Contracting of companies for the preparation of detailed technical design (FEED) and supervision services for educational facilities to repair or reconstructed													UNDP
Activity 1.3: Contracting construction companies and implementation of the civil, mechanical and electrical works for repair and reconstruction													UNDP

Activity	2020		2021										Implementing Body
	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	
Activity 1.4: Testing and commissioning for repaired /reconstructed facilities													UNDP, Municipalities
Activity 1.5: Formal handover of repaired and reconstructed education facilities													UNDP, Municipalities
Activity 1.6: Final inspection of works at the end of defects notification period													UNDP
Activity 2.1: Preparation of technical specifications for furniture and equipment for repaired /reconstructed facilities													UNDP, Municipalities
Activity 2.2: Purchase and delivery of furniture and equipment for each repaired and reconstructed educational facility													UNDP
Activity 2.3: Conducting a training needs assessment of the teachers of primary and basic education in IT and digital													UNDP, Relevant authorities

Activity	2020		2021										Implementing Body
	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	
literacy to identify gaps and upgrading strategies													
Activity 2.4: Strengthen local capacities in Operations and Maintenance and health and safety in school environment													UNDP
Activity 3.1: Signature of Memorandum of Understanding (MoU) with municipalities and specific dialogue and interventions to ensure their full commitment during the Action implementation and at the end for the maintenance of the facilities													UNDP, Municipalities
Activity 3.2: Organisation of community led local consultations on the interventions													UNDP, Municipalities, Relevant authorities, Communities
Activity 3.3: Updating the online, publicly accessible BI (Business Intelligence)													UNDP, Municipalities

Activity	2020		2021										Implementing Body
	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	
dashboard available to all partners and the public through web technologies, for showing Action progress													
Activity 3.4: Communicate the results through visibility actions													UNDP

This project is funded by the European Union

REPUBLIKA E SHQIPËRISË
KËSHILLI I MINISTRAVE
MINISTËR SHTETI PËR RINDËRTIMIN

ANNEX 7 – BUDGET OF THE PROGRAMME

Budget Phase 2

3. Expected sources of funding & summary of estimated costs

		Amount EUR	Percentage %
Expected sources of funding			
EU contribution sought in this application **(A)**		60,000,000.00	98.93%
Other contributions (Applicant, other Donors etc)			
Name	*Conditions*		
UNDP Albania		650,000.00	1.07%
Estimated Costs			
Estimated TOTAL ELIGIBLE COSTS **(B)**		60,650,000.00	
EU contribution expressed as a percentage of total eligible costs **(A/B x 100)**			98.93%

Please refer to *EU4S Annual Financial Report + Notification Letter.pdf* document.

ANNEX 8 – TECHNICAL ASSURANCE GROUP TERMS OF REFERENCE

1. *Background*

"EU4Schools" Programme is an initiative funded by the European Union in response to the earthquake of 26 November 2019. It aims to improve Albania's education sector by repairing and reconstructing educational facilities in municipalities affected by the earthquake. It is part of the European Union's financial package to support Albanian citizens during the donor conference organized in Brussels on 17 February 2020. The Programme will be implemented by UNDP Albania in collaboration with Albanian government.

The overall objective of this Programme is to further support local and national governments in reducing social and economic losses, and to accelerate the recovery process through educational facility repairs and reconstruction. The specific objectives are:

i. To support repairing and rebuilding, including the basic furnishing and equipping of education facilities in municipalities affected by the earthquake according to the EU standards;
ii. To provide increased transparency, accountability and inclusiveness to the recovery process; and
iii. To improve capacities of central and local governments in accelerating the recovery processes according to the highest international standards.

It will target more than 60 educational facilities, including creches, pre-schools, primary education, secondary schools – including VET schools and respective dormitories in municipalities affected by the earthquake, such as: (i) Lezha, (ii) Tirana, (iii) Rrogozhina, (iv) Mirdita (v) Vora, (vi) Shijak, (vii) Durresi, (viii) Kruja, (ix) Kurbini, (x) Kamza and (xi) Kavaja.

The Programme will ensure that the recovery process does not recreate the vulnerability that led to the disaster in the first place and must leave the communities safer by reducing risks and building resilience. Therefore, a Build Back Better (BBB) approach will be taken for the repairing and reconstruction. The recovery within a BBB framework would give the impacted communities the chance to reduce risk from the immediate hazard and provide an opportunity to reduce the future risk sustainably. BBB offers the opportunity to rebuild stronger, safer, more disaster-resilient infrastructure and systems and with higher standards.

EU4Schools programme will adopt the most-up-to-date BBB approaches. At the same time, institutional and regulatory frameworks that promote resilient reconstruction will be established, including codification of multi-hazard risk reduction aligned with the Eurocodes, improved construction quality control, assurance that settlement designs pursue concepts of liability and infrastructure resilience. To ensure sustainability, the reconstruction process will support broader urban development goals, including the

promotion of transformative urban development that is modern, green, energy-efficient, low-carbon, and community-friendly.

To move fast and assist affected communities, the recovery interventions will strengthen resilience, build capacity and social capital, and reduce future disasters' risks and effects. In addition to the "build back better" approach, the intervention will apply a "build back together" approach within each locality, working together with local governments, local public institutions, and communities to design and implement recovery activities rapidly with a participatory approach a transparent and accountable system.

Education facilities staff, students, and parents will be valuable sources of information to guide the new facilities' Design. The education facilities' external environment, entrances, internal circulation, evacuation, other facilities, and classrooms will be given attention when designing for accessibility. The Programme will make all efforts to consider the unique requirements of the various groups of persons with disabilities. Inclusion of communities, including teacher staff, students, parents, local authorities, etc..., will be considered during all the Programme phases. It is crucial to ensure that all stakeholders are involved, and their needs will be addressed.

2. Management arrangement

The "EU4Schools" Programme is managed as a sole integrated programme by the same consolidated institutional structures which include: (i) Steering Committee, (ii) Technical Assurance Group and (iii) Programme Team, interacting in a broader programme context with partners and all interested stakeholders.

The Programme Steering Committee (PSC) oversees and coordinates the operations of Programme interventions. Based on the programme's initial plan and budget as well as on monitoring data, the PSC oversees the programme's implementation and takes all the necessary strategic decisions. The Steering Committee is composed of representatives from the European Union Delegation to Albania, as the Donor, UNDP, as the Implementing Agency, a representative of the Ministry of State for Reconstruction, representative from the Ministry of Education Sports and Youth, UN Resident Coordinator and one representative from each of beneficiary municipalities. It is co-chaired by representative of EU Delegation to Albania and UNDP representative.

In a technical level, an ad hoc structure such as Joint technical team is established, including representatives from EU Delegation to Albania, UNDP, Ministry of State for Reconstruction and Ministry of Education Sports and Youth. It gathers once a month and aims to discuss technical issues, based on PSG guidance.

EU4Schools team is composed by 23 staff of different specialties, including management, procurement, engineers, monitoring/reporting and data management, community coordinators, contract management, financial and administrative support, and communication person.



To support the "EU4Schools" team, by assuring that works performed by contractors for preparation of technical designs, civil works and supervisions are done properly and in line with standards, the Technical Assurance Group will be established.

3. Technical Assurance Group (TAG)- responsibilities and composition

The Technical Assurance Group will assist the "EU4Schools" team whenever significant changes related to the intervention measures will be needed. Its members are expected to act in an advisory role to the "EU4Schools" team and commit sufficient time to promote and oversee the "EU4Schools" Programme.

TAG will focus on achieving the following objectives:

- Use an inclusive and transparency approach based on build back together and build back better principles during all life cycle of the Programme.
- Promote and support effective partnership between stakeholders.
- Identify problems quickly and address them appropriately.
- Promote principles such as: transparency, human rights, environmental protection, health and safety throughout the life cycle of the Programme.

3.1 Responsibilities

Main responsibilities include but are not limited to:

- Review the technical aspects of the programme from the design preparation, permitting, construction and defects liability period until the complete handover of the facility to the beneficiary, including reviewing all project development milestones and proposals for project construction, and making recommendations for consideration
- Participate in the process of technical review of the educational facilities designs and advise as relevant.
- Engage in periodic consideration of technical issues, challenges and risks and advise on appropriate solutions and risk mitigations

3.2 Composition

TAG will be composed by following members[‡]:

- Representatives of the Programme Team
- Representative from the Ministry of Education Sports and Youth and/or educational regional offices
- Representative from the Institute of Construction
- Technical staff from each of the beneficiary municipalities
- Different consultants based on the expertise required

[‡] Each institution may propose more than one expert as a backup to ensure the presence.



4. Meeting procedures

Frequency of Meetings: For individual or group of projects prepared, divided as per the respective affected municipalities based on the programme timeline.

Format: In person, by teleconference or by videoconference.

Location: At the relevant municipality or EU4School programme premises

Agenda: Developed by "EU4Schools" team in consultation with the group members.

Secretariat support: Provided by the "EU4Schools" team, including meeting coordination, preparation and distribution of materials and drafting meeting minutes.

5. Minutes of the meeting

Minutes of the meeting including follow up actions of different programme partners will be prepared and shared with all members within a week from the meeting date.
