DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

United Nations Development Programme

PROJECT DOCUMENT

[Afghanistan]

Project Title: **Area Based Approach to Development Emergency Initiatives (ABADEI 2.0)**
Project Number:
Implementing Partner: UNDP Afghanistan
Start Date: 01 April 2023 **End Date:** 31 December, 2025.
LPAC Meeting date: 13th February 2023

Brief Description

The post-15 August 2021 power shift in Afghanistan resulted in severe political and social-economic instability in a climate of heightened uncertainty. The country faced challenges on multiple fronts, including COVID-19, poverty, food insecurity, droughts, energy crisis and micro- and macro-economic impacts. In response, UNDP launched the Area Based Approach for Emergency Initiatives (ABADEI), establishing eight regional offices to support the re-establishment of basic essential services and economic recovery.

For the period 2023-2025, UNDP will continue to deliver critical economic and community resilience interventions through the implementation of ABADEI Phase Two, building upon established capacities, know-how and lessons learned. ABADEI Phase II Outputs include a). The Provision of Essential Services; b). Strengthening Community Livelihoods and Local Economic Activities; c). Strengthening Resilience to Climate and Disaster Risks and d). The Promotion of Community Ownership, Engagement and Social Cohesion.

The project will partner with Community-based Organizations (CBOs), Non-Governmental Organizations (NGOs), Civil Society Organizations (CSOs), other social structures, the private sector, UN Agencies (UNAs) and other relevant stakeholders to strengthen and expand existing results and reach. The key goal of the project is to contribute towards generating two million (2,000,000) employment and income generating opportunities for Afghans over the course of three years, restoring local economies, livelihoods and essential services, while significantly impacting community and climate resilience, well-being and social inclusion/cohesion.

Contributing Outcome (UNSF)

- **UNSF Outcome 1:** By the end of 2025, more people in Afghanistan, particularly the most marginalized, can equitably access essential services that meet minimum quality standards.
- **UNSF Outcome 2:** By the end of 2025, more people in Afghanistan will benefit from an increasingly inclusive economy, with greater equality of economic opportunities, jobs, and more resilient livelihoods, increased food production, and improved natural resources management.
- **UNSF Outcome 3:** By the end of 2025, more people in Afghanistan can participate in an increasingly socially cohesive, gender equal, and inclusive society, where the rule of law and human rights are progressively upheld, and more people can participate in governance and decision-making.

Total resources required:		**US$ 401,300,000**
Total resources allocated:		
	Japan (Japan Supplementary Budget (2020, and 2022)	US$ 64,962,962[1]
	EU	US$ 5,300,000
	STFA-MPTFO	US$ 9,900,000
	UNDP Funding Windows – Fund 26800 (2023)	US$ 2,500,000
	UNDP TRAC-2 (2023)	US$ 5,483,000
	Resources to be allocated (hard pipeline)	US$ 27,300,000
Total Allocated Resources		**US$ 115,445,962**
Unfunded:		**US$ 285,854,038**

Agreed by :

Mr. Abdallah Al Dardari
Resident Representative
DocuSigned by:
9BC324BC8E9449F...
13-Mar-2023

[1] USD7,962,962 from JSB 2022 is earmarked for 2024

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

DEVELOPMENT CHALLENGE

In 2019, Afghanistan ranked 170th out of 189 countries on the Human Development Index which was already in the bottom 20[2]. However, the post-15 August 2021 power shift in Afghanistan resulted in severe political and social-economic instability in a climate of heightened uncertainty. The country faced challenges on multiple fronts, including COVID-19, poverty, food insecurity, droughts, energy crisis and micro- and macroeconomic impacts. UNDP's analysis showed that these factors could drive the country to near universal poverty, with people falling below the poverty line projected to be over 95-97 percent by mid-2022. The UN Strategic Framework (UNSF 2022) also "estimated that a record 28.3 million people" would be in dire need of humanitarian and protection assistance during 2023, "an increase from 24.4 million in 2022 and 18.4 million in 2021" The cessation of development aid inflows and the recent poor harvest suggest that the Afghan economy will not experience a rapid economic recovery by 2023. (EU financial intelligence). According to the World Bank, "limited educational opportunities for girls and barriers to completing 12 years of education cost countries between $15 trillion and $30 trillion in lost lifetime productivity and earnings." Overall revenue collection reached AFN135.9 billion (US$ 1.54 billion) between March 22, 2022, and December 21, 2022, in line with 2020 results. Afghanistan continued to rely relatively heavily on revenue collected at the border — as opposed to inland revenue collection. (World Bank Economic Monitor, Jan 2023) UNDP analysis also anticipated that over half a million people had already been displaced by conflict[3] and thousands more were affected by natural disasters. Nearly 19 million Afghans, or 45 percent of the population, were food insecure,[4] with a larger number and proportion amongst rural populations. That number was expected to rapidly rise to 22.8 million during the winter season (November-March)[5].

Essential services in health, water, education, sanitation, energy, road and other critical infrastructure maintenance also became severely disrupted. Trash and garbage were no longer disposed of by waste management companies, and unattended waste accumulated presenting health hazards and often blocking drainage canals creating flooding hazards. Clean water became in short supply and health facilities suddenly lacked adequate electricity to maintain minimum lighting and for cold chain storage of medicines and supplies. Power and energy (including renewable) companies stopped generating enough power to meet minimal demand, resulting in frequent power outages.

Drought, high food prices and the economic collapse contributed to the decline in available food. Farmers faced shortages of critical inputs, and both cereal and grains that would normally be set aside as seed for the next planting season are being consumed, while breeding livestock are being slaughtered for sale and consumption. In September 2022, despite the high levels of humanitarian assistance targeting 38 percent of the population, OCHA (United Nations Office for the Coordination of Humanitarian Affairs) estimated that 84 percent of Afghan households were experiencing moderate to severe food insecurity and lacked consistent access to food. Food insecurity is now widespread, with high rates of malnutrition reported in all regions.

[2] Human Development Report, UNDP 2019

[3] OCHA Afghanistan weekly humanitarian update (16-21 August 2021)

[4] According to the Integrated Food Security Phase Classification (IPC) report, co-led by the Food and Agriculture Organization and the UN World Food Programme

[5] See: www.afghan-analysts.org

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

The January 2022 UN Secretary-General Report to the Security Council and General Assembly stated that half of all Afghan children under five are facing acute malnutrition. UNICEF estimated that 1,100,000 Afghan children suffer from severe acute malnutrition. Areas with high concentrations of Internally Displaced persons (IDPs), or where returnees have neither found employment nor successfully reintegrated into their communities of origin, are among the hardest hit by food insecurity.

Core government functions and essential service providers have also collapsed. The discontinuation of development funds and programmes has led to significant gaps in service provision, salaries of government staff and replenishment of essential equipment and supplies. Some banks' branches have closed, and others that remain in operation have limited capital, with high incidences of non-performing loans. Consequentially, access for Medium, Small and Micro Enterprises (MSMEs) to much needed finance is greatly reduced. With commerce and trade constrained, previously healthy private sector companies have laid off employees and are becoming increasingly dependent on grant assistance from donor sources.

The political instability, economic volatility and the collapse of basic essential services, compounded by the uncertainty over continued international aid and the severe disruption in financial and banking services, have meant that the risks faced by the Afghan population are acute and urgent. Without rapid and sustained support to re-establish these systems, Afghanistan will face a humanitarian catastrophe and the total collapse of its economy.

Within this overall socio-economic context, the Global Gender Gap Index (GGGI) rank for Afghanistan was 156 out of 156,[6] the Women, Peace and Security Index score in 2021 was 170 out of 170 countries,[7] and overall, Gender Development Index in 2019: 166 out of 167 countries.[8] Following the August 2021 strategy, women have no space for political participation, with very limited space in civic engagements, along with multiple bans on women's mobility and their rights to work with international INGOs and NGOs and their rights to pursue study after sixth-grade education. Half of the population in Afghanistan are women, and the lack of enabling conditions for women to meet basic human needs and participate in community resilience and socioeconomic recovery clearly poses a threat to the country's stability. In every area of accessing services, women are discriminated against and have normalized both by the decree of DfA and by the community norms in the name of culture.

Although there is a lack of data after powershift, however looking at the situation before August 2021, it is palpable that women's access to finance has been deteriorated. Only two percent of firms take out loans[9], and nearly 85 percent of adults in Afghanistan are unbanked and do not own an account in any financial institution;[10] those who had accounts, among them only seven percent were Afghan women compared with 23 percent for Afghan men.[11] It was estimated in 2020 that the unmet demand for financing from micro, small

[6] World Economic Forum, 2021

[7] Gender Alert 1, UNWomen 2022

[8] Gender Alert 1, UNWomen 2022

9 IFC Supports Afghan Women's Access to Financial and Non-Financial Services, 2020. IFC Supports Afghan Women's Access to Financial and Non-Financial Services - The Khaama Press News Agency

10 https://blogs.worldbank.org/endpovertyinsouthasia/pathway-financial-inclusion-afghanistan/?cid=SHR_BlogSiteTweetable_EN_EXT via @worldbank

11 https://blogs.worldbank.org/endpovertyinsouthasia/pathway-financial-inclusion-afghanistan/?cid=SHR_BlogSiteTweetable_EN_EXT via @worldbank

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

and medium-sized enterprises (MSMEs) in Afghanistan is about $4.7 billion, which included $113.5 million in unmet demand from women-owned enterprises.[12]

With the current situation in the private sector following the powershift, it has also been aggravated, which can be understood by looking at the fact how women-led SMEs are closing their operations, such as 42 percent of women-owned small businesses had closed, compared with 26 percent closure of firms owned by men[13]. Women employees in surveyed businesses faced more severe job losses than men employees – overall, three-quarters of women workers were laid off from surveyed firms since August 2021.[14]

The changed context has affected women and girls in a disproportionately negative manner, especially manifested in the restrictions imposed on female mobility, opportunities to work and access to secondary and higher education, the dissolution of the state institutions that facilitated women's representation in social and political affairs, and the blockage of avenues for women to seek legal justice.

A World Bank survey reported that 42 percent of women-owned businesses had closed, compared with 26 percent closure of firms owned by men. A 2020 ILO report stated that 53 percent of women with jobs were employed in agriculture, 24 percent in the manufacturing sector, and 18 percent in public administration and social services. These last two employment areas being now restricted, have seen women's employment plummet or virtually disappear. Consumer spending on a rising food basket, as well as export markets drying up, placed in jeopardy women's ability to remain employed by producing carpets, embroideries, and other non-essential handicrafts from their homes.

In addition, inputs needed for Afghan women-owned/led businesses have become more expensive, scarce, and difficult to obtain due to supplier closures, supply chain disruptions, and border restrictions. Despite international pressure, education beyond primary levels was discontinued for girls and young women. Currently, 80 percent of school-aged Afghan girls and young women – 2.5 million people are out of school.[15] Until late December 2022, some Afghan women were allowed to attend university; however, on 20 December 2022, university education for women was suspended until further notice, affecting over 100,000 women students attending government and private higher education institutions.[16] . The ongoing crisis has had a detrimental impact on young women in higher education as well, with a 60 per cent decline in enrollment recorded. [17] On 24 December 2022, the DfA prohibited Afghan women from working for national and international NGOs.[18]Despite international pressure, education beyond primary levels was discontinued for girls and young women.

Data from 2018 indicates that there has been a progressive change in TVET both in terms of volume and quality over the years, such as the number of students in formal TVET has grown significantly from 1,510 in

12 https://blogs.worldbank.org/endpovertyinsouthasia/pathway-financial-inclusion-afghanistan/?cid=SHR_BlogSiteTweetable_EN_EXT via @worldbank

[13] *World Bank Survey: Afghanistan's Private Sector Hit Hard by Political Crisis*

[14] *World Bank Survey: Afghanistan's Private Sector Hit Hard by Political Crisis*

[15] Let girls and women in Afghanistan learn! | UNESCO

[16] Let girls and women in Afghanistan learn! | UNESCO

[17] UNESCO, June 2022: Afghanistan | Agriculture & Rural Development | World Bank Development Indicators (tradingeconomics.com)

[18] UNESCO, June 2022: Afghanistan | Agriculture & Rural Development | World Bank Development Indicators (tradingeconomics.com)

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

2002 to 61,663 in 2018, as well as the number of TVET instructors increased from 550 in 2002 to 3,824 in 2018. Since 23 March 2022, 1.1 million secondary school girls and young women have been prevented from attending school until further notice. Currently, 80 percent of school-aged Afghan girls and young women – 2.5 million people, are out of school. On 20 December 2022, university education for women was suspended until further notice, affecting over 100,000 women students from attending government and private higher education institutions, and on 24 December 2022, the DFA banned women from working for national and international NGOs. The ongoing crisis has had a detrimental impact on young women in higher education as well, with a 60 percent decline in enrolment having been recorded. Since August 2021, UNESCO has shifted its interventions to ensure continuity of education through community-based literacy and skills development classes for over 25,000 youth and adults, including 60 per cent of women and adolescent girls in 20 provinces. The unfair participation of women in the labour force and rigid restriction on women's freedom of mobility indicates the low participation of women in TVET and skill development. With the current attitude of DFA towards women and girls, it is easy to assume the situation of women in formal TVET and tertiary education is not feasible. However, non-formal and informal TVETs are feasible for women and girls.

Impact of the crisis on GDP

Gross Domestic Product (GDP) grew by 3.9 percent in 2019, declined by 1.9 percent in 2020, and before the August 15 power shift, the previous Government had forecast a four percent growth for 2021. UNDP's analysis estimates that for the next fiscal year (June 2021-2022), GDP growth will be lower by 3.6 - 13.2 percentage points than the four percent growth predicted[19]. Based on a preliminary analysis by UNDP modelling team, an annual loss of two percent GDP due to the freeze of electricity project, and five percent GDP loss due to the freeze of all kinds of infrastructure projects or 2022-25 is estimated. In August 2022, UNICEF reported that depriving girls of secondary education resulted in a loss of at least US$500 million for the Afghan economy in the last 12 months, and if the current cohort of three million girls were able to complete their secondary education and participate in the job market, girls and women would contribute at least US$5.4 billion to Afghanistan's economy.[20] According to the World Bank, the Taliban regime has collected 144 billion144 billion Afghani ($1.64 billion) in revenues. Inflation stood at 11 percent by November 2022, as per the figures shared by the World Bank. The bank predicted that Afghanistan's real GDP would further contract through the end of 2022.[21]

Impact of the crisis on the Sustainable Development Goals (SDGs)

The current crisis will have a negative impact on Afghanistan's path toward achieving Agenda 2030[22]. Overall poverty impact estimates range between an increase of 7-25 percentage points from a baseline poverty rate of 72 percent in 2020 (SDG-1). This, in turn, implies a deterioration in food security (SDG- 2) by between 4

[19] UNDP (2021). Rapid Appraisal of Economic Instability & Uncertainty in Afghanistan

[20] UNICEF, August 2022, 'Cost of Inaction: Girls Education in Afghanistan', https://reliefweb.int/report/afghanistan/cost-inaction-girls-education-afghanistan-executive-summary

[21] https://thediplomat.com/2023/01/afghanistans-uncertain-economic-future-as-the-new-year-dawns/

[22] Linking the GDP changes estimated using the Afghanistan General Trade TAP (Turkmenistan Afghanistan Pakistan) Computable General Equilibrium (CGE) model to near-term SDG indicators points to a deterioration in progress towards the agenda 2030.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

and 19 percentage points; and in health and well-being (SDG-3) by between 6 and 21 points compared to their levels in 2020 (considering the COVID-19 impact). Also, the crisis has aggravated the energy access issues affecting SDG 7.

These projected estimates vary in terms of the intensity of the domestic instability and disruption to international trade. In turn, these affect the supply of basic goods such as food and public services such as health care. All scenarios show a markedly negative impact on all SDGs, including SDG-10 (inequality), gender equality and women's empowerment (SDG 5) with the exception of SDG-12 (sustainable consumption and production), given lower economic activity translating into less environmental pollution.

STRATEGY

A. BACKGROUND

The Area-Based Approach to Development Emergency Initiatives (ABADEI) Strategy has been designed as a response to the ongoing crisis in Afghanistan upon a call of the UN Executive Committee Working Group for Afghanistan.

The ABADEI Strategy is a tailored area-based integrated programming approach to support basic human needs, complementing short-term humanitarian life-saving assistance with safeguarding livelihoods and strengthening community resilience. It is centered around addressing worsening poverty and vulnerability, supporting community resilience and social cohesion, and enabling the rehabilitation of small-scale infrastructure vital for basic human needs. It supports the creation of immediate sources of income through cash-for-work (CfW), cash- for- market (CfM), small businesses and livelihood opportunities with a particular focus on agri-business and regenerative agriculture infrastructure and services (critical for food security) that are under threat. It is sensitive to the chronic and newly emerging vulnerabilities and marginalisation of Afghan women and girls and aims at providing them assistance in a manner that does not exacerbate their susceptibility to violence and deprivation of opportunities and rights.

The ABADEI Strategy is grounded in partnerships in order to maximize synergies and capitalize on existing capacities at the local level. It draws inspiration from the One-UN concept by combining resources, experience and the collective knowledge of UN agencies and development partners. ABADEI interventions will complement the Humanitarian Response Plan (HRP) and seek to address, through a resilience- building approach, key humanitarian concerns such as food insecurity, emergency needs for essential goods and services, and the effects of displacement on IDPs, hosts and refugee returnees.

The value proposition of Area Based Programming (ABP), which forms the core of context-sensitive needs-based targeting of the ABADEI Strategy, lies in its contribution to preserving human, social, cultural and institutional capital in a context of multi–dimensional crisis. It recognizes that while life-saving humanitarian assistance is essential to address urgent needs, it must be simultaneously accompanied by measures to reduce further displacement and the rapid rise of the humanitarian caseload. The distinguishing feature of the area-based approach is that it is an integrated response that addresses multiple vulnerabilities simultaneously to avoid the socio-economic collapse of the country, in a context of severe instability.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

In the volatile circumstances of crisis, the political, security and operational risks of delivering assistance in Afghanistan will remain substantial. The ABADEI Strategy is therefore grounded in a thorough risk analysis, informed by the UN's work on the ground, that includes a review of socio-economic and conflict trends and identifies likely scenarios for the next 36 months. No analysis can eliminate risk, but this will help the UN to design its work in a risk-informed way and mitigate the risks of delivering assistance in this unpredictable context.

The Project will mainstream gender by applying three approaches, such as (i) facilitate women's improved access to essential services and opportunities for community-based economic activities and skill development, as well as strengthen community resilience and social cohesion within all interventions as feasible; (ii) targeted interventions for women and girls that enable strengthening women's agency, voice, participation, and support to alter the existing social relationship where women are in a weaker position and mitigate the risk of GBV through regular safety planning, (iii) Continuous advocacy efforts will be made at the community and different community formal and informal institutions and platforms through all programme outputs of ABADEI, as well as capitalizing social cohesion pillar. The Project will support community leaders to include diversity, inclusivity, equity, non-discrimination and equality principles in local activity planning, implementation, dispute resolution, and resource management. The Project will also dedicate activities to increase the use of gender-disaggregated data, gender analysis and access and to mainstream gender equality and empowerment into the procedures and processes for the design, selection, and implementation monitoring of community interventions.

The Project has gender-specific results and activities such as support to women MSMEs, women's access to health, energy, and community-based-vocational training and increased opportunities for women, girls and survivors and at-risk women to participate actively in alternative livelihoods or income generation activities supported with cash-based interventions (CBIs). The gender-specific results will be measured with both qualitative and quantitative analysis. Sex-disaggregated data of the resulting framework will provide a basis to assess the gender results with regard to the changes at the level of women's Agency and voices, changed relational dynamics, and changes in the structures, especially norms and social institutions.

Against the above background, ABADEI expects to achieve three main UNSF outcomes through the implementation of four outputs, and subsequent 18 activities/interventions in eight (8) targeted geographic locations that enable the provision of immediate support and long-term development through the ABADEI integrated package: All the above programme strategies and approaches will support ABADEI 2.0, contributing towards UNDP's two strategic outcomes –(Outcome 2 and 3) , as well as all five signature solutions, presented below:

ABADEI 2.0 Outputs	**UNDP's Strategic Frameworks (2022-2025)**
Output 1: Essential services improved in the area of infrastructure, agriculture, health, education and energy	Outcome 3: Resilience built to respond to systemic uncertainty and risk

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

	Signature Solution 3: Energy : Increasing energy access for those furthest behind and accelerating the transition to renewable energy. *Signature Solution 4:* Environment : Putting nature and the environment at the heart of the natural economies and planning: helping governments protect, manage and value their natural assets.
Output 2: Local economies improved through gender-responsive community -based livelihoods	Outcome 3: Resilience built to respond to systemic uncertainty and risk *Developmental Outputs: SS 3 and 6* Signature Solution 2 Gender Equality : Confronting the structural obstacles to gender equality and strengthening women's economic empowerment and leadership. Signature Solution 5: Resilience : Supporting countries and communities in building resilience to diverse shocks and crises. Including conflict, climate change, disasters, and epidemics.
Output 3: Local communities' resilience capacity enhanced to better respond and adapt to the disaster and climate- induced risks	Outcome 3: Resilience built to respond to systemic uncertainty and risk. *Signature Solution 4:* Environment : Putting nature and the environment at the heart of the natural economies and planning: helping governments protect, manage and value their natural assets. Signature Solution 5: Resilience : Supporting countries and communities in building resilience to diverse shocks and crises. Including conflict, climate change, disasters, and epidemics.
Output 4: Communities' capacity, ownership, engagement improved for better social cohesion and access to justice (especially for those who are systematically discriminated against, such as women, girls, ethnic and persons with disabilities).	Outcome 2: No one left behind, centering on equitable access to opportunities and a rights-based approach to human agency and human development. *Signature Solution 2* Gender Equality : Confronting the structural obstacles to gender equality and strengthening women's economic empowerment and leadership. *Signature Solution 3:* Resilience : Supporting countries and communities in building resilience to diverse shocks and crises. Including conflict, climate change, disasters, and epidemic *Signature Solution* 6: Governance : Helping countries address emerging complexities by "future-proofing" governance systems through anticipatory approaches and better management of risk. (in the context

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

	of Afghanistan, governance means community governance such as CDC and other community structurers)

To the UN Strategic Framework (UNSF) across all three outcomes:

UNSF Outcomes	Contributing ABADEI 2.0 Outcomes
Outcomes 1: By the end of 2025, more people in Afghanistan particularly the most marginalized, will be able to equitably, particularly the most marginalized, will be able to equitably access essential services that meet minimum quality standards.	Outputs 1, 2, 3 (e.g Essential food security)
Outcome 2: By the end of 2025, more people in Afghanistan will benefit from an increasingly stable, inclusive and employment rich economy, with greater equality of economic opportunities and more resilient livelihoods.	Output 2
Outcome 3: By the end of 2025, more people in Afghanistan will be able to participate in an increasingly socially cohesive, gender equal, and inclusive society, where the rule of law and human rights are progressively upheld, and more people can participate in governance and decision-making.	Output 2 and 4

Output 1: Essential services improved in the area of infrastructure, agriculture, health, education and energy.

Activity results-1.1: Essential physical critical infrastructure constructed, rehabilitated, repaired, equipped and maintained, including infrastructure for water management, shelter, WASH, transportation, agriculture, health, education, basic services etc.
Activity results -**1.2:** Provision of improved essential health services (including women and girls accessing health care).
Activity results -1.3: Provision of essential education services (including gender- integrated TVET).
Activity results-1.4: Provision of clean/ renewable/ alternate energy services, technologies and applications supported and sustained.

Output 2: Local economies improved through gender-responsive community -based livelihoods.
Activity results -**2.1:** Households (women led and people with disabilities) in high poverty and high insecurity areas provided with Unconditional Cash Transfer (UCT) / Temporary Basic Income (TBI).
Activity results -**2.2**: Local-level livelihoods and economies sustained through Cash- for -Work (CfW) including women and girls, vulnerable groups accessing CFW).
Activity results -2.3: Local private sector development sustained through technical, and financial support to informal and formal businesses, including assisting micro, small and medium-sized enterprises (MSMEs) to

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

access and/or expand to new market areas, support to local traders, to women-led businesses and community- led social enterprises (Cash- for- Markets- CfM).

Activity results -**2.4:** Cross-border trade and access to market supported (including women-led-businesses).
Activity results -2.5: Access to finance, and Digital Solutions supported and sustained.

Output 3: Local communities' resilience capacity enhanced to better respond and adapt to disaster and climate-induced risks.

Activity results 3.1- Essential food security and regenerative agriculture infrastructure, inputs and services supported.
Activity results -3.2: Community preparedness for disasters improved.
Activity results -3.3 Water security and access enhanced through climate-smart systems (e.g., solar- based irrigation, water pumping, energy efficiency).
Activity results -**3.4** Natural ecosystem restoration and management supported.


Output 4: Communities' capacity, ownership, engagement improved for better social cohesion and access to justice (especially for those who are systematically discriminated against, such as women, girls, ethnic and persons with disabilities).

Activity results-4.1: Communities for peace, well-being, civic engagement, and social cohesion promoted.
Activity results 4.2: Gender equality and women's empowerment (GEWE) programme and protection services for women and girls integrated and implemented in ABADEI.
Activity results 4.3: Rights-based access to justice, including gender justice, human rights, and human security, fostered.
Activity results 4.4: Community-led local recovery, and social cohesion and resilience programmes supported.
Activity results 4.5: Territorial development plans for eight regions in Afghanistan designed and developed.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

B. THEORY OF CHANGE (TOC)

The ABADEI Strategy theory of change indicates that:

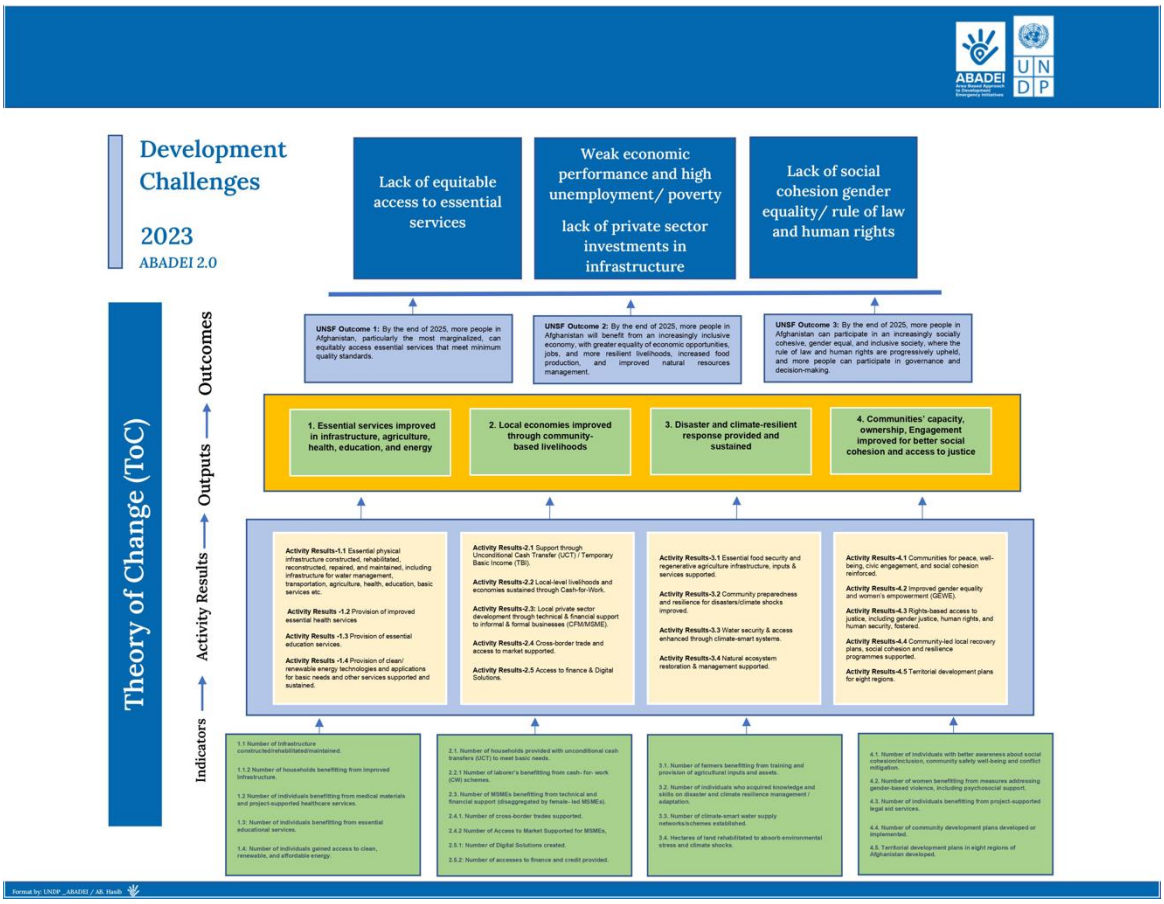

Assumptions

- Strong linkage and coordination with the HRP exist in terms of priority setting and targeting based on key humanitarian indicators and data, including the severity of food insecurity, emergency needs and the presence of internally displaced persons.
- Dedicated support to women and girls can be delivered in view of the new restrictions, applying new ways to provide assistance in a sensible and realistic way that will create no unintended negative consequences for the women involved, their families or their communities.
- Sufficient engagement with local-level stakeholders can be established to foster ownership of activities and identification of demand-based interventions and, in turn, strong support for what is being achieved together.
- Operational and access arrangements for target areas are strong enough to allow access for contractors, partners, and freedom of movement.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

TOC: PROJECT STRATEGY ADDRESSING the DEVELOPMENTAL CHALLENGES

The Theory of Change (TOC) in essence for ABADIE 2.0 is as follows:

IF essential basic services are functioning, **THEN** people can meet their basic needs without humanitarian assistance.

IF the most vulnerable receive livelihood support & local economies are revitalized, **THEN** people can earn a living, and communities can flourish.

IF communities are prepared for disaster management and water/natural ecosystems are restored, **THEN** livelihoods will be protected, and displacement reduced.

IF reconciliation, inclusive participatory and planning processes, gender equality and access to justice improved, **THEN** social cohesion and resilience are strengthened at the community level.

C. PHASE I RESULTS (October 2021 to 31 March 2023)

During ABADEI phase I, the following results have been achieved23:

Provision of Essential Services

- **Infrastructure:** Physical infrastructure such as roads, canals, floodwalls, or reservoirs improve access to basic essential services, and connect farms to markets, positively impacting the economy, education, health and well-being, and quality of life. ABADEI rehabilitates community infrastructure by cleaning debris and physically upgrading existing structures and building new infrastructure to meet urgent needs for water management, transportation, and access to basic services. UNDP under the ABADEI programme, completed 682infrastructure rehabilitation projects involving cleaning, construction or rehabilitation including: Improving 351 canals, improving 60 roads, 81CBE (community-based education) classrooms, 69 flood walls, 33 culverts, 25 water reservoirs, 17 karez (irrigation water tables) underground 13 health facilities and 10 check dams, 152 hand washing stations were constructed in schools in the Eastern, Northeastern and Southeastern regions, and 16 latrines. Under ABADEI in 2022, under Output 1, 495,673 households benefitted through infrastructure activities. Under the infrastructure component of ABADEI, through infrastructure ABADEI rehabilitated and protected 72,904 Hectares area of land, improving access to local communities through 131,240 meters of road.
- **Health:** UNDP supported 293,197 individuals (206,583 women 60%) with basic health care services through 60 mobile health teams (MHT): 12,323 health kits were distributed to 395 institutions, including health facilities, schools and COVID-19 awareness training.
- **Education:** In the Eastern, Northern and Southeastern Regions of Afghanistan, 150 CBE schools were established, catering to 4654 students (2639 women or girls), recruiting 165 teachers. Further, 48 CBE classrooms were cleaned (23) or constructed (25) by UNDP.

23 As the implementation has not been completed under Phase II by the time this document has been developed, the figures below refer to results achieved as of December 2022.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

- **Energy:** To improve communities' access to energy services, ABADEI has installed 378 decentralized solar PV or thermal systems for meeting lighting, heating and other uses; in mosques (360 systems) but also in health facilities (10 systems) and schools (8 systems). These energy systems benefit a total of 276,735 individuals (4,555 women). Furthermore, 564 sets of Solar PV kit chargers were distributed to individuals and institutions, benefitting 12,586 individuals (6224 of these women). These included solar cookers (11 kits); solar lamps (18kits); solar pumps (27 kits); and efficient stoves (511 kits).

Community Livelihoods and Local Economic Activities[24]

- **Unconditional Cash Transfer***:* ABADEI provided 20,504 households with UCT (4,906 female -led). 151,427 people benefitted (58,529 women). Altogether, US$5,322,589 was distributed through UCT. Under the ABADEI programme, UNDP also offered relief support in the form of essential items (relief kits). In 2022, 4030 relief kits were distributed, one per household, (1613 of these females led). Relief kits were primarily distributed in the Southeastern Region (3980 kits) but also Central (320), Eastern (80) and Northern Regions (360). An additional cash support package was delivered to 550 households (4 female -led) totaling US$97,500.
- **Cash- for-Work (CfW):** 204,599 laborers (1,115 women, 175,375 youth) benefited from ABADEI's cash-for- work (CfW)schemes across all regions, creating 2,307,906 labour days and distributing US$13,189,345 in wages. The schemes include all the infrastructure interventions already reported under Outcome 1 "Public infrastructure".
- **MSME support:** A total of 7,600 businesses (women-led, 6,297), including Grants, Tools and Vocational Training benefited from ABADEI support across all regions. Further, 5614 of the businesses supported were informal SMEs, and 1986 of them were formal SMEs. Among the businesses, 6600 received technical support on business development and all received financial support, amounting to US$7,915,653. An additional 1000 trainees received vocational training in phone repair, Solar Home Repair, and tailoring. Training took place over 36 days, 3-4 hours per day.
- **Savings groups:** ABADEI has set up 637 groups, comprising 11,661 members (7611 female), across the Northern, Central and South-eastern regions.

Protection of Farm-based Livelihoods from Natural Disasters

- **Agro-Kits:** ABADEI also constructed 820 agro structures, such as drip irrigation and greenhouses and distributed 17922 agro kits, benefitting 24,300 people (10,795 women).
- **DRR awareness raising:** Raising awareness about disaster risk reduction in local areas helps mobilize community members in participating in ABADEI's disaster management committees and contributes to local efforts to manage disaster risks. During the first phase, ABADEI organized awareness raising on disaster management for 11,727 people (4,482 were women).

---

[24] UCT or targeted basic income (TBI) provides vulnerable households with money to meet basic needs on a temporary basis. The exact amount a household receives is determined by the RPs on the ground and informed by the guideline from the Afghanistan Cash & Voucher Working Group. As of now, the average cash package is around US$261.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

- **Establishing Disaster Management Committees (DMC):** DMCs consist of volunteers who play a role in identifying and reducing the various disaster risks in their local communities. During the first phase, , ABADEI established 232 DMC (4434 members, 1143 members were women) committees. Depending on the RPs in question, the DMCs consist of 11 to 30 members each, who take up different roles such as search and rescue, first aid, shelter management, early warning, and saving boxes.
- **Environment awareness raising:** 3843 people (1804 women) participated in these events in the Central, Northeastern, Northern and Southeastern Regions.

Community Planning and Social Cohesion

- **Social cohesion interventions:** In total, ABADEI has reached 523,446 (76,211 women) community members across all regions. Most workshops for community engagement and awareness were in EORE (Explosive Ordnance Risk Education ') with 509,947 members reached.
- **Local coordination bodies (LCBs):** Local coordination bodies are informal institutions where community elders and religious leaders can meet to resolve disputes peacefully. During the first phase, ABADEI established 271 LCBs with 4202 members (1611 women). The LCB members support ABADEI in facilitating dialogues about dispute resolution and social cohesion. Following the powershift, DfA banned women from public spaces, and ABADEI has made efforts to include women in the LCBs.
- **Legal Aid:** ABADEI provided legal counselling for 1226 people (637 women). However, the legal issues linked to gender-based violence (GBV) and domestic violence need further attention and resources as these types of cases are hardly defended in a duly established court system represented by civilian defence lawyers in the current shariya context in Afghanistan.
- **Awareness Raising on Basic Rights:** 16,042 people (8401 women learnt about their civil rights during awareness raising sessions. Peer-to-peer justice networks refer cases that need support or legal counselling on family law (marriage certificate, child custody, dowry), inheritance, and property law to legal counsellors. Eight justice networks were established with 80 members (41 female).
- **Community Planning:** Developing community development plans (CDPs) help communities identify development priorities based on local contexts. During this reporting period, ABADEI supported 441 communities in revising their community development plans (CDPs).

D. LESSONS LEARNED

Over the last 20 years, the UN has learnt valuable lessons on what works and what does not work in providing humanitarian and development assistance to Afghanistan. Neither a one-size-fits-all approach nor a fragmented, siloed, tailor-made approach to development interventions has been effective. Instead, a more integrated, socially inclusive, multi- disciplinary approaches are needed that account for the significant differences in basic service delivery and need across provinces and regions and recognizes that humanitarian and basic human needs gains in one area are linked to and dependent on humanitarian and basic human needs gains in other areas. While integrated approaches are being utilized, stand-alone sectoral programs such as energy, private sector, banking, education and health are needed in Afghanistan to increase equitable access to services for people left behind and improve development outcomes in these critical sectors. Humanitarian assistance alone will not be enough to avert famine and a major humanitarian crisis. A calibrated and integrated approach is needed to safeguard progress and prevent an increase in the

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

humanitarian caseload by directing assistance at the local level to support basic human needs by mitigating the immediate impact of the crisis on lives and livelihood.

- In the context of the De *facto* Authority and its isolation from the International Community, working directly with local leaders, shuras and community development councils, fostering community ownership and social cohesion and promoting a robust Private Sector is essential to a healthy Afghan economy, while securing that immediate response and development assistance reach the most vulnerable.
- Priority-driven interventions by the community needs to be articulated territorially that are integrated and clustered geographically, maximize the impact of interventions and impact on the target communities.
- Increasing access to essential services and education for Afghan women, empowering women in business and agriculture, developing skills and vocational employability and providing other tailored interventions for Afghan women have been critical to giving women a space in the social and community life within a patriarchal system such as that in Afghanistan.
- Working with the DFA leadership from the highest to the middle level, including religious bodies, is essential to reduce harmful restrictions on women's freedom of mobility and right to work. As Afghanistan is a patriarchal society, there should be special programs to address harmful social norms and practices against women and girls. Gender equality and women's empowerment approaches should take a whole-of-society and whole-of-community approach which also tackles embedded gender issues in the family, community and institutions such as the de-facto authorities.
- Over the passage of time, Area's offices need to increase their understanding of community needs and build trust and cooperation with communities in their dialogues. Further, it is vital to evaluate and better understand the specific capacities of RPs, find alternative implementing companies and partners, and improve implementing capacities is therefore becoming critical to advance ABADEI results.
- Road infrastructure linking remote villages and districts to provincial centers, marketplaces, and hospitals and health facilities is suboptimal, but remains critical to economic transactions, community connectivity, digital infrastructure, communication and social cohesion.
- ABADEI as a strategic project approach, can be potentially synergized with sectoral interventions that are mainstreamed regionally such as energy, private sector, banking, requiring scale, enabling frameworks and investments.
- Adopting the community-based approach was one of the most successful initiatives, which helped UNDP in reaching the most vulnerable and poor people, who were affected by the last two decades of conflict, and there was no access to basic living facilities.
- Supporting local-level enterprises in a crisis situation, which affected most of the formal and informal businesses (especially those led by women), was another very effective and sustainable initiative. Under this initiative, the ABADEI project not only created thousands of permanent employment opportunities but also saved many enterprises that were on the verge of collapse following the 15th of August 2021 turnover.
- ABADEI project helped the community start saving groups which was an excellent initiative. The saving groups help the community get some benefits by taking loans from the group and, at the same time,

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

make them self-sufficient. The saving groups helped many women who did not have a breadwinner at home to start their own small businesses and knew how to earn for themselves.

E. ABADEI PHASE II (2023-2025)

The first phase of ABADEI prioritized the preservation and safeguarding of essential services and livelihoods to support the delivery of services in areas such as health, education and skill training, water and electricity (energy) in an equitable manner, while providing critical short-term income generation opportunities, targeting basic income and safeguarding livelihoods. ABADEI phase II will continue to enhance community resilience and deliver on the four areas of intervention prioritizing the following:

i) Leverage social cohesion (Output 4) as the building block to accelerate the implementation of activities around essential services (Output 1), Community livelihoods (Output 2) and Disaster Response (Output 3) to boost local development value chains, and solidarity economies[25] along Islamic Finance principles. This will be achieved by pursuing the following strategies:

- **Community engagement**: Engaging diverse community members in the planning, implementation, and evaluation of activities related to essential services, community livelihoods, and disaster response to build a sense of ownership and participation.
- **Building partnerships:** Partnering with local organizations, such as faith-based organizations, community-based organizations, and local businesses to bring together different stakeholders and promote collective action.
- **Promoting inclusive decision-making**: Encouraging participation from marginalized groups (women, girls, ethnic minorities, people with disabilities) and promoting inclusive decision-making processes to ensure that the needs and perspectives of all community members are taken into account, leaving no one behind (LNOB).
- **Emphasizing Islamic finance principles**: Incorporating Islamic finance principles such as risk sharing, and ethical investing will help to promote local development value chains and solidarity economies

ii) Integrate spatial planning and land use tools to develop territorial development plans for improved and integrated programming, beneficiary targeting and financial efficiency. This will be achieved by:


- Conducting spatial analysis: Using tools such as Geographic Information Systems (GIS) to analyze the physical, economic, and social characteristics of a territory.
- Identifying land use opportunities: Identifying land use opportunities such as underutilized land, brownfield sites, and areas suitable for infrastructure development
- Engaging stakeholders: Engaging stakeholders to ensure that territorial development plans take into account the needs and perspectives of all relevant parties.
- Prioritizing interventions: Prioritizing interventions such as infrastructure development and maintenance housing, and community services based on the results of spatial analysis and stakeholder engagement to ensure that territorial development plans are targeted to areas of greatest need.

[25] Economic activities that aim to prioritize social profitability instead of purely financial profits

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

- Monitoring and evaluation: Regularly monitoring and evaluating the progress of territorial development plans to ensure that they are achieving their intended objectives and making the best use of available resources.

iii). Strengthen integrated approaches by bolstering synergies, linkages, and complementarities between the projects' four areas of intervention[26], while expanding the scope of interventions to include access to finance, digital transformation (in line with UNDPs Digital Strategy 2022-2025), natural resource management and gender empowerment.

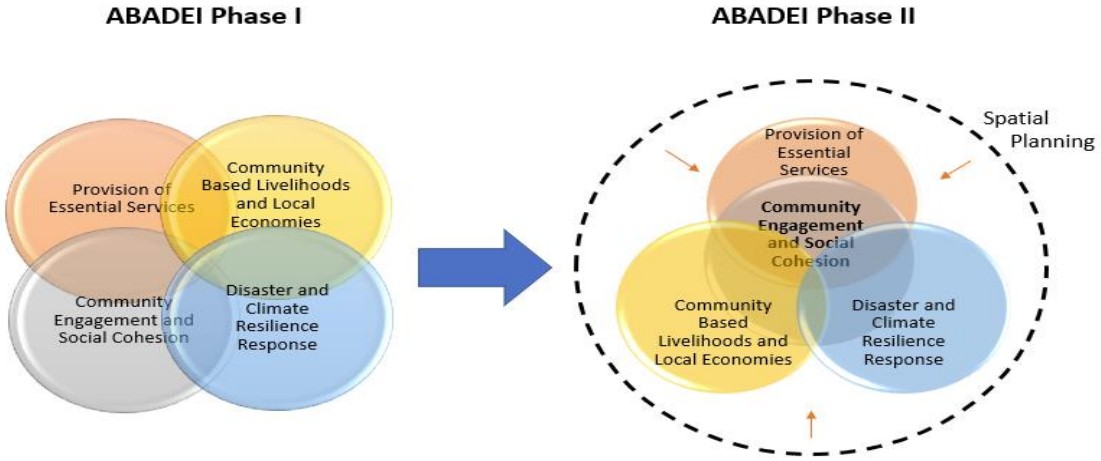


IMPLEMENTATION ARRANGEMENTS

The Project activities will be managed through the eight (8) UNDP AFG regional offices, which will also facilitate the delivery of all UNDP projects at the field level, under the direction of the Project Manager (PM) and supported by a Project Management Unit (ABADEI-PMU). The ABADEI Program Manager will report to the SDDR (Senior Deputy Resident Representative). Responsible Parties (RPs) with proven capacities will be engaged to operate at the field level. As the capacities of the regional offices and PMU are strengthened, a mix of RPs and other implementation modalities as feasible with be adopted. The technical and operational capacities of the PMU will serve to ensure the timely and technically sound implementation of the Project's activities in the provinces.

Project activities will be clustered wherever possible to maximize tangible impact to target communities. The Project targets the social and economic challenges currently faced in Afghanistan and will deliver significantly on addressing immediate priorities identified at the local level, in the water, energy, health services, road and other critical community-based infrastructure, supply chains, flood prevention, disaster preparedness, community-based TVET, job creation for communities, IDPs and vulnerable groups, with gender equality and women's empowerment, and other cross-cutting themes throughout the Project's activities.

[26] Namely: i) The Provision of Essential Services ii) Improving Community Livelihoods and Local Economic Empowerment iii). Strengthening Resilience to Climate and Disaster Risks, and iv) the Promotion of Community Ownership/Engagement and Social Cohesion.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

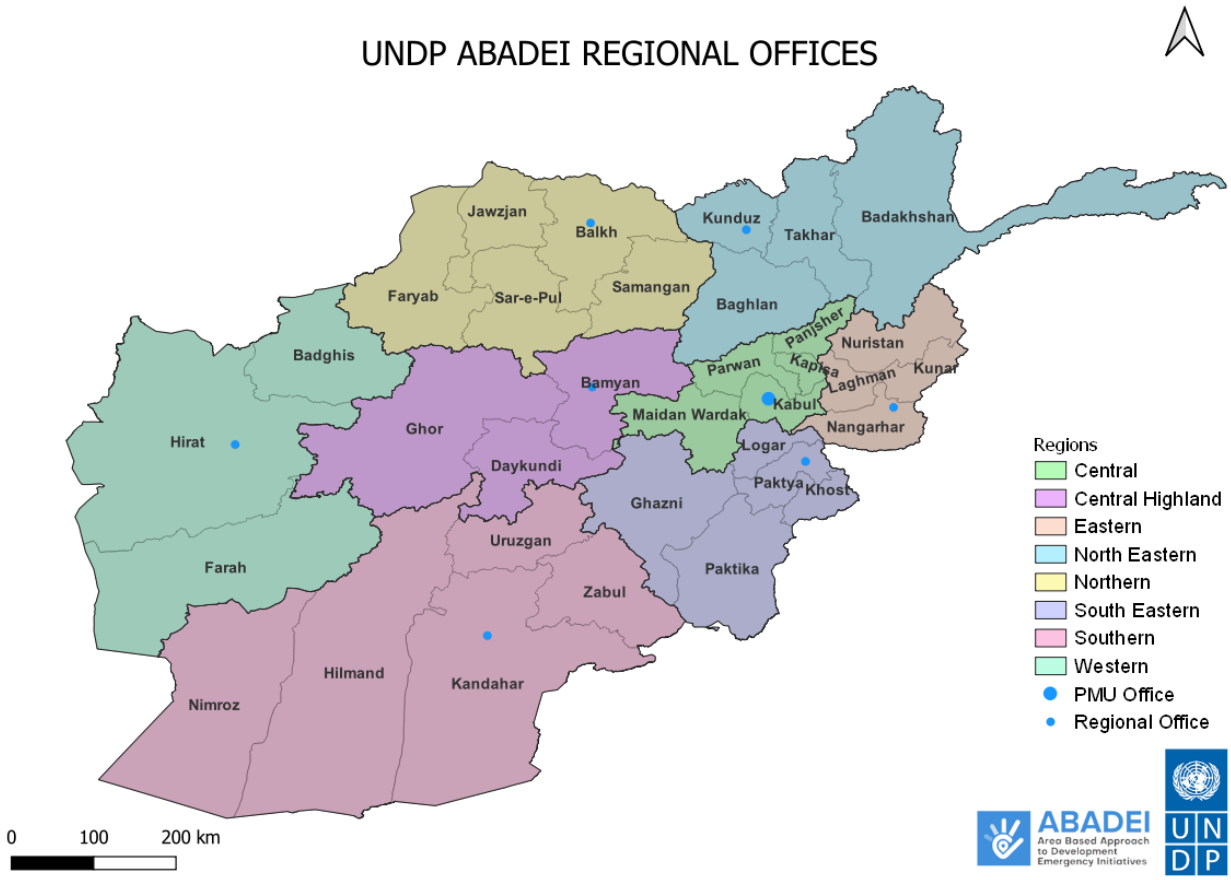


F. MONITORING & REPORTING FRAMEWORK

UNDP has developed an Area-Based Monitoring and Reporting Framework that relies on a mix of tested tools and methods, which will be offered as a common service to the UN system, with the option of supplementing it with additional support offered by the other sister agencies. It provides an ongoing tracking and reporting capability, based on three main components.

- **Component 1** - addresses the higher-level factors that influence the substantive and operational context of the ABADEI Strategy implementation. Situation/context monitoring is driven by socio- economic assessments and situation analysis through the UNDP SDGs Integration, Economic Modelling and Policy Unit, and political and security situation analysis through UN mechanisms supported by UNAMA (United Nations Assistance Mission in Afghanistan) and UNCT (UN Country Team).
- **Component 2** - comprises standard programme implementation monitoring processes, tools and systems but with reporting mechanisms, supported by a dedicated online system for activity reporting by implementing partners (IPs) on a monthly basis. Further, vetting of IPs, contractors carried out by the IRMU (Integrated Risks Management Unit) and the selection criteria of beneficiaries for ABADEI programme are in place before activity implementation.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

- **Component 3** - embedded within two components is the risk monitoring covering a spectrum of issues from the highest level to the operational level on the ground, anchored in the UN/UNDP project management rules and regulations to identify emerging risks early on and undertake mitigation measures in time. This component is facilitated by the Integrated Risk Monitoring Unit (IRMU) undertakes rigorous vetting of IPs, contractors and beneficiaries and ensures compliance with relevant UN and international risk management standards, including Anti-Money Laundering (AML) and Combatting Financing Terrorism (CFT) policies. CO risk escalation policy has been established in compliance with the corporate Enterprise Risk Management Policy and contextualized in the UNDP Afghanistan Adaptive Risk Management and Mitigation Strategy. Further,ABADEI program will also involve Crisis Bureau when needed for technical advice and support.

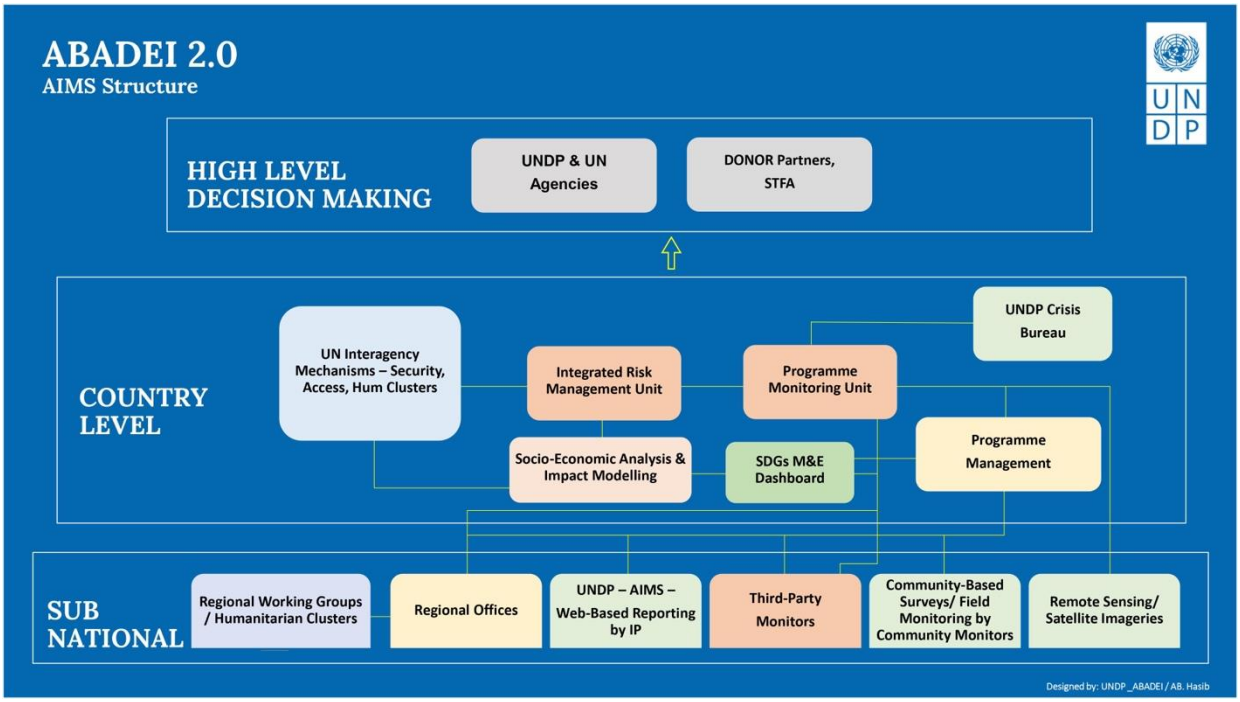

The ABADEI monitoring framework is implemented through systems and capacities of UNDP and UN entities across the eight (8) regions as described below.

- **ABADEI Information Management System (AIMS):** Monthly data collection and a progress monitoring mechanism was established wherein each ABADEI RP and Regional Area Teams implementing activities directly report their status and progress on a set of indicators, sub-indicators, and actions. The information/data collected through AIMS is processed and cleaned by a Reporting Specialist (i.e., quality assurance) and then validated through Regional Teams and Third-Party Monitoring Agents.
- **Geographical Information System:** Information recorded on the AIMS will be linked with geographical mapping of each region to map all the activities implemented under ABADEI in order to determine the cost- benefit analysis and impact of the budget utilized in the region/province/districts.
- **Community-based surveys:** Community-based surveys will be conducted to collect data on key output indicators as well as outcome indicators, including perception surveys commissioned through local partners or conducted through local enumerators. The surveys are conducted biannually or on a need's basis across a non-parametric sample of the target beneficiaries and analyzed to gauge and demonstrate

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

the assistance's impact, detect changes in the situation and inform course correction measures, where applicable.

- **Field Monitoring:** Field monitoring will validate results reported by implementing agencies and partners and quarterly/annual reports. The monitoring activities will help obtain first-hand observation of the project setting at the target community level and verify data for assessing project relevance, effectiveness, efficiency, and impact. UNDP and UN partners will use their sub-offices across the eight regions for field monitoring, data validation and verification. M&E Unit has appointed 30% of female monitors in order to ease access to women beneficiaries and recording their perspective/knowledge regarding the project activities.
- **Third Party Monitoring (TPM):** TPM is the main monitoring mechanism in areas where the security situation deteriorates or is considered "No Go" areas for UN staff. UN/DP have experience in utilizing third -party monitoring services, which will be activated and/or expanded for additional support in insecure districts and project sites where access is restricted or limited. Project agreed with TPM to engage female enumerators to access female beneficiaries in the regions.
- **Integrated Risk Management Unit (IRMU):** The Unit has been operational since November 2021 to monitor the changing situation in the country and the related risks of implementing the ABADEI Strategy. IRMU conducts risk analysis, and due diligence, and ensures compliance with UNDP corporate guidelines on risk management, international sanctions regimes and AML/CFT policy, and establishes country-specific tools and practices to strengthen the due diligence and accountability through the implementation of programmes and projects in partnership with other UN Agencies, Funds and Programmes and donor countries. This action-oriented capacity is designed to ensure a consistent "Do No Harm (DNH)" approach across all ABADEI interventions, and to support the adaptation of programmes in a rapidly changing context.

To ensure data integrity and the security of the often-sensitive data, information is uploaded by authorized personnel in the regional sub-offices. All this data is stored centrally so that all interventions can be tracked together in one monitoring system. A key feature of the monitoring system is the use of digital technologies to upgrade the evidence-based approach into almost 'real-time' monitoring. Through the creation of analytics, collective analysis, actionable intelligence, this aggregated data will be used to inform sub-national and national decision-making processes and the allocation of budgets. This will allow partners to observe and monitor progress and thus adopt a more flexible and adaptive approach to programming that suits the highly volatile context.

Project will focus on monitoring activities at different phases i.e., during initiation of the activity, mid-level, at the completion stage and post completion. In addition, activities completion, handing over site and beneficiary's satisfaction checklists would also be developed by ABADEI PMU. Project will also take into consideration the dynamic monitoring mechanisms i.e., remote monitoring and validation of the information. GRM mechanisms would further strengthen to record the grievances from the field/implementation sites.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

Results and Partnerships

A. EXPECTED RESULTS

The Project aims to provide UNDP with a focused delivery mechanism in an integrated approach that will address both the current priority needs as well as provide decision-makers with a flexible and agile approach that will respond to new opportunities and unforeseen future externalities and exigencies. The expected results of the Project are listed below, linked to the four Outputs of the Project as well as the three Outcomes of the UN Strategic Framework (UNSF), as per the UNSF January 2023 draft.

The overall impact of the Project will reach all 34 provinces of Afghanistan with an integrated 'package' of interventions, bringing economic benefits, strengthening essential services, linking communities with improved transportation infrastructure, involving local leaderships in priority identification, fostering women and girls economic and social empowerment, creating two million permanent jobs; all interventions aims at reducing vulnerability, building stability, social cohesion, strengthening civil society and community resilience. The Project will engage with UNAs and INGOs working in the field to strengthen and expand the existing partnerships.

Output 1 (GEN 1): Essential services improved in the area of infrastructure, agriculture, health, education and energy.

The rehabilitation of essential infrastructure and services is key to establishing and maintaining livable conditions in vulnerable areas. Interventions will provide targeted support to:

- Public infrastructure for the delivery of essential health services; electricity, shelter, solid waste management (SWM) and water supply, such as the rehabilitation of basic community services in health, education, roads rehabilitation and transportation etc.
- This also includes essential health services such as general essential (primary) health services, and other infectious disease prevention support and support to provide Basic Package of Health Services (BPHS) and the Essential Package of Hospital Services (EPHS) in rural and urban areas).
- Food security-based economic infrastructure such as local roads, bridges, marketplaces, as well as boreholes and irrigation channels for agricultural communities; productive infrastructures such as greenhouses and the rehabilitation of degraded lands; and
- Renewable energy provision is required to support these essential services.

This Output includes activities under four activity results as follows:

1.1 Essential physical critical infrastructure constructed, rehabilitated, repaired, equipped and maintained, including infrastructure for water management, transportation, agriculture, health, education, basic services etc.
1.2 Provision of improved essential health services (including women and girls accessing health care).
1.3 Provision of essential education services (including gender- integrated TVET).
1.4 Provision of clean and renewable/ alternate energy services, technologies and applications supported and sustained.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

This output will ensure that people's both urgent and basic needs are met to maintain positive coping capacities and pursue dignified livelihoods and prevent the aggravation of humanitarian needs beyond what can be addressed through the humanitarian response. Therefore, the activities under these four areas focus on preserving core service delivery mechanisms (including infrastructure) for health services and COVID-19 and other infectious disease prevention response; water, sanitation, and hygiene (WASH) and solid-waste management (SWM) services; reducing food insecurity by providing short-term emergency support in the form of agricultural inputs, services, and infrastructure; and the energy required to support essential service and household level needs.

Targeted activities are as follows:

- **Water**. The Project will design and deliver multiple interventions that increase the availability of clean water to communities with special attention given to finalizing water supply projects that were initiated by international efforts during the Government of the Islamic Republic of Afghanistan (GoIRA), i.e., those that were nearing completion when programmes were halted, and where international financing was suspended following the de Facto Authority (DfA) takeover.
- **Food security.** Food insecurity is a major constraint for any socio-economic recovery effort, as it is a conflict driver and thus an important consideration for programming. Nearly 20 million people are projected to be acutely food-insecure between November 2022 and March 2023, including more than 6 million people in IPC Phase 4 (Emergency), according to preliminary estimates. Four million people are acutely malnourished, including 3.2 million children under the age of five - 28.3 million people – two-thirds of Afghanistan's population – require multi-sectoral humanitarian assistance in 2023[27].
- **Waste management.** In Year One, each of the 34 provincial capitals will undergo primary assessment to under that governance mechanism for waste management. In Year Two, more waste management systems will be strengthened, in small cities and larger towns in the districts of the 34 provinces, and in Year Three, even more waste management systems will be delivered in the larger towns and villages of the 400+ districts within Afghanistan's 34 provinces. TVET will be provided to all target waste management companies or structures, unless already provided for by other more specialized funding sources. The Project will strengthen those structures engaged in the management and removal of solid and liquid wastes, through interventions that in early phases, finance waste removal and clean-ups. Special attention will be given to finalizing waste management and sewerage system projects that were initiated by international efforts during the GoIRA, i.e., those that were nearing completion when programmes were halted, and where international financing was suspended following the DfA takeover. The Project will transition from clean-ups, to building durable capacities of waste management structures and support them to establish cost recovery systems so that minimal external support, if any, is required for them by the end of the Project's three-year cycle.
- **TVET (Tertiary, Vocational, Educational Training), Skills Development and Education Sector:** Training and upskilling female students for demanded specializations through community-based technical and vocational services providers and instructors. The project will target women and girls and young people who will be trained by the service providers. The training materials will be developed, and Training of Trainers (ToTs) will be conducted to pilot the private TVET institution's capacity, as well as used to train

[27] 21 February 2023, Afghanistan, WFP situational report

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

beneficiaries. The project will contribute to improved human capital and access to technical education through community-based technical and vocational education and training for women/young people.

- **Health services.** Health facilities that provide services to women and girls will be prioritized. Each year of the Project, health facilities will be supported in all of Afghanistan's 34 provinces, and the corresponding quality and availability of health services will be greatly improved. The Project will support hospitals, health posts and clinics, targeting priority gaps and needs identified in consultation with community representatives, health experts and CDCs. The Project will procure solar- powered electricity for health facilities, procure missing medical equipment and supplies, and refurbish surgical areas and patient facilities, in partnership with UNAs and INGOs specialized in the health sector. Health facilities that provide services to women and girls will be prioritized.
- **Clean energy (renewable energy) access/services.** The Project will enable essential services and support services for the provision of basic human and development needs with improved and reliable clean energy access. Economic, industrial (small and medium enterprises), agriculture and institutional services (in health, education), and other sectors requiring energy will be facilitated with appropriate technical solutions – electrical, thermal and mechanical. Agri- based livelihoods with energy linkages such as processing, cold storage and overall agriculture value chain will be supported. Micro/mini-grids for meeting captive energy demand with limited investments in transmission and distribution will be considered based on cost-benefit/feasibility analysis. In principle, the focus remains to strengthen energy access on the demand side with decentralised technical solutions and integrated with potential sectoral interventions with the possible strengthening of the energy sector at scale and on the supply side, given the present regulatory, institutional and capacity constraints.
- **Transportation infrastructure, Roads and Bridges, Maintenance and Expansion of Road Network.** By the end of the three-year cycle of the Project, nearly all rural settlements will have greater road access. Training for road maintenance crews will be a part of each road work activity, and new mechanisms will be put in place for communities to generate revenues that will cover recurrent costs to sustainably maintain newly opened and newly rehabilitated roads, creating many jobs during construction and repair works and many permanent jobs in the field of road maintenance. The Project will identify roads and bridge structures that require repair, expanding rural road networks at every opportunity. The Project will engage RPs with road building expertise, that utilizes an optimal mix of heavy equipment, and labour, to rehabilitate damaged and neglected roads and bridges, with the aim of linking isolated villages in rural districts to larger towns and cities, increasing community access to markets and to health services. Resilience agenda documents elaborated and updated in close consultation with local leadership, will map and identify the road networks of each province, detailing which road and bridge works are of first, secondary and tertiary priority, and move forward the activities implemented in order of priority, utilizing criteria that prioritize the economic benefits and social potential of individual road work activities (e.g., road access for rural communities to health services for men, boys, women and girls to be prioritized).
- **Spatial Planning:** Using land planning tools such as remote sensing and Geographic Information Systems (GIS) will play a significant role in advancing local community development, agriculture, infrastructure, health, and social cohesion. GIS will be used to create detailed maps of land use, topography, and natural resources, to identify areas suitable for agriculture and infrastructure development, promote sustainable land use, conserve natural resources, and support local livelihoods while identifying areas that are

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

vulnerable to natural hazards such as floods, landslides, and droughts, which can help to improve disaster risk reduction and emergency management. Furthermore, GIS (geographical information system) will support the planning and monitoring of infrastructure projects, such as roads, water supply systems, and health clinics, which can improve access to essential services for local communities. Each region will launch a territorial development plan.

Output 2 (GEN2): Local economies improved through gender-responsive community-based livelihoods.
The revitalization of local economies is an important dimension of the ability of communities to cope with the current environment while also addressing the drivers of vulnerabilities they face. UNDP is already working directly with communities to address extreme poverty by providing immediate financial assistance to households, leveraging digital and innovative delivery mechanisms, and creating opportunities for immediate income generation, targeting unemployed youth. UNDP and UN agencies are already supporting local economies by developing green, inclusive value-chains based on local market assessments, strengthening the private sector by providing access to innovative financial services, new markets and products and supporting producers and micro- enterprises, including women-owned small and medium-sized businesses and accompanying infrastructure needs.

This Output includes five activity results as follows:

2.1 Households in high poverty and high insecurity areas are provided with Unconditional Cash Transfer (UCT) and Temporary basic income (TBI).[28]
2.2 Local level livelihoods and economies are sustained through Cash- for- Work (CfW) including women and girls, vulnerable groups accessing CFW).
2.3 Local private sector development through technical and financial support to informal and formal businesses, including assisting micro, small, medium-sized enterprises (MSMEs) to access and/or expand to new market areas, support to local traders, to women-led businesses and community- led social enterprises (Cash-for Markets -CfM).
2.4 Cross-border trade and access to market supported (including women-led-businesses).
2.5 Access to finance and digital solutions supported and sustained.

These outputs will contribute to safeguarding livelihoods so that communities can continue to function "independently" in the face of the crisis. Therefore, the activities under these five result areas will focus on a range of social protection measures and the creation of livelihood opportunities. Temporary basic income (TBI) will target households in high-poverty, high-insecure areas, with a specific focus on children (0-3), elders (above 65) and the disabled. Interventions will include CfW for agriculture, disaster-resilient infrastructure, maintenance, and construction work. Further, CfM will support MSMEs and prioritize women-led informal businesses and community-owned social enterprises. The cash grants and credit to support the MSMEs will use UNDP AFG's framework of Cash-Based Interventions (CBI) approach, which will facilitate efficient grant-making activities under the project. UNDP Grant approach for CBI will help MSME (Micro Small Medium Enterprises) to scale up their operation without expectation to pay back. As 97 percent of people are under

[28] This is a targeted interventions for women-heads of households in poverty, child heads of households, households with sick and elderly persons, households with person with disabilities, who have suffered multi-dimensional poverty. ABADEI will participate in FSAC to ensure coordination with WFP and other food cluster agencies to avoid any duplication of efforts.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

the poverty line and lack credible financial institutions in the country, credit-based interventions will not apply to the MSMEs. UNDP will monitor and sets out parameters for grant-making facilities to ensure effectiveness and proper usage. Further, Cash-based interventions, such as conditional/unconditional cash transfer initiatives under ABADEI will be coordinated with UNICEF and WFP through the cash-voucher working group.

Moreover, the interventions will support vulnerable groups, especially youth and women, through training for income- generating activities. Different options will be explored, including aggregation, basic processing, packaging and marketing of local agricultural products in support of rapid socio-economic recovery at the community level.

Targeted activities are as follows:

- **Support to the Private Economy:** Agriculture, Business, MSMEs, Employment: Throughout the three-year project cycle, the Projects activities will result in a healthier private economy, increase permanent employment jobs, increased farm income, and the number of skilled workers available for businesses to hire for business expansion. The Project will engage with the business and agricultural community, through the regional offices, to identify interventions that fill gaps in the supply chains, that strengthen business and agricultural productivity (e.g., irrigation), to increase both the supply as well as the demand for increased production. The Project will work with business and agricultural organizations to promote effective consultations, establish more business and marketing connections, identify and open access to export/import markets, to understand how modern packaging and cold storage facilities will enhance the marketing of their products domestically and overseas, and to support agriculture processing and the food industry. The Project will organize TVET programmes for companies as well as business and farming organizations, and women's groups to increase the number of qualified employees. The Project will partner with other UNAs, private companies, NGOs and CSOS and organizations specialized in agriculture, to support commercial farmers in provinces where cost-effective transportation of agricultural products to urban and cross-border markets is feasible, and to support subsistence farmers in more isolated rural areas, to increase the availability of food for increased food security.

- **Support women's empowerment through business, especially (MSMEs) in Handicraft Industries, Agricultural value chain, and women's access to vocational education that enhances their employability.** Women- owned MSME businesses and women- owned farming and food distribution companies throughout Afghanistan will have their revenues significantly increased, through better production techniques and improved access to markets, internal and foreign, with many durable jobs for women created. The Project will promptly engage with the Afghan Women's Chamber of Commerce and Industry (AWCCI) and support the Afghan Women's Union in Agriculture (AWUA), at the national level, while also working in tandem and independently with branches at the subnational level. The Project will design interventions that strengthen these organizations' ability to support women-owned businesses, handicraft production and agricultural products and other feasible areas. As mentioned above, for the general economy, emphasis will be placed not only on increasing the supply of goods and agricultural products, but also on building demand, by identifying means by which women owned businesses and agricultural concerns, can have better access to foreign and domestic markets, creating innovative solutions (e.g. websites dedicated to marketing agricultural products and handicrafts, representation of

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

farmers and handicrafts as producers at international trade fairs, advertisements in trade journals) where products produced by Afghan women will be advertised and sold to new markets). The Project will proactively provide robust advocacy, in its engagement with local leadership and support to women's groups for increasing women's and girls' open access to education at all levels of study.

- **Digital Transformation:** Digital transformation and the use of digital technologies will be used to advance local development by improving the delivery of essential services, increasing agricultural productivity, and creating opportunities for economic growth and job creation through access to the gig economy. A multi-pronged approach will be followed for digital transformation, i.e., e-commerce platforms for connecting micro entrepreneurs' products with the market and economic growth, provision of future skills in youth to promote the gig economy, use of digital tools including eLearning, IVR and WhatsApp chatbots for delivering training, strengthening of echo system for mobile wallets to promote financial inclusion.

- **Access to Finance: Technical** business development and access to finance support will be provided to existing local businesses and individuals in support of building local economic development infrastructures. To promote financial inclusion, MSMEs will be provided loans on Islamic Baking principles by subsidizing the interest rates. Also, MSME grants will be provided to support entrepreneurs, especially women-led enterprises. For communities, in hard-to-reach areas, without banking/financing institutions infrastructure, in ABADEI-II, revolving loan funds at the community level will be promoted through Community-based Saving Groups (CBSG). To promote financial discipline and gradually reduce the humanitarian caseload, the project will adopt a graduation approach for MSME grants by initiating a matching grants programme, where 50 percent of grants will be matched by 50% loans from the private sector, i.e., microfinance banks/institutions. Technical assistance to MSMEs and value chains in business and product development, including financial literacy, bookkeeping, product packing, packaging, marketing, and sales, will be provided to ensure sustained growth of livelihood and local economies.

Output 3 (GEN1): Local communities' resilience capacity enhanced to better respond and adapt to the natural disasters and climate induced risks

Due to geographical location and years of environmental degradation and dependence on agriculture and natural resources for sustenance, Afghan communities are highly prone to intense and recurring natural hazards such as flooding, earthquakes, snow avalanches, landslides, and droughts. Beyond humanitarian assistance, farmers and vulnerable households need to be supported to produce locally in the face of natural disasters. As these factors intensify the crisis, adopting a climate-resilient approach is important to protect and sustain development gains from the start. Priority will be given to improving the ability of communities to avoid and recover quickly from disasters, increase their access to renewable energy, water, and promote sustainable food production through regenerative agriculture and agroforestry. Poor and marginalized communities, particularly displaced women and youth will be provided with environmentally sustainable livelihood opportunities. The existing social capital at the grassroots level (such as the functioning community-based organisations, District Management Teams (DMTs), and other formal and informal community representative bodies (Shuras)) will be utilized to the extent possible to assess the needs.

The Output includes four activity results as follows:

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

3.1. Essential food security and regenerative agriculture infrastructure, inputs and services supported
3.2. Community preparedness for disasters improved.
3.3. Water security and access enhanced through climate-smart systems.
3.4. Natural ecosystem restoration and management supported.

The objective of this Output is to ensure that the natural resources upon which livelihoods and rapid socio-economic recovery critically depends, are managed as sustainably as possible in a crisis context. Therefore, the activities under these results areas focus on providing short-term emergency support that ensures continued access to critical resources whilst at the same time generating rapid income- generating opportunities and engaging communities in designing and implementing projects that lead to collective outcomes.

Targeted activities

ABADEI will build or rebuild flood protection walls and structures to prevent flood waters from destroying roads, bridges, settlements, and farmlands. The Project will avoid building ad hoc structures downstream, which can themselves be at risk if upstream flooding moves suddenly downstream eroding their foundations. When designing flood prevention interventions, the Project will aim at creating holistic solutions, with upstream and downstream structures, that offer a durable mitigation measure for future floods, as well as for landslides, and avalanches wherever deemed advisable. Floods, landslides, avalanches, and earthquakes, occur continuously throughout Afghanistan, cutting off road access, destroying structures and farmlands, negatively impacting daily life and trade, and access to health facilities and livelihoods while putting human lives at risk. The Project will analyse climate and disaster risks and build risk-informed resilience plans aimed at increasing knowledge and identifying concrete actions for local actors. For seasonal slow and sudden onset climate hazards, the Project will set up appropriate early warning systems in individuals or groups of at-risk communities to increase their preparedness, encourage anticipatory actions and save lives.

As earthquakes are unpredictable and occur frequently in Afghanistan, the ABADEI will work with communities to inform them through planning and training on how best to prepare themselves for minimizing casualties and extreme hardship, through the prepositioning of equipment and tools, emergency medical supplies, temporary shelters and bedding, that can be accessed promptly should an earthquake strike, and deploy with trained personnel that address rapidly the sometimes tragic aftermath of earthquakes and other natural hazards. Training interventions will also include skills development for community members in building earthquake-resistant housing and appropriate community infrastructure to reduce the loss of lives and assets. Risk-informed planning interventions will include scenario-based community planning for earthquake risks *vis a vis* other hazards faced by communities. In the event of a disaster, the Project will also help speed up the disaster recovery process by rebuilding key structures, and by debris clearing through cash –for- work (CfW).

Finally, all infrastructure built through ABADEI, including roads, bridges, flood defence and community infrastructure, among others, will be designed and constructed with disaster resilience as a core consideration.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

Output 4 (GEN3): Communities' capacity improved for better social cohesion and access to justice (especially for those who are systematically discriminated, such as women, girls, ethnic and persons with disabilities).

To protect development gains, ABADEI interventions will support the development of community-led needs-based socio-economic assessments and recovery plans that promote reconciliation and prevent conflict, improve access to justice, support alternative dispute resolution mechanisms, and protect the rights of women and girls. ABADEI interventions will be designed and implemented in a participatory manner to ensure that activities are responsive to local needs and priorities and contribute to community resilience-building.

This Output includes five activity results:
4.1. Communities for peace, well- being, civic engagement, social cohesion/ inclusion reinforced.
4.2. Improved gender equality and women's empowerment (GEWE) programmes and protection services for women and girls integrated and implemented in ABADEI.
4.3. Rights-based access to justice, including gender justice, human rights and human security fostered.
4.4. Community-led local recovery plans and social cohesion and resilience programmes supported.
4.5. Territorial development plans for the eight regions of Afghanistan designed.

The activities of these outputs will prioritize local civil society organizations (CSOs), youth, grassroots organizations, and women's self-help groups. It is critical to ensure the voice of vulnerable groups is not excluded. Communities will be supported through the establishment of District Management Teams (DMTs) which will play a critical role in the designing of community gender-sensitive resilience plans, identifying priorities, community and resource mobilization, and the implementation of the prioritized community initiatives through small-scale rehabilitation and social harmony, trust, connectedness, positive social relationships, diversity, inclusion and social networking promotional projects.

These interventions will contribute to the improvement of service delivery, human security, social cohesion and community resilience. At the same time, they will provide an indirect contribution to peacebuilding through activities designed to reduce the potential for further conflict and lay the ground for more direct peacebuilding and conflict prevention initiatives, particularly for vulnerable groups such as women and youth.

Targeted activities
Each region in Afghanistan will develop a social cohesion strategy, that will guide ABADEI's activities in the field. The strategies will be the result of consultations with communities, RPs, UN Agencies and DFA structured around mechanisms to promote community engagement, Education and training programs, Job creation and production initiatives, social inclusion strategies, Conflict resolution and mediation programs, Sports and cultural events, and activities focused on promoting access to finance, digital transformation, natural resource management (NRM) and gender equality and women's empowerment.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

Furthermore, ABADEI will promote the drafting of Territorial development plans for each of the eight regions that will help guide the prioritization of ABADEI interventions and thus, accelerate social cohesion by developing:

- Baseline and characterization of the territory integrating social, economic, environmental, and institutional data, accompanied by the respective cartography to have a spatialization overview of the existing structures and dynamics in the territory.
- Forecast methodologies to measure the scope, reach and impact of ABADEI interventions generated from the territorial characterization.
- Shared territorial visions with partners, capturing perceptions, demands and aspirations of local actors establishing clear-cut guidelines on the potentialities and competitiveness of the territory. complementarities existing in the territory.
- Territorial development guidelines with recommendations for all stakeholders.

Through the consultative process, and the identification of interventions by local leadership, the Project will widen the membership of people participating in the decision-making process, foster community ownership of the Project's interventions, and build social cohesion by having a diverse set of communities engaged in a priority intervention identification and reliance building process under the Project.

B. RESOURCES REQUIRED TO ACHIEVE THE EXPECTED RESULTS

Project phase two will allocate roughly USD 133 million in its budget in year one, with approximately USD 93 million for contracts with Responsible Parties (RPs), and earmark approximately 13 million USD each year, for DPC, GOE, HR and GMS. The project will seek additional funding during 2023, to continue at the same level of delivery for 2024 and 2025.

The Project will utilize the eight regional offices, the international and national staff (See Staff Table in Annex 2) that have been recruited, and positioned in 2022, as well as the equipment and vehicles procured during Phase One, to design and oversee the delivery of numerous interventions in the three-year project cycle of Phase Two.

UNDP Afghanistan Country Office will establish a Project Board (PB), to meet periodically, to provide oversight, review evidence of performance, and ABADEI Annual Work Plans (AWP), annual work plans of the Regional Offices, track progress and endorse the overall direction that the Project adopts. (For more details , page 81, Annex 5) The makeup of the Project Board will be decided by the UNDP Resident Representative (RR), and Senior Deputy Resident Representative-Programme (SDRR-P), who will co-chair the PB meetings and will include the Deputy Resident Representative–Operations (DRR-O), key donors to the Project, Beneficiary Representative(s) and UNA partners. (Refer to Annex 5)


The Project will maintain both technical and operational staff for the Regional Offices, and they will report to the Area Managers is also the head of the regional office. The Area Managers will report to the Project Manager (P6), and will direct the Programme Management Specialist, for providing the day-to-day leadership for the Project Management Unit (ABADEI-PMU) based in Kabul, made up of technical and

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

operational posts, whose function is to support the technically sound and timely delivery of the Project. (Refer to Annex 2).

Each of the eight regions, with its 34 provinces, will have individual characteristics and specific needs, to restore weakened essential services, bolster productivity in the private sector and agriculture, increase sales and revenues for businesses and farmers, address critical infrastructure gaps, and strengthen the status of women and girls, and their access to employment, health services and education.

Annex 2

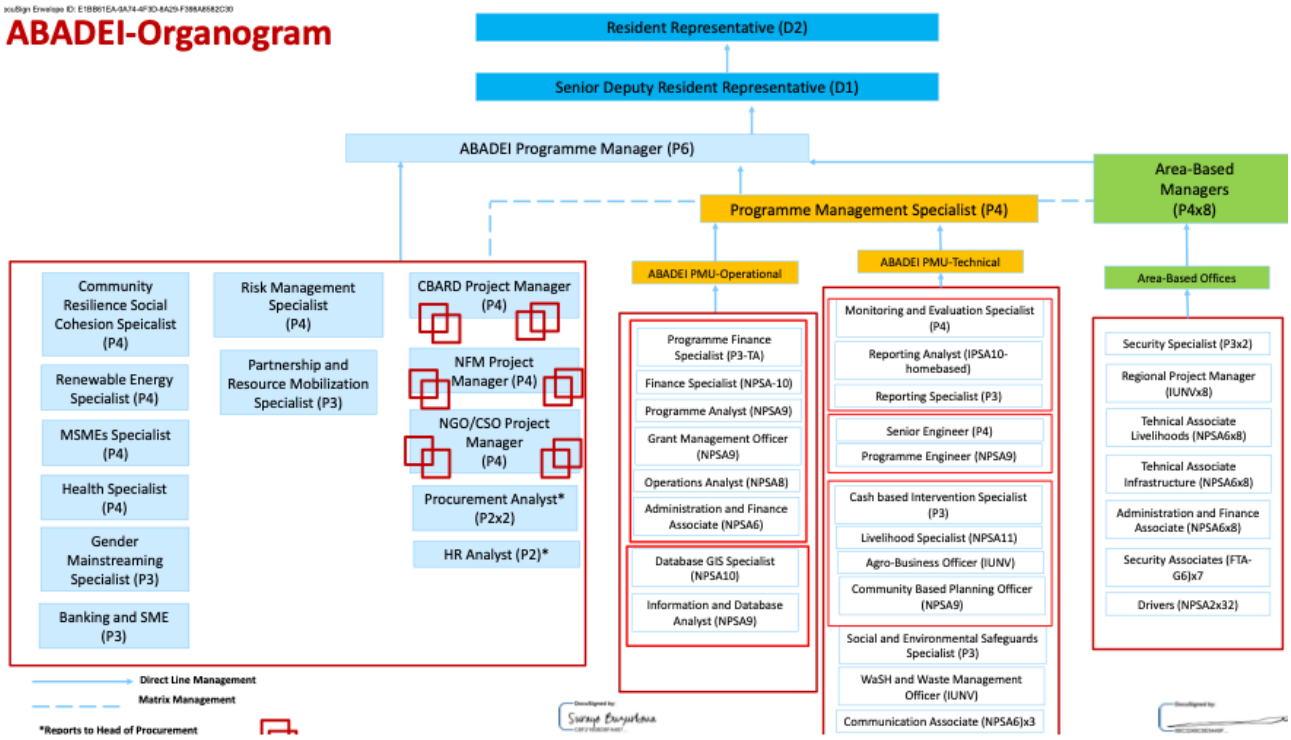

C. PARTNERSHIPS

Community leaders, shuras, Afghan women's empowerment advocacy organizations and groups, will be important partners of the Project, for the identification of priority needs, through consultations, to firmly establish the national ownership of the Project. It is important to note that most community development councils (CDCs), shuras, Jirgas and other community structures, at present, are male- dominated. The Project will seek to address this gender imbalance, at every opportunity, and will seek to confirm community priorities, with women's empowerment advocacy groups, women-led NGOs and CSOs when detailing activities to be included in the social cohesion, conflict mitigation strategies and territorial development plans.

Partners for the Project will be UNAs, specialized INGOs, and local NGOs/CSOs, who have the technical and logistical capacities to work effectively in the provinces as Responsible Parties, to deliver the activities deemed of priority interest as articulated by the eight regional offices and territorial development plans.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

In the sectors of health, education, WASH, and agriculture, the Project will seek partnerships with UNAs specialized in the health and agriculture sectors, and experienced INGOs to implement the ABADEI activities. ABADEI continues to build on the existing partnerships as well with UNHCR, ILO, IOM, UNFPA, UNWOMEN, UNHABITAT, UNCTAD and UNODC and in phase II, sister agencies will be essential and critical to deliver as ONE UN.

In the sectors and thematic areas of electrical energy, repair and expansion of road networks, natural disaster mitigation measures and risk management, the Project will engage the capacities of INGOs, NGOs and qualified construction companies contractually, to implement activities that are listed in the territorial development plans.

In the thematic areas of support to private businesses, and women's economic empowerment, the Project will build partnerships with local Chambers of Commerce and business organizations, as well as the Afghan Women's Chamber of Commerce and Industry (AWCCI) and the Afghan Women's Union in Agriculture (AWUA), using these organizations to design and deliver activities that address the priority needs identified in the territorial development plans.

For the elaboration of the social cohesion and territorial development plans, the Project will build partnerships with the local leaders, and local shuras that may be present, by establishing a consultative process to articulate the priorities. Wherever possible, this will be done by direct contact and consultation of the Project staff with local leaders, ad hoc committees and shuras: when not possible, the task of engaging with the community leaders and shuras may be outsourced to RPs, with diligent M&E oversight from the Regional Offices, supported by technical capacities within the PMU.

Women-owned businesses and women's employment, and the status of women and girls, will be fostered by partnering with the Afghan Women's Chamber of Commerce and Industry (AWCCI) and the Afghan Women Union in Agriculture, and other women's empowerment groups. Each intervention will be designed to include a component on women's and girls' empowerment at every opportunity.

ABADEI will promote the humanitarian-development-peace (HDP) nexus throughout the design, coordination, and implementation of the Project's interventions which aim to meet peoples' needs, mitigate risks and vulnerabilities and move toward peace and social cohesion. This application will be made by linking a people-centric multi-sectorial approach, do-no-harm (DNH) and conflict sensitivity (CS) approach, whole-of-society approach with an emphasis on support to vulnerable communities, in resilience-building activities identified and implemented through a developmental lens, that foster social cohesion, well-being and stability. To this end, the ABADEI programme will collaborate with humanitarian agencies such as UNHCR and IOM in areas such as work IDP and Solutions Strategy for Afghan Refugees (SSAR).

ABADEI interventions would be coordinated with humanitarian response mechanisms, such as UNHCR's Community-based Protection and Solutions Programme Response (Co-PROSPER) Strategy, aligning with the UN Afghanistan's Transitional Engagement Framework and Solutions Strategy for Afghan Refugees. Joint

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

pilot projects in 'Priority Areas of Return and Reintegration (PARR)' have demonstrated the HDP nexus at the community level, delivering job opportunities to displaced people, returnees, and marginalized host communities by supporting scalable enterprises in demand-driven value chains. This joint work between UNDP and UNHCR showcases UNDP Afghanistan's leadership in HDP Nexus programming, which enables humanitarian response to support community development visions in the mid-and long-term, providing vital stability and protection to communities affected by displacement. Building resilient communities through combined efforts in PARRs contributes to mitigating further displacement and addressing economic deterioration, extreme poverty, inequality, and widespread hunger.

D. RISKS AND ASSUMPTIONS

The Project and UNDP face several potential threats and associated risks. Broadly speaking, the threats and risks can be characterized as those related to the following three aspects: 1) security, 2) political, and 3) reputational.

D.1 Security Threats and Risks:

Threats from terrorist and outlaw groups to UN and UNDP personnel working in Afghanistan are very real, and over the past decades, a history of sudden and violent attacks on international and national staff has been recorded. In the past, UNDP personnel have been targeted by vehicle-born improvised explosive devices (VBIED) when vehicles laden with explosives have exploded at premises where UNDP staff live or work. Attacks from personnel born improvised explosive devices (PBIED), when a suicide bomber explodes their IED (improvised explosive devices) near targeted persons, have occurred, however, this threat is more common when the target is an Afghan political figure. Roadside IEDs have been detonated when UN vehicles pass by, causing casualties. Attacks on UN vehicles travelling in Afghanistan, by armed groups, are always a threat. Each of the above threat's risks causing tragic casualties for UNDP staff that subsequently risks the possible suspension of UNDP Project activities, the closure of premises and the relocation of UNDP contract holders.

D.2 Security Risk Mitigation:

Project offices are situated within secure UNAMA and UNA compounds, where resources have been pooled to provide guarded gates and secure access avenues, and where armed personnel provide a high degree of compound protection. The Project offices are in cities and towns where the DfA has taken measures to safeguard the UN compounds, and the UN vehicles entering and exiting them. The Project will submit detailed mission plans to UNDSS for approval, whenever the mission travels outside of the prescribed security zone desirable. Paying for de facto armed escorts by police cars for UNDP vehicles when travelling outside the security zones will remain a necessary cost of doing business. UNDP Project and CO staff are required to take security training, through online courses before arrival in the field with more extensive security training (three-day SSAFE - Safe and Secure Approaches in Field Environments) course and one day AST (Afghanistan Specific Training) provided by UNDSS (United Nations Department of Safety and Security) and UNDP security offices, which are mandatory for all UN and UNDP staff that arrive in the country.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

D.3 Political Threats and Risks:

As this Project document is written, in January 2023, the UN and international donor community have not recognized the current *de facto* authorities (DfA), and the traditional agreements between the UN and a member state host government, in the case of Afghanistan, are indistinct and tenuous. The DfA have threatened Afghan female employees of the national and international NGO community if they continue to work, which has caused protests from the international community and the possibility that many NGOs and INGOs will feel compelled to suspend their work in the country. As INGOs form the largest part of the Project's responsible parties (RPs) the closure of any significant RP presence puts at risk the delivery of the Project's interventions and the delivery of its activities to the beneficiary communities.

The potential for unforeseen political threats to the UN presence in Afghanistan remains; however, as the trajectory of political developments is beyond the scope of this document to predict, any assessment of their associated risks to the Project is very limited.

At the political level, seasoned observers have expressed the hypothesis that the DfA will not allow a complete break with the UN and its agencies and programmes, for fear of putting at great risk the DfA's own position and its continued ability to rule. Discussions continue regularly between the UNAMA, O/SRSG, O/DSRSG/RC/HC and the DfA, on reversing the recent edicts adversely impacting the status of Afghan women, which represents a key stumbling block to normalizing the relationship with the UN and international community, and the DfA.

At the field level, it is reported that the DfA are increasingly assertive in its efforts to bring the UN agencies and INGO programmes under its control. Not all these efforts have appeared negatively to field personnel, as being of a purely self-serving nature. On a positive note, there have been anecdotes reported of DfA technocrats requesting adjustments to programmes for what were perceived as having behind them sound and justifiable technical reasons.

The DfA have threated women employees of national and INGOs, and barred their access to their jobs, and may threaten in some provinces, women seeking meetings with the Project staff. Any threats of this nature will be reported to the UNDP Resident Representative (RR) or his/her designated officer immediately, who will advise the Project on the required course of action.

UNDP Project staff will follow the directives of the UN Secretary-General and his Special Representative, as communicated to them by the UNDP Resident Representative, and work with the assurance that the privileges and immunities of UNDP apply to them. The risk of future confrontations between UNDP Project staff and the DfA is mitigated as communications with DfA are made indirectly through the RPs, who currently perform the additional role of serving as an indispensable buffer between the DfA and the UNDP Project personnel.

D.4. Reputational Risks:

Should RPs or other contractors to the Project, not deliver adequately in the provinces on the funds entrusted to RPs by the Project or should any misuse of the funding by the RPs be discovered, then this could generate questions by stakeholders on the capacity of UNDP as custodian of donor funding.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

Should not enough competent RPs step up to bid for contract awards to deliver the priority activities as outlined by the eight regional offices and planning instruments and should no alternatively stream of delivery be identified to substitute for the RPs, this could negatively impact the reputation of the Project as having the wherewithal to deliver funds entrusted to it.

To prevent the above risks to the reputation of the Project and to that of UNDP, the Project management will undertake in the early months of Year One, a determined scrutiny of the past delivery performance of all RPs that have to date been contracted during Phase One. Findings from this study will be used to guide the awards of future UNDP contracts to RPs.

The Project, under the guidance of the UNDP Country Office (CO), is reviewing its M&E procedures and capacities intending to strengthen these for Phase Two. In parallel, the Project will identify procurement processes, to identify how it can directly contract activities with local contractors, whenever RPs are not identified to implement critical activities promptly, or whenever procurements are time sensitive and require rapid delivery and fast-tracking procedures and recruitments of vacant Project staff positions.

Reputational risks will be mitigated by the engagement of the Project staff, from the Regional Offices, with robust support from technical experts and operational staff of the PMU, to engage in diligent M&E of contracted activities, and to shore up the M&E processes in all regions, by the proactive undertaking of monitoring field missions whenever security constraints allow. The staffing table of the Project has sufficient scope in its breadth and depth, for Project staff to fill in, as necessary, for vacant staff positions that have not been filled, or when staff are absent, on leave or mission, or otherwise away from their duty station, both to allow adequate monitoring and evaluation (M&E) as well as to ensure technically sound activities with accurate bills of quantities and specifications, are designed in all Project interventions and their contracts with RPs.

Compliance with UNDP's Rules and Procedures, together with continual M&E by the Project staff and a proactive risk management approach, will be of paramount importance in eliminating potential threats associated with internal or external misconduct/malfeasance, waste and misuse of funds by RPs, which pose reputational risks to UNDP.

The reputational risks can be derived from the wrongdoing and unethical behaviours towards the beneficiaries by UNDP staff/personnel/contractual service personnel, and responsible party staff. This includes but is not limited to lack of accurate knowledge on the standard code of conduct when working for UNDP/implementing projects for UNDP, lack of knowledge by the beneficiaries about their rights and power to provide feedback, lack of feedback providing system, which is not user-friendly, and lack of support mechanism to mitigate risk for (sexual exploitation and abuse) SEA victims.

(For a more detailed breakdown of the risks faced by the Project, and risk mitigation strategies and measures, with security and political risks, and where reputational risks are divided into fiduciary risks, organizational risks, operational risks, and social and environmental risks, See, Annex 4, Project Risk Log).

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

D.5. Social and Environmental Risks:

In compliance with UNDP corporate Social Environmental Safeguards (SES) policy applicable for a development project, the project will regularly screen social and environmental risks from the design stage based on lessons learnt from Phase I with additional assessments and mitigation of any significant social and environmental, and occupational health and safety (OHS) risks and impacts leveraging the mechanisms[29] already created during the Phase I. Potentially adverse gender and social impacts related to project activities will be identified, and measures introduced to reduce gender-based violence, gender-based discrimination, disability, sexual exploitation and the abuse of men, women, girls, and boys. Potential risks to full participation and stakeholder engagement will be addressed by UNDP's Stakeholder Engagement (SE) plans with formal and confidential Complaints Handling Mechanism (CHM).

In order to mitigate the risk, active monitoring will be conducted both on the policy level and social and environmental hazards, and the PMU will carefully implement gender equality and women empowerment approaches and tools for accessing women into technical and financial support by adhering to Islamic principles such as the Maharam policy, segregation policy etc.

The project with partners will develop steps for implementation of activities on women empowerment in line with Islamic values. In order to mitigate the risk, active monitoring will be conducted both on the policy level and social risks, and the results of the risk assessment will be recorded. The female entrepreneurs covered within several capacity-building activities and previously supported with small grants will be involved in providing training for women. The project will explore opportunities for conducting mobile-based/community-based and home-based business training for women. All segregation soft infrastructure facilities will be provided for the capacity building training, i.e., curtains and separate venues for women provided by the implementing partner. Women trainers will be engaged in delivering the training to the women entrepreneurs and community-based vocational training. Contingency planning will be considered for women empowerment-related activities. i.e., online training modality would be considered. For this measure, facilities such as internet will be provided to the beneficiaries to continue home-based training.

E. STAKEHOLDER ENGAGEMENT

E.1 National Stakeholders

Key national stakeholders that are the direct target beneficiaries of the Project's interventions, encompass the communities of Afghanistan in all 34 provinces and in as many of the 400+ districts that can be addressed during the three-year duration of Phase Two. Adequate attention will be given to women and girls, considering the current discriminatory environments where women and girls are disproportionately lagging in each sector. As gender norms require time to change, culture affects women's meaningful participation in many development projects, such as agricultural production, control over resources, and infrastructure-related projects. Women, persons with disabilities, individuals from ethnic minorities, youth, women who head households, and adult women will be prioritized. To ensure women's inclusion and safety, their Mahram will also be part of the programme. IDPs and returnees also have the chance of being systematically

[29] ABADEI GRM

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

discriminated against. Hence, they will be supported to be an integral part of the community programme. NGOs, and CSOs, who work for women and who support persons with disabilities and ethnic minorities will be partnered to ensure the most marginalized and vulnerable groups have been included. In addition, the Afghan business community, MSMEs, AWCCI, and farmers, women's business and farming organizations, NGOs, CSOs, CBOs and other women's empowerment advocacy groups, women- owned businesses and producers of agriculture products, the trucking and public transport sector, operators and users of health posts and water facilities, operators and users of the waste management and sanitation companies, and communities facing climate and disaster risks, IDPs, community leaders and CDCs.

As set out previously, the Project will engage in consultations with provincial and district leaders, e.g., Community Development Committees (CDCs), business groups, and women's organizations, to articulate territorial development plans and social cohesion strategies that present an overview of the territorial structures (cultural, social, economic, infrastructure etc) and list of specific priority interventions to be achieved in each year of the three-year Project cycle. There may be occasions when the Project will need to leverage the Responsible Parties' access to provinces, to gain information from the communities on their priority needs.

It will be important for RPs to understand that ABADEI II is not seeking "beneficiary lists" for cash for work in its new Phase Two, instead, the Project would benefit from the information that will allow Area Managers to identify priority needs in the sector and thematic areas of its focus, to articulate the territorial development plans and social cohesion strategies that will form the foundation for all interventions in each province. The responsibility for developing the draft and final version of the social cohesion strategies will rest with the Area Managers, and how information is gathered will vary from province to province.

The territorial development plans will be used to inform all stakeholders.

E.2. International Stakeholders

The United Nations entities working in Afghanistan, Office of the Special Representative of the Secretary-General (O/SRSG), Deputy Special Representative of the Secretary- General (O/DSRSG), Resident Coordinator (RC) Humanitarian Coordinator (HC), UNAMA, UNAs), IFI (international financial institutions) and donors (such as EU, Government of Japan) are key international stakeholders of the Project, as are the international donor community, the World Bank Group and other international financial institutions (IFIs) and development banks. These international stakeholders will be made aware of the progress of the Project interventions and may be invited by the Project Manager, through the Office of the UNDP Resident Representative, to send observers to participate at Project Board members, or to attend Project Board meetings when selected by the UNDP Resident Representative.

The Territorial Development Plans and social cohesion strategies, once approved by the Project Board for implementation, will be shared with international stakeholders, including the regional offices of UNAMA, UNAs and INGOs, to allow them to be fully appraised of the Project's planned interventions in the provinces. In the case of the UNAs and INGOs, the sharing of the Territorial Development Plans will allow these agencies to plan corresponding interventions of their own, to maximize impact on a target community, to avoid duplicating efforts, or bid for contract awards, to implement the interventions as RPs of the Project.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

E.3. South-South and Triangular Cooperation (SSC/TrC)

The Project will support Afghan businesses, farmers, and women-owned enterprises, to expand their marketing opportunities for Afghan- produced goods and agriculture products in neighbouring countries and beyond. To this end, a study will be made by the Project, in consultation with Afghan stakeholders, of how to stimulate demand for Afghan products in neighbouring countries (Iran, Turkmenistan, Uzbekistan, Tajikistan, China, Pakistan, and India) will be launched, followed by an exploration of how to better market Afghan products in Russia, the European Union (EU), China, Japan, the Americas, Australia and elsewhere.

E.4. Knowledge

The project will produce a series of publications/briefing notes and guidance notes drawing on lessons learned for each of the four outputs of the project. These publications/guidance notes will capture how UNDP project has strengthened climate resilience throughout region, province and district and up to the community settlement. UNDP will also work with its Communications Specialist to enhance the visibility of all knowledge products and lessons learned generated by the project so others can benefit.

The Project's knowledge, good practices and lessons will be captured and assessed regularly by the project team in place-based regional offices and thematic orientations. In addition, data actively sourced from other projects and partners will be verified by community teams before being integrated with the planned interventions. The project will develop and disseminate knowledge products for use by the project's beneficiaries (CSOs, private sector organizations, MSMEs, youth groups, women's groups etc.)

This knowledge will be shared through UNDP publications issued by the project (including UNDP's annual reports, progress reports, sector-specific reports and the quarterly reports of the responsible parties). The lessons learnt and success stories will be shared among the duty-bearers and communities in Afghanistan, including development partners.

E.5. SUSTAINABILITY AND SCALING-UP

The project will work closely with those service provider agencies covering health, social services, vocational training, employment training, essential basic services, and those supporting returnees and IDPs or women-specific services, to improve sustainability and provide a scaling-up mechanism. The community-based protection network (CBPN) will be linked with service providers, "safe spaces", and agencies through mobile applications so that "referral pathways" can be improved. Given the current political system in Afghanistan, the civil society engagement space and the level of civic and community ownership will be strengthened by this project. The project will also collaborate with the Humanitarian Cluster and the Protection Cluster and their partners in scaling up the efforts where the interventions are linked with IDPs and returnees. The project will facilitate the interface between district-level service providers and community-based institutions to strengthen the referral pathways. Linking livelihood opportunities with protection service providers will ensure the potential to scale up through the cluster mechanism to support the most vulnerable communities and at-risk-groups affected by fragility and hostilities. The networking through these clusters will enhance UNDP's "human security" approach for upcoming interventions and help to scale up any future project(s). Interventions will adopt a value chain approach by promoting and linking together local producers, market actors, private sectors, and economic institutions. The project will strengthen value chains and sustain

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

MSMEs by building horizontal and vertical linkages. For example, MSMEs and micro-businesses have a significant advantage over larger organisations in addressing sustainability issues - their size means they can react very quickly to changes in the business environment. The project will also contribute to building capacities of local structures that will continue to function after the project ends by other development partners.

E.6. Communication

Given the current security environment in Afghanistan, UNDP will regularly discuss the project with donors, UNDSS, and communication experts in balancing any security concerns with the need to ensure that the support received from donors is as visible as possible and is represented in a mutually acceptable manner in significant activities and advocacy events. For example, UNDP's communication team will include recognition of the support received from donors in all publications and in all printed, electronic and display materials produced by the project, as well as ensure that donors' contributions are acknowledged properly in any communications by project partners (with the consent of the donor). UNDP will carry out specific outreach, sensitization and public information campaigns for specific activities and the ABADEI communication strategy is in place to address communication needs for the project.

PROJECT MANAGEMENT

A. COST EFFICIENCY AND EFFECTIVENESS

Business-oriented solutions and mobilizing different stakeholders' and utilizing the resources in an "integrated" way will be key for the project to maximize efficiency and effectiveness and ensure sustainability. The project is designed to support (introducing new business-oriented, innovative and multistakeholder approaches to) the implementation of ABADEI 2.0. Under Direct Implementation Modality (DIM), cost efficiency and effectiveness in the management of this project are maximized through the following elements:

- **Acquiring services through procurement modality**: The project will achieve cost efficiency through an effective procurement strategy in a potential collaboration with agencies and expert resources to consider economies of scale and quality standards. This is likely to reduce transaction and administrative costs. ABADEI will be implemented with eight regional offices that are already set up and will enable cost-sharing arrangements with other projects. This project will optimize available capacity and resources in IRMU (including DEU) and Policy Units that are housed with UNDP Afghanistan CO as DEU facilitate programmatic approach with responsible parties and IRMU check on partner and risk verifications. Further, early procurement planning, and consolidation of procurement requests will be considered in the implementation.
- **Working through experienced Responsible Parties**: Selection of RPs would be selected as Responsible Parties will be based on their prior proven experience in managing projects for UNDP/other UN AFPs and/or expertise in the area they would be contracted and will follow UNDP's rules and procedures for the selection of RPs Partner's management systems should be HACT compliant. Responsible Parties will be engaged in the Project after selection through a competitive process or an existing roster. UNDP will maintain close interactions with all RPs in Afghanistan through the project management unit, and in the

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

field, through the regional teams, to maintain quality in project implementation and guarantee value for money.

- **Joint Operation**: ABADEI will use joint operations when available such as with other UN partners to increase effectiveness and efficiency, for example, in monitoring or procurement, security services, and long-term agreements for money service provision with other UN partners to increase effectiveness and efficiency.
- **Building partnerships with financial and technical development partners**: UNDP will coordinate closely with relevant financial institutions, project donors and other international partners and UN agencies implementing projects in the same geographical and thematic areas.
- **Digital Solutions:** The use of electronic platforms for cash transfer to beneficiaries is expected to yield a minimum of 3.8 percent cash transfer fee savings that would otherwise be incurred when using the traditional banking network. For the potential implementation partners, the savings could be much more significant, enabling the freeing up of additional funds for the programmatic implementation.
- **Harmonised Due Diligence of new and existing responsible parties on the ground**: UNDP uses the harmonized approach when working with agencies / NGOs who have already undergone due diligence from other UN entities and are considered low risk. Further, UNDP uses integrated operational approaches in digital payments through a cash voucher working group. UNDP uses the harmonized approach when working with agencies / NGOs who have already undergone due diligence from other UN entities and are considered low risk. Further, UNDP uses integrated operational approaches in digital payments through a cash voucher working group.

The project will be implemented within a broader programmatic framework proven UN approach, notably implementing livelihoods, local economic development, disaster-risk reduction (DRR), social cohesion, conflict resolution, and disaster response, thereby making the ABADEI interventions more coordinated among UN agencies.

B. PROJECT MANAGEMENT

The Project will be implemented by the UNDP Afghanistan Country Office, under the direct implementation modality, under the overall direction of a Programme Manager, supported by a Project Management Unit (ABADEI-PMU) led by a Project Management Specialist, through the UNDP's eight regional offices, who in turn are led by eight Area Managers, supported by Regional Offices Teams. The eight Regional Offices locations appear below in bold, along with the provinces under their area of responsibility. When provincial capital cities' names differ from the name of their province, they appear in parathesis e.g., the capital of Nangarhar (Jalalabad), where the Eastern Regional office is located.

1.	**Central Region**	Kabul, Kapisa, Parwan, Panjsher, Wardak
2.	**Central Highlands Region**	Bamyan, Daikundi, Ghor
3.	**Western Region**	Herat, Badghis, Farah
4.	**Northern Region**	Balkh (Mazar e Sharif), Faryab, Jawzjan, Samangan, Sari Pul
5.	**North-Eastern Region**	Kunduz, Badakhshan, Baghlan, Takhar
6.	**Eastern Region**	Nangahar (Jalalabad), Kunar, Laghman, Nuristan
7.	**South-Eastern Region**	Paktya (Gardez), Ghazni, Khost, Logar, Paktika
8.	**Southern Region**	Kandahar, Helmand, Nimroz, Uruzghan, Zabul

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

C. RISK MANAGEMENT FRAMEWORK

UNDP has developed an Adaptive Management and Risk Mitigation Strategy to support the delivery of the ABADEI strategic objectives, with a high level of accountability, conflict sensitivity and informed decision-making to maximize impact and effective fund and programme management.

UNDP Afghanistan Adaptive Management and Risk Mitigation Strategy is compliant with the corporate ERM, AML/CFT Policy and Accountability framework, and applies the following risk management principles:

- No support can be provided directly or indirectly to the DfA, whether in Kabul or at the local level.
- Support has to be implemented free from the involvement of the DfA concerning (hiring/recruitment) policy, implementation and management. Additionally, the DfA will not influence project decisions about the selection of beneficiaries, project locations or project partners. This also means that female staff should be able to continue to work.
- No support will be provided to structures that institutionalize discrimination or violate human rights.
- At a minimum, service providers should ensure that services are accessible to girls and women in an equal fashion.

The strategy is anchored in a risk framework based on a 'three lines of defence' model adapted from the UNDP Enterprise Risk Management policy and the ISO 31000 2018 risk management approach: Programme and operations functions that own and manage risks; Functions that oversee and/or specialize in risk management and compliance; Functions that provide independent assurance, evaluation, audit and investigation.

The IRMU brings the additional capacity, expertise and tools to continuously review, analyze and mitigate risks involved in implementing the tailored area-based projects. The IRMU undertake proactive risk assessments of vendors and implementing partners, including vetting of the entities, their key personnel and board members.

During the design of the ABADEI Strategy, UNDP conducted a comprehensive risk analysis guided by knowledge of its staff on the ground in the different regions, the review of socio-economic and conflict trends and the development of likely scenarios for the coming 6-12 months. It constitutes a starting point for risk-informed programme planning and implementation and will ensure a consistent 'Do No Harm' approach to ABADEI interventions, as well as proactively applying the UN's organizational standards and principles. The I-RMU will monitor risks at three levels:

- Organizational level (high-level reputational and political risks as well as regional geopolitical and programmatic risks)
- Country-level (political, reputational, security, programmatic and operational risks)
- Local level (political, security, programmatic and operational risks). As an important feature, it will connect risk levels and risk escalation, using adaptive management principles and through the continuous analysis of developments and their implications on the efforts on the ground.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

In addition, a UN Due Diligence Working Group has been established to facilitate joint risk management related to ABADEI joint programming and implementation. The working group aims to tailor risk frameworks for ABADEI joint programmes, bring together participating UN organizations to provide risk management solutions on common risks and develop a coherent response, identifying opportunities for pooling tools and resources and developing joint mechanisms where possible. The members of the group will escalate risks and measures within their organization or refer them to the relevant ABADEI programme governance mechanism.

D. RISK REGISTER Annex 4

#	Description	Risk Category	Impact & Likelihood = Risk Level	Risk Treatment / Mitigation Measures	Risk Owner
1	**Event:** The security of the project staff (national and international) may be compromised **Cause:** There is a risk that the de-facto authorities (DFA) or other insurgency groups may target UN premises, staff, or project locations and create challenges for the project staff to operate. **Impact:** Human lives are in danger or may be lost. There will be limitations in implementing ABADEI project; project objectives may not be met; the reputation of UNDP may be damaged, and the delivery target may not be achieved as planned.	Safety and Security Subcategory: Manmade Hazards	L = 3 I = 3 Risk Level: moderate	• Under UNCT, Country Office (CO), will advocate with de-facto administration about the UNDP programme, type of interventions, and protection of IPs and UNDP local/international staff. As this project is related to service delivery (health, community-based vocational education, and MSME), livelihood, disaster risk reduction and social cohesion, UNDP will communicate the project interventions to the MoF at the central level. • The security and conflict situation will be continuously monitored, with (at least) a monthly review of operating modalities and weekly reports from the region. This will be done in close collaboration with UNAMA and UNCT. The ABADEI coordination structure is in place in eight regions. The safety and security of UNDP staff in accessing project locations will be monitored and assured by UNDSS. • Regional offices will be upgraded and equipped with the required technical and human resources. On the other hand, coordination will be strengthened at the regional level with the de-facto authorities. • UNDP, through the area-based program, is establishing a dynamic risk management mechanism which will	UNDP Security and UNDSS

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

				implement risk mitigation strategies for all activities and be continuously reviewed and updated. This will include engagement with local authorities (in accordance with UN rules of engagement) to ensure their agreement to activities and that a structure is in place to ensure UNDP has a license to operate. • Regular communication and coordination protocols with local, regional, and central DFA authorities will be established. • The security and conflict situation will be continuously monitored, with (at least) a monthly review of operating modalities. This will be done in close collaboration with UNAMA and UNCT. The ABADEI coordination structure is in place in eight regions. The safety and security of UNDP staff in accessing project locations will be monitored and assured by UNDSS. • The international staff for ABADEI has been reduced to five at a time on a rotational basis in Kabul. In contrast, ABADEI national project staff are allowed only five persons at a time. For the ABADEI program, less than 25 percent will physically appear for work, while others will engage remotely to minimize security risks.	
3	**Event:** Because of the de-facto authority (DFA) with no clear rules and regulations, the security of the IPs and beneficiaries might be compromised. **Cause:** Since the de-facto authorities will be asking to share the IPs and beneficiaries' data, it will result in putting the privacy of IPs and beneficiaries being compromised.	Safety and Security Subcategory: Manmade Hazards	L = 3 I = 3 Risk Level = Moderate	• Communications that demonstrate transparency and pre-empt misperceptions and ill-founded accusations will be supported proactively and corporately. • A crisis communication team will be put in place to address any potential politicization and use of programme interventions by local and central political forces. • A data-driven mechanism that will guide targeting and allocations (ref Yemen: “Distress Index”) will be established. • UNDP data privacy policy will be applied and no data of beneficiaries	UNDP Security and UNDSS /RR/DSRR (P) Project Manager CO/ Regional Offices

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

	Impact: Lack of IPs and beneficiaries' trust in UNDP interventions will result in lack/delay in delivery or loss of lives			with descriptive details will be shared with the DFA and their confidentially will not be compromised • UNDP will closely collaborate with communities and engage local authorities as appropriate through ongoing meetings and visits to monitor the security situation and utmost attention will be paid to the safety of women, and female beneficiaries engaged in UNDP's interventions, which is a priority area for the dynamic risk management mechanism.	
4	**Event:** Possible project politicization. **Cause:** Due to the pressure from the DFA programme, interventions may be politicized and used to support local and central political forces. **Impact:** Lack or slow programme and projects activities delivery; UNDP's reputation may be damaged, having an impact on resource mobilisation.	Political Subcategory: Government Commitment	L = 2 I = 2 Risk Level = Low	Regular communication with the DFAs to raise their awareness about the UNDP programme of work and its criticality for maintaining the country's economic stability and meeting the needs of the people in need. A crisis communication team will be put in place to address any potential politicization and use of programme interventions by local and central political forces. A communication channel will be established with the senior officials of the DfA at central and provincial levels to get in touch directly in case the project staff feels any pressure in the field from the local DFA forces. Through the area-based program, UNDP establishes a dynamic risk management mechanism that will implement risk mitigation strategies for all activities and be continuously reviewed and updated. This will include engagement with local authorities (in accordance with UN rules of engagement) to ensure their agreement to ABADEI activities are in line with the UN human rights due diligence framework, and beneficiaries are selected	Project Manager CO/ Regional Area Managers

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

				only from communities, not with any members connected to the DFA forces.	
5	**Event:** UNDP may not be able to fully adhere to the "do not harm" approach. **Cause:** Due to the quick and unexpected transition, UNDP may not be able to guarantee the "do no harm (DNH) " approach. **Impact:** Because of the no guarantee of the "do no harm" approach, UNDP programmes may trigger human rights violations and conflict.	Social and Environmental Subcategory: Human Rights and CHSS	I = 2 L = 2 Risk Level = Low	Social and Environment screening guidelines/checklists and SOPs will be fully adopted and strictly followed to ensure the "do no harm" approach and conflict sensitivity (CS) approach. The CO will gradually build confidence and discuss sensitive topics (e.g., dialogues, discussions and conversations offered to the Taliban middle management that addresses human rights (HR) considerations). A continuous “dynamic impact, conflict & risk monitoring capacity” and adaptive management processes will be established. Activities which have the potential to capacitate or trigger human rights violations will be excluded. Risk will be jointly identified and endorsed, and the burden will be shared with key partners (donors). To mitigate the risk, the project will ensure that the global safety and security standards are in place in project sites by allocating the necessary amount in procurement plans. In addition to that, the skilled and unskilled labour working on the project will be trained on basic safety issues and observing the safety protocols will be considered as a must for all skilled and unskilled labour before they initiate their work.	Project Manager / Area Managers
6	**Event:** It is possible that UNDP may not respond to the populations in need. **Cause:** Due to the restrictions put in place	Social and Environmental	I = 2 L = 2 Risk Level = Low	A continuous “dynamic impact, conflict &risk monitoring capacity” and adaptive management processes will be established that will help identify the people most in	CO, Project Manager and IRMU

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

	by the DFA, UNDP interventions may not be able to reach those most in need, especially women, girls, and youth. **Impact:** The project may fail to meet its objectives; reputational risk.	Subcategory: Gender equality and women's empowerment		need and prioritize related interventions. Regular communication protocol and hotline with local, regional, and central authorities will be established. The CO will also gradually build confidence and discuss sensitive topics (e.g., women's participation in the economy) with middle and low-order officials of DFA. Regular communication with local, regional, and central authorities will be established. The CO will also gradually build confidence and discuss sensitive topics (e.g., women's participation in the economy and c) with, middle and low-order officials of DFA. Project activities will be firmly grounded in conflict and gender analysis and risk assessments conducted on the ground and employ conflict-sensitive approaches (including conflict sensitivity training, cultural and religious awareness and providing Islamic ways of segregation materials (e.g., curtains, separate units for any training, mahram policies) for implementing partners Regular communication with local, regional, and central authorities will be established.	
7	**Event**: Climate-induced natural disasters may happen. **Cause:** The project may not be able to allocate resources to respond to the affected people on time. **Impact**: ABADEI project intervention may not	Environmental Subcategory: Climate change and disaster	I = 3 L = 3 Risk Level =moderate	Regular monitoring visits and follow-ups will be conducted by the regional offices and the CO to ensure the interventions comply with environmentally friendly approaches and the lowest possible carbon emission technologies (green technology) are used.	Project Manager/ SES Specialist

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

	respond to climate-related disaster risk reduction.			Under the UNCT, in coordination with other UN agencies, ABADEI programme will channel its resources to collectively address any potential natural disaster. The ABADEI Programme will have some emergency budget, which could be utilised in case of any emergency situations, including recovery from any natural disaster.	
	Event: The female employees of UNDP and its partners and beneficiaries implementing the project/ benefitting from the project activities may not be able to go to work/participate **Cause:** If the DfA strictly follows the recent decree and extends the bans to the private sector, UN agencies and women's freedom of mobility. **Impact**: Because of the negative impacts of the ban on women's work with national and international NGOs, the project will not be able to implement some of the activities and may not be able to meet the delivery target or beneficiaries may not be able to participate in capacity building events	Social and Environmental **Subcategory**: Human Rights and Gender	I = 3 L =4 Risk Level: Moderate	The project expects to implement home-based, community-based vocational training for women, which will comply with local social norms, customs and religious concepts and adhere to the Islamic behavioral standards for men and women. UN female staff will adhere to Maharam policy and UNDP will provide Maharm incentives when they travel more than 72 kilometres as per the DfA rule. UNDP implementing partners will apply Maharam incentives in their financial proposal for female staff to Implement activities. The project with partners will develop steps for implementation of activities on women empowerment in line with Islamic values. Women-led MSMEs and all gender-related activities will adhere to Islamic principles. In order to mitigate the risk, active monitoring will be conducted both on the policy level and social risks, and the results of the risk assessment will be recorded. The CO will carefully experiment with women empowerment modality and tools for accessing	Project Manager/ SES/Gender Specialist

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

				women into technical and financial support by adhering to Islamic principles such as Maharam policy, segregation policy etc The female entrepreneurs covered within the several capacity-building activities and previously supported with small grants will be involved in providing training for women. The project will explore opportunities for conducting mobile-based/community-based and home-based business training for women. All segregation soft infrastructure facilities will be provided for the capacity building training, i.e., curtains and separate venues for women provided by the implementing partner. Women trainers will be engaged in delivering the training to the women entrepreneurs and community-based vocational training. Contingency planning will be considered for women empowerment-related activities. i.e., online training modality would be considered. For this measure, facilities such as internet will be provided to the beneficiaries to continue home-based training.	
8	**Event:** Pressure on fiscal sustainability and service delivery by CSOs and NGOs may affect cash availability **Cause:** If the banking system continues to remain weak with a continuous lack of liquidity.	**Subcategory**: Budget availability and cash flow	I = 2 L = 2 Risk Level = Low	Adopt alternative financial systems, digital payment systems and procedures that are independent of the ITA to support humanitarian and development activities and basic services including health.	Project Manager DRRO

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

	Impact: Delayed payment for the vendors and suppliers and RPs within the agreed period				

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

V. Results Framework

- **Intended Outcome as stated in the UNSF (Draft) UNSF Outcome**
- **1:** By the end of 2025, more people in Afghanistan, particularly the most marginalized, can equitably access essential services that meet minimum quality standards.
- **UNSF Outcome 2**: By the end of 2025, more people in Afghanistan will benefit from an increasingly inclusive economy, with greater equality of economic opportunities, jobs, and more resilient livelihoods, increased food production, and improved natural resources management.
- **UNSF Outcome 3:** By the end of 2025, more people in Afghanistan can participate in an increasingly socially cohesive, gender equal, and inclusive society, where the rule of law and human rights are progressively upheld, and more people can participate in governance and decision-making.

TEF Outcome 1: More people in Afghanistan will have benefitted from life-saving humanitarian assistance that enable them to live in safety and dignity [Saving lives]
TEF Outcome 2: Essential services are sustained that address basic human needs for the people in Afghanistan [Saving livelihoods]
TEF Outcome 3: Afghanistan will preserve social investments and community-level systems essential to meeting basic human needs and contributing to resilience, social cohesion, and peaceful coexistence [Strengthening institutions]

Country Programme Results and Resource Framework (RRF):

Outcome indicators as stated in the Country Programme Results and Resources Framework (CPRF), including baseline and targets:
SP Outcome 3: Resilience built to respond to systemic uncertainty and risk Indicative.
CPRF: Outcome 1. Provision of essential services.
Output 1.1: Essential basic services and infrastructure (health, WASH, Solid Waste Management, education etc.) including COVID 19 support enabled and supported.
CPRF Indicator. 111: Number of non-farm infrastructure constructed or rehabilitated (disaggregated by type of infrastructure - including roads, bridges, schools, health facilities, water supply, waste management centres, emergency shelters, flood protection walls etc.); Baseline: 1017, Targets: 429
CPRF Indicator 113: Number of health centers supported with COVID 19 equipment and materials; Baseline:72, Targets:

CPRF Outcome 2: Community Livelihoods and Local Economic Activities
Output 2.1: Households in high poverty, high insecurity areas provided with basic income (TBI)
CPRF Indicator. 211: Number of people benefitting from targeted basic income (TBI) (Disaggregated by age and gender) Baseline: 231,798, Target:
Output 2.2: Local livelihoods and economies sustained through Cash- for-Work and Cash- for- Market.
CPRF Indicator 221: Number of CSOs and communities who received conditional grants for community service management in areas with limited presence of development actors (disaggregated by sector); Baseline:49, Targets:

Output 2.3: Local economic ecosystem enhanced through financial and non-financial support to private sector, access to market and cross border trade.
CPRF Indicator 231 (a): Number of formal and informal businesses who received technical support and/or grants (disaggregated by formal and informal businesses); Baseline: 15691, Targets: 3076
CPRF Indicator 231 (b): Number of women-led businesses receiving technical and/or financial support; Baseline: 14436, Targets: 2356
CPRF Indicator 232: Number of MSMEs and informal businesses supported with investment funds (start- ups, innovative SMEs, youth and women led companies, export companies) Baseline: 2534, Targets: 500

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

CPRF Indicator 235: Number of small and medium trade businesses operating in the cross-border markets (disaggregated by men-owned and women-owned businesses) Baseline: 0, Target : TBA

CPRF Outcome 3: Improved climate smart agriculture, access to renewable energy, and resilience to natural disasters
Output 3.1: Climate smart agriculture promoted to enhance community resilience and food security.
CPRF Indicator 311: Number of farming infrastructure constructed or rehabilitated (disaggregated by type of infrastructure - including irrigation channels, storage facilities etc.); Baseline: 211, Targets: N/A
CPRF Indicator 312: Length of irrigation channels constructed or rehabilitated (in km); Baseline: 221.5, Targets: N/A
CPRF Indicator 313: Number of farmers receiving farming inputs, and assets - (disaggregated by type of inputs - including seeds, tools, fertilizers, equipment, livestock etc.) ON FARM; Baselines: 24105, Target: N/A-
Output 3.2: Access to clean and affordable energy enhanced.
CPRF Indicator 321: Number of basic facilities powered through renewable energy (disaggregated by type of facility); Baseline: 390, Targets: 189
CPRF Indicator 333: Number of businesses powered with renewable energy; Baseline: 192, Targets: N/A
Output 3.3: Community preparedness to disasters and climate risk improved.
CPRF Indicator: 331: Number of communities where early warning systems have been established. Baseline: 129, Targets: N/A
Output 3.4: Natural resources and ecosystem management promoted.
CPRF Indicator 341: Number of communities engaged in managing local ecosystems including watershed management. Baseline: 0, Targets: N/A
CPRF Outcome 4: Community Resilience and Social Cohesion
Output 4.1: Communities for peace and social cohesion reinforced.
CPRF 411: Number of social cohesion interventions supported with LVGs (disaggregated by type) Baseline: 213, Targets: N/A
CPRF 412: Number of former Afghans national police and judiciary women officers supported with alternative livelihood options. Baseline: 0, Targets: N/A
Output 4.2: Gender equality and women's empowerment improved.
CPRF Indicator 423: Number of gender-based violence survivors benefitting from safe houses and safe spaces. Baseline: 0, Targets: N/A
Output 4.3: Rights-based access to justice and human security fostered.
CPRF Indicator 431(a) Number of legal aid cases registered and adjudicated Baseline: 566, Targets: N/A
CPRF Indicator 431 (b) Number of people reached through legal counselling awareness (disaggregated by gender) Baseline: 1226, Targets: N/A
CPRF Indicator 432: Number of local actors and groups (such as Ulama councils, religious scholars) supported to promote positive traditional justice practices Baseline: 34, Targets: N/A
Output 4.4: Community led needs-based local recovery & resilience plans formulated.
CPRF Indicator 441: Number of community groups supported in recovery planning to revitalize services & resilience (such as CDCs, multi stakeholder standing committees) Baseline: 68, Targets: N/A

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

CPRF Indicator 442: Number of community resilience/recovery plans formulated. Baseline: 331, Targets: N/A
Applicable Output(s) from the UNDP Strategic Plan: Outcome 1: Eradicate Poverty in all its forms and dimensions. **Applicable Output(s) from the UNDP Strategic Plan 2022 -2025:** **Signature Solutions: 1 (Poverty and Inequality), 3 (Resilience) and 6 (Gender)** **SP Output 1.3: Access to basic services and financial and non-financial assets and services** improved to support productive capacities for sustainable livelihoods and jobs to achieve prosperity. **SP Indicator 1.3.1**: Number of people accessing basic services (disaggregated by female and male) **SP Outcome 3: Resilience** built to respond to systemic uncertainty and risk Indicative. **SP Output 3.3:** Risk informed and gender-responsive **recovery solutions, including stabilization efforts and mine action,** implemented at regional, national and sub-national levels. **SP Indicator 3.3.1** Number of people benefitting from jobs and improved livelihoods in crisis or post-crisis settings disaggregated by: • Female, Male, Youth, Persons with disabilities, internally displaced populations, Refugees **SP Indicator 3.3.2:** Number of people benefitting from improved infrastructure for recovery in crisis or post-crisis settings disaggregated by: • Female, Male, Youth, Persons with disabilities, internally displaced populations, Refugees • **SP Output 5.1: Energy gap closed** **SP Indicator 5.1.1**: Number of people, who gained access to clean, affordable and sustainable energy (disaggregated by female and male)
Project title and Atlas Project Number: Area-Based Approach to Development Emergency Initiatives in Afghanistan (Phase II)

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

Outputs	Activity Results	Indicators	Baseline (2022) Value (2022)	Target[30]	Year-1	Year-2	Year-3	Source of information/Means of Verification	Data Collection Methods	Risks
Output 1: Essential services improved in the area of infrastructure, agriculture, health, education and energy.	1.1. Essential physical, critical infrastructure constructed, rehabilitated, repaired, equipped and maintained, including infrastructure for water management, transportation, agriculture, health, education, basic services etc.	*1.1.1. Number of Infrastructures constructed/ re constructed/rehabilitated/repaired, equipped,disaggregated by type of infrastructure and location (wellbeing and social environmental safeguard standard met)*	682	2000	429	TBC	TBC	Monthly Reports, Quarterly Reports, Annual Reports, Engineer Reports, Infrastructure Associate Reports, Regional M&E Reports, Filed Visits, RPs/IPs reports	Reports from Area Managers, M&E Regional, Engineer, and/or Infrastructure Associates, AIMS and TPMA and SES compliance monitoring reports Transactional Tracking, social safety analysis report	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination
		1.1.2. Number of households benefitting from improved infrastructure (including women-headed immunocompromised and or disabled households)	495,673	1,200,000	300,000	TBC	TBC	Monthly Reports, Quarterly Reports, Gender Specialist Reports, Infrastructure Associate Reports, Regional M&E Reports, Filed Visits, GRM and SES reports, Ps/IPs reports, Heath facilities	Reports from Area Managers, M&E Regional, AIMS and TPMA, FGD, Direct Observation, Field visits and social safety analysis report,	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination

[30] The targets are additional to the baseline.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

								inspected in the reporting period.		
	1.2: Provision of improved essential health services (including women and girls accessing health care)	*1.2.1 (a): Number of health care facilities equipped with materials and medical equipment*	53	300	100	TBC	TBC	Monthly Reports, Quarterly Reports, Health Specialist Reports, Gender Mainstreaming Reports, WASH Specialist Reports or data, Public Infrastructure Associate Reports, Regional M&E Reports, Filed Visits, SES compliance monitoring reports, WHO health sector report, UNDP's policy unit report, Heath facilities inspected in the reporting period.	Area Managers field visits and progress reports M&E Regional officers mission reports, AIMS and TPMA Document with instructions for implementation of monitoring mechanism Transactional Tracking,	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

		1.2.1 (b). Number of individuals benefitting from medical materials and health care services, disaggregated by sex, age and location	285,671	1,220,406	400,000	TBC	TBC	Monthly Reports, Quarterly Reports, Health Specialist Reports, Gender Mainstreaming Reports, WASH Specialist Reports or data, Public Infrastructure Associate Reports, Regional M&E Reports, Field visits, SES compliance monitoring reports, WHO health sector report, UNDP's policy unit report	, Area Managers field visits and progress reports, M&E Regional officers' mission, reports AIMS and TPMA Records and Documents from UNDP supported hospitals /	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination
	1.3. Provision of essential education services (Including gender-integrated culturally sensitive TVET)	*1.3.1*. Number of individuals benefitting from project-supported TVET and skilled education programmes, disaggregated by sex, age, location and duration	5,654	14,654	5,000	TBC	TBC	Monthly Reports, Quarterly Reports, Gender Mainstreaming Specialist Reports, Regional M&E Reports, Filed Visits, SES compliance monitoring reports, UN Women reports, training score cards for TVET	Area Managers field visits and progress reports, M&E Regional officers' mission reports, AIMS and TPMA, Beneficiary stories	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

	1.4: Provision of clean, renewable and alternate energy services, technologies and applications supported and sustained	*1.4.1: Number of basic facilities powered through renewable energy, disaggregated by type of facility (e.g health, education, sanitation) and location*	38	1,000	400	TBC	TBC	Monthly Reports, Quarterly Reports, Renewable Energy Specialist Reports, Gender Specialist Reports, Public Infrastructure Associate, Regional M&E Reports, Filed Visits, SES compliance monitoring reports	Area Managers field visits and progress reports, M&E Regional officers' mission, reports AIMS data collection and TPMA monitoring	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination
		1.4.2. Number of households who gained access to clean and affordable energy (including women-headed immunocompromised and or disabled households)	67,074	150,000	50,000	TBC	TBC	Monthly Reports, Quarterly Reports, Renewable Energy Specialist Reports, Gender Specialist Reports, Public Infrastructure Associate, Regional M&E Reports, Filed Visits, SES compliance monitoring reports,	Area Managers field visits and progress reports, M&E Regional officers' mission, reports, AIMS and TPMA monitoring, field monitoring, energy related survey for UNDP supported work	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

Output 2: **Local economies improved through gender responsive community - based livelihoods**	2.1 Households in high- poverty and high insecurity areas provided with Unconditional Cash Transfer (UCT) / Temporary Basic Income (TBI)	*2.1.1 Number of households provided with unconditional cash transfer (UCT) to meet basic needs, disaggregated by female-headed households and households with people with disabilities*	20,504	30,000	10,000	TBC	TBC	Monthly Reports, Quarterly Reports, Livelihood Specialist Reports, Community Resilience Specialist Reports, Gender Specialist Report, Regional M&E Reports, Filed Visits, SES compliance monitoring reports	Area Managers field visits and progress reports, M&E Regional officers' mission, reports, Livelihood Specialist, AIMS and TPMA, Cash-based Intervention Specialist Transactional Tracking of money service providers Lists of participants	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordnation
	2.2: Local- level livelihoods and economies sustained through Cash- for -Work (CfW) including women and girls, vulnerable groups accessing CFW)	2.2.1. Number of labourers benefitting from cash- for- work (CfW) schemes (wellbeing and social environmental safeguard standard met)	204,599	500,000	150,000	TBC	TBC	Monthly Reports, Quarterly Reports, Cash-based Interventions Specialist Reports, Livelihood Specialist Reports, Community Resilience Specialist Reports, Gender Specialist Reports, Regional M&E Reports, Filed Visits	Area Managers field visits and progress reports, M&E Regional officers' mission, reports, Livelihood Specialist, AIMS and TPMA, Cash-based Intervention Specialist Transactional Tracking Lists of participants	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

	2.3. Local private sector development through technical and financial support to informal and formal businesses, including assisting micro, small and medium-sized enterprises (MSMEs) to access and/or expand to new market areas, support to local traders, to women-led businesses and community- led social enterprises (Cash for Markets-CfM)	*2.3.1 Number of MSMEs benefitting from technical and financial support, disaggregated by female- led MSMEs (including minority under represented women, women-at-risk, GBV_victims, and persons with disabilities)*	34,000	90,000	30,000	TBC	TBC	Monthly Reports, Quarterly Reports, MSME Specialist Reports, Community Resilience Specialist Reports, Gender Specialist Reports, Regional M&E Reports, Filed Visits	Area Managers field visits and progress reports, M&E Regional officers' mission, reports, Livelihood Specialist, AIMS and TPMA, Cash-based Intervention Specialist Transactional Tracking/ Community -based monitoring,	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

	2.4. Cross-border trade and access to the market supported (including women-led-businesses)	*2.4.1. Number of cross border trades established by ABADEI supported SMEs/MSME (disaggregated by women/men-led SMEs)*	0	2	TBC	TBC	TBC	Monthly Reports, Quarterly Reports, Cash-based Interventions Specialist Reports, Livelihood Specialist Reports, Community Resilience Specialist Reports, Gender Specialist Reports, Regional M&E Reports, Filed Visits	Area Managers field visits and progress reports, M&E Regional officers' mission, reports, Livelihood Specialist, AIMS and TPMA Lists of participants	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination
	2.5. Access to finance and Digital Solutions supported and sustained.	*2.5.1: Number of business operationalized/ extended their scope of business and continue operations for more than six months beyond ABADEI support*	0	25,000	TBC	TBC	TBC	Monthly Reports, Quarterly Reports, Cash-based Interventions Specialist Reports, Livelihood Specialist Reports, Community Resilience Specialist Reports, Gender Specialist Reports, Regional M&E Reports, Filed Visits	Area Managers field visits and progress reports, M&E Regional officers' mission, reports, Livelihood Specialist, AIMS and TPMA, Banking consultant Transactional Tracking	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination
		2.5.2: Number of digital solutions established to support MSMEs. (by location)	1	1	TBC	TBC	TBC	Monthly Reports, Quarterly Reports, Cash-based Interventions Specialist Reports, Livelihood Specialist Reports, Community Resilience Specialist Reports,	Area Managers field visits and progress reports, M&E Regional officers' mission, reports, Livelihood Specialist, AIMS and TPMA, Banking consultant	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

								Gender Specialist Reports, Regional M&E Reports, Filed Visits, number of enrolled people /accesses points on the digital dashboard		
Output 3: Local communities' resilience capacity enhanced to better respond and adapt to the disaster and climate -induced risks.	3.1. Essential food security and regenerative agriculture infrastructure, inputs and services supported.	3.1.1 Number of farmers benefitting from agricultural inputs, assets and training, disaggregated by sex and location (Ensuring the social and environmental safeguard standard)	24,300	30,000	10,000	TBC	TBC	Monthly reports, quarterly reports, mid-year reports, regional M&E reports, filed visits	Area Managers field visits and progress reports, M&E Regional officers' mission, reports, Livelihood Specialist, AIMS and TPMA, Agro-business Specialist,	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination
	3.2: Community preparedness and resilience for disasters and climate change improved	*3.2.1 Number of individuals who acquired knowledge and skills on disaster risk reduction/management and climate resilience , and adaptation, disaggregated by sex and location*	11,727	36,000	12,000	TBC	TBC	Monthly reports, quarterly reports, mid-year reports, regional M&E reports, filed visits	Area Managers field visits and progress reports, M&E Regional officers' mission, reports, Livelihood Specialist, AIMS and TPMA, Agro-business Specialist,	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

	3.3 Water security and access enhanced through climate-smart systems.	3.3.1 Number of climate smart water supply networks/schemes established. (Ensuring the social and environmental safeguard standard)	177	30	10	TBC	TBC	Monthly reports, quarterly reports, mid-year reports, regional M&E reports, filed visits	Area Managers field visits and progress reports, M&E Regional officers' mission, reports, Livelihood Specialist, AIMS and TPMA, Agro-business Specialist	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination
	3.4 Natural ecosystem restoration and management supported.	3.4.1 Hectares of land rehabilitated to absorb environmental stress and climate shocks (by location and ensuring the social and environmental safeguard standard)	473	300	125	TBC	TBC	Monthly reports, quarterly reports, mid-year reports, regional M&E reports, filed visits	Area Managers field visits and progress reports, M&E Regional officers' mission, reports, Livelihood Specialist, AIMS and TPMA, Agro-business Specialist,	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination
Output 4: Communities' capacity, Ownership, and engagement improved for better social cohesion.	4.1. Communities for peace well-being, civic engagement and social cohesion reinforced	*4.1.1 Number of individuals with better awareness about social cohesion, conflict prevention disaggregated by sex, types of structures engaged and and duration of the invention)*	524,444	700,000	200,000	TBC	TBC	Monthly Reports, Quarterly Reports, Community Resilience Specialist Reports, Social and Environmental Safeguards Specialist Reports, Community-based Planning Officer Reports, Gender Specialist Reports,	Reports from Area Managers, M&E Regional officers , Community Resilience and Social Cohesion Specialist, Social and Environmental Safeguarding Specialist, Community-based Planning Officer, Gender Mainstreaming Specialist, AIMS and TPMA	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

								Regional M&E Reports, Filed Visits		
	4.2. Improved gender equality and women's empowerment (GEWE) programmes and protection services for women and girls integrated and implemented in ABADEI.	*4.2.1 Number of women/girls benefitting from measures addressing gender-based violence (GBV), including psychosocial including temporary economic survival support*	642	2,000	1,250	TBC	TBC	Monthly Reports, Quarterly Reports, Community Resilience Specialist Reports, Social and Environmental Safeguards Specialist Reports, Community-based Planning Officer Reports, Gender Specialist Reports, Regional M&E, SES Reports, Filed Visits	Reports from Area Managers, M&E Regional, Community Resilience and Social Cohesion Specialist, Social and Environmental Safeguarding Specialist, Community-based Planning Officer, Gender Mainstreaming Specialist, AIMS and TPMA Lists of participants, PESA network referral data	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

	4.3. Rights-based access to justice, including gender justice, human rights and human security fostered	*4.3.1 Number of individuals benefitting from project-supported legal aid services, disaggregated by sex, age and location*	1,226	2,000	1,000	TBC	TBC	Monthly Reports, Quarterly Reports, Community Resilience Specialist Reports, Social and Environmental Safeguards Specialist Reports, Community-based Planning Officer Reports, Gender Specialist Reports, Regional M&E Reports, Filed Visits, SES compliance monitoring reports	A Reports from rea Managers, M&E Regional, Community Resilience and Social Cohesion Specialist, Social and Environmental Safeguarding Specialist, Community-based Planning Officer, Gender Mainstreaming Specialist, AIMS and TPMA, Transactional Tracking, Lists of participants	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination
	4.4. Community-led local recovery plans, social cohesion and resilience programs identified and implemented	*4.4.1 Number of community development plans developed, or updated, (including highlighting the vulnerabilities, natural disaster-prone areas, natural resources, social economic indicators and future development opportunities, etc.*	441	340	75	TBC	TBC	Monthly Reports, Quarterly Reports, Community Resilience Specialist Reports, Social and Environmental Safeguards Specialist Reports, Community-based Planning Officer Reports, Gender Specialist Reports, Regional M&E Reports, Filed Visits	Reports from Area Managers, M&E Regional, Community Resilience and Social Cohesion Specialist, Social and Environmental Safeguarding Specialist, Community-based Planning Officer, Gender Mainstreaming Specialist, AIMS and TPMA, People's Testimonies	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

		4.4.2 Number of social cohesion programmes carried out by community networks/structures (location, time duration, types of intervention)	0	50	10	tbc	tbc	Monthly Reports, Quarterly Reports, Community Resilience Specialist Reports, Social and Environmental Safeguards Specialist Reports, Community-based Planning Officer Reports, Gender Specialist Reports, Regional M&E Reports, Filed Visits	Reports from Area Managers, M&E Regional, Community Resilience and Social Cohesion Specialist, Social and Environmental Safeguarding Specialist, Community-based Planning Officer, Gender Mainstreaming Specialist, AIMS and TPMA, *People's Testimonies, Surveys (Perception surveys, KAP (knowledge, attitude and perceptions)*	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination
	4.5 Regional strategies for eight regions of Afghanistan designed and developed	*4.5.1 Number of regional strategies developed to integrate population projections and resource needs*	4	4	4			Monthly Reports, Quarterly Reports, Community Resilience Specialist Reports, Social and Environmental Safeguards Specialist Reports, Community-based Planning Officer Reports, Gender Specialist Reports, Regional M&E Reports, Filed Visits	Reports from Area Managers, M&E Regional, Community Resilience and Social Cohesion Specialist, Social and Environmental Safeguarding Specialist, Community-based Planning Officer, Gender Mainstreaming Specialist, AIMS and TPMA, People's Testimonies, Surveys (Perception surveys, KAP (knowledge, attitude and perceptions)	Safety and Security, Programmatic, Operational, Reputational, Fiduciary, Management, Coordination

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

VI. MONITORING AND EVALUATION

In accordance with UNDP's programming policies and procedures, the project will be monitored through the following monitoring and evaluation plans: *[Note: monitoring and evaluation plans should be adapted to project context, as needed]*

Monitoring Plan

Monitoring Activity	Purpose	Frequency	Expected Action	Partners (if joint)	Cost (if any)
Track results progress (including third party contractors)	Progress data against the results indicators in the RRF will be collected and analysed to assess the progress of the project in achieving the agreed outputs. Data will be collected and analysed through the AIMS system	Quarterly, or in the frequency required for each indicator.	Slower than expected progress will be addressed by project management. Monitoring and verification work will be carried out by Regional Teams to track the results progress		750,000
Monitor and Manage Risk i	Identify specific risks that may threaten the achievement of intended results. Identify and monitor risk management actions using a risk log. This includes monitoring measures and plans that may have been required as per UNDP's Social and Environmental Standards. Audits will be conducted in accordance with UNDP's audit policy to manage financial risk. To ensure the quality of data, third-party monitoring agents, including will also be engaged for data verification and validation.	Quarterly	Risks are identified by project management and actions are taken to manage risk. The risk log is actively maintained to keep track of identified risks and actions taken.		150,000
ABADEI Informationa Management System (AIMS) and Spatial Mapping	Information Management system to be established and linked with GIS Maps for remote monitoring and to better presentation to the management for better knowledge of the scope of work and activities under-taken in each region, province and district, helping decision makers in better resource mobilization and allocations.	Quarterly	System linking with GIS maps may results in delays due to acquiring Coordinates and authentic demographic information at community level in each region, province and district.		200,000
Learn	Knowledge, good practices and lessons will be captured regularly, as well as actively sourced from other projects and partners and integrated back into the project. Knowledge management products and lessons learned to be captured through individual contracts and agents. The identified learning will be used for adaptive management to adjust result/outputs.	At least annually	Relevant lessons are captured by the project team and used to inform management decisions.		100,000
Annual Project Quality Assurance	The quality of the project will be assessed against UNDP's quality standards to identify project strengths and	Annually	Areas of strength and weakness will be reviewed by project management, Project Board and used to inform		25,000

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

Monitoring Activity	Purpose	Frequency	Expected Action	Partners (if joint)	Cost (if any)
	weaknesses and to inform management decision making to improve the project.		decisions to improve project performance.		
Review and Make Course Corrections	Internal review of data and evidence from all monitoring actions to inform decision making.	At least annually	Performance data, risks, lessons and quality will be discussed by the project board and used to make course corrections.		15,000
Project Report	A progress report will be presented to the Project Board and key stakeholders, consisting of progress data showing the results achieved against pre-defined annual targets at the output level, the annual project quality rating summary, an updated risk long with mitigation measures, and any evaluation or review reports prepared over the period.	Quarterly, Annually, and at the end of the project (final report)			5,000
Project Review (Project Board)	The project's governance mechanism (i.e., project board) will hold regular project reviews to assess the performance of the project and review the Multi-Year Work Plan to ensure realistic budgeting over the life of the project. In the project's final year, the Project Board shall hold an end-of project review to capture lessons learned and discuss opportunities for scaling up and to socialize project results and lessons learned with relevant audiences.	Specify frequency (i.e., at least annually)	Any quality concerns or slower than expected progress should be discussed by the project board and management actions agreed to address the issues identified.		0

Evaluation Plan[31]

[31] Optional, if needed

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

Evaluation Title	Partners (if joint)	Related Strategic Plan Output	UNSDCF/CPD Outcome	Planned Completion Date	Key Evaluation Stakeholders	Cost and Source of Funding
Mid-Term Evaluation	N/A	Outcome 1: Eradicate Poverty in all its forms and dimensions	CPRF Outcome 1, Outcome 2 and Outcome 3	15 June 2024	UNDP Management, RBH and Donors	155,000
Terminal Evaluation	N/A	Outcome 1: Eradicate Poverty in all its forms and dimensions	CPRF Outcome 1, Outcome 2 and Outcome 3	15 January 2026	UNDP Management, RBH and Donors	300,000

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

VII. Multi-Year Work Plan [32,33]

All anticipated programmatic and operational costs to support the project, including development effectiveness and implementation support arrangements, need to be identified, estimated and fully costed in the project budget under the relevant output(s). This includes activities that directly support the project, such as communication, human resources, procurement, finance, audit, policy advisory, quality assurance, reporting, management, etc. All services which are directly related to the project need to be disclosed transparently in the project document.

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year			RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1 (2023)	Y2 (2024)	Y3 (2025)		Funding Source	Budget Description	Amount
Output 1: Essential services improved in the area of infrastructure, agriculture, health, education and energy Gender marker: (GEN1)	1.1 Activity: Essential physical, critical infrastructure constructed, rehabilitated, repaired, equipped and maintained, including infrastructure for water management, transportation, agriculture, health, education, basic services etc[1]	3,445,117	TBC	TBC	TBC	STFA-MPTFO (East)	**72100**-Contractual Services Companies	3,445,117
	1.2 Activity: Provision of improved essential health services (including women and girls accessing health care)	745,759	1,586,228	1,509,109	TBC	STFA-MPTFO (East)	**72100**-Contractual Services-Companies **72300**-Material and Goods	3,841,096
	1.3 Activity: Provision of essential education services (including gender-integrated culturally sensitive TVET)	25,000,000	TBC	TBC	TBC	Japan (JSB 2020)	**72100**-Contractual Services-Companies	25,000,000

[32] Cost definitions and classifications for programme and development effectiveness costs to be charged to the project are defined in the Executive Board decision DP/2010/32

[33] Changes to a project budget affecting the scope (outputs), completion date, or total estimated project costs require a formal budget revision that must be signed by the project board. In other cases, the UNDP programme manager alone may sign the revision provided the other signatories have no objection. This procedure may be applied for example when the purpose of the revision is only to re-phase activities among years.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year			RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1 (2023)	Y2 (2024)	Y3 (2025)		Funding Source	Budget Description	Amount
	1.4 Activity: Provision of clean, renewable and alternate energy services, technologies and applications supported and sustained	7,805,923	12,214,674	11,620,827	TBC	Japan (JSB 2022) STFA-MPTFO (East) UNDP Funding Windows (Fund 26800) 2023	**72100**-Contractual Services-Companies **72300**-Material and Goods **72400**-Constractual Services-individual	31,641,440
	1.5 Activity: Area offices technical and admin. assurance and oversight activities, and related running costs.	1,314,759	1,115,783	1,407,714	TBC1	STFA-MPTFO (North, South, and East)	**71400**-Professional Services	3,838,255
	1.6 Activity: Monitoring and Evaluation	250,000	250,000	250,000	TBC	STFA-MPTFO (North, South, and East)	**72100**-Contractual Services-Companies	750,000
	Sub-Total for Output 1	38,561,557	15,166,685	14,787,650				68,515,892
Output 2: Local economies improved through gender-responsive community -based livelihoods **Gender marker: GEN 2**	2.1 Activity: Households in high-poverty and high-insecurity areas provided with Unconditional Cash Transfer (UCT) / Temporary Basic Income (TBI)	1,441,772	3,066,646	2,917,553	TBC	STFA-MPTFO (North, South, and East)	**72100**-Contractual Services-Companies	7,425,971
	2.2 Activity: Local-level livelihoods and economies sustained through Cash- for -Work (CfW) including women and girls, vulnerable groups accessing CFW).	5,667,385	19,382,282	18,439,963	TBC	EU STFA-MPTFO (East) Japan (JSB 2022)	**72100**-Contractual Services-Companies **72300**-Material and Goods **71300**-Contractual Services-individual	43,489,630

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year			RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1 (2023)	Y2 (2024)	Y3 (2025)		Funding Source	Budget Description	Amount
	2.3 Activity: Local private sector development through technical and financial support to informal and formal businesses, including assisting micro, small and medium-sized enterprises (MSMEs) to access and/or expand to new market areas, support to local traders, to women-led businesses and community-led social enterprises (Cash- for Markets-CfM)	29,454,118	60,503,520	57,561,985	TBC	Japan (JSB 2022) STFA-MPTFO (East) UNDP Funding Windows (Fund 26800) 2023 UNDP TRAC 2	**72100**-Contractual Services-Companies 72300-Material and Goods 71300-Contractual Services-individual	147,519,623
	2.4 Activity: Cross-border trade and access to market supported (including women-led-businesses)	407,390	866,518	824,391	TBC	Japan (JSB 2022)	**72100**-Contractual Services-Companies	2,098,299
	2.5 Activity: Access to finance and Digital Solutions supported and sustained	1,607,343	3,418,817	3,252,602	TBC	Japan (JSB 2022)	**72100**-Contractual Services-Companies	8,278,761
	2.6 Activity: Area offices technical and admin. assurance and oversight activities, and related running costs.	1,314,759	1,115,783	1,407,714	TBC	STFA-MPTFO (North, South, and East)	**71400**-Contractual Services - Individuals	3,838,255
	2.7 Activity: Monitoring and Evaluation	250,000	250,000	250,000	TBC	EU STFA-MPTFO (East)	**72100**-Contractual Services-Companies	750,000

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year			RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1 (2023)	Y2 (2024)	Y3 (2025)		Funding Source	Budget Description	Amount
						Japan (JSB 2022)		
	Sub-Total for Output 2	40,142,766	88,603,566	84,654,207				213,400,539
Output 3: Local communities' resilience capacity enhanced to respond better and adapt to the disaster and climate-induced risks. Gender marker: GEN 1	3.1 Activity : Essential food security and regenerative agriculture infrastructure, inputs and services supported	3,387,968	7,206,204	6,855,855	TBC	STFA-MPTFO (North, South, and East)	**72100**-Contractual Services-Companies **72300**-Material and Goods **71300**-Contractual Services-individual	17,450,028
	3.2 Activity: Community preparedness and resilience for disasters and climate change improved.	268,920	2,698,991	2,567,773	TBC	STFA-MPTFO (North, South, and East)	**72100**-Contractual Services-Companies 72300-Material and Goods	5,535,684
	3.3 Activity: Water security and access enhanced through climate-smart systems	1,000,000	TBC -	TBC -	TBC	STFA-MPTFO (North, South, and East)	**72100**-Contractual Services-Companies 72300-Material and Goods -	1,000,000-
	3.4 Activity: Natural ecosystem restoration and management supported	1,649,127	3,507,692	3,337,156	TBC	STFA-MPTFO (North, South, and East)	**72100**-Contractual Services-Companies **72300**-Material and Goods **71300**-Contractual Services-individual	8,493,975
	3.5 Activity: Area offices technical and admin. assurance and oversight activities, and related running costs.	1,314,759	1,115,783	1,407,714	TBC	STFA-MPTFO (North, South, and East)	**71400**-Contractual Services - Individuals	3,838,255

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year			RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1 (2023)	Y2 (2024)	Y3 (2025)		Funding Source	Budget Description	Amount
	3.6 Activity: Evaluation (Mid-term and final)	N/A	75,000	75,000	TBC	STFA-MPTFO (North, South, and East)	**72100**-Contractual Services-Companies	150,000
	Sub-Total for Output 3	7,620,773	14,603,670	14,243,498				36,467,942
Output 4: Communities' capacity improved for better social cohesion and access to justice (especially for those who are systematically discriminated against, such as women, girls, ethnic and persons with disabilities). Gender marker: GEN 3	4.1 Activity: Communities for peace, well-being, civic engagement, and social cohesion/ inclusion are reinforced.	486,548	1,376,335	1,309,420	TBC	STFA-MPTFO (North, and South)	**72100**-Contractual Services-Companies	3,172,303
	4.2 Activity: Improved gender equality and women's empowerment (GEWE) programmes and protection services for women and girls integrated and implemented in ABADEI.	300,000	TBC	TBC	TBC	STFA-MPTFO (North, and South)	**72100**-Contractual Services-Companies -	300,000 -
	4.3 Activity: Rights-based access to justice, including gender justice, human rights and human security fostered.	200,000	TBC	TBC	TBC	STFA-MPTFO (North, and South)	**72100**-Contractual Services-Companies - -	200,000-
	4.4 Activity: Community-led local recovery plans and social cohesion and resilience programmes supported.	564,664	1,686,914	1,604,900	TBC	STFA-MPTFO (East)	**72100**-Contractual Services-Companies	3,556,478
	4.5 Activity: Territorial development plans for eight regions in Afghanistan designed and developed.	400,000	TBC	TBC	TBC	STFA-MPTFO (North, and South), STFA-MPTFO (East)	**72100**-Contractual Services-Companies -	400,000-

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year			RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1 (2023)	Y2 (2024)	Y3 (2025)		Funding Source	Budget Description	Amount
	4.6 Activity: Area offices technical and admin. assurance and oversight activities, and related running costs.	1,314,759	1,115,783	1,407,714	TBC	STFA-MPTFO (North, South, and East)	**71400**-Contractual Services - Individuals	3,838,255
	4.7 Activity: Evaluation (Mid-term and final)	-	75,000	75,000	TBC	STFA-MPTFO (North, South, and East)	**72100**-Contractual Services-Companies	150,000
	Sub-Total for Output 4	3,265,971	4,254,032	4,397,034				11,917,036
Output 5- Programme Management Cost	5.1 Activity: Staff cost, Consultants-Technical (Short Term), Common Premises and Services, Communication, Travel, Vehicle Fuel, Miscellaneous Maintenance, rental.	4,126,923	7,400,000	7,100,000	TBC	EU STFA-MPTFO (North, South, and East) Japan (JSB 2022)	**61300-**Salary and Post Adjustment	14,901,538
					TBC		**74500**-Miscellaneous	3,725,385
	CO DPC	6,073,585	8,490,566	8,150,943	TBC		**64300**-Staff Mgmt Cost	18,172,075
					TBC		**74500**-Miscellaneous	4,543,019
	Sub-Total for Output 5	10,200,508	15,890,566	15,250,943				41,342,017
	Total Outputs 1 - 5	99,351,852	138,518,518	133,333,332				371,203,703
General Management Support (GMS 8%)		7,508,410	11,481,481	10,666,668				29,656,559
Grand Total		**107,300,000**	**150,000,000**	**144,000,000**				**401,300,000**

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

VIII. GOVERNANCE AND MANAGEMENT ARRANGEMENTS

The Project will utilize the ABADEI Project Board (Annex-5) meetings to provide an oversight and project governance mechanism that approves ABADEI development interventions , for inclusion in the Project's Annual Workplan. This Board has the following roles:

- **Chair:** The UNDP Resident Representative/Senior Deputy Resident Representative (Programme) of the Afghanistan Country Office will chair the Board to guide discussions and provide overall leadership.
- **Donor:** Individual donors funding the Project will participate at the Board meetings, with one of more donors a Board member representing the interests of all donor stakeholders when UNDP approves for implementation of the provincial resilience agendas that form the basis for the Project's annual work plans. The Senior Suppliers' primary function within the Board is to assess the technical feasibility of proposed interventions and to review and endorse decisions taken by the Board.


- **Country Office Programme Management Unit (CO PMU):** The Project Board will be supported by the CO Programme Management Unit that works independently of the Project Manager to carry out objective and independent project oversight and monitoring functions to ensure objective and autonomous assurance. This team will ensure that the necessary management approvals are obtained, and that implementation is in accordance with the relevant UNDP rules and procedures. In addition, they will also carry out monitoring of the progress of achieving the outputs detailed in the project document. The CO PMU will also ensure that the documentation produced by the project team complies with the necessary quality assurance standards and carry out any other assurance functions entrusted to them by the Project Board.
  1.

- **Project Quality Assurance Unit:** The Project Board will be supported by a Project Quality Assurance Unit that works independently of the Project Manager to carry out objective and independent project oversight and monitoring functions to ensure objective and autonomous assurance. This team will ensure that the necessary management approvals are obtained, and that implementation is in accordance with the relevant UNDP rules and procedures. In addition, they will also support monitoring of the progress of achieving the outputs detailed in the project document. The Project Assurance Unit will also ensure that the documentation produced by the project team complies with the necessary quality assurance standards and carry out any other assurance functions entrusted to them by the Project Board.

ABADEI Project Management Unit (PMU) includes eight Regional Offices: The PMU's role provides project administration, both management and technical support, to the Regional Offices. The PMU is led by the ABADEI Project Management Specialist under the direct supervision of the Project Manager, with guidance from and under the authority of the UNDP SDRR Program and Resident Representative. The staff of the PMU will be required to engage regularly with the Area Managers and staff from the Regional Offices and augment and occasionally supplement vacant Regional Offices' capacities when deemed advisable by the Project Manager or the Project Management Specialist. Technical specialists from the PMU (e.g., Engineers, SES, CBI, WASH, Gender) will review technical specifications and bills of quantity submitted by RPs bidding for contract awards with a view to ensuring that only cost-effective and technically sound interventions are implemented. Furthermore, site visits to the provinces, when feasible, by the technical staff of the PMU, on a regular basis will be part of the Monitoring and Evaluation (M&E) methodology adopted by the Project and should be a prerequisite to the release of progress payments to the RPs. The PMU will be involved with overall day-to-day project delivery, activity planning through the elaboration of the Provincial Resilience Agenda documents, managing procurement and recruitment processes and agreements with responsible parties, coordinating with local counterparts and development partners, providing guidance to responsible parties and overseeing

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

their performance, collating and analysing, monitoring data, and preparing periodic progress reports that are submitted to the UNDP Country Office and the Project Manager.

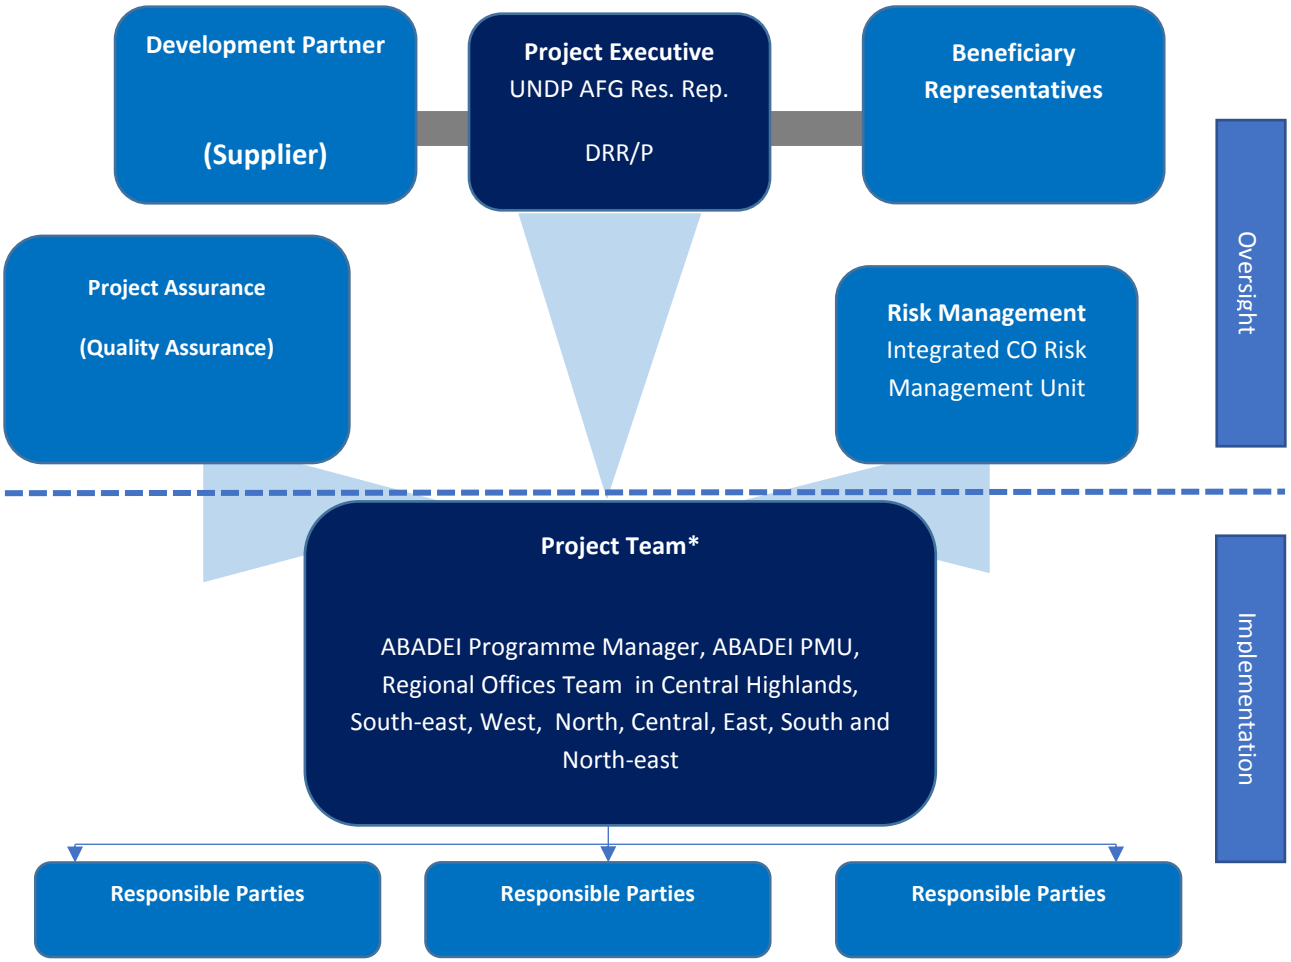

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

IX. LEGAL CONTEXT

As UNDP Afghanistan currently does not have a Standard Basic Assistance Agreement (SBAA) with the current DfA, the project document shall be the instrument envisaged and defined in the Supplemental Provisions to the Project Document, attached hereto and forming an integral part hereof, as "the Project Document".

This project will be implemented by UNDP in accordance with its financial regulations, rules, practices and procedures only to the extent that they do not contravene the principles of the Financial Regulations and Rules of UNDP. Where the financial governance of UNDP applies and will provide the required guidance to ensure the best value for money, fairness, integrity, transparency, and effective international competition.

X. Risk MANAGEMENT (Refer to Section E: RISKS AND ASSUMPTIONS (pages-29-31)

D: RISK REGISTER (40-48-)

UNDP (DIM)

1 UNDP as the Implementing Partner will comply with the policies, procedures and practices of the United Nations Security Management System (UNSMS.)

2 UNDP as the Implementing Partner will undertake all reasonable efforts to ensure that none of the [project funds][34] [UNDP funds received pursuant to the Project Document][35] are used to provide support to individuals or entities associated with terrorism, that the recipients of any amounts provided by UNDP hereunder do not appear on the United Nations Security Council Consolidated Sanctions List, and that no UNDP funds received pursuant to the Project Document are used for money laundering activities. The United Nations Security Council Consolidated Sanctions List can be accessed via https://www.un.org/securitycouncil/content/un-sc-consolidated-list. This provision must be included in all sub-contracts or sub-agreements entered into under this Project Document.

3 Social and environmental sustainability will be enhanced through application of the UNDP Social and Environmental Standards (http://www.undp.org/ses) and related Accountability Mechanism (http://www.undp.org/secu-srm).

4 UNDP as the Implementing Partner will: (a) conduct project and programme-related activities in a manner consistent with the UNDP Social and Environmental Standards, (b) implement any management or mitigation plan prepared for the project or programme to comply with such standards, and (c) engage in a constructive and timely manner to address any concerns and complaints raised through the Accountability Mechanism. UNDP will seek to ensure that communities and other project stakeholders are informed of and have access to the Accountability Mechanism.

5 In the implementation of the activities under this Project Document, UNDP as the Implementing Partner will handle any sexual exploitation and abuse ("SEA") and sexual harassment ("SH") allegations in accordance with its regulations, rules, policies and procedures.

6 All signatories to the Project Document shall cooperate in good faith with any exercise to evaluate any programme or project-related commitments or compliance with the UNDP Social and Environmental Standards. This includes providing access to project sites, relevant personnel, information, and documentation.

7 UNDP as the Implementing Partner will ensure that the following obligations are binding on each responsible party, subcontractor, and sub-recipient:

---

[34] To be used where UNDP is the Implementing Partner

[35] To be used where the UN, a UN fund/programme or a specialized agency is the Implementing Partner

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

a. Consistent with the Article III of the SBAA *[or the Supplemental Provisions to the Project Document]*, the responsibility for the safety and security of each responsible party, subcontractor and sub-recipient and its personnel and property, and of UNDP's property in such responsible party's, subcontractor's and sub-recipient's custody, rests with such responsible party, subcontractor and sub-recipient. To this end, each responsible party, subcontractor and sub-recipient shall:
   i. put in place an appropriate security plan and maintain the security plan, taking into account the security situation in the country where the project is being carried;
   ii. assume all risks and liabilities related to such responsible party's, subcontractor's and sub-recipient's security, and the full implementation of the security plan.
b. UNDP reserves the right to verify whether such a plan is in place, and to suggest modifications to the plan when necessary. Failure to maintain and implement an appropriate security plan as required hereunder shall be deemed a breach of the responsible party's, subcontractor's and sub-recipient's obligations under this Project Document.
c. Each responsible party, subcontractor and sub-recipient (each a "sub-party" and together "sub-parties") acknowledges and agrees that UNDP will not tolerate sexual harassment and sexual exploitation and abuse of anyone by the sub-parties, and other entities involved in Project implementation, either as contractors or subcontractors and their personnel, and any individuals performing services for them under the Project Document.
   (a) In the implementation of the activities under this Project Document, each sub-party shall comply with the standards of conduct set forth in the Secretary General's Bulletin ST/SGB/2003/13 of 9 October 2003, concerning "Special measures for protection from sexual exploitation and sexual abuse" ("SEA").
   (b) Moreover, and without limitation to the application of other regulations, rules, policies and procedures bearing upon the performance of the activities under this Project Document, in the implementation of activities, each sub-party, shall not engage in any form of sexual harassment ("SH"). SH is defined as any unwelcome conduct of a sexual nature that might reasonably be expected or be perceived to cause offense or humiliation, when such conduct interferes with work, is made a condition of employment or creates an intimidating, hostile or offensive work environment. SH may occur in the workplace or in connection with work. While typically involving a pattern of conduct, SH may take the form of a single incident. In assessing the reasonableness of expectations or perceptions, the perspective of the person who is the target of the conduct shall be considered.
d. In the performance of the activities under this Project Document, each sub-party shall (with respect to its own activities) and shall require from its sub-parties (with respect to their activities) that they, have minimum standards and procedures in place, or a plan to develop and/or improve such standards and procedures in order to be able to take effective preventive and investigative action. These should include policies on sexual harassment and sexual exploitation and abuse; policies on whistleblowing/protection against retaliation; and complaints, disciplinary and investigative mechanisms. In line with this, sub-parties will and will require that their respective sub-parties will take all appropriate measures to:
   (i) Prevent its employees, agents or any other persons engaged to perform any services under this Project Document, from engaging in SH or SEA.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

(ii) Offer employees and associated personnel training on prevention and response to SH and SEA, where sub-parties have not put in place its own training regarding the prevention of SH and SEA, sub-parties may use the training material available at UNDP.

(iii) Report and monitor allegations of SH and SEA of which any of the sub-parties have been informed or have otherwise become aware, and status thereof.

(iv) Refer victims/survivors of SH and SEA to safe and confidential victim assistance; and

(v) Promptly and confidentially record and investigate any allegations credible enough to warrant an investigation of SH or SEA. Each sub-party shall advise UNDP of any such allegations received and investigations being conducted by itself or any of its sub-parties with respect to their activities under the Project Document, and shall keep UNDP informed during the investigation by it or any of such sub-parties, to the extent that such notification (i) does not jeopardize the conduct of the investigation, including but not limited to the safety or security of persons, and/or (ii) is not in contravention of any laws applicable to it. Following the investigation, the relevant sub-party shall advise UNDP of any actions taken by it or any of the other entities further to the investigation.

e. Each sub-party shall establish that it has complied with the foregoing, to the satisfaction of UNDP, when requested by UNDP or any party acting on its behalf to provide such confirmation. Failure of the relevant sub-party to comply of the foregoing, as determined by UNDP, shall be considered grounds for suspension or termination of the Project.

f. Each responsible party, subcontractor and sub-recipient will ensure that any project activities undertaken by them will be implemented in a manner consistent with the UNDP Social and Environmental Standards and shall ensure that any incidents or issues of non-compliance shall be reported to UNDP in accordance with UNDP Social and Environmental Standards.

g. Each responsible party, subcontractor and sub-recipient will take appropriate steps to prevent misuse of funds, fraud, corruption or other financial irregularities, by its officials, consultants, subcontractors and sub-recipients in implementing the project or programme or using the UNDP funds. It will ensure that its financial management, anti-corruption, anti-fraud and anti-money laundering and countering the financing of terrorism policies are in place and enforced for all funding received from or through UNDP.

h. The requirements of the following documents, then in force at the time of signature of the Project Document, apply to each responsible party, subcontractor and sub-recipient: (a) UNDP Policy on Fraud and other Corrupt Practices (b) UNDP Anti-Money Laundering and Countering the Financing of Terrorism Policy; and (c) UNDP Office of Audit and Investigations Investigation Guidelines. Each responsible party, subcontractor and sub-recipient agrees to the requirements of the above documents, which are an integral part of this Project Document and are available online at www.undp.org.

i. In the event that an investigation is required, UNDP will conduct investigations relating to any aspect of UNDP programmes and projects. Each responsible party, subcontractor and sub-recipient will provide its full cooperation, including making available personnel, relevant documentation, and granting access to its (and its consultants', subcontractors' and sub-recipients') premises, for such purposes at reasonable times and on reasonable conditions as may be required for the purpose of an investigation. Should there be a limitation in meeting this obligation, UNDP shall consult with it to find a solution.

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

j. Each responsible party, subcontractor and sub-recipient will promptly inform UNDP as the Implementing Partner in case of any incidence of inappropriate use of funds, or credible allegation of fraud, corruption other financial irregularities with due confidentiality.
Where it becomes aware that a UNDP project or activity, in whole or in part, is the focus of investigation for alleged fraud/corruption, each responsible party, subcontractor and sub-recipient will inform the UNDP Resident Representative/Head of Office, who will promptly inform UNDP's Office of Audit and Investigations (OAI). It will provide regular updates to the head of UNDP in the country and OAI of the status of, and actions relating to, such investigation.

k. *Choose one of the three following options:*

Option 2: Each responsible party, subcontractor or sub-recipient agrees that, where applicable, donors to UNDP (including the Government) whose funding is the source, in whole or in part, of the funds for the activities which are the subject of the Project Document, may seek recourse to such responsible party, subcontractor or sub-recipient for the recovery of any funds determined by UNDP to have been used inappropriately, including through fraud corruption or other financial irregularities or otherwise paid other than in accordance with the terms and conditions of the Project Document.

XI.ANNEXES

1. **Project Quality Assurance Report (See Annex 1)**
2. **Social and Environmental Screening Template (See Annex 2)** [English] [French] [Spanish], including additional Social and Environmental Assessments or Management Plans as relevant. (NOTE: The SES Screening is not required for projects in which UNDP is Administrative Agent only and/or projects comprised solely of reports, coordination of events, trainings, workshops, meetings, conferences, preparation of communication materials, strengthening capacities of partners to participate in international negotiations and conferences, partnership coordination and management of networks, or global/regional projects with no country level activities).
3. **Risk Analysis**. Use the standard Risk Register template. Please refer to the Deliverable Description of the Risk Register for instructions (*See Section D above)*
4. **Capacity Assessment:** Results of capacity assessments of Implementing Partner (including Partner Capacity Assessment Tool (PCAT) and HACT Micro Assessment)-N/A
5. **Project Board Terms of Reference and TORs of key management positions.** The standard Project Board TOR can be found here**.**

Annex 5

UNDP Standard Terms of Reference (ToR) for the

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

Project Board of the ABADEI programme

I. Background

UNDP has been working across Afghanistan for more than 50 years on challenges related to climate change and resilience, gender, governance, health, livelihoods and the rule of law. Area-Based Approach to Development Emergency Initiatives (ABADEI) is a UNDP- led local economic recovery programme that brings UN agencies and a large number of NGO and CSO partners together, through a coherent approach and funding platform, to enable joined-up programming, wide geographic coverage and results at scale. ABADEI's focus is to help meet basic human needs and services, by revitalizing local markets and helping local communities rebuild their own lives and livelihoods. Enhancing human security and reducing the humanitarian caseload, is fundamental to its approach. ABADEI interventions provide an integrated response to the economic crisis in the country through 1) the provision of essential services, 2) investments in community livelihoods and local economic activities, 3) protecting farming and farm lands from natural disasters, and 4) building community resilience and social cohesion.

The ABADEI programme combines a local area-based programme approach within each of Afghanistan's administrative regions, with specific vertical sector initiatives. These six sector initiatives include: renewable energy, health systems strengthening, tertiary education, banking and finance services, CSO/NGO capacity strengthening and private sector development.

The following presents the structure and key duties/responsibilities of a multi-stakeholder project board to be established to provide oversight to the project and review the performance based on certain metrics to ensure quality delivery of results. For the purpose of this ToR and to ensure standardization, henceforth, as regards project documentation, such a body shall only be referred to as 'Project Board'. The Project Board will be the most senior, dedicated oversight body which will act as an instrument that "Delivers outputs where UNDP has accountability for design, oversight and quality assurance of the entire project."

II. Duties and Responsibilities

Specific responsibilities of the Project Board include the following:

- Provide overall guidance and direction to the project, ensuring it remains within any specified constraints and promoting gender equality and social inclusion in the project implementation.
- Review project performance based on monitoring, evaluation and reporting, including standard quality assurance checks, progress reports, risk logs, spot checks/audit reports and the combined delivery report.
- Address any high-level project issues as raised by the project manager and project assurance.
- Provide guidance on emerging and/or pressing project risks and agree on possible mitigation and management actions to address specific risks (including ensuring compliance with UNDP's Social and Environmental Standards, Fraud/corruption, Sexual Exploitation and Abuse and Sexual Harassment).

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

- Agree or decide on the project manager's tolerances as required, within the parameters set by UNDP and the donor, and provide direction and decisions for exceptional situations when the project manager's tolerances are exceeded.
- Advise on major and minor amendments to the project within the parameters set by UNDP and the donor.
- Agree or decide on a project suspension or cancellation, if required.
- Provide high-level direction and recommendations to the project management unit to ensure that the agreed deliverables are produced satisfactorily according to plans.
- Receive and address project-level grievances, including overseeing whatever specific compliance and stakeholder response (or grievance) mechanisms have been put in place so that individuals and communities potentially affected by the project have access to effective mechanisms and procedures for raising concerns about the social and environmental performance of the project[1].
- Approve the Project Inception Report, Mid-term Review and Terminal Evaluation reports and corresponding management responses.
- Review the final project report package during an end-of-project review meeting to discuss lessons learned and opportunities for scaling up.

III. Composition of the Project Board

The Project Board will have three categories of formal members. Project Board will contain the following roles:

1. **An Executive:** UNDP Resident Representative of Afghanistan Country Office (CO) - representing the project ownership and chairs the group.
2. **Development Partner:** Representative(s) of the donor funding the project.
3. **Beneficiary Representative(s):** A total of four members, two from a local Community Organization from project intervention areas, representatives of local Women's Business Associations, and the private sector.

A **UNDP representative must always be represented in the Project Board** in either the project executive or development partner role. This Project Board will meet one time annually according to this provisional schedule.

Project Board members cannot receive remuneration from project funds for their participation in the Board.

Unless otherwise specified, Project Board decisions are made by unanimous consensus. If a consensus cannot be reached within the Board, the final decision shall rest with the UNDP representative on the Project Board or a UNDP staff member with delegated authority as the programme manager.[2]

Project Board will be supported by the Project Assurance function (independent of the project manager) to carry out objective and independent oversight. This function will ensure the necessary approvals of management and operational policy and procedures. They will also ensure the quality implementation of activities and support the progress monitoring of the entire project. The Project Assurance will also ensure effective liaison and facilitation to ensure the necessary guidance on policies and procedures between the

DocuSign Envelope ID: 490203DB-F95D-4F2C-816E-424AEB9AB88B

UNDP office and other UNDP offices. Project Board members, provide quality assurance of the documentation produced by the Project team and other assurance functions entrusted by the Project Board.

The Project Manager is responsible for the day-to-day management and decision-making for the project, and for delivering the expected outputs. The project manager will ensure that the project will produce the expected outputs specified in the work plan, to the required standard of quality and within the specific constraints of time and cost.

The UNDP programme team will provide quality assurance and technical support for project's implementation. The team will report on progress to UNDP senior management and support the development of solutions to emerging operational/contextual risks. Their contributions to progress monitoring will also inform programme adaptations. Additional technical guidance and support will be provided through UNDP's regional hub in Bangkok.

Continuous integrated implementation support will be provided by the strengthened CO operations team, including financial, procurement and recruitment services in view of project-specific needs. Risk management and the implementation of mitigation measures will be performed by a dedicated risk management capacity that combines the UNDP Country Office in Afghanistan and the HQ colleagues, under the leadership of a Risk Manager. Outcome and output monitoring and the adaptive management process will be ensured by the CO Development Effectiveness Unit.

[1] The responsibilities of the board in this regard should follow UNDP's Social and Environmental Standards (SES) as codified in the PPM. It should be noted that while a project board can play a role in addressing or assisting with the compliance and stakeholder response (or grievance) mechanisms put in place for a given project (as part of their quality assurance and oversight function), this will be in addition to and does not substitute for UNDP's core responsibility to ensure compliance with the SES throughout the project management cycle as part of UNDP's Programming Quality Assurance system.

[2] UNDP has this special right since the ultimate legal and fiduciary accountability for a UNDP project, irrespective of modality, rests with UNDP and UNDP must (in line with its obligations to donors and to the Executive Board) be able to ensure that no action is taken by anybody in a UNDP project that contravenes UNDP rules and regulations.

6. **On-Granting Provisions Applicable to the Implementing Partner[36].** On-granting clauses for non-UNDP Implementing Partners can be found here.

[36] Applicable for non-UNDP Implementing Partner as Grant Making Institution facilitating on-granting.
