# PROJECT DOCUMENT

**Project Title**: Catalysing Lower Emissions through Advancing National Adoption of Commercially viable Technologies (CLEAN-ACT) – Shifting Investment Flows Towards Green Transformation (SHIFT)
**Project Number:** 01003048
**Implementing Partner:** United Nations Development Programme (UNDP)

**Start Date:** September 2024 **End Date:** December 2027 **PAC Meeting date:** 20 Sep 2024


**Brief Description**

Viet Nam is a middle-income country with a fast-growing economy and aims to reach a high-income country status by 2045. However, according to a World Bank study, Viet Nam is estimated to require approximately $368 billion to reach its 2050 net zero goal, the achievement of this goal requires at this early stage to strengthening the Government's capacity to coordinate and implement economic policy reforms and public investments, as well as a shift in its economic growth model. Further, estimates provided by MOIT in 2020 highlight a total investment of US$134.7 billion towards new power projects by 2030 is needed to finance projected shortages. Viet Nam has declared its pledge of achieving net-zero emissions by 2050 and signed a Just Energy Transition Partnership (JETP) with the G7 countries, Norway, and Denmark, committing to accelerate its climate mitigation efforts in exchange for substantial international financial support. This calls for comprehensive market and regulatory reform to facilitate and accelerate relevant investment to achieve a rapid and radical green transformation.

In support of these endeavours, a consortium of six partners will join forces to implement the 'Shifting Investment Flows Towards Green Transformation (SHIFT)' project in Viet Nam, enhancing know-how and capacities of relevant public and private stakeholders in the areas of green finance and energy transition. The consortium consists of Agora Energiewende/the Smart Energy for Europe Platform (SEFEP), the Banking Academy of Viet Nam (BAV), International Finance Cooperation (IFC), SNV Netherlands Development Organisation Viet Nam, the United Nations Development Programme (UNDP) and the Deutsche Gesellschaft für Internationale Zusammenarbeit (GIZ) as the consortium lead.

Within the framework of SHIFT, UNDP is responsible for the design and implementation of two Work Packages. The objective is to generate interest and build technical capacity in the private sector especially women-led enterprises or enterprises with a proven approach to promote gender equality concerning RE, EE and energy transition technologies. UNDP will receive 3 million Euros (of 15 million Euros for the entire project) to implement the following two work packages: (1) design and implementation of replicable investment projects in energy transition technologies to substantially reduce greenhouse gas emissions in high energy consuming sectors; and (2) catalyse and facilitate the replication and scale-up of the piloted energy transition technologies and other energy transition technologies.


| **Contributing Outcome (UNSDCF, CPD, RPD):** |
|---|
| United Nations Sustainable Development Cooperation Framework (UNSDCF): |
| **Outcome 2**: Climate Change Response, Disaster Resilience & Environmental Sustainability |
| **Outcome 3**: Shared Prosperity through Economic Transformation |
| |

| | | |
|---|---|---|
| **Total resources required:** | | **USD 3,160,607** |
| **Total resources allocated:** | BMWK/Germany | **USD 3,160,607** |
| | In-Kind: | **USD 0** |
| | | |

| | |
|---|---|
| **Global Output 1.1:** Drive private investment in clean, affordable, and reliable energy.<br>**Global Output 1.3:** Support national and local governments to achieve decarbonization through just transition.<br><br>UNDP Country Programme Document:<br>**Outcome 2:** Climate Change, Disaster Resilience and Environmental Sustainability.<br>***Output 2.2***: Policies and solutions designed and implemented for transformation to low-carbon development, circular economy, and environmental protection.<br><br>Indicative Output(s) with gender marker: GEN2<br>Output 1: GEN2<br>Output 2: GEN2 | |

Agreed by (signature):

| UNDP | |
|---|---|
| Print Name: Ramla Khalidi | |
| Date: 14/11/24 | |

## Contents

I. Development Challenge ..... 4
II. Strategy ..... 5
2.1 Objectives ..... 5
2.2 Theory of Change ..... 6
III. Results and Partnerships ..... 7
3.1 Expected results ..... 7
3.2. Project Log-frame ..... 10
3.3 Resources required to achieve the expected results ..... 16
3.4 Partnerships ..... 17
3.5 Risks and assumptions ..... 19
3.6 Stakeholder engagement ..... 19
3.7 South-South and Triangular Cooperation (SSC/TrC) ..... 19
3.8 Digital solutions ..... 20
3.8 Knowledge and visibility ..... 20
3.9 Sustainability and scaling up ..... 20
3.10 Cost efficiency and effectiveness ..... 21
IV. Project Management ..... 21
4.1 Project management ..... 21
4.2 UNDP standard management services ..... 22
V. Results Framework ..... 23
TARGETS (by frequency of data collection) ..... 23
DATA COLLECTION METHODS & RISKS ..... 23
VI. Monitoring And Evaluation ..... 26
VII. Multi-Year Work Plan ..... 28
VIII. Governance and Management Arrangements ..... 31
IX. Legal Context ..... 32
X. Risk Management ..... 33
XI. ANNEXES ..... 36

# I. DEVELOPMENT CHALLENGE

The Government of Viet Nam has made very ambitious commitments to reduce its greenhouse gases (GHG) emissions. In 2022, a second update of Viet Nam's Nationally Determined Contribution (NDC) was submitted, raising the country's GHG emissions reduction targets for 2030, compared to business-as-usual (BAU), from 9.0 percent to 15.8 percent unconditionally, and from 27.0 percent to 43.5 percent conditional upon receiving adequate international financial support. This NDC is complemented by Viet Nam's National Climate Change Strategy (NCCS) to 2050 which, inter alia, aims for national emissions to peak in 2035, execution of greenhouse gas inventories among facilities emitting at least 3,000 tCO2eq annually, and promoting the implementation of EE and RE technology options to assure that RE accounts for at least 55 percent of total electricity produced by 2050.

At the 26th United Nations Climate Change Conference of the Parties (COP26) in Glasgow, United Kingdom, the Prime Minister of Viet Nam committed to achieving net-zero GHG emissions by 2050. Viet Nam also signed the Global Coal to Clean Power Transition Statement and committed to reducing methane emissions by 30 percent by 2030, relative to 2020 levels. Viet Nam is a middle-income country with a fast-growing economy and aims to reach a high-income country status by 2045. However, according to a World Bank study, Viet Nam is estimated to require approximately $368 billion to reach its 2050 net zero goal. It requires at this early stage to strengthening the Government's capacity to coordinate and implement economic policy reforms and public investments, as well as a shift in its economic growth model. Further, estimates provided by MOIT in 2020 highlight a total investment of US$134.7 billion towards new power projects by 2030 is needed to finance projected shortages.

On 14 December 2022, the Government of Viet Nam and the International Partners Group (IPG) comprising the European Union, the United Kingdom of Great Britain and Northern Ireland, the United States of America, Japan, the Federal Republic of Germany, the French Republic, the Italian Republic, Canada, the Kingdom of Denmark and the Kingdom of Norway, announced the Political Declaration on the Viet Nam Just Energy Transition Partnership (JETP). The JETP will mobilize US$ 15.5 billion in public and private finance over the next three to five years to support Viet Nam's energy transition. Launched at COP28 in November 2023, the JETP Resource Mobilisation Plan (JETP RMP) and its associated scope of actions represent the first step towards implementing the JETP. Specifically, the RMP identifies a pipeline of defined investment and technical assistance projects, as well as priority policy action, consistent with the Government of Viet Nam's position to be implemented and ensure all of society benefit from a low-carbon transition. The provision of a catalytic $15.5 billion investment over the next 3 to 5 years represents a promising start to addressing the funding shortfall.

Within this overall context, it is crucial to design, approve and implement all required policy, regulatory and financial instruments to complement the existing frameworks. Additionally, to achieve Viet Nam's ambitious targets, significant contributions must be made in terms of improvements in enhancing EE as well as increasing the share of RE share across all sectors of the economy.

During the full SHIFT project proposal preparation phase, UNDP, in coordination with the Deutsche Gesellschaft für Internationale Zusammenarbeit (GIZ) and with inputs from the Government of Viet Nam (particularly MPI and MOIT) and other partners of the SHIFT Consortium, has indicated sectors and sub-sectors with high potential for GHG emissions reduction and energy savings on the basis of a preliminary review. However, a thorough evaluation of sectors and sub-sectors with high energy consumption, an examination of available and viable energy transition technologies as well as their financial viability is required during the early phase of project implementation.


Placed in the context of Viet Nam's JETP RMP, NCCS, NGGS, and PDP8, the CLEAN-ACT project directly contributes towards Viet Nam's achievement of each of these government strategies and their affiliated targets, specifically by facilitating access green finance and enabling the scale-up of energy transition technologies. The CLEAN-ACT project is closely aligned with the ongoing efforts of the international community to support the Government of Viet Nam in attaining the aforementioned GHG emissions reduction and energy efficiency targets, particularly in the context of enabling catalytic investments in energy transition technologies and the creation of decent jobs.

# II. STRATEGY

## 2.1 Objectives

- The main objective of the overall SHIFT project is to redirect financial flows towards energy transition and increase investments in RE and EE. The successful implementation of the SHIFT project will contribute to achieving Viet Nam's GHG emissions reduction targets set out in the NDC and other national strategies.
- UNDP is responsible for the design and implementation of two Work Packages (WPs), specifically WP IV.1 and WP IV.2, both falling under Output IV. The objective of Output IV is to generate interest and build technical capacity in the private sector especially women-led enterprises or enterprises with a proven approach to promote gender equality concerning RE, EE and energy transition technologies. Improved knowledge and interest in these technologies and their benefits will lead to increased private sector investments.
- In particular, WP IV.1 will focus on the design and implementation of viable and replicable investment projects in energy transition technologies in emissions-intensive sectors, while the emphasis of WP IV.2 will be on facilitating the replication and scale-up of the investments piloted under WP IV.1, as well as other energy transition technologies.
- The two UNDP-led WPs will pilot, replicate, improve confidence in and scale-up green investment projects in energy transition technologies. The findings of WPs IV.1 and IV.2 will be used to draw lessons learned and recommendations to inform Outputs II and III, and concomitantly financial instruments developed under Output III will be accessed to finance investment projects under WPs IV.1 and IV.2.
- For the design and implementation of the two WPs, UNDP is adopting an all-encompassing approach and fostering gender equality, spanning from piloting design and implementation of green investment projects to their monitoring and evaluation (M&E), from strengthening sustainability through capacity building programmes and lessons learned to replication and scale-up of the piloted investment projects, and from identification and mobilization of financial resources to provision of recommendations for the formulation and updating of supportive policies. The underlying methodology applied during implementation will be based on the reassessment and removal of all identified barriers, while fostering women empowerment and supporting the inclusion of gender and marginalized groups. This approach will guarantee a long-lasting impact of the results achieved.
- UNDP will ensure that the relevant Milestones outlined in the offer will be achieved:
  - Milestone IV.1: Energy transition technologies to be promoted under the four work packages of Output IV have been defined (12/2024) (responsible: GIZ, UNDP, SNV)
  - Milestone IV.2: Implementation of one investment pilot project of Work Package IV.1 (12/2026) (responsible: UNDP)
- Lastly, the focus of the two UNDP-led WPs are, respectively: 1) design and implementation of viable and replicable investment projects in energy transition technologies; and 2) facilitating the replication and scale-up of the investments piloted under WP IV.1 as well as other energy transition technologies.

**2.2 Theory of Change**

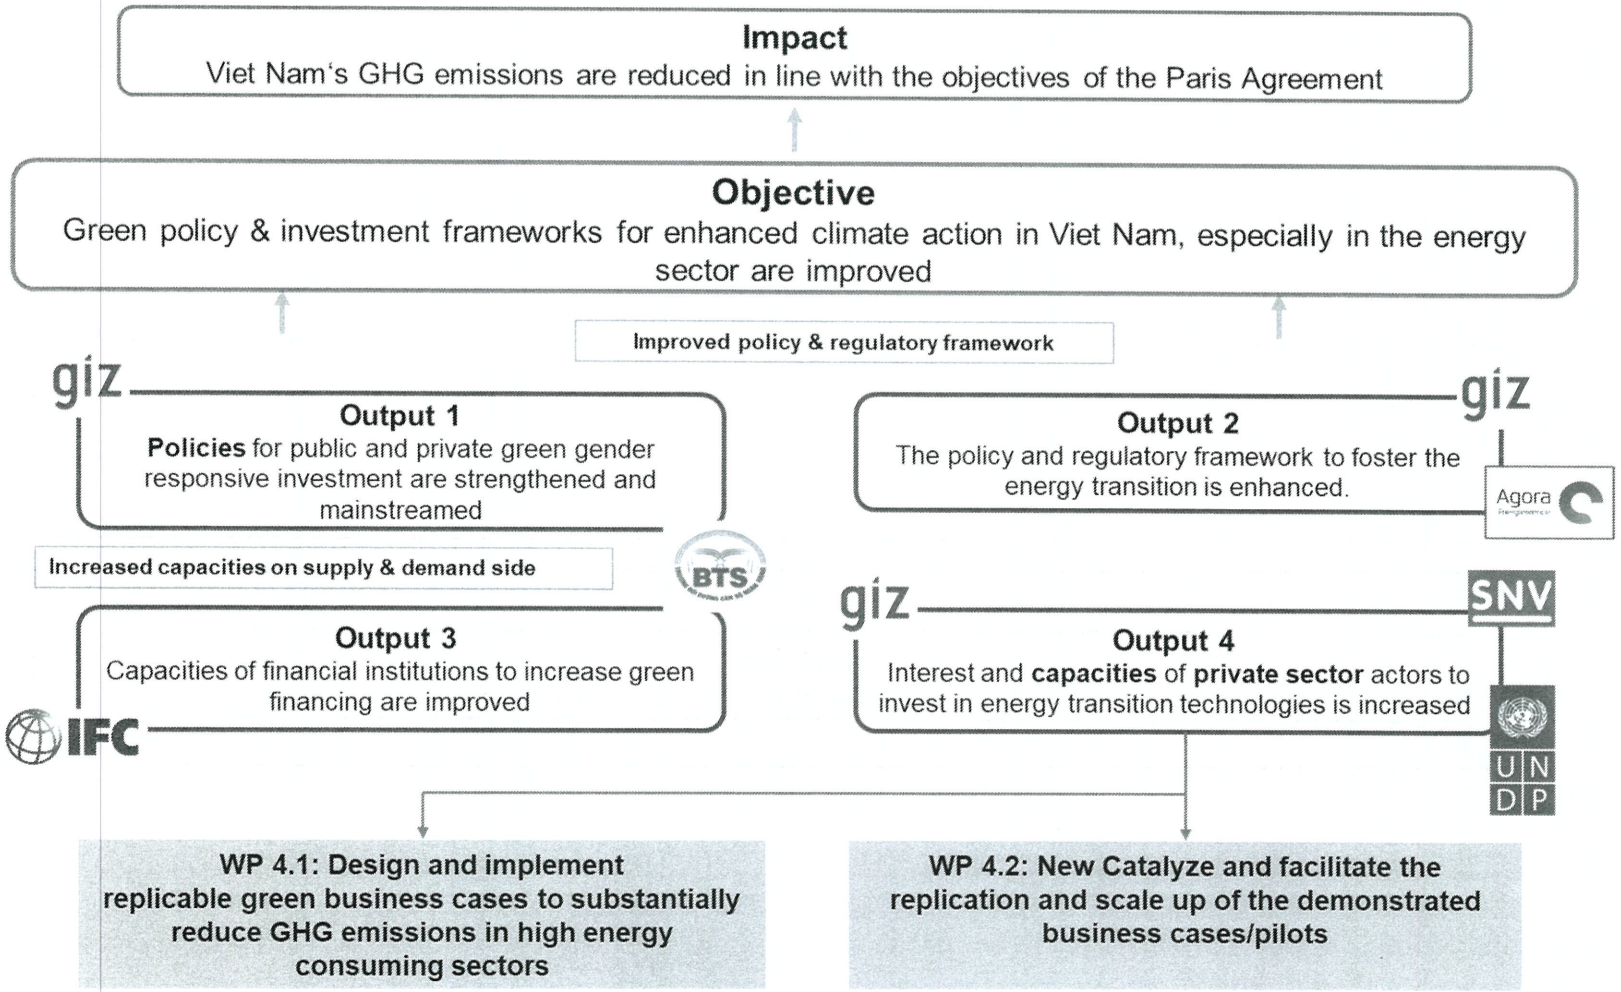

# III. RESULTS AND PARTNERSHIPS

### 3.1 Expected results

Complementing the Outputs of SHIFT, Output IV will take a bottom-up approach and aim to trigger companies to invest in best available energy transition technologies and so establish their viability and replicability in the Vietnamese context. UNDP work package, CLEAN-ACT project covers the WP IV.1 and IV.2, which will focus on large enterprises in high energy consuming and least energy efficient sectors and pilot state-of-the-art solutions for energy transition. WP IV.3 (SNV) will focus exclusively on the promotion of EE in SME of the industry sector via the creation of EE networks and fostering ESCOs. WP IV.4 (GIZ) will explore opportunities for innovative energy transition technologies in SME. Supporting women-led enterprises, or enterprises with a proven approach to promote gender equality, e.g. through positive gender discrimination and active programmes to remove gender-related barriers, will be a priority in all four work packages. The WPs will identify technologies which have the potential to be replicated and upscaled in Viet Nam, and in so doing to contribute significantly to GHG emissions mitigation efforts. The Output will prioritise creating the conditions for a sustained and long-lasting impact beyond the duration of SHIFT through capacity building programs on energy transition technologies and green investments for relevant players from the private sector, as well as for government officials and national organisations.

The CLEAN-ACT project aims to achieve the improved interest and capacities of the private sector – the interest and capacities of private sector actors especially women-led enterprises or enterprises with a proven approach to promote gender equality to invest in RE, EE or other energy transition technologies are increased. Detailed objectives as follows:

| Activity | Sub-activities | Results / Milestones | Sources of Verification, documentation* |
|---|---|---|---|
| **Output IV: Improved interest and capacities of the private sector – the interest and capacities of private sector actors especially women-led enterprises or enterprises with a proven approach to promote gender equality to invest in RE, EE or other energy transition technologies are increased** | | | |
| **Work Package IV.1: Design and implementation of replicable investment projects in energy transition technologies to substantially reduce GHG emissions in high energy consuming sectors** | | | |
| Activity (A IV.1.1): Conduct a thorough assessment of high energy consuming sectors and sub-sectors, and available energy transition technologies, select focus sectors and technologies to be piloted. | • Sub-Activity (S-A) IV.1.1.1: Study to select a minimum of two sectors/sub-sectors with high potential for energy savings, RE adoption, electrified equipment, and GHG emissions reductions and to identify the best energy transition technologies to be piloted.<br>• S-A IV.1.1.2: Presentation of assessment results to SHIFT steering structure (here: MPI, MOIT, GIZ, and other relevant consortium partners) and agreement on sectors/sub-sectors and technologies to be selected and piloted.<br>• S-A IV.1.1.3: Conduct energy audits with a detailed analysis of energy use and direct emissions inventory, if not available, in the two enterprises[1] chosen in the selected sectors. | Finalized Assessment Report to be produced at the end of 4Q-Yr1 | • Sector/sub-sector Surveys and Energy Audits.<br>• Assessment Report. |

[1] To select the enterprises, clear selection criteria such as strong balance sheet and financial creditworthiness, willingness to participate

| | | | |
|---|---|---|---|
| | • S-A IV.1.1.4: Presentation of energy audits and GHG emissions inventory to SHIFT steering structure (here: MPI, MOIT, GIZ, and other relevant consortium partners).<br>• S-A IV.1.1.5: Preparation of the final assessment report. | | |
| Activity (A IV.1.2): Design a minimum of two inclusive green investment projects to validate the technical and financial viability of the assessed energy transition technologies. | • S-A IV.1.2.1: Selection of minimum two the enterprises/companies within the identified sectors/sub-sectors that will implement the pilot projects in agreement with SHIFT's steering structure (here: MPI, MOIT, GIZ, and other relevant consortium partners), prioritizing women-led enterprises or enterprises with a proven approach to promote gender equality.<br>• S-A IV.1.2.2: Design of a minimum of two inclusive green investment pilot projects.<br>• S-A IV.1.2.3: Conduct Environmental and Social Impact Assessments for the two pilot projects. | Two project designs to be completed by the end of 4Q-Yr2 | • Project designs, incl. the preparation of roadmaps and workplans for implementation, assessment of budget required, selection of optimal financing schemes and financing sources, etc.<br>• Project implementation plans. |
| Activity (A IV.1.3): Provide technical support to selected enterprises to identify the best technology suppliers and most favourable financing instruments. | • S-A IV.1.3.1: Provide technical support to the enterprises to identify and procure the energy transition technologies.<br>• S-A IV.1.3.2: Provide technical support to the enterprises to identify and access the most favourable financing instruments and, if needed, facilitate the dialogue between the enterprises and the financial institutions. | Selection of technology supplier(s) and financing sources will be completed: by the end of 2Q-Yr3 for the first pilot, and by the end of 2Q-Yr4 for the second pilot, which will however start at the same time as the first pilot. | • Documentation for technology procurement.<br>• Documentation for requesting financial resources. |
| Activity (A IV.1.4): Oversee and provide support e.g. technical monitoring and recommendations throughout the implementation of the investment pilot projects. | • S-A IV.1.4.1: Provide technical support to the enterprises to implement the pilots,<br>• S-A IV.1.4.2: Collect and analyse data quarterly, including on GHG emissions and energy performance.<br>• S-A IV.1.4.3: Preparation of case studies and lessons learned for replication and scale-up. | Case studies and lessons learned by the end of 4Q-Yr4 | • Implementation progress reports.<br>• Case studies and lessons learned reports. |

and implement energy transition technologies, metric(s) of gender-equality, size, and significant potential for energy savings and GHG emissions reduction can be communicated among the SHIFT steering structure (*see Strategic sector orientation, sec. 7).*

| **Work Package IV.2: Catalyse and facilitate the replication and scale-up of the piloted energy transition technologies and other energy transition technologies** | | | |
|---|---|---|---|
| Activity (A IV.2.1): Design and implement a training programme for government officials and managers from national organizations on the assessment of 'next gen' transition technologies. | • S-A IV.2.1.1: Assessment of the gaps and needs to be filled and identification of the participants to the training programme.<br>• S-A IV.2.1.2: Development of gender inclusive training programme materials on "next gen" energy transition technologies.[2]<br>• S-A IV.2.1.3: Administration of the developed training materials.<br>• S-A IV.2.1.4: Evaluation of the training activities.<br>• S-A IV.2.1.5: Development of a catalogue of next-gen energy transition technologies.<br>• S-A IV.2.1.6: Establishment of sharing platform for the catalogue. | First next-gen energy transition technologies catalogue to be completed by the end of 2Q-Yr3 | • Training materials.<br>• Capacity building evaluation survey results.<br>• First next-gen energy transition technologies catalogue. |
| Activity (A IV.2.2): Design and implement a training programme on financial, environmental and social risks assessment, and technical and financial benefits of investment in energy transition technologies. | • S-A IV.2.2.1: Assessment of the gaps and needs to be filled and identification of the participants to the training programme by conducting a survey.<br>• S-A IV.2.2.2: Development of gender-inclusive training programme materials on financial, environmental, and social risks and benefits of investments in energy transition technologies.<br>• S-A IV.2.2.3: Administration of the developed training materials.<br>• S-A IV.2.2.4: Evaluation of the training activities.<br>• S-A IV.2.2.5: Training programme to Toot on the same subjects.<br>• S-A IV.2.2.6: Evaluation of these additional training activities. | Relevant stakeholders are capacitated to administer future capacity building programmes for enterprises by the end of 2Q-Yr3 | • Training materials, including the Toot programme.<br>• Capacity building evaluation survey results including the ToT programme. |
| Activity (A IV.2.3): Provide technical assistance and recommendations to enterprises[3] to integrate energy transition technology applications[4] within their business strategies and to develop | • S-A IV.2.3.1: Provide technical support to enterprises to develop investment portfolios in energy transition technologies.<br>• S-A IV.2.3.2: Provide technical support to enterprises to develop implementation budgets, timelines and workplans. | Replication of the investment projects and energy transition technologies piloted under | • Implementation progress reports for the replication projects.<br>• Enterprises' business |

[2] The term 'next-gen' (generation) technologies refers to technologies that are the current state-of-the-art or best available technologies at a certain moment in time: over the five years of the project, this will inevitably change as new technological advances are launched on global markets.

[3] UNDP will support 30 enterprises, 9 of which are led by women or with a proven approach promoting gender equality, contributing to the achievement of Indicator IV.1.

[4] Including the development and, where appropriate, the adoption of social and environmental safeguards procedures.

| | | | |
|---|---|---|---|
| respective investment portfolios. | • S-A IV.2.3.3: Provide technical support to enterprises to implement a minimum of 1 replication for each pilot. | WP IV.1 by the end of 4Q-Yr4 | strategies and annual reports. |
| Activity (A IV.2.4): Elaboration of lessons learned to inform policy development and awareness-raising events and initiatives to enhance replicability of pilots. | • S-A IV.2.4.1: Collect and analyse GHG emissions and energy performance data from the replication and scale-up projects of piloted as well as other energy transition technologies.<br>• S-A IV.2.4.2: Preparation of lessons learned and recommendations, based on the analysis performed in sub-activity S-A IV.2.4.1, to inform policy development.<br>• S-A IV.2.4.3: Awareness raising events and initiatives on benefits of investment projects.<br>• S-A IV.2.4.4: Establishment of a digital info platform to support the design and financing of investment projects.[5] | Lessons learned and a digital platform by the end of 4Q-Yr4 | • Awareness raising events.<br>• Documented lessons learned.<br>• Digital platform for data sharing. |

### 3.2. Project Log-frame

**Work Package IV.1: Design and implementation of replicable investment projects in energy transition technologies to substantially reduce GHG emissions in high energy consuming sectors**

***Activity (IV.1.1): Conduct a thorough assessment of high energy consuming sectors and sub-sectors, and available energy transition technologies, select focus sectors and technologies to be piloted.***

***Outputs***

- *One assessment report to select the high energy consuming sectors and sub-sectors, and the most suitable energy transition technologies to pilot.*
- *Two energy audits and one GHG emissions inventory in two chosen enterprises/companies, one for each selected sector/sub-sector (minimum of two).*

***Activities***

- UNDP will prepare the terms of reference and launch a competitive bidding process utilising UNDP procurement channels and applying UNDP evaluation and selection procedures for the recruitment of a specialized and experienced national consulting firm, to undertake the completion of a detailed assessment study.
- The procured national consulting firm will perform a thorough analysis for the selection of a minimum of two sectors/sub-sectors as well as the identification of the best and most financially sound energy transition technologies to be piloted (in that respective sector), using a combination of in-house expertise, information from public and business association databases, scientific literature, company reports, surveys and data collection procedures and other best practices. The national consulting firm will periodically report to UNDP, and if needed to the SHIFT Steering Committee (i.e., MPI, MOIT, GIZ, and other consortium partners), to assure that the assessment study is on track and report obstacles.

[5] To optimize resources and avoid duplication of efforts, it is planned to establish a single platform that will host all information under Activities IV.2.1 and IV.2.4.

- After completing the study, the national consulting firm will present its findings and the recommended criteria for selection to UNDP and the SHIFT Steering Committee to enable the selection of two sectors/sub-sectors and associated best available energy transition technologies.
- Once the sectors/sub-sectors and appropriate energy transition technologies are identified, the national firm will further support UNDP and the SHIFT Steering Committee for the selection of at least one enterprise/company for each of the selected sectors/sub-sectors and it will conduct a detailed on-site energy audit, including a GHG emissions inventory to establish a baseline scenario. The selection will be done in a gender inclusive manner, prioritizing women-led enterprises or enterprises with a proven approach to promote gender equality.
- The results of the energy audits and the GHG emissions inventory will be presented to UNDP and the SHIFT Steering Committee.
- As last step of the consultation, the national firm will prepare a detailed assessment report to be used for the design and implementation of two investment pilot projects.

***Activity (IV.1.2): Design a minimum of two inclusive investment projects to validate the technical and financial viability of the assessed energy transition technologies***

*Outputs:*

- *Two detailed designs of investment pilot projects, completed of implementation roadmaps, work plans, budgets, and selection of best financial scheme and financial sources.*
- *Two social and environmental safeguards reports for the installation of the energy transition technologies and the disposal of the replaced, obsolete technologies.*

*Activities*

- UNDP will prepare the terms of reference and launch a competitive bidding process utilising UNDP procurement channels and applying UNDP evaluation and selection procedures for the recruitment of a specialized national or international engineering firm, through a competitive bidding process, to undertake the design of a minimum of two investment projects based on the assessment report completed in Activity IV.1.1.
- Selection of the enterprises/companies that will implement the investment projects (preferably, the selected enterprises will be chosen among those audited under Activity IV.1.1, but it is not mandatory). Selection of enterprises will be done in close coordination with the SHIFT steering structure (MPI, MOIT, GIZ, and other consortium partners), in a gender inclusive manner, prioritizing women-led enterprises or enterprises with a proven approach to promote gender equality.
- The procured national or international engineering firm will execute a design of a minimum of two investment projects to pilot the chosen energy transition technologies. The designs will include detailed engineering designs, implementation roadmaps and work plans, an assessment of the technical and financial viability, selection of the optimal financing schemes and financing sources, etc.
- The procured national or international firm will develop an Environmental and Social Impact Assessment report, in alignment with the implementation of the energy transition technology. This may consider national and UNDP safeguard regulations and policies, monitoring & evaluation plan, mitigation and management plans, stakeholder mapping, review of potential gender-specific impacts etc.
- Completion of environmental and social safeguards procedures (i.e., mitigation and management) to guarantee the risk-free implementation of the new energy transition equipment as well as recycling and safe disposal of replaced obsolete equipment, and preparation of final reports with submission to UNDP and the Steering Committee for review and approvals before project implementation.

***Activity (IV.1.3): Provide technical support to selected enterprises to identify technology suppliers and financing instruments***

*Outputs*

- *One shortlist of domestic/international suppliers of the energy transition technologies to be implemented in the two investment projects to be piloted.*
- *One shortlist of market available financial instruments (including those designed and developed under Output III).*

*Activities*

- Recruitment of both national and/or international specialists, following UNDP recruitment and procedures and using UNDP recruitment channels, to integrate UNDP officials to form a Project Management Unit (PMU) for the implementation of all project activities and sub-activities under both WPs IV.1 and IV.2.
- The newly established PMU, in coordination with the engineering firm engaged under Activity IV.1.2, will provide technical support to the selected enterprises/companies to create a shortlist of domestic/international suppliers for the chosen energy transition technologies to be implemented in the investment projects to be piloted, based on considerations such as vendor surveys, market research, referrals, review of technical capabilities, financial evaluation (i.e., pricing proposal, O&M costs), delivery time, and due diligence (e.g., financial stability of supplier) etc, ranking each against the initial screening. The PMU will provide additional support for the selection of an optimal supplier.
- The PMU, in coordination with the engineering firm engaged under Activity IV.1.2, will provide technical support to the selected enterprises/companies to help them identify and access the most favourable financing instruments (either readily available on the market or designed and developed under Output III), by creating a shortlist which takes into consideration criteria such as available instruments (e.g., debt financing, equity, grants, bank loans etc.), project cost estimation and financing gap, priorities of the enterprise/company (e.g., minimising up-front costs, securing long-term funding etc.), preferences of the enterprise/company preference, matching requirements, interest rates, and repayment schedule etc. The PMU will provide additional support for the selection of an optimal financing instrument.

***Activity (IV.1.4): Oversee and provide support e.g. technical monitoring and recommendations throughout the implementation of the investment pilot projects***

***Outputs***

- *Two case studies/lessons learned reports, one for each investment project to be piloted, to be used for replication and scale-up. The reports will include also the GHG emissions and energy performance data collected and a subsequent analysis of the data collected*

***Activities***

- The engineering firm contracted in Activity IV.1.2, with support from UNDP and the PMU, will establish a communication channel with the selected enterprises to support the implementation stage. This will involve a combination of meetings upon pre-established intervals as well as organised on an ad hoc (as needed) basis.
- The engineering firm will perform annual on-site monitoring and evaluation of technical and energy performance, including GHG emissions to be compared to the baseline established under Activity IV.1.1 to determine energy savings and GHG emissions reduction as well as review of adherence to the S/EIA safeguards and gender equality initiatives.

- The engineering firm will prepare case studies and lessons learned which will be submitted to UNDP and the SHIFT Steering Committee for approval and later used for replication and scale-up under WP IV.2

**Work Package IV.2: Catalyse and facilitate the replication and scale-up of the piloted energy transition technologies and other energy transition technologies**

***Activity (IV.2.1): Design and implement a training programme for government officials and managers from national organizations on the assessment of 'next gen' transition technologies***

*Outputs*

- *One training programme for government officials, and managers from national organization and sectoral business associations on the assessment of next-gen energy transition technologies.*
- *One completed next-gen energy transition technologies catalogue.*
- *One sharing platform for sharing the next-gen energy transition technologies catalogue.*

*Activities*

- Recruitment of a specialized national consulting firm, through a competitive bidding process following UNDP procurement procedures and utilizing UNDP procurement channels, to undertake a capacity needs assessment and subsequently identify the participants to the training program among government officials, and managers from national organisations, e.g. the Viet Nam Chamber of Commerce and Industry (VCCI), or sectoral business associations. Participation of women will be actively pursued and encouraged.
- The contracted national consulting firm, based on the findings of the capacity needs assessment, will design the content of the gender-inclusive capacity building programme on the evaluation of "next gen" energy transition technologies, to capacitate these institutions to develop and periodically update catalogues of viable technologies in the Vietnamese context.
- The administration of the training activities will be done in person, unless unforeseeable condition will require virtual meetings, in a suitable location to be determined. The contracted national firm will deliver the training program in coordination with UNDP and the PMU.
- The consulting firm will be also responsible of performing an evaluation of the success of the training activities by preparing and administering a survey to the trainees after the capacity building programme is completed. Based on feedback of participants at the capacity building, the national consulting firm shall improve and modify the capacity building programme content.
- The trained stakeholders, under the supervision of UNDP and the national consulting firm, will develop the first catalogue of next-gen energy transition technologies. Communication channels and periodic meetings, both virtual and in person, will be set up to facilitate the completion of this task. The update of the catalogue will be an ongoing effort to be performed periodically also after the end of the SHIFT implementation period.
- UNDP will issue a technical terms of reference for the recruitment of a specialized national consulting firm, through a competitive bidding process and utilizing UDNP procurement channels, to design and establish a sharing platform for the catalogue and siting it at the offices of one of the participating institutions who will be responsible for operating and managing the platform (to be identified during the implementation of the activity). This process will require UNDP and the consulting firm to engage potential users and stakeholders by surveying and interviewing in order to understand their needs; determine their level of interest in the use of the platform on a sustained basis; and develop the platform for the participating institution based on the needs assessment and contacting potential users in order to tailor to their specific needs and catalogue formats
