DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

UNITED NATIONS DEVELOPMENT PROGRAMME

Empowered lives.
Resilient nations.

PROJECT DOCUMENT

State of Palestine

Project Title: Supporting transitions to solar energy in education and improving energy efficiency in Refugee Camps

Project Award/Number: PAL 10 120474/116664

Implementing Partners: Ministry of Education (MoE), Palestinian Energy and Natural Resource Authority (PENRA), Prime Minister's Office (PMO), Palestinian Electricity Regulatory Council (PERC), Palestinian Liberation Organisation (PLO) Refugee Committee, and UNRWA

Start Date:1 March 2021 **End Date:** 28 February 2022 **PAC Meeting date:**

Brief Description

Energy is essential for sustainable livelihoods as well as promoting a sustainable business environment. In the occupied Palestinian territory (oPt), energy scarcity and lack of access to energy are among the major constraints to socio-economic development, and a major contributor to the growing public debt. To this regard, this project aims to tackle two elements to enhance accessibility to quality electricity services through the expansion of solar energy for schools and universities, while also developing a pilot scheme to reduce electricity consumption in refugee camps. The project is in line with government priorities as highlighted in the National Policy Agenda, alongside emerging priorities post-COVID-19 to ensure quality service provision while also working towards enhancing the fiscal sustainability of the public budget. Beneficiaries of the project include 3,451 female students in the Gaza Strip and 150 refugees in one refugee camp in the West Bank.

Contributing Outcome (UNDAF/CPD, RPD or GPD):

UNDAF Strategic Priority 3: Supporting sustainable and inclusive economic development

- Outcome 3.3: Palestine's infrastructure, and natural and cultural resources are more sustainably used and managed

UNDAF Strategic Priority 4: Leaving no one behind: social development and protection

- Outcome 4.1: More Palestinians, especially the most vulnerable, benefit from safe, inclusive, equitable and quality services

Indicative Output(s) with gender marker[2]: GEN 2

Output 1: Improved educational facilities and learning environment for public schools through access to sustainable solar energy
Output 2: Feasibility of micro-gridding assessed for solar systems on schools and universities in the Gaza Strip to serve the surrounding community

Output 3: Pilot scheme developed in one refugee camp in the West Bank to reduce household electricity consumption

Total resources required:	USD 548,324	
Total resources allocated:		
	UNDP TRAC:	
	Government of Japan:	548,324
	Government:	
	In-Kind:	
Unfunded:		

Agreed by (signatures)[1]:

Government of Japan	UNDP	Implementing Partner
	Yvonne Helle	
Print Name:	Print Name: Special Representative	Print Name: PAPP
Date:	Date: 21-Jun-2021	Date:

[1] Note: Adjust signatures as needed

[2] The Gender Marker measures how much a project invests in gender equality and women's empowerment. Select one for each output: GEN3 (Gender equality as a principle objective); GEN2 (Gender equality as a significant objective); GEN1 (Limited contribution to gender equality); GEN0 (No contribution to gender quality)

Husam Tubail
Programme Portfolio Manager
17-Jun-2021


DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

I. DEVELOPMENT CHALLENGE

Energy is essential for sustainable livelihoods as well as promoting a sustainable business environment. In the occupied Palestinian territory (oPt), energy scarcity and lack of access to energy are among the major constraints to socio-economic development. Development challenges in the energy sector relate to poor energy security and efficiency, as 91% of energy is imported from Israel and between 15%-25% of energy is lost due to poor infrastructure. As a result, electricity prices in the oPt are the highest in the Middle East and North Africa (MENA) region.[2] Ultimately, high costs of electricity have a serious impact on reliable delivery of services, livelihoods and economic activity.

In the Gaza Strip, there has been a chronic electricity deficit since 2006, which was aggravated during the 2014 hostilities when the Gaza Power Plant (GPP) and large sections of internal distribution networks were destroyed. For a steady 24/7 power supply for the Gaza Strip between 500 and 600 megawatts of electricity is required, however only up to 200 megawatts is available, including 120 directly from Israel through 10 power lines and 60-80 generated by Gaza's power plant dependant on fuel purchases from international donors.[3] As a result, electricity supply is between 8-15 hours per day, not only affecting households but also critical public facilities including hospitals and schools.

Figure 1. Available electricity per month and electricity supply vs demand per month in the Gaza Strip in 2019[4]

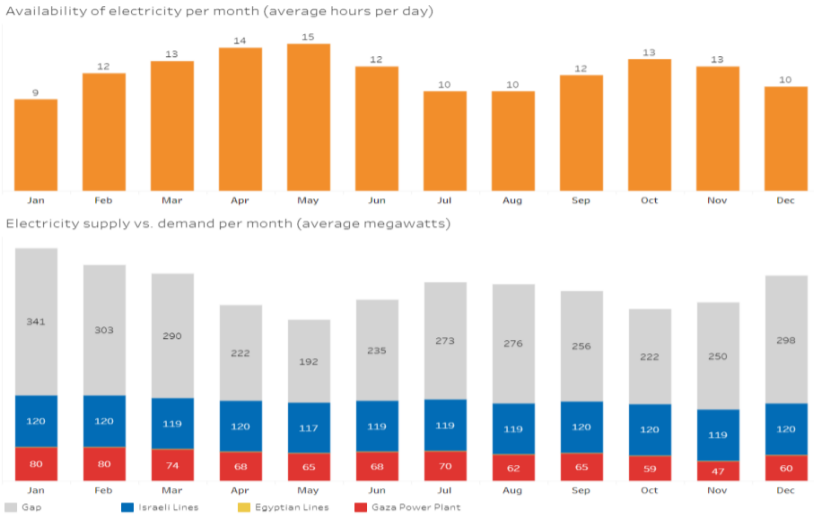

According to the Ministry of Education (MoE) statistical report from 2019, there are 409 governmental schools in the Gaza Strip, housed in 291 school buildings, where approximately 265,809 students (127,425 boys and 138,384 girls) attend class on daily basis. The majority - 57.7% of the schools - are operated on a two-shift system and are suffering from overcrowding. The students to classroom ratio stands at 39.4 students per classroom in governmental schools[5]. The shortage of electricity supply for schools has compromised students' access to adequate learning environment affecting students' ability to see the blackboards in the classrooms, especially during winter when daylight hours are shorter, and during early and late hours of the day brought about by the double shift system in schools.

In the West Bank, the accumulation of high debts over the last 5 years has been creating additional pressure on the Jerusalem District Electricity Company (JDECO) to meet the growing electricity demand. Last year, the Israeli Electricity Company (IEC) started reducing electricity supply to pressure JDECO to pay the accumulated debts. During which, over one million Palestinians living in large urban districts in Ramallah, Bethlehem, Jericho and Jerusalem were severely impacted by the shortage of electricity supply.

Based on JDECO's estimate, the overdue debt to IEC amounts to US$ 374 million and has accumulated largely on account of non-payment of electricity bills, mainly in the refugee camps and areas where Palestinian security do not have reach, such as rural areas in Area C. The non-payment of electricity in refugee camps is mainly due to the policy issued by the PA in 2000 exempting the Palestinians living in the refugee camps in the West Bank from paying electricity bills. According to JDECO's record for the period

[2] Palestine Investment Promotion Agency (PIPA), Renewable Energy Sector: Invest in Palestine

[3] Ibid.

[4] OCHA, Gaza Strip Electricity Supply

[5] According to MoEHE Annual Statistical Report 2018/2019

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

2014- 2020, the total accumulated debt for 13 refugee camps located in its jurisdiction in the West Bank was estimated at US$ 160 million, and the average payment for year 2019 was less than 10% of the cost of electricity purchased from IEC.

In attempt to solve this chronic problem, JDECO signed MOUs with 8 Banks operating in the West Bank, under which the Banks shall buy JDECO's entire debt to the IEC, provided that the Government pays its financial dues to JDECO in the form of monthly instalments. Amidst the Palestinian Authority's ongoing fiscal crisis, a technical committee was formed under the decision of Meeting # 67 on July 27, 2020 to find solutions to manage growing electricity debts incurred by refugee camps.

Recognizing the importance of reliable and affordable domestic sources of energy, the Palestinian Government has worked towards improving the enabling environment for renewable energy investment through improving government regulation and providing incentives. Furthermore, there has been a growing emphasis to contribute to greater energy efficiency through reducing technical and non-technical losses as a means to improve electricity provision while also reducing the overall costs incurred by the Palestinian Authority in electricity provision.

II. STRATEGY

With the growing socio-economic impacts of the COVID-19 pandemic on households alongside the growing public debt, the Palestinian Authority requires targeted support to reduce the financial burden on the public budget to continue to provide much needed service provision, while also improving the scope and quality of public services and utilities. The proposed project, thus, will support those furthest left behind in improving educational and living environments as a means to contribute to reducing electricity consumption in line with reducing the overall financial burden of electricity debts to the Palestinian Authority, in consideration of principles of climate change and mitigation.

UNDP/PAPP will employ the transformative resilience approach, which places national ownership and leadership, self-reliance, and Palestinian identity at its core. The transformative resilience approach through these pillars entails operationalizing the humanitarian-development (H-D) nexus on the ground through comprehensive and targeted interventions that address the multidimensional needs of vulnerable households, communities and institutions and ensure that no one is left behind.

To ensure access to quality education environment in Gaza, the project will introduce solar energy source as a sustainable solution, and energy efficiency measures such as LED luminaries. Solar photovoltaic (PV) panels are cost-effective and environmentally friendly solutions and offer multiple benefits of a clean and low-carbon source of energy for the education system. Where the Palestinian Authority and more specifically the Ministry of Education has been placing greater importance on the use of school rooftops for solar PV panels, UNDP and the Ministry of Education conducted a joint assessment of the potential of governmental schools' buildings to deploy solar energy. Through the assessment 250 school buildings were identified as suitable and prioritised based on first, second and third priority. Already 41 school buildings serving 51 schools have existing solar systems in place with the capacity of 18KWp.

Additionally, the project will aim to improve the living conditions of Palestinian refugees and incentivise their contribution to reducing electricity consumption through developing a pilot scheme to enhance energy efficiency of refugee households, with the potential to facilitate access to solar panels.

Under this initiative, UNDP in cooperation with the Palestinian Government, the PLO public committee for refugee camps, and UNRWA is looking towards developing and piloting an electricity consumption reduction scheme targeting Palestinians living in refugee camps.

The proposed project is aligned with the SDGs, namely ensuring quality education and protecting the environment, and access to energy (SDGs 4, 7, 11, 13, and 15). It is also in line with UNDP's strategy for safeguarding the environment and protecting natural resources, while securing proper access to basic services. Moreover, it is consistent with the UN initiative to mainstream renewable energy in vital service areas through sustainable practices and reducing the need for humanitarian fuel that is currently underfunded.

All interventions will be in line with the National Policy Agenda 2018-2022 and the Palestinian Energy Authority plans regarding the use of renewable energy. This project is also in direct alignment with the National Energy Efficiency Action Plan (2018-2020), which aims to:

- Increase sustainable use of energy in Palestine
- Achieving rational levels of energy independence and security of supply
- Achieving social and economic development in Palestine

This project is also in direct alignment with the national energy strategy, which aims to meet the following objectives:

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

- Strategic objective 1: Ensure greater capacity to meet and secure energy needs
- Strategic objective 2: Secure energy to consumers in sufficient quantities and technical and environmental specifications that meet international standards
- Strategic objective 3: Develop competent and efficient institutions working in the energy sector
- Strategic objective 4: A more efficient energy sector

This project aims to contribute to two of the overall goals in the government strategies - to reach 384 GWh energy efficiency by 2020 and develop renewable energy projects with a capacity of 120MW, from each strategy respectively. As such the theory of change is as follows:

Outcome	**Outcome 1:** Reduced reliance on conventional energy sources in targeted public schools and refugee households	
	If (1) educational facilities and the learning environment for targeted public schools in the Gaza Strip are improved through solar energy; if (2) the feasibility of micro-gridding is assessed for solar systems on schools and universities in the Gaza Strip to serve the surrounding community; and if (3) a pilot scheme is developed in one refugee camp in the West Bank to incentivize refugee households to undertake energy efficiency measures to reduce household electricity consumption; then the targeted public schools and refugee households will have a reduced reliance on conventional energy sources in line with meeting national energy security priorities	
Outputs	**Output 1**: Improved educational facilities and learning environment for targeted public schools in the Gaza Strip through access to sustainable solar energy	**Output 3**: Pilot scheme developed in one refugee camp in the West Bank to reduce household electricity consumption
	Output 2: Feasibility of micro-gridding assessed for solar systems on schools and universities in the Gaza Strip to serve the surrounding community	
Assumptions	-Increasing renewable energy generation on the rooftops of public buildings will reduce operational costs of public facilities -Solar energy produced will be able to allow for additional energy for the wider community if micro-gridding is undertaken -the Ministry of Education has the capacity to oversee and manage newly constructed solar infrastructure	-Refugee households will voluntarily want to engage in the scheme to improve their housing conditions to improve HH energy efficiency -Improving HH energy efficiency in targeted HH will reduce electricity consumption of targeted HH by up to 25% -If successful this model can be scaled up in other refugee camps
Risks and barriers	- Potential damage to infrastructure if conflict escalates - Restrictions to access to required materials	- Refugee camps reluctant to engage in the scheme in light of current policy of free electricity for refugee HHs - Potential conflict of interest between stakeholders that could delay or hinder project implementation

III. RESULTS AND PARTNERSHIPS

The overarching objective of this project is to ***reduce the reliance on conventional energy sources in targeted public schools and refugee households*** through energy efficiency measures and installation of rooftop solar PV cells. The project is divided into two components based on geography and interventions: component 1, which aims to increase the number of schools in the Gaza Strip benefiting from solar energy; and component 2, which aims to develop a pilot scheme to incentivise refugee households in one refugee camp in the West Bank to reduce household electricity consumption.

Project component 1: Solar for educational facilities in the Gaza Strip

Through previous and ongoing programming, UNDP/PAPP has coordinated with the MoE to evaluate the potential for utilising school rooftops for the installation of solar PV systems in the Gaza Strip, in line with the government priorities and ongoing initiatives in public schools in the West Bank. Through the joint assessment "Solar Energy Needs Assessment for Governmental Schools in the Gaza Strip" carried out by UNDP/PAPP and the MoE three school buildings have been identified in line with the project scope identified in the following table. Where in recent years UNRWA and governmental schools have been utilised as shelters during crises periods in the Gaza Strip, the selected three schools also have the capacity to host 2,492 internally displaced persons (IDPs), who would also benefit from the generated electricity supply from the installed solar systems.

School Name	Location	# Shifts	Level	School Sex	# Students	Has Shelter?	# IDPs

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

Mostafa Hafez	West Gaza	2	Primary	Female	1,869	Yes	800
Mamdouh Sidam	Middle / Al-Nuseirat	1	Secondary	Female	900	Yes	846
Hamad Ben Khalifa	North / Beit Lahia	1	Secondary	Female	682	Yes	846

Based on technical assessments and in consultation with the MoE, the energy requirement for the schools was determined at 25 KWp for each school building which covers the needed energy loads. Through installation of solar PV cells to cover the needed energy for the school buildings, while undertaking energy efficiency measures within the selected buildings, the project will also contribute to the improvement of the quality of educational services delivered to 3,451 female primary and secondary students through improved lighting, insulation and services within the school building. To ensure the sustainability, the project will also provide training for the engineering team at the Ministry of Education who will be responsible of operation and maintenance of these facilities.

Furthermore, to pave the way for future investments in solar energy for educational facilities in Gaza, a study will be carried out to investigate the feasibility of implementing microgrid-operational opportunities with schools' and universities' solar systems to be able to serve the surrounding community. A microgrid is a self-sufficient localised energy system that serves a discrete area, for example hospital complexes, university campuses or neighbourhoods. Microgrids have the potential to improve the security of the electricity supply, particularly valuable in the context of intermittent electricity supply in the Gaza Strip, through the flexibility of switching between 'island mode' or supply from the wider grid.

To this regard the project outputs and activities under component 1 are as follows:

- **Output 1:** Improved educational facilities and learning environment for public schools through access to sustainable solar energy

Activities:


1.1 Selection of schools and setting up relevant technical arrangements, including coordination with the MoE
1.2 Procurement and installation of solar systems in 3 targeted schools
1.3 Application of energy efficiency measures in the schools' premises
1.4 Capacity building of the engineering team at the Ministry of Education

- **Output 2:** Feasibility of micro-gridding assessed for solar systems on schools and universities in the Gaza Strip to serve the surrounding community

Activities:

1.1 Feasibility study on the application of microgrid system on educational facilities
1.2 Private sector engagement through stakeholder meetings
1.3 Dissemination of study findings

Figure 1 Refugee camps West Bank (Source: UNRWA)

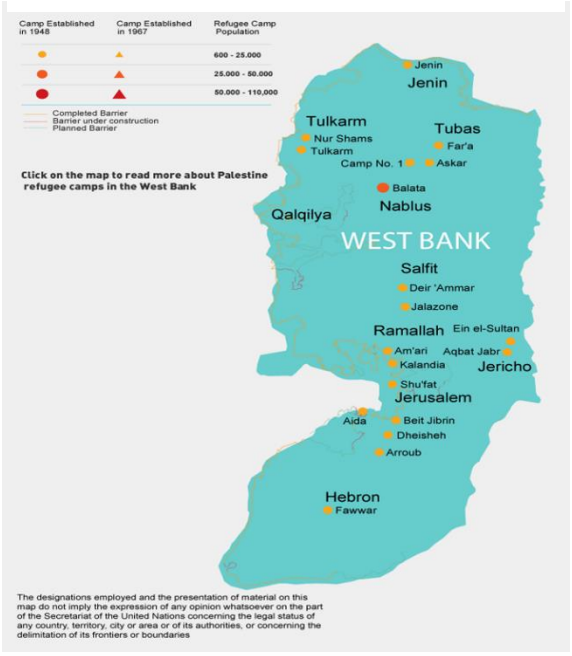

Project component 2: Reducing electricity consumption in targeted refugee camps

Under this component, the project aims to develop and pilot an incentive scheme to reduce electricity consumption that can be replicated and scaled up in the future, as a framework for reducing the contribution of the 19 refugee camps located in the West Bank to overall electricity debt. The scheme aims to reduce the overall electricity debt associated with the non-payment of refugee households of electricity and electricity loss. Annual electricity consumption per capita in the West Bank in 2018 was 1,148.7 KWh/capita according to PCBS, where according to PENRA, refugee camps consume significantly more

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

electricity than other areas in the West Bank, owing to electricity provision being free for refugee camps. Payment collection in refugee camps can be as low as 7%. With an increasing population and growing electricity demand, the compounding electricity debt is a critical challenge for the Palestinian government to overcome.

As a pilot, the scheme will be designed in cooperation with PENRA, JDECO and other stakeholders highlighted below to contribute to reducing the overall debt through the following measures:

<table>
<tr><td colspan="3">Incentives to attract voluntary Household (HH) participation into the project</td></tr>
<tr><td colspan="3">• Eligible for HHs with existing electricty debts
• Potential to reschedule existing HH electricity debt payments with JDECO
• Improved housing conditions in terms of insulation, solar water heaters, lighting, and appliances</td></tr>
<tr><td colspan="3">⏬ ⏬</td></tr>
<tr><td colspan="3">Interventions implemented by:</td></tr>
<tr><td>To</td><td>UNDP</td><td>JDECO/PENRA</td></tr>
<tr><td>Reduce Consumption by 20-25%</td><td>Home improvement energy efficiency measures;
advocate for behavioural change</td><td></td></tr>
<tr><td>Increase collection and reduce theft in the future</td><td></td><td>Installation of prepaid meter and tracking system for theft for participating households</td></tr>
<tr><td colspan="3">⏬ ⏬</td></tr>
<tr><td colspan="3">Impact</td></tr>
<tr><td colspan="3">• Reduction of electricity debt from targeted refugee HHs</td></tr>
</table>

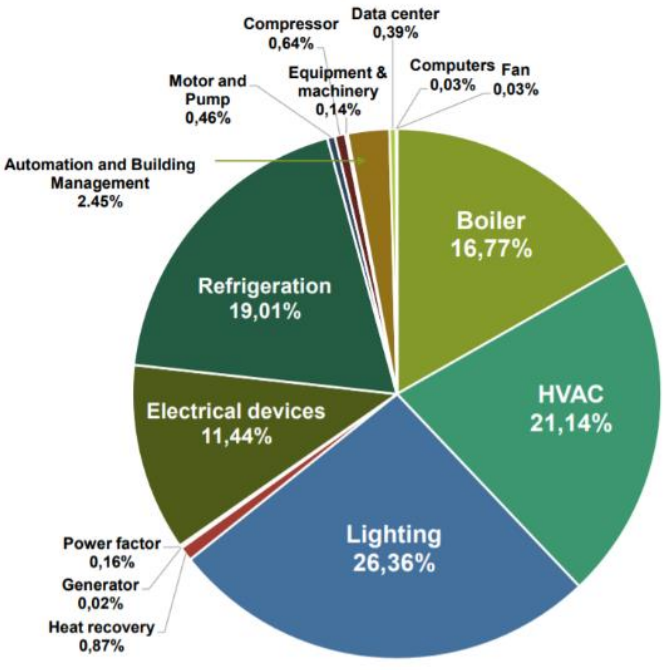


Figure 2 Share of national energy saving potential (source: meetMED)

There are around 775,000 registered refugees in the West Bank, where approximately one quarter live in the 19 refugee camps in the West Bank. This scheme will be tested in one refugee camp in the West Bank, prioritising smaller refugee camps to achieve a higher impact in the total electricity consumption reduction of the camp. Households will be asked to participate voluntarily, where 20 will be selected that meet the basic criteria, in coordination with Public refugee committee in the selected Camp and PENRA, including current housing conditions, poverty levels and other socioeconomic indicators, and validated through site visits. Home improvement measures will prioritise insulation, solar rooftop water heaters, lighting and refrigerators as the areas with the highest potential to increase the share of national energy saving potential across HHs. End beneficiaries will be around 140 men, women and children.

The output and activities under component 2 are as follows:

Output 3: Pilot scheme developed in one refugee camp in the West Bank to reduce household electricity consumption

UNDP in coordination with the Prime Minister's Office, PLO Public Committee for Refugee Camps, Palestinian Energy and Natural resources Authority, Palestinian Electricity regulatory Council, Jerusalem District Electricity Company and UNRWA will undertake the following activities to develop an electricity consumption reduction scheme to incentivise the reduction of electricity consumption in refugee camps.

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

Activities:

1.1 Stakeholder mapping and analysis of relevant actors and interventions targeting energy consumption and efficiency in refugee camps
1.2 Preparation for the pilot phase. This activity includes undertaking a detailed methodology, feasibility study and detailed design for the pilot phase, including selection of the refugee camp to pilot the scheme in coordination with stakeholders. This includes relevant data collection and validation about electricity consumption, payment rates, and compounding debts in in the selected camp to feed into the formulation of baselines for the project.
1.3 Energy efficiency measures for selected 20 households in accordance to the recommendation of the feasibility study and the detailed design, including home improvement measures to enhance the insulation of the house and ensure replacement of old and inefficient large appliances
1.4 New directives to reduce and regulate electricity consumption
1.5 Awareness raising for behavioral change to reduce electricity consumption

Partnerships

Under component 1 focused on enhancing the share of renewable energy production and impact for educational facilities in Gaza, the primary partner is the Ministry of Education, to which UNDP has already partnered with towards this goal in other projects, and PENRA for the technical oversight of the solar systems. This includes the joint assessment and planning activities conducted to highlight the feasibility and priority sites across government school buildings in the Gaza Strip. The MoE has been consulted for the development of this project to validate the 3 targeted school buildings proposed, in line with the ministry's priorities and plan. The MoE and PENRA will be engaged throughout the implementation of this component to ensure alignment with standards required and to facilitate the handover of the solar systems to the MoE, more specifically the Engineering team, for operation and maintenance post-project.

Under component 2 focused on developing a pilot incentive scheme targeting refugee households to reduce electricity consumption, this project builds on existing and new partnerships with several government and UN stakeholders including the Prime Minister's Office (PMO), the Palestinian Energy and Natural Resources Authority (PENRA), the Palestinian Electricity Regulatory Council (PERC), the Jerusalem District Electricity Company (JDECO), the Palestinian Liberation Organisation (PLO) Public Committee for Refugee Camps and the United Nations Relief and Works Agency for Palestinian Refugees (UNRWA). Where UNDP is currently engaged with the PMO to support the effective socioeconomic response and recovery planning and measures taken on account of the COVID-19 pandemic, this component aligns with the government decision to form a technical committee to find solutions to manage growing electricity debts incurred by refugee camps. PENRA's engagement is a key and ensured on the basis of their mandate and responsibility for policymaking, development and implementation of the national strategy with regards to renewable energy and energy efficiency measures, while PERC is engaged as the regulatory body for the energy sector, including granting licenses. JDECO is the largest and oldest electricity distribution company, where JDECO's share of total electricity imports to the oPt is approximately 38%. Following an agreement between the Palestinian Authority and Israel in 2016 making the Palestinian Authority exclusively responsible for the electricity sector, JDECO's liabilities (i.e. debts) were transferred to the Palestinian Authority, and therefore became subject to deductions form clearance revenues. As a result, the Palestinian Authority bears financial liability to the Israeli Electricity Company, including the bill for 13 refugee camps located within JDECO's service area. The PLO public committee for refugee camps and UNRWA are key partners to this component, on account of their mandate over refugees and refugee camps. The PLO public committee will particularly be an important partner to ensure the interests of refugees are represented and to facilitate voluntary applications from refugee HH to engage in the scheme.

Risks and Assumptions

	Description	**Risk category**	**Impact and Likelihood**	**Risk treatment/Management Measures**	**Risk owner**
1	Continued outbreak of COVID 19 may prevent timely implementation of the project.	Operational	Likelihood = 4 Impact = 2	UNDP will monitor government announced restrictions to determine necessary adjustment in the implementation measures. If COVID 19 restrictions continue much of the work associated with the project activities will be implemented virtually as in person meetings and gatherings will be restricted.	UNDP's Operations Head

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

2	Deterioration of the security situation in the WB, EJ and Gaza and increased movement restrictions	Operational Safety and Security	Likelihood = 2 Impact = 3	UNDP will continuously monitor the situation in coordination with UNDSS. UNDP has dealt with similar scenarios in the past and has the necessary experience to adapt to changes in programme implementation.	UNDP's Head of Security in coordination with UNDSS
3	Restricted access to relevant materials required for implementation in Gaza	Operational	Likelihood = 2 Impact = 4	UNDP has substantial previous experience in undertaking solar projects in Gaza, whereby UNDP can also utilise other programming, such as the access coordination unit project, to facilitate the entry of needed materials and items into the Gaza Strip.	UNDP's Operations Head and UNDP's Programme Analyst
4	The Palestinian government or associated institutions willingness to engage in the programme decreases and/or elections result in change of government and government priorities	Political	Likelihood = 2 Impact = 4	UNDP has a longstanding partnership with the Palestinian government and has ongoing projects that aim to build national capacities to be responsive to the needs of the Palestinian people. This includes the Prime Minister's Office and several line ministries, to which UNDP has an excellent working relation with. Furthermore, as compounding electricity debt remains to be an important issue on account of the diminishing financial sustainability of the Palestinian government, in the case of a change in government, this issue will likely to persist in its importance. Furthermore, the programme also engages with ministerial staff at the technical level, who often remain the same despite a change in government.	UNDP's Programme Analyst
5	Exchange rate fluctuation has an impact on available resources.	Financial	Likelihood = 2 Impact = 4	UNDP will monitor markets and UNDP official exchange rate. If any major fluctuation occurs will be reported to donor for discussion.	UNDP's Programme Analyst
6	Refugee HH reluctant to participate and/or low number of applications	Strategic	Likelihood = 3 Impact = 3	In the selection of the targeted refugee camp to pilot the scheme, UNDP will engage with PENRA and the PLO public committee for refugee camps to select a refugee camp, where residents would be more likely to want to participate in such a scheme. Furthermore, the PLO public committee will be engaged throughout the implementation of the component to have a direct channel to refugees to facilitate awareness and information dissemination to refugees on the importance of energy saving measures, and enable a channel for refugees to voice their concerns over the component. During the first year of the project, UNDP with partners will develop a communications strategy in light of the sensitivity of the issue to be implemented prior to the start of implementation in 2022.	UNDP Programme Analyst and UNDP communications specialist
7	Breakdown in partnership amongst stakeholders	Strategic	Likelihood = 3 Impact = 3	This risk is particularly relevant for component 2, where the success of the scheme depends on cooperation and a successful partnership amongst several stakeholders with slightly competing interests. As such, during the first year of the project UNDP will regularly engage partners bilaterally and jointly as a means to enhance engagement and communication amongst partners, where UNDP will act as a facilitator. In the development of the scheme each partner will be engaged to also ensure the elements of the scheme are diverse to	UNDP Programme Analyst

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

				meet the interests of all stakeholders, including refugee households, JDECO and the government.	

Knowledge

Within the scope of this project, 1 knowledge product will be generated, including the results from the feasibility assessment undertaken under component 1 around islanding/micro gridding potential for solar systems on educational facilities to meet the wider community's energy needs, and the development of the pilot scheme under component 2 following the finetuning and implementation of the component highlighting the process of the development of the scheme, evaluation and impact. The document will be utilised as a basis for future resource mobilisation on these two components.

Sustainability and Scaling Up

Through the consultations and partnerships engaged and envisioned for the project, the project ensures strong national ownership of the project scope and results in its alignment with government priorities and engagement of relevant ministries. For component 1, this project builds on ongoing engagements with the Ministry of Education and successful transfer of solar systems to the MoE engineering team to manage and operate, with the technical support of PENRA. Furthermore, through the feasibility study, the goal is to enhance the sustainability of future solar energy projects for educational facilities through expanding service provision for the wider community surrounding educational facilities.

For component 2, as a pilot scheme, the strategy for scaling up builds on the numerous partners engaged in its implementation, whereby, following demonstratable success, all stakeholders will have an interest to scale up the scheme, with the potential of it being taken on as a national initiative to enhance energy efficiency and tackle electricity consumption of refugee camps in the West Bank under the leadership of the Prime Minister's Office, with the support of UNDP.

Both components are designed in a way that catalyses additional resource mobilisation in renewable energy and energy efficiency towards strengthening the energy security of the oPt.

IV. PROJECT MANAGEMENT

The project will be directly executed by UNDP following the Direct Implementation Procedures (DIM). Under this modality, UNDP takes full responsibility for implementation, management, and achievement of project objectives. The UNDP technical team will be working in close cooperation with the concerned national stakeholders, namely, MoE, PENRA and GDECO to deliver the results under the first component and with the Prime Minister's Office, PLO Public Committee for Refugee Camps, Palestinian Energy and Natural resources Authority, Palestinian Electricity regulatory Council, JDECO, and UNRWA to deliver the results of the second component. UNDP will also partner with the Palestinian Green Building Council, specialized NGO in promoting green buildings in Palestine, to undertake survey, design of energy efficiency measures for the pilot phase under component #2.

The UNDP team will carry out day-to-day management and supervision of the project's activities with proper monitoring and evaluation as well as quality assurance. UNDP will also ensure stakeholders engagement throughout the planning, design and implementation processes and will cooperate with relevant bodies and donors in all stages of the process in order to achieve sustainable results. Moreover, entry of materials and equipment for project activities under the first component will be facilitated by UNDP through the existing UNDP access mechanism, managed by a team dedicated to securing material access to its projects in the Gaza Strip.

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

V. RESULTS FRAMEWORK[6]

Intended Outcome as stated in the UNDAF/Country [or Global/Regional] Programme Results and Resource Framework:

UNDAF Strategic Priority 3: Supporting sustainable and inclusive economic development

- Outcome 3.3: Palestine's infrastructure, and natural and cultural resources are more sustainably used and managed

UNDAF Strategic Priority 4: Leaving no one behind: social development and protection

- Outcome 4.1: More Palestinians, especially the most vulnerable, benefit from safe, inclusive, equitable and quality services

Project outcome: Reduced reliance on conventional energy sources in targeted public schools and refugee households

Outcome indicators as stated in the Country Programme [or Global/Regional] Results and Resources Framework, including baseline and targets:

Project outcome indicator:

- Reduced consumption from non-renewable energy sources reflected in KW and USD savings

Applicable Output(s) from the UNDP Strategic Plan:

Project title and Atlas Project Number:

EXPECTED OUTPUTS	OUTPUT INDICATORS[7]	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)						DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2				FINAL	
Output 1 *Improved educational facilities and learning*	***1.1*** *Number of schools targeted*	*Reporting*	*-*	*-*	*3*	*-*				*3*	*Reporting*
	1.2 *Total capacity of installed solar energy systems in targeted schools*	*Reporting*	*-*	*-*	*75KWp*	*-*	*-*	*-*	*-*	*75KWp*	*Electricity meter and technical assessment by project team*

[6] UNDP publishes its project information (indicators, baselines, targets and results) to meet the International Aid Transparency Initiative (IATI) standards. Make sure that indicators are S.M.A.R.T. (Specific, Measurable, Attainable, Relevant and Time-bound), provide accurate baselines and targets underpinned by reliable evidence and data, and avoid acronyms so that external audience clearly understand the results of the project.

[7] It is recommended that projects use output indicators from the Strategic Plan IRRF, as relevant, in addition to project-specific results indicators. Indicators should be disaggregated by sex or for other targeted groups where relevant.

environment for public schools through access to sustainable solar energy	***1.3** Number of students benefiting from improved access to renewable energy*	*Reporting*	-	-	*3,451 (100% F)*	-	-	-	-	*3,451 (100% F)*	*Schools' enrolment information*
Output 2 *Feasibility of micro-gridding assessed for solar systems on schools and universities in the Gaza Strip to serve the surrounding community*	***2.1** Number of studies conducted*	*Copy of final assessment*	-	-	*1*	-	-	-	-	*1*	*Copy of final assessment*
	***2.2** Number of schools and universities assessed*		-	-	*TBD*	-	-	-	-	*TBD*	*Through the feasibility assessment*
Output 3: *Pilot scheme developed in one refugee camp in the West Bank to reduce household electricity consumption*	***3.1** Number of refugee HH targeted*		-	-	-	*20*	-	-	-	*20*	*Project reporting*
	***3.2** Average electricity consumption of targeted HH*		1,148.7 KWh/ capita for WB HHs For targeted HH: (TDB)	*2018*	-	-	-	-	-	*20% reduction*	*Through electricity meters and technical assessment of project team*

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

VI. MONITORING AND EVALUATION

In accordance with UNDP's programming policies and procedures, the project will be monitored through the following monitoring and evaluation plans:

Monitoring Plan

Monitoring Activity	Purpose	Frequency	Expected Action	Partners (if joint)	Cost (if any)
Track results progress	Progress data against the results indicators in the RRF will be collected and analysed to assess the progress of the project in achieving the agreed outputs.	Quarterly, or in the frequency required for each indicator.	Slower than expected progress will be addressed by project management.		
Monitor and Manage Risk	Identify specific risks that may threaten achievement of intended results. Identify and monitor risk management actions using a risk log. This includes monitoring measures and plans that may have been required as per UNDP's Social and Environmental Standards. Audits will be conducted in accordance with UNDP's audit policy to manage financial risk.	Quarterly	Risks are identified by project management and actions are taken to manage risk. The risk log is actively maintained to keep track of identified risks and actions taken.		
Learn	Knowledge, good practices and lessons will be captured regularly, as well as actively sourced from other projects and partners and integrated back into the project.	Annually	Relevant lessons are captured by the project team and used to inform management decisions.		
Annual Project Quality Assurance	The quality of the project will be assessed against UNDP's quality standards to identify project strengths and weaknesses and to inform management decision making to improve the project.	Annually	Areas of strength and weakness will be reviewed by project management and used to inform decisions to improve project performance.		
Review and Make Course Corrections	Internal review of data and evidence from all monitoring actions to inform decision making.	Annually	Performance data, risks, lessons and quality will be discussed by the project board and used to make course corrections.		
Project Report	A progress report will be presented to the Project Board and key stakeholders, consisting of progress data showing the results achieved against pre-defined annual targets at the output level, the annual project quality rating summary, an updated risk long with mitigation measures, and any evaluation or review reports prepared over the period.	Annually, and at the end of the project (final report)			

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

Project Review (Project Board)	The project's governance mechanism (i.e., project board) will hold regular project reviews to assess the performance of the project and review the Multi-Year Work Plan to ensure realistic budgeting over the life of the project. In the project's final year, the Project Board shall hold an end-of-project review to capture lessons learned and discuss opportunities for scaling up and to socialize project results and lessons learned with relevant audiences.	Annually	Any quality concerns or slower than expected progress should be discussed by the project board and management actions agreed to address the issues identified.		

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

VII. MULTI-YEAR WORK PLAN [89]

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount (USD)
Output 1 *Improved educational facilities and learning environment for public schools through access to sustainable solar energy*	1.1Installation of 25KWp solar systems on three school buildings, implementation of energy efficiency measures, and training for the MoE engineering team	195,000	-	-	-	UNDP	GoJ	Contractual services	195,500
	Sub-Total for Output 1								
Output 2: *Feasibility of micro-gridding assessed for solar systems on schools and universities in the Gaza Strip to serve the surrounding community*	1.2 Feasibility assessment of islanding/micro-grid operational opportunities for solar systems on educational facilities	25000	-	-	-	UNDP	GoJ	Contractual services	25,000
	Sub-Total for Output 2								
Output 3: *Pilot scheme developed in one refugee camp in the West Bank to reduce household electricity consumption*	1.3 Pilot scheme to reduce electricity consumption in refugee camps tested in one refugee camp	80,000	100,000	-	-	UNDP and PALGBC	GoJ	Contractual services	180,000
	Sub-Total for Output 2								
Knowledge production	Development of knowledge product for output 2 and output 3	-	15,000	-	-	UNDP	GoJ	Contractual services	15,000

[8] Cost definitions and classifications for programme and development effectiveness costs to be charged to the project are defined in the Executive Board decision DP/2010/32

[9] Changes to a project budget affecting the scope (outputs), completion date, or total estimated project costs require a formal budget revision that must be signed by the project board. In other cases, the UNDP programme manager alone may sign the revision provided the other signatories have no objection. This procedure may be applied for example when the purpose of the revision is only to re-phase activities among years.

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

Project implementation costs	*Energy efficiency expert for 6 months* *2 site engineers for 4 months* *GOE* *Project associate DPC for 2 months* *Procurement and finance DPC* *Misc.* *Audit*	67,500	20,181	-	-	UNDP	GoJ		87,681
General Management Support 8%		29,400	10,814	-	-	UNDP	GoJ		40,214
Sub-total									542,895
Levy 1%		5,429							5,429
TOTAL									**548,324**


DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

VIII. GOVERNANCE AND MANAGEMENT ARRANGEMENTS

The project will be overseen by a Project Board, comprising the Government of Japan (as senior supplier), the PMO (as senior beneficiary), the UNDP executive (as implementing partner), and JICA. The direct oversight of the project within UNDP will be through the Programme Analyst responsible for the UNDP Energy and natural resources portfolio, who will hold a programmatic quality assurance role during the implementation phase to be responsible for ensuring all deliverables of the project, including the annual work plan, are achieved. The project board will meet annually to review progress and undertake decision-making relevant for the project.

Other Programme Analysts responsible for natural resources, governance and economic development portfolios will be called upon to provide technical advice and support, if required and based on their capacities and projects' areas of focus. The team will be supported by the Assistant Special Representative who would provide overall strategic guidance and direction, and by the Deputy Special Representative who will provide high-level oversight.

The project team will consist of a project coordinator who will be responsible for the day to day management, and 2 site engineers to support implementation and oversight of infrastructure-related components. In addition, UNDP's business services support unit, finance and procurement teams will support project finances and perform procurement and other support requirements for the team.

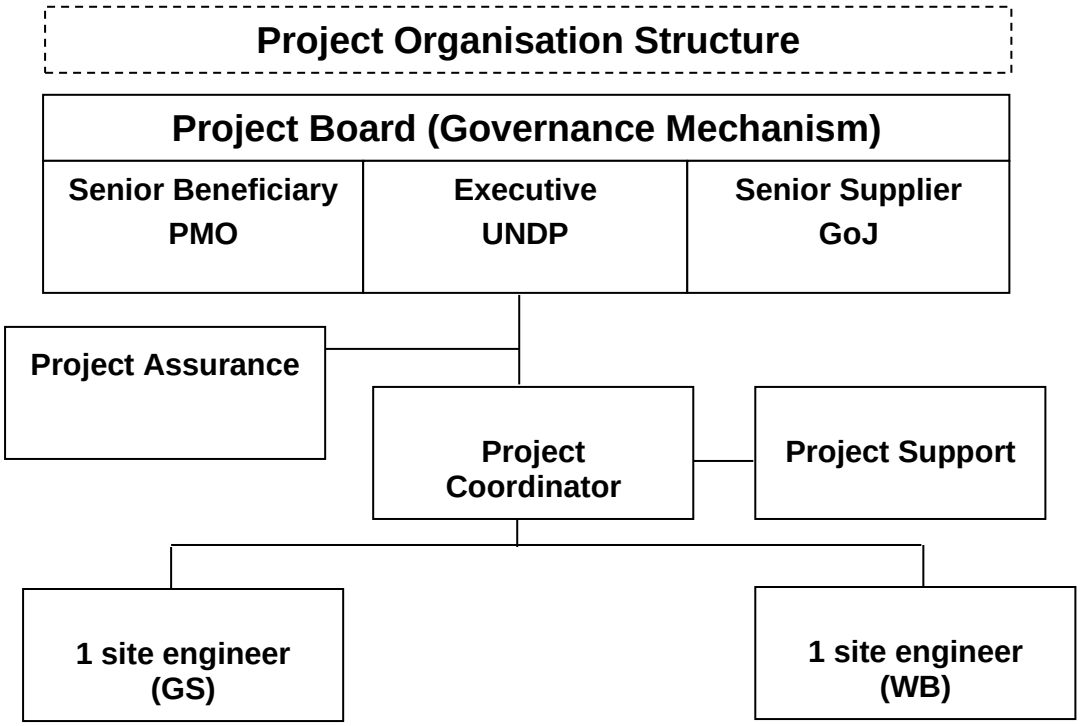

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

IX. LEGAL CONTEXT

*[NOTE: Please choose **one** of the following options, as applicable. Delete all other options from the document]*

Option a. Where the country has signed the Standard Basic Assistance Agreement (SBAA)

This project document shall be the instrument referred to as such in Article 1 of the Standard Basic Assistance Agreement between the Government of (country) and UNDP, signed on (date). All references in the SBAA to "Executing Agency" shall be deemed to refer to "Implementing Partner."

This project will be implemented by [name of entity] ("Implementing Partner") in accordance with its financial regulations, rules, practices and procedures only to the extent that they do not contravene the principles of the Financial Regulations and Rules of UNDP. Where the financial governance of an Implementing Partner does not provide the required guidance to ensure best value for money, fairness, integrity, transparency, and effective international competition, the financial governance of UNDP shall apply.

Option b. Where the country has NOT signed the Standard Basic Assistance Agreement (SBAA)

The project document shall be the instrument envisaged and defined in the Supplemental Provisions to the Project Document, attached hereto and forming an integral part hereof, as "the Project Document".

This project will be implemented by [name of entity] ("Implementing Partner") in accordance with its financial regulations, rules, practices and procedures only to the extent that they do not contravene the principles of the Financial Regulations and Rules of UNDP. Where the financial governance of an Implementing Partner does not provide the required guidance to ensure best value for money, fairness, integrity, transparency, and effective international competition, the financial governance of UNDP shall apply.

Option c. For Global and Regional Projects

This project forms part of an overall programmatic framework under which several separate associated country level activities will be implemented. When assistance and support services are provided from this Project to the associated country level activities, this document shall be the "Project Document" instrument referred to in: (i) the respective signed SBAAs for the specific countries; or (ii) in the Supplemental Provisions to the Project Document attached to the Project Document in cases where the recipient country has not signed an SBAA with UNDP, attached hereto and forming an integral part hereof. All references in the SBAA to "Executing Agency" shall be deemed to refer to "Implementing Partner."

This project will be implemented by [name of entity] ("Implementing Partner") in accordance with its financial regulations, rules, practices and procedures only to the extent that they do not contravene the principles of the Financial Regulations and Rules of UNDP. Where the financial governance of an Implementing Partner does not provide the required guidance to ensure best value for money, fairness, integrity, transparency, and effective international competition, the financial governance of UNDP shall apply**.**

X. RISK MANAGEMENT

*[NOTE: Please choose **one** of the following options that corresponds to the implementation modality of the Project. Delete all other options.]*

Option a. Government Entity (NIM)

1. Consistent with the Article III of the SBAA *[or the Supplemental Provisions to the Project Document]*, the responsibility for the safety and security of the Implementing Partner and its personnel and property, and of UNDP's property in the Implementing Partner's custody, rests with the Implementing Partner. To this end, the Implementing Partner shall:
   a) put in place an appropriate security plan and maintain the security plan, taking into account the security situation in the country where the project is being carried;
   b) assume all risks and liabilities related to the Implementing Partner's security, and the full implementation of the security plan.

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

2. UNDP reserves the right to verify whether such a plan is in place, and to suggest modifications to the plan when necessary. Failure to maintain and implement an appropriate security plan as required hereunder shall be deemed a breach of the Implementing Partner's obligations under this Project Document.

3. The Implementing Partner agrees to undertake all reasonable efforts to ensure that no UNDP funds received pursuant to the Project Document are used to provide support to individuals or entities associated with terrorism and that the recipients of any amounts provided by UNDP hereunder do not appear on the list maintained by the Security Council Committee established pursuant to resolution 1267 (1999). The list can be accessed via http://www.un.org/sc/committees/1267/aq_sanctions_list.shtml.

4. The Implementing Partner acknowledges and agrees that UNDP will not tolerate sexual harassment and sexual exploitation and abuse of anyone by the Implementing Partner, and each of its responsible parties, their respective sub-recipients and other entities involved in Project implementation, either as contractors or subcontractors and their personnel, and any individuals performing services for them under the Project Document.

   (a) In the implementation of the activities under this Project Document, the Implementing Partner, and each of its sub-parties referred to above, shall comply with the standards of conduct set forth in the Secretary General's Bulletin ST/SGB/2003/13 of 9 October 2003, concerning "Special measures for protection from sexual exploitation and sexual abuse" ("SEA").

   (b) Moreover, and without limitation to the application of other regulations, rules, policies and procedures bearing upon the performance of the activities under this Project Document, in the implementation of activities, the Implementing Partner, and each of its sub-parties referred to above, shall not engage in any form of sexual harassment ("SH"). SH is defined as any unwelcome conduct of a sexual nature that might reasonably be expected or be perceived to cause offense or humiliation, when such conduct interferes with work, is made a condition of employment or creates an intimidating, hostile or offensive work environment.

5. a) In the performance of the activities under this Project Document, the Implementing Partner shall (with respect to its own activities), and shall require from its sub-parties referred to in paragraph 4 (with respect to their activities) that they, have minimum standards and procedures in place, or a plan to develop and/or improve such standards and procedures in order to be able to take effective preventive and investigative action. These should include: policies on sexual harassment and sexual exploitation and abuse; policies on whistleblowing/protection against retaliation; and complaints, disciplinary and investigative mechanisms. In line with this, the Implementing Partner will and will require that such sub-parties will take all appropriate measures to:

   i. Prevent its employees, agents or any other persons engaged to perform any services under this Project Document, from engaging in SH or SEA;

   ii. Offer employees and associated personnel training on prevention and response to SH and SEA, where the Implementing Partner and its sub-parties referred to in paragraph 4 have not put in place its own training regarding the prevention of SH and SEA, the Implementing Partner and its sub-parties may use the training material available at UNDP;

   iii. Report and monitor allegations of SH and SEA of which the Implementing Partner and its sub-parties referred to in paragraph 4 have been informed or have otherwise become aware, and status thereof;

   iv. Refer victims/survivors of SH and SEA to safe and confidential victim assistance; and

   v. Promptly and confidentially record and investigate any allegations credible enough to warrant an investigation of SH or SEA. The Implementing Partner shall advise UNDP of any such allegations received and investigations being conducted by itself or any of its sub-parties referred to in paragraph 4 with respect to their activities under the Project Document, and shall keep UNDP informed during the investigation by it or any of such sub-parties, to the extent that such notification (i) does not jeopardize the conduct of the investigation, including but not limited to the safety or security of persons, and/or (ii) is not in contravention of any laws applicable to it. Following the investigation, the Implementing Partner shall advise UNDP of any actions taken by it or any of the other entities further to the investigation.

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

b) The Implementing Partner shall establish that it has complied with the foregoing, to the satisfaction of UNDP, when requested by UNDP or any party acting on its behalf to provide such confirmation. Failure of the Implementing Partner, and each of its sub-parties referred to in paragraph 4, to comply of the foregoing, as determined by UNDP, shall be considered grounds for suspension or termination of the Project.

6. Social and environmental sustainability will be enhanced through application of the UNDP Social and Environmental Standards (http://www.undp.org/ses) and related Accountability Mechanism (http://www.undp.org/secu-srm).

7. The Implementing Partner shall: (a) conduct project and programme-related activities in a manner consistent with the UNDP Social and Environmental Standards, (b) implement any management or mitigation plan prepared for the project or programme to comply with such standards, and (c) engage in a constructive and timely manner to address any concerns and complaints raised through the Accountability Mechanism. UNDP will seek to ensure that communities and other project stakeholders are informed of and have access to the Accountability Mechanism.

8. All signatories to the Project Document shall cooperate in good faith with any exercise to evaluate any programme or project-related commitments or compliance with the UNDP Social and Environmental Standards. This includes providing access to project sites, relevant personnel, information, and documentation.

9. The Implementing Partner will take appropriate steps to prevent misuse of funds, fraud or corruption, by its officials, consultants, responsible parties, subcontractors and sub-recipients in implementing the project or using UNDP funds. The Implementing Partner will ensure that its financial management, anti-corruption and anti-fraud policies are in place and enforced for all funding received from or through UNDP.

10. The requirements of the following documents, then in force at the time of signature of the Project Document, apply to the Implementing Partner: (a) UNDP Policy on Fraud and other Corrupt Practices and (b) UNDP Office of Audit and Investigations Investigation Guidelines. The Implementing Partner agrees to the requirements of the above documents, which are an integral part of this Project Document and are available online at www.undp.org.

11. In the event that an investigation is required, UNDP has the obligation to conduct investigations relating to any aspect of UNDP projects and programmes in accordance with UNDP's regulations, rules, policies and procedures. The Implementing Partner shall provide its full cooperation, including making available personnel, relevant documentation, and granting access to the Implementing Partner's (and its consultants', responsible parties', subcontractors' and sub-recipients') premises, for such purposes at reasonable times and on reasonable conditions as may be required for the purpose of an investigation. Should there be a limitation in meeting this obligation, UNDP shall consult with the Implementing Partner to find a solution.

12. The signatories to this Project Document will promptly inform one another in case of any incidence of inappropriate use of funds, or credible allegation of fraud or corruption with due confidentiality.

    Where the Implementing Partner becomes aware that a UNDP project or activity, in whole or in part, is the focus of investigation for alleged fraud/corruption, the Implementing Partner will inform the UNDP Resident Representative/Head of Office, who will promptly inform UNDP's Office of Audit and Investigations (OAI). The Implementing Partner shall provide regular updates to the head of UNDP in the country and OAI of the status of, and actions relating to, such investigation.

13. *Choose one of the three following options:*

    Option 1: UNDP shall be entitled to a refund from the Implementing Partner of any funds provided that have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of the Project Document. Such amount may be deducted by UNDP from any payment due to the Implementing Partner under this or any other agreement. Recovery of such amount by UNDP shall not diminish or curtail the Implementing Partner's obligations under this Project Document.

    Option 2: The Implementing Partner agrees that, where applicable, donors to UNDP (including the Government) whose funding is the source, in whole or in part, of the funds for the activities which are the subject of this Project Document, may seek recourse to the Implementing Partner for the recovery of any

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

funds determined by UNDP to have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of the Project Document.

Option 3: UNDP shall be entitled to a refund from the Implementing Partner of any funds provided that have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of the Project Document. Such amount may be deducted by UNDP from any payment due to the Implementing Partner under this or any other agreement.

Where such funds have not been refunded to UNDP, the Implementing Partner agrees that donors to UNDP (including the Government) whose funding is the source, in whole or in part, of the funds for the activities under this Project Document, may seek recourse to the Implementing Partner for the recovery of any funds determined by UNDP to have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of the Project Document.

Note: The term "Project Document" as used in this clause shall be deemed to include any relevant subsidiary agreement further to the Project Document, including those with responsible parties, subcontractors and sub-recipients.

14. Each contract issued by the Implementing Partner in connection with this Project Document shall include a provision representing that no fees, gratuities, rebates, gifts, commissions or other payments, other than those shown in the proposal, have been given, received, or promised in connection with the selection process or in contract execution, and that the recipient of funds from the Implementing Partner shall cooperate with any and all investigations and post-payment audits.

15. Should UNDP refer to the relevant national authorities for appropriate legal action any alleged wrongdoing relating to the project, the Government will ensure that the relevant national authorities shall actively investigate the same and take appropriate legal action against all individuals found to have participated in the wrongdoing, recover and return any recovered funds to UNDP.

16. The Implementing Partner shall ensure that all of its obligations set forth under this section entitled "Risk Management" are passed on to each responsible party, subcontractor and sub-recipient and that all the clauses under this section entitled "Risk Management Standard Clauses" are included, *mutatis mutandis*, in all sub-contracts or sub-agreements entered into further to this Project Document.

Option b. UNDP (DIM)

1. UNDP as the Implementing Partner will comply with the policies, procedures and practices of the United Nations Security Management System (UNSMS.)

2. UNDP as the Implementing Partner will undertake all reasonable efforts to ensure that none of the [project funds][10] [UNDP funds received pursuant to the Project Document][11] are used to provide support to individuals or entities associated with terrorism and that the recipients of any amounts provided by UNDP hereunder do not appear on the list maintained by the Security Council Committee established pursuant to resolution 1267 (1999). The list can be accessed via http://www.un.org/sc/committees/1267/aq_sanctions_list.shtml. This provision must be included in all sub-contracts or sub-agreements entered into under this Project Document.

3. Social and environmental sustainability will be enhanced through application of the UNDP Social and Environmental Standards (http://www.undp.org/ses) and related Accountability Mechanism (http://www.undp.org/secu-srm).

4. UNDP as the Implementing Partner will: (a) conduct project and programme-related activities in a manner consistent with the UNDP Social and Environmental Standards, (b) implement any management or mitigation plan prepared for the project or programme to comply with such standards, and (c) engage in a constructive and timely manner to address any concerns and complaints raised through the Accountability Mechanism. UNDP will seek to ensure that communities and other project stakeholders are informed of and have access to the Accountability Mechanism.

[10] To be used where UNDP is the Implementing Partner

[11] To be used where the UN, a UN fund/programme or a specialized agency is the Implementing Partner

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

5. In the implementation of the activities under this Project Document, UNDP as the Implementing Partner will handle any sexual exploitation and abuse ("SEA") and sexual harassment ("SH") allegations in accordance with its regulations, rules, policies and procedures.

6. All signatories to the Project Document shall cooperate in good faith with any exercise to evaluate any programme or project-related commitments or compliance with the UNDP Social and Environmental Standards. This includes providing access to project sites, relevant personnel, information, and documentation.

7. UNDP as the Implementing Partner will ensure that the following obligations are binding on each responsible party, subcontractor and sub-recipient:

    a. Consistent with the Article III of the SBAA *[or the Supplemental Provisions to the Project Document]*, the responsibility for the safety and security of each responsible party, subcontractor and sub-recipient and its personnel and property, and of UNDP's property in such responsible party's, subcontractor's and sub-recipient's custody, rests with such responsible party, subcontractor and sub-recipient. To this end, each responsible party, subcontractor and sub-recipient shall:
        i. put in place an appropriate security plan and maintain the security plan, taking into account the security situation in the country where the project is being carried;
        ii. assume all risks and liabilities related to such responsible party's, subcontractor's and sub-recipient's security, and the full implementation of the security plan.

    b. UNDP reserves the right to verify whether such a plan is in place, and to suggest modifications to the plan when necessary. Failure to maintain and implement an appropriate security plan as required hereunder shall be deemed a breach of the responsible party's, subcontractor's and sub-recipient's obligations under this Project Document.
    c. In the performance of the activities under this Project, UNDP as the Implementing Partner shall ensure, with respect to the activities of any of its responsible parties, sub-recipients and other entities engaged under the Project, either as contractors or subcontractors, their personnel and any individuals performing services for them, that those entities have in place adequate and proper procedures, processes and policies to prevent and/or address SEA and SH.

    d. Each responsible party, subcontractor and sub-recipient will take appropriate steps to prevent misuse of funds, fraud or corruption, by its officials, consultants, subcontractors and sub-recipients in implementing the project or programme or using the UNDP funds. It will ensure that its financial management, anti-corruption and anti-fraud policies are in place and enforced for all funding received from or through UNDP.

    e. The requirements of the following documents, then in force at the time of signature of the Project Document, apply to each responsible party, subcontractor and sub-recipient: (a) UNDP Policy on Fraud and other Corrupt Practices and (b) UNDP Office of Audit and Investigations Investigation Guidelines. Each responsible party, subcontractor and sub-recipient agrees to the requirements of the above documents, which are an integral part of this Project Document and are available online at www.undp.org.

    f. In the event that an investigation is required, UNDP will conduct investigations relating to any aspect of UNDP programmes and projects. Each responsible party, subcontractor and sub-recipient will provide its full cooperation, including making available personnel, relevant documentation, and granting access to its (and its consultants', subcontractors' and sub-recipients') premises, for such purposes at reasonable times and on reasonable conditions as may be required for the purpose of an investigation. Should there be a limitation in meeting this obligation, UNDP shall consult with it to find a solution.

    g. Each responsible party, subcontractor and sub-recipient will promptly inform UNDP as the Implementing Partner in case of any incidence of inappropriate use of funds, or credible allegation of fraud or corruption with due confidentiality.

        Where it becomes aware that a UNDP project or activity, in whole or in part, is the focus of investigation for alleged fraud/corruption, each responsible party, subcontractor and sub-recipient will inform the UNDP Resident Representative/Head of Office, who will promptly inform UNDP's Office of Audit and Investigations (OAI). It will provide regular updates to the

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

head of UNDP in the country and OAI of the status of, and actions relating to, such investigation.

h. Choose one of the three following options:

Option 1: UNDP will be entitled to a refund from the responsible party, subcontractor or sub-recipient of any funds provided that have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of this Project Document. Such amount may be deducted by UNDP from any payment due to the responsible party, subcontractor or sub-recipient under this or any other agreement. Recovery of such amount by UNDP shall not diminish or curtail any responsible party's, subcontractor's or sub-recipient's obligations under this Project Document.

Option 2: Each responsible party, subcontractor or sub-recipient agrees that, where applicable, donors to UNDP (including the Government) whose funding is the source, in whole or in part, of the funds for the activities which are the subject of the Project Document, may seek recourse to such responsible party, subcontractor or sub-recipient for the recovery of any funds determined by UNDP to have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of the Project Document.

Option 3: UNDP will be entitled to a refund from the responsible party, subcontractor or sub-recipient of any funds provided that have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of the Project Document. Such amount may be deducted by UNDP from any payment due to the responsible party, subcontractor or sub-recipient under this or any other agreement.

Where such funds have not been refunded to UNDP, the responsible party, subcontractor or sub-recipient agrees that donors to UNDP (including the Government) whose funding is the source, in whole or in part, of the funds for the activities under this Project Document, may seek recourse to such responsible party, subcontractor or sub-recipient for the recovery of any funds determined by UNDP to have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of the Project Document.

Note: The term "Project Document" as used in this clause shall be deemed to include any relevant subsidiary agreement further to the Project Document, including those with responsible parties, subcontractors and sub-recipients.

i. Each contract issued by the responsible party, subcontractor or sub-recipient in connection with this Project Document shall include a provision representing that no fees, gratuities, rebates, gifts, commissions or other payments, other than those shown in the proposal, have been given, received, or promised in connection with the selection process or in contract execution, and that the recipient of funds from it shall cooperate with any and all investigations and post-payment audits.

j. Should UNDP refer to the relevant national authorities for appropriate legal action any alleged wrongdoing relating to the project or programme, the Government will ensure that the relevant national authorities shall actively investigate the same and take appropriate legal action against all individuals found to have participated in the wrongdoing, recover and return any recovered funds to UNDP.

k. Each responsible party, subcontractor and sub-recipient shall ensure that all of its obligations set forth under this section entitled "Risk Management" are passed on to its subcontractors and sub-recipients and that all the clauses under this section entitled "Risk Management Standard Clauses" are adequately reflected, *mutatis mutandis*, in all its sub-contracts or sub-agreements entered into further to this Project Document.

Option c. CSO/NGO/Non-UN or other IGO with no signed SBEAA with UNDP

1. Consistent with the Article III of the SBAA *[or the Supplemental Provisions to the Project Document]*, the responsibility for the safety and security of the Implementing Partner and its personnel and property, and of UNDP's property in the Implementing Partner's custody, rests with the Implementing Partner. To this end, the Implementing Partner shall:

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

a) put in place an appropriate security plan and maintain the security plan, taking into account the security situation in the country where the project is being carried;

b) assume all risks and liabilities related to the Implementing Partner's security, and the full implementation of the security plan.

2. UNDP reserves the right to verify whether such a plan is in place, and to suggest modifications to the plan when necessary. Failure to maintain and implement an appropriate security plan as required hereunder shall be deemed a breach of the Implementing Partner's obligations under this Project Document and the Project Cooperation Agreement between UNDP and the Implementing Partner[12].

3. The Implementing Partner agrees to undertake all reasonable efforts to ensure that no UNDP funds received pursuant to the Project Document are used to provide support to individuals or entities associated with terrorism and that the recipients of any amounts provided by UNDP hereunder do not appear on the list maintained by the Security Council Committee established pursuant to resolution 1267 (1999). The list can be accessed via http://www.un.org/sc/committees/1267/aq_sanctions_list.shtml.

4. The Implementing Partner acknowledges and agrees that UNDP will not tolerate sexual harassment and sexual exploitation and abuse of anyone by the Implementing Partner, and each of its responsible parties, their respective sub-recipients and other entities involved in Project implementation, either as contractors or subcontractors and their personnel, and any individuals performing services for them under the Project Document.

(a) In the implementation of the activities under this Project Document, the Implementing Partner, and each of its sub-parties referred to above, shall comply with the standards of conduct set forth in the Secretary General's Bulletin ST/SGB/2003/13 of 9 October 2003, concerning "Special measures for protection from sexual exploitation and sexual abuse" ("SEA").

(b) Moreover, and without limitation to the application of other regulations, rules, policies and procedures bearing upon the performance of the activities under this Project Document, in the implementation of activities, the Implementing Partner, and each of its sub-parties referred to above, shall not engage in any form of sexual harassment ("SH"). SH is defined as any unwelcome conduct of a sexual nature that might reasonably be expected or be perceived to cause offense or humiliation, when such conduct interferes with work, is made a condition of employment or creates an intimidating, hostile or offensive work environment.

5. a) In the performance of the activities under this Project Document, the Implementing Partner shall (with respect to its own activities), and shall require from its sub-parties referred to in paragraph 4 (with respect to their activities) that they, have minimum standards and procedures in place, or a plan to develop and/or improve such standards and procedures in order to be able to take effective preventive and investigative action. These should include: policies on sexual harassment and sexual exploitation and abuse; policies on whistleblowing/protection against retaliation; and complaints, disciplinary and investigative mechanisms. In line with this, the Implementing Partner will, and will require that such sub-parties will take all appropriate measures to:

i. Prevent its employees, agents or any other persons engaged to perform any services under this Project Document, from engaging in SH or SEA;

ii. Offer employees and associated personnel training on prevention and response to SH and SEA, where the Implementing Partner and its sub-parties referred to in paragraph 4, have not put in place its own training regarding the prevention of SH and SEA, the Implementing Partner and such sub-parties may use the training material available at UNDP;

iii. Report and monitor allegations of SH and SEA of which the Implementing Partner and its sub-parties referred to in paragraph 4 have been informed or have otherwise become aware, and status thereof;

iv. Refer victims/survivors of SH and SEA to safe and confidential victim assistance; and

v. Promptly and confidentially record and investigate any allegations credible enough to warrant an investigation of SH or SEA. The Implementing Partner shall advise UNDP of any

[12] Use bracketed text only when IP is an NGO/IGO

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

such allegations received and investigations being conducted by itself or any of its sub-parties referred to in paragraph 4 with respect to their activities under the Project Document, and shall keep UNDP informed during the investigation by it or any of such sub-parties, to the extent that such notification (i) does not jeopardize the conduct of the investigation, including but not limited to the safety or security of persons, and/or (ii) is not in contravention of any laws applicable to it. Following the investigation, the Implementing Partner shall advise UNDP of any actions taken by it or any of the other entities further to the investigation.

b) The Implementing Partner shall establish that it has complied with the foregoing, to the satisfaction of UNDP, when requested by UNDP or any party acting on its behalf to provide such confirmation. Failure of the Implementing Partner, and each of its sub-parties referred to in paragraph 4, to comply of the foregoing, as determined by UNDP, shall be considered grounds for suspension or termination of the Project.

6. Social and environmental sustainability will be enhanced through application of the UNDP Social and Environmental Standards (http://www.undp.org/ses) and related Accountability Mechanism (http://www.undp.org/secu-srm).

7. The Implementing Partner shall: (a) conduct project and programme-related activities in a manner consistent with the UNDP Social and Environmental Standards, (b) implement any management or mitigation plan prepared for the project or programme to comply with such standards, and (c) engage in a constructive and timely manner to address any concerns and complaints raised through the Accountability Mechanism. UNDP will seek to ensure that communities and other project stakeholders are informed of and have access to the Accountability Mechanism.

8. All signatories to the Project Document shall cooperate in good faith with any exercise to evaluate any programme or project-related commitments or compliance with the UNDP Social and Environmental Standards. This includes providing access to project sites, relevant personnel, information, and documentation.

9. The Implementing Partner will take appropriate steps to prevent misuse of funds, fraud or corruption, by its officials, consultants, responsible parties, subcontractors and sub-recipients in implementing the project or using the UNDP funds. The Implementing Partner will ensure that its financial management, anti-corruption and anti-fraud policies are in place and enforced for all funding received from or through UNDP.

10. The requirements of the following documents, then in force at the time of signature of the Project Document, apply to the Implementing Partner: (a) UNDP Policy on Fraud and other Corrupt Practices and (b) UNDP Office of Audit and Investigations Investigation Guidelines. The Implementing Partner agrees to the requirements of the above documents, which are an integral part of this Project Document and are available online at www.undp.org.

11. In the event that an investigation is required, UNDP has the obligation to conduct investigations relating to any aspect of UNDP programmes and projects in accordance with UNDP regulations, rules, policies and procedures. The Implementing Partner shall provide its full cooperation, including making available personnel, relevant documentation, and granting access to the Implementing Partner's (and its consultants', responsible parties', subcontractors' and sub-recipients') premises, for such purposes at reasonable times and on reasonable conditions as may be required for the purpose of an investigation. Should there be a limitation in meeting this obligation, UNDP shall consult with the Implementing Partner to find a solution.

12. The Implementing Partner will promptly inform UNDP in case of any incidence of inappropriate use of funds, or credible allegation of fraud or corruption with due confidentiality.

    Where the Implementing Partner becomes aware that a UNDP project or activity, in whole or in part, is the focus of investigation for alleged fraud/corruption, the Implementing Partner will inform the UNDP Resident Representative/Head of Office, who will promptly inform UNDP's Office of Audit and Investigations (OAI). The Implementing Partner shall provide regular updates to the head of UNDP in the country and OAI of the status of, and actions relating to, such investigation.

13. Choose one of the three following options:

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

Option 1: UNDP shall be entitled to a refund from the Implementing Partner of any funds provided that have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of this Project Document. Such amount may be deducted by UNDP from any payment due to the Implementing Partner under this or any other agreement. Recovery of such amount by UNDP shall not diminish or curtail the Implementing Partner's obligations under this Project Document.

Option 2: The Implementing Partner agrees that, where applicable, donors to UNDP (including the Government) whose funding is the source, in whole or in part, of the funds for the activities which are the subject of the Project Document, may seek recourse to the Implementing Partner for the recovery of any funds determined by UNDP to have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of the Project Document.

Option 3: UNDP shall be entitled to a refund from the Implementing Partner of any funds provided that have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of the Project Document. Such amount may be deducted by UNDP from any payment due to the Implementing Partner under this or any other agreement.

Where such funds have not been refunded to UNDP, the Implementing Partner agrees that donors to UNDP (including the Government) whose funding is the source, in whole or in part, of the funds for the activities under this Project Document, may seek recourse to the Implementing Partner for the recovery of any funds determined by UNDP to have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of the Project Document.

Note: The term "Project Document" as used in this clause shall be deemed to include any relevant subsidiary agreement further to the Project Document, including those with the Implementing Partner, responsible parties, subcontractors and sub-recipients.

14. Each contract issued by the Implementing Partner in connection with this Project Document shall include a provision representing that no fees, gratuities, rebates, gifts, commissions or other payments, other than those shown in the proposal, have been given, received, or promised in connection with the selection process or in contract execution, and that the recipient of funds from the Implementing Partner shall cooperate with any and all investigations and post-payment audits.

15. Should UNDP refer to the relevant national authorities for appropriate legal action any alleged wrongdoing relating to the project, the Government will ensure that the relevant national authorities shall actively investigate the same and take appropriate legal action against all individuals found to have participated in the wrongdoing, recover and return any recovered funds to UNDP.

16. The Implementing Partner shall ensure that all of its obligations set forth under this section entitled "Risk Management Standard Clauses" are passed on to each responsible party, subcontractor and sub-recipient and that all the clauses under this section entitled "Risk Management" are included, *mutatis mutandis*, in all sub-contracts or sub-agreements entered into further to this Project Document.

Option d. UN Agency other than UNDP, and IGO with signed SBEAA with UNDP

1. [Name of UN Agency/IGO] as the Implementing Partner will comply with the policies, procedures and practices of the United Nations Security Management System (UNSMS.)

2. In the implementation of the activities under this Project Document, [Name of UN Agency/IGO] as the Implementing Partner will handle any sexual exploitation and abuse ("SEA") and sexual harassment ("SH") allegations in accordance with its regulations, rules, policies and procedures. Notwithstanding the foregoing, the [Name of UN Agency/IGO], as the Implementing Partner, will notify UNDP of any such allegations and investigations it may conduct further to such allegations.

3. [Name of UN Agency/IGO] as the Implementing Partner will ensure that the following obligations are binding on each responsible party, subcontractor and sub-recipient that is not a UN entity:

    a. Consistent with the Article III of the SBAA *[or the Supplemental Provisions to the Project Document]*, the responsibility for the safety and security of each responsible party, subcontractor and sub-recipient and its personnel and property, and of [Name of UN Agency/IGO]'s property in such responsible party's, subcontractor's and sub-recipient's

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

custody, rests with such responsible party, subcontractor and sub-recipient. To this end, each responsible party, subcontractor and sub-recipient shall:

i. put in place an appropriate security plan and maintain the security plan, taking into account the security situation in the country where the project is being carried;
ii. assume all risks and liabilities related to such responsible party's, subcontractor's and sub-recipient's security, and the full implementation of the security plan.

b. [Name of UN Agency/IGO] reserves the right to verify whether such a plan is in place, and to suggest modifications to the plan when necessary. Failure to maintain and implement an appropriate security plan as required hereunder shall be deemed a breach of the responsible party's, subcontractor's and sub-recipient's obligations under this Project Document.

c. In the performance of the activities under this Project, [Name of UN Agency/IGO] as the Implementing Partner shall ensure, with respect to the activities of any of its responsible parties, sub-recipients and other entities engaged under the Project, either as contractors or subcontractors, their personnel and any individuals performing services for them, that those entities have in place adequate and proper procedures, processes and policies to prevent and/or handle SEA and SH.

4. [Name of UN Agency/IGO] agrees to undertake all reasonable efforts to ensure that none of the [project funds][13] [UNDP funds received pursuant to the Project Document][14] are used to provide support to individuals or entities associated with terrorism and that the recipients of any amounts provided by UNDP hereunder do not appear on the list maintained by the Security Council Committee established pursuant to resolution 1267 (1999). The list can be accessed via http://www.un.org/sc/committees/1267/aq_sanctions_list.shtml.

5. Social and environmental sustainability will be enhanced through application of the UNDP Social and Environmental Standards (http://www.undp.org/ses) and related Accountability Mechanism (http://www.undp.org/secu-srm).

6. The Implementing Partner shall: (a) conduct project and programme-related activities in a manner consistent with the UNDP Social and Environmental Standards, (b) implement any management or mitigation plan prepared for the project or programme to comply with such standards, and (c) engage in a constructive and timely manner to address any concerns and complaints raised through the Accountability Mechanism. UNDP will seek to ensure that communities and other project stakeholders are informed of and have access to the Accountability Mechanism.

7. All signatories to the Project Document shall cooperate in good faith with any exercise to evaluate any programme or project-related commitments or compliance with the UNDP Social and Environmental Standards. This includes providing access to project sites, relevant personnel, information, and documentation.

8. The Implementing Partner will take appropriate steps to prevent misuse of funds, fraud or corruption, by its officials, consultants, responsible parties, subcontractors and sub-recipients in implementing the project or programme or using the UNDP funds. The Implementing Partner will ensure that its financial management, anti-corruption and anti-fraud policies are in place and enforced for all funding received from or through UNDP.

9. [*This text should be included when the Implementing Partner is a non-UN IGO*: The requirements of the following documents, then in force at the time of signature of the Project Document, apply to the Implementing Partner: (a) UNDP Policy on Fraud and other Corrupt Practices and (b) UNDP Office of Audit and Investigations Investigation Guidelines. The Implementing Partner agrees to the requirements of the above documents, which are an integral part of this Project Document and are available online at www.undp.org.]

10. [*This text should be included when the Implementing Partner is a non-UN IGO*: In the event that an investigation is required, UNDP has the obligation to conduct investigations relating to any aspect of

[13] To be used where UNDP is the Implementing Partner

[14] To be used where the UN, a UN fund/programme or a specialized agency is the Implementing Partner

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

UNDP projects or programmes. The Implementing Partner shall provide its full cooperation, including making available personnel, relevant documentation, and granting access to the Implementing Partner's (and its consultants', responsible parties', subcontractors' and sub-recipients') premises, for such purposes at reasonable times and on reasonable conditions as may be required for the purpose of an investigation. Should there be a limitation in meeting this obligation, UNDP shall consult with the Implementing Partner to find a solution.]

11. The Implementing Partner and UNDP will promptly inform one another in case of any incidence of inappropriate use of funds, or credible allegation of fraud or corruption with due confidentiality.

    Where the Implementing Partner becomes aware that a UNDP project or activity, in whole or in part, is the focus of investigation for alleged fraud/corruption, the Implementing Partner will inform the UNDP Resident Representative/Head of Office, who will promptly inform UNDP's Office of Audit and Investigations (OAI). The Implementing Partner shall provide regular updates to the head of UNDP in the country and OAI of the status of, and actions relating to, such investigation.

12. *Choose one of the three following options:*

    Option 1: UNDP shall be entitled to a refund from the Implementing Partner of any funds provided that have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of this Project Document. Such amount may be deducted by UNDP from any payment due to the Implementing Partner under this or any other agreement. Recovery of such amount by UNDP shall not diminish or curtail the Implementing Partner's obligations under this Project Document.

    Option 2: The Implementing Partner agrees that, where applicable, donors to UNDP (including the Government) whose funding is the source, in whole or in part, of the funds for the activities which are the subject of the Project Document, may seek recourse to the Implementing Partner for the recovery of any funds determined by UNDP to have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of the Project Document.

    Option 3: UNDP shall be entitled to a refund from the Implementing Partner of any funds provided that have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of the Project Document. Such amount may be deducted by UNDP from any payment due to the Implementing Partner under this or any other agreement.

    Where such funds have not been refunded to UNDP, the Implementing Partner agrees that donors to UNDP (including the Government) whose funding is the source, in whole or in part, of the funds for the activities under this Project Document, may seek recourse to the Implementing Partner for the recovery of any funds determined by UNDP to have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of the Project Document.

    Note: The term "Project Document" as used in this clause shall be deemed to include any relevant subsidiary agreement further to the Project Document, including those with responsible parties, subcontractors and sub-recipients.

13. Each contract issued by the Implementing Partner in connection with this Project Document shall include a provision representing that no fees, gratuities, rebates, gifts, commissions or other payments, other than those shown in the proposal, have been given, received, or promised in connection with the selection process or in contract execution, and that the recipient of funds from the Implementing Partner shall cooperate with any and all investigations and post-payment audits.

14. Should UNDP refer to the relevant national authorities for appropriate legal action any alleged wrongdoing relating to the project, the Government will ensure that the relevant national authorities shall actively investigate the same and take appropriate legal action against all individuals found to have participated in the wrongdoing, recover and return any recovered funds to UNDP.

15. The Implementing Partner shall ensure that all of its obligations set forth under this section entitled "Risk Management Standard Clauses" are passed on to each responsible party, subcontractor and sub-recipient and that all the clauses under this section entitled "Risk Management" are included, *mutatis mutandis*, in all sub-contracts or sub-agreements entered into further to this Project Document.

DocuSign Envelope ID: 78A81D1F-1555-4474-BC40-9758FC393B71

Special Clauses. In case of government cost-sharing through the project, the following clauses should be included:

1. The schedule of payments and UNDP bank account details.

2. The value of the payment, if made in a currency other than United States dollars, shall be determined by applying the United Nations operational rate of exchange in effect on the date of payment. Should there be a change in the United Nations operational rate of exchange prior to the full utilization by the UNDP of the payment, the value of the balance of funds still held at that time will be adjusted accordingly. If, in such a case, a loss in the value of the balance of funds is recorded, UNDP shall inform the Government with a view to determining whether any further financing could be provided by the Government. Should such further financing not be available, the assistance to be provided to the project may be reduced, suspended or terminated by UNDP.

3. The above schedule of payments takes into account the requirement that the payments shall be made in advance of the implementation of planned activities. It may be amended to be consistent with the progress of project delivery.

4. UNDP shall receive and administer the payment in accordance with the regulations, rules and directives of UNDP.

5. All financial accounts and statements shall be expressed in United States dollars.

6. If unforeseen increases in expenditures or commitments are expected or realized (whether owing to inflationary factors, fluctuation in exchange rates or unforeseen contingencies), UNDP shall submit to the government on a timely basis a supplementary estimate showing the further financing that will be necessary. The Government shall use its best endeavors to obtain the additional funds required.

7. If the payments referred above are not received in accordance with the payment schedule, or if the additional financing required in accordance with paragraph [] above is not forthcoming from the Government or other sources, the assistance to be provided to the project under this Agreement may be reduced, suspended or terminated by UNDP.

8. Any interest income attributable to the contribution shall be credited to UNDP Account and shall be utilized in accordance with established UNDP procedures.

In accordance with the decisions and directives of UNDP's Executive Board:

The contribution shall be charged:

(a) […%] cost recovery for the provision of general management support (GMS) by UNDP headquarters and country offices

(b) Direct cost for implementation support services (ISS) provided by UNDP and/or an executing entity/implementing partner.

9. Ownership of equipment, supplies and other properties financed from the contribution shall vest in UNDP. Matters relating to the transfer of ownership by UNDP shall be determined in accordance with the relevant policies and procedures of UNDP.

10. The contribution shall be subject exclusively to the internal and external auditing procedures provided for in the financial regulations, rules and directives of UNDP."

Yvonne Helle

Special Representative UNDP PAPP

21-Jun-2021

Husam Tubail

Programme Portfolio Manager

17-Jun-2021
