DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

**UNDP Afghanistan – Project Document Clearance Process**

*This clearance slip will accompany the Pro Doc when submitting to UNDP Resident Representative Signature*

**I. General Information** *(To be filled by Project Manager)*

| | |
|---|---|
| **Project Name:** | Sustainable Energy Services for Education and Health in Afghanistan (SESEHA) |
| **Project Duration:** | 66 months (1 Jan 2023 – 30 June 2028) |
| **Project Manager Name:** | Usha Rao a.i. |
| **CPD Output (CPRF 2022):** | Output 3.2: Access to clean and affordable energy enhanced |
| **Atlas Project Number (Award ID):** | **00147445** |
| **ATLAS Output IDs (if applicable)** | Output 1: 00134061 (Health Facilities Electrified)<br>Output 2: 00134062 (Schools productivity enhanced)<br>Output 3: 00134063 (O&M Delivery Model established)<br>Output 4: 00134064 (Project Management Support) |

**II. List of Supporting Documents for Pro Doc Signature by UNDP Resident Representative**

| **Items Checked** | **Yes** | **No** | **N/A** |
|---|---|---|---|
| 1. Cleared Pro Doc (DEU) | Yes | | |
| 2. Cleared Social and Environmental Screening - SES (DEU) | Yes | | |
| 3. Cleared Risk Register – Offline and Online/ATLAS PPM (DEU) | Yes | | |
| 4. LPAC Completed with Signed Minutes (DEU) | Yes | | |
| 5. Partner Capacity Assessment completed or initiated (Either PCAT or HACT Micro Assessment as applicable) (HACT Focal Point) | | | N/A |
| 6. Cleared Design PQA Rating Tool – Offline and Online (DEU) | Yes | | |
| 7. Approved MY/AWP (Resource Management) | Yes | | |
| | | | |

| | *Name* | *Signature* | *Date* |
|---|---|---|---|
| **Cleared by DEU:** | Anisha Thapa | DocuSigned by: Anisha Thapa 9E2F629C547F485... | 13-Dec-2022 |
| **Cleared by Resource Management:** | Akiko Hasegawa | DocuSigned by: Akiko Hasegawa 9205090886DE4C3... | 14-Dec-2022 |
| **Cleared by HACT Focal Point:** | Mohammad Yousuf Walizada | N/A | |
| **Approved by SDRR (P):** | Surayo Buzurukova | DocuSigned by: Surayo Buzurukova C8F21608D8FA487... | 14-Dec-2022 |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

United Nations Development Programme

**PROJECT DOCUMENT**

***Afghanistan***

**Project Title: Sustainable Energy Services for Education and Health in Afghanistan (SESEHA)**

**Project Number: 00147445**

**Implementing Partner: UNDP**

**Start Date:** 01 Jan 2023 **End Date:** 30 June 2028 **LPAC Meeting date:** 08 Nov 2022

## Brief Description

The project aims to support adoption of renewable energy and energy efficiency measures in public facilities (primarily in health and education sectors) for sustained delivery of essential services for basic human needs in Afghanistan. The project will be implemented initially in 18 provinces that are either not connected with grid or receive less than 6 hours of average supply of electricity that constraints the services of public facilities. Approx. 792 facilities will be targeted based on technical criteria for selection. Further, the following project interventions are considered in the identified facilities: a) supply of decentralised renewable energy-based electricity and energy efficiency measures in both education and health sectors and b) Support Operations & Maintenance (O&M) of decentralised renewable energy systems through appropriate service delivery models and capacity building/ training (e.g. private sector/gender inclusion). The estimated funding is EUR 59.99 million over a period of 66 months from the receipt of Contributions from KfW.

### UNDP Strategic Plan Outcome / Outputs

**Outcome 3:** Resilience built to respond to systemic uncertainty and risk

**Output 5.1:** Energy gap closed

### Strategic Framework for Afghanistan 2023-2025

**Outcome 1:** By the end of 2025, more people in Afghanistan, particularly the most marginalized, can equitably access essential services that meet minimum quality standards.

**Outcome 2:** By the end of 2025, people in Afghanistan, especially women, youth, and other marginalized groups, and those at risk of being left behind, benefit from a more equitable, inclusive, sustainable, and resilient employment-rich economy and shared economic opportunities with enhanced productive capacities for improved livelihoods and decent work.

### UNDP CPRF 2022 Results:

**Outcome 3:** Improved climate smart agriculture, access to renewable energy, and resilience to natural disasters

**Output 3.2:** Access to clean and affordable energy enhanced

**Project Output(s) with Gender Marker:**

Output 1: GEN 2
Output 2: GEN 2
Output 3: GEN 2

| | | |
|---|---|---|
| **Total resources required:** | | **EUR 59,990,000** |
| **Total resources allocated:** | | |
| | **UNDP TRAC:** | Nil |
| | **Donor:** | **EUR 59,990,000 (KFW)** |
| | **Government:** | Nil |
| | **In-Kind:** | Nil |
| **Unfunded:** | | |

**AGREED BY:**

DocuSigned by:
Surayo Buzurkova
C8F21608D8FA487...

**Ms. Surayo Buzurukova**

**Resident Representative OIC**

**UNDP Afghanistan**

**Date:** 14-Dec-2022

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

# 1. DEVELOPMENT CHALLENGE

**General Context:**

Economic growth in Afghanistan had slowed down considerably since 2018. Among the reasons attributed are the longer-term implications of deteriorated security conditions of the past, delayed agricultural production following a prolonged drought, and increased prevalence of COVID-19 with the country's third wave peaking in June 2021. Following the takeover by the Taliban in August 2021, Afghanistan continued to feel the enduring effects of the crisis both on economic and humanitarian fronts. Some security constraints remain, international sanctions, liquidity and banking crises, weak market infrastructures, and recent directives on women have negatively impacted the overall situation. Women (constituting 50% of the total population) have been kept out of labour force participation[1] in the public sector, as well as in the private sector followed by August 2021, where women enterprises and women workers had been affected disproportionately[2]. While inflation increased gradually during the first half of 2021, the country's energy price rises had remained higher in line with global trends at 12 per cent, and the prices of basic household goods, notably fuel and food, have since significantly increased due to disrupted supply chains, population displacement, and disabled transit hubs. As per estimates[3], more than 24 million Afghan people need humanitarian assistance as nearly 95-97% population is likely to experience universal poverty.

Afghanistan's historical reliance on external financial transfers and large trade deficits (at 28 per cent of GDP in 2020[4]) cause further uncertainties. It is critical to note that the country imports approximately 80 per cent of electricity and almost all fuel resources[5]. The country's current domestic power supply is around 1,200 GWh (20-25% of total supply) and power imports from Central Asia account for (75 -80%) of the total supply. The payments have been impacted with the abrupt suspension of the flow of foreign aid which constitutes 75% of the national budget.

DABS purchases electricity from six suppliers. It includes imports from neighbouring countries and purchases from Independent Power Producers (IPPs). As per the recent study of energy sector assessments (ADB-UNDP), post-August 2021, the imports from Tajikistan and Uzbekistan to date are estimated at USD 147 million (55% of total costs). After 15 August, only Uzbekistan restricted supply by 50% due to delays in payments. Overall, total electricity costs at USD 169.25 million and revenue deficits stand at 50%. This adds to the DABS arrears of approx. 10% from pre-2021 levels. Besides electricity purchase from different sources, DABS also generates electricity internally form different sources, mainly hydro, thermal and diesel generators.

Due to the lack of availability of a grid, some of the provinces may not be able to import electricity. The Provinces which are not connected to the National Grid and the main source of energy is mini-grids and diesel Generator are Nooristan, Kunar, Paktika, Zabul, Orozgan, Farah, Daikundi and Ghor.

Currently, IPPs supply 50% of domestic generation and face many constraints due to lack of access to finance, delay in payments and other issues with the banking sector, difficulties in obtaining insurance and dealing the disrupted supply chain, uncertainties in regulations and changes of clauses in the agreements. Besides, weak grid infrastructure, technical issues with grid stability, transmission and distribution losses and limited capacity of utility impede new project development.

[1] See the UN TEF report 2021 Afghanistan; World Bank Survey 2022 on private sectors for Afghanistan.
[2] World Bank 2022. World Bank Survey: Afghanistan's Private Sector Hit Hard by Political Crisis
3 Socioeconomic Outlook 2021-2022, UNDP Afghanistan.
[4] https://www.worldbank.org/en/country/afghanistan/overview#1
[5] https://www.worldbank.org/en/country/afghanistan/overview#1

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

**Prevalence of Energy Poverty:**

Even with imports, Afghanistan's per capita electricity consumption is at approximately 100 kWh, which is less than a tenth of the levels of neighbouring countries, which in turn is much lower than the world's average and lower than the IEA recommended provision of at least 150 kWh per person per year. Afghanistan is one of the poorest counties in terms of Multidimensional Energy Poverty[6] (Abbas et al. 2020) and remains the lowest among the countries in the region. Nearly 24.5 million people in Afghanistan are not connected to the national grid, energy efficiency is significantly below the global average (1.8 vs 4.8 MJ per US$ PPP 2017), 36 per cent of the population has access to clean cooking (2019), and 21 per cent of the final energy consumed is from renewable sources (2018).

Energy poverty affects the quality of lives of women and men differently in varying degrees and impacts their health, employment and many basic services. Currently, the demand for energy in the country far exceeds its supply, the transmission and distribution grid is unreliable, and load shedding and outages of electricity supply are common. Many provinces[7] are not connected to the grid and are therefore largely served through local diesel generating units that increase the costs of supply. Thus, lack of access is linked to affordable energy and impedes economic, social and educational opportunities for the poor and rural residents.

Afghanistan's electricity demand is projected to grow at 12-15% annually over the next decade resulting in a supply shortfall of over 6,000 MW by 2032. In the absence of an integrated/ synchronised national grid, Afghanistan is constrained to access energy sources from its different regions due to technical limitations. Improvement of the national grid will have its own benefits, but strengthening it is a long-drawn and expensive (capital-intensive) process. It will be necessary to supplement the grid system with expanding distributed and decentralised energy generation systems based on renewable energy sources . This will have both medium and longer-term implications for meeting the basic needs of Afghan people sustainably, in particular, health and education as it transcends to food security and provision of other essential services (e.g., water supply).

**Impact of low energy access on health and education sectors**

There are approximately 4,000 health and 20,000 educational facilities across 34 provinces and most of them are deprived of access to reliable electricity even when they have access to grid. Poor people face major challenges as they rely on public services that were mainly supported through aid programmes of donors and the donors' suspension of programmes after August 2021, and their withdrawal has led to severity in terms of lack of basic and essential services. Although, the recent assessment by WHO confirms that 99% of the 2730 health facilities evaluated are operational.[8]

The experience indicates that reduced access to electricity has meant that doctors in Afghanistan must choose which patients they can save. Without power, they lack access to basic facilities such as ECG machines and ventilators; furthermore, they cannot conduct even minor surgeries. Unreliable energy supply creates an added burden for health professionals serving in rural clinics that are already constrained by a lack of qualified medical staff, equipment and medicine for providing critical basic health services for the rural population. Reports of worsening situations saw c-sections operated with flashlights of cellphones, and hospitals delivering babies of five mothers with just one pair of gloves[9] in maternity wards and operation theatres. A significant linkage

[6] A household is identified as multidimensionally energy-poor if: (1) deprivation occurs in three of the four dimensions of indoor air pollution, education/entertainment, household appliances, and telecommunications; (2) there is also deprivation in cooking and lighting; and if (3) it is deprived in one of the two dimensions of lighting and cooking, in addition to one of any other dimensions.

[7] The Provinces which are not connected to the National Grid and the main source of energy is mini-grids and diesel Generator are: Nooristan, Kunar, Paktika, Zabul, Orozgan, Farah, Daindi and Ghor.

8 herams_afg_baseline_report_2022_operational_status.pdf

[9] https://www.trtworld.com/magazine/under-a-cellphone-light-how-babies-are-born-in-afghanistan-now-52850

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC


between energy and maternal health, and gender equality impact is noted in the context of Afghanistan, where energy intervention in the health facility can make an impact because only 10% of women in a very recent assessment expressed that they could cover their basic health needs compared to 23% men[10]. This implies that there is already a problem in accessing basic health care by women, as well as poor men. Disruptions in electricity supply have been linked to reduced oxygen production, which proved a crucial issue during the pandemic. Vulnerable patients on ventilators were at higher risk due to power cuts, and many lives were reported lost due to breaks in the oxygen supply coupled with equipment failure.

It is critical to emphasize the harsh weather and extreme cold weather for nearly 4 to 5 months, people need heat, especially sick persons, pregnant and lactating mothers, and elderly persons. Hospitals in Afghanistan lacked the energy to heat rooms during the winter months. This was due to multiple issues: lack of funding, alongside the new regime's inability to settle unpaid bills to Central Asian suppliers as noted above. At Kabul's Indira Gandhi hospital last October, staff had to cut down trees for firewood, which could be used to heat some rooms in the hospital. According to doctors, patients have been seen shivering due to the cold, which puts them at risk of developing complications such as pneumonia.

The complexity and severity of the ongoing crises have increased the need for health assistance by 20 per cent, according to the Humanitarian Response Plan for Afghanistan 2022. There are currently 18.1 million people projected to need humanitarian health assistance alone in 2022. It prioritizes ensuring available and accessible routine, emergency, and specialised health care services, essential for meeting the needs of the most vulnerable. It requires to cope with other unanticipated disasters like the recent earthquake that severely impacted infrastructure at the provincial levels. At least 1,163 people died and more than 6000 were injured and over 700 homes were destroyed by the earthquake in June. In addition, the flash flood in July affected 500 families (agriculture, shelter, infrastructure) in the Eastern Region. Therefore, humanitarian assistance needs to be reinforced by emergency social services, without which the local population cannot access basic essential health services. There is an urgent need to renovate and equip the health centres[11],[12] but at the same time, they are made functional with access to electricity to provide health care.

Figure 1 shows the percentage of healthcare facilities across Afghanistan which have access to electricity. However, the average hours of electricity supply are unreliable and require health facilities to rely on diesel generators and the cost of fuel is often funded through donor programmes


Figure 1: Percentage of health facilities with access to electricity in Afghanistan

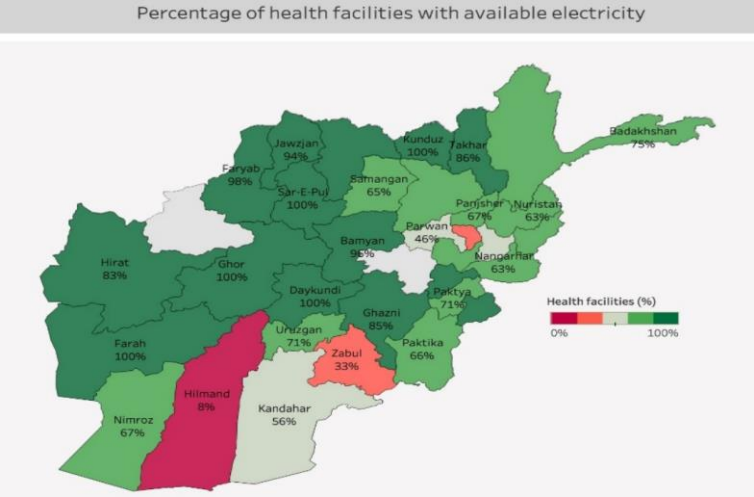


[10] ibid
[11] AHSR2020.pdf
[12] https://dashboard.whe-him.org/index.php/maps-3/

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

Figure 2: Percentage of healthcare facilities with diesel generators in Afghanistan

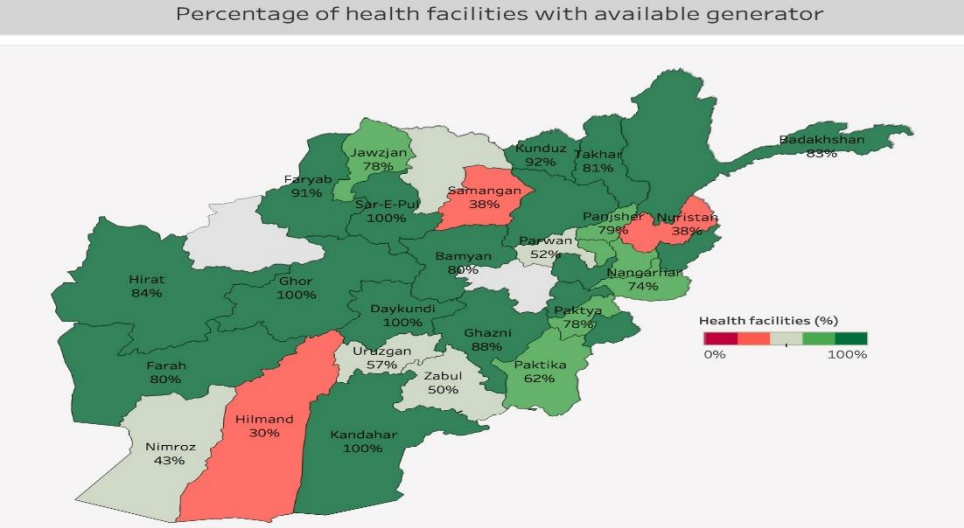


Afghanistan's education system is among the poorest in the world, which is reflected in the low literacy and numeracy of its population and the low capacity of its educational system from insufficient infrastructure and regulation to chronic shortages of textbooks and human resources.[i] While infrastructure constrains go beyond energy, the majority of schools have no or limited access to electricity. A preliminary analysis of primary schools in Afghanistan show more than 5000 schools (for both boys and girls) that are operational are not having access to electricity. Lack of reliable supply of electricity is mainly addressed through the alternative of diesel generators and relying on donor contributions for the costs of fuels. In few schools, captive solar systems for electricity supply have been set up. Women's and girls' access to education services is influenced by the availability of electricity for water and sanitation. Lack of access to basic infrastructure in schools impacts in the disproportionate dropouts, particularly girls.


During the pandemic, when schools were shut down for lengthy periods, the Afghan government promoted distance learning via radio and TV stations. However, as a significant proportion of the population either had no access to electricity or to radio/ television stations, the program could not take off. According to a teacher in Afghanistan, over 3000 students in Kabul alone, who belonged to poor families, did not have either internet or mobile access. Those that did, could not utilize their devices because Kabul received electricity for only a few hours each day. According to Save the Children, 3.7 million children were not in school before Covid-19, and only 28.6% of children were expected to access distance learning though TV; 13.8% though radio and only 0.2% could access learning via the internet. According to a UNICEF report, while 94% of urban households and 85% of rural households own a mobile phone, internet provision remains severely limited, which would prevent children from accessing remote learning opportunities. This prevents young girls, in particular, from accessing education, given that the new government has maintained its ban on their education.

Since August 2021 education above 6$^{th}$ grade has been suspended for young girls, adolescents and adult women. These are countered through various measures with support from donors and private schools. For instance, UNICEF provides stationery, textbooks, and other learning materials to 785,000 public school first graders through community-based councils and pursues professional development of women teachers through provincial development centres. Emphasis on blended and digital learning opportunities is being explored. However, electricity forms a part of critical infrastructure to deliver basic services effectively. Without access to electricity in educational institutions, this is expected to exacerbate gender barriers and inequalities notwithstanding the catalytic nature of education in transforming the lives and livelihoods of Afghan people and in creating jobs and income opportunties. Access to electricity provides with alternative learning tools as well as improves the quality of education services.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

Figure 3 shows as an example in Kapisa province with very few schools having access to electricity which will be no different in other provinces, given the basic standards of operating schools across provinces.

Figure 3: Percentage of schools with access to electricity in Kapisa province of Afghanistan

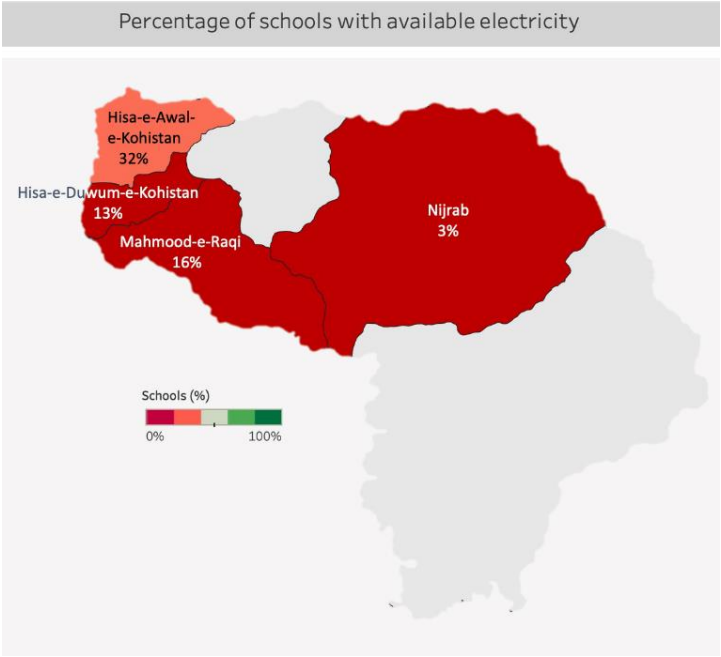


Most institutions and public facilities in the health and education sectors are thus relying on polluting diesel generators or other sub-optimal solutions that impact the efficiency and effectiveness of services. Lack of educational and medical services is even forcing people to migrate or travel to neighbouring countries.

The project recognizes, among other factors, the lack of infrastructure to deliver essential services and its accompanying development challenges of energy poverty, reliance on polluting energy sources and lack of deployment of reliable sources of renewable energy. The project proposes to address the impacts of lack of energy access on social and essential services in key sectors of education and health. It further promotes use of renewable energy to enhance the quality of essential servicesfor basic human needs. Furthermore, this project will engage private sector for energy services' provision , which would enable improving livelihoods and lives. There is adequate research that shows the positive correlation between access to electricity and HDI.[13]

## II. STRATEGY

The proposed project addresses the challenges of access to reliable electricity in public facilities in the education and health sectors through the provision of decentralized and distributed renewable energy technologies and services. The proposed interventions consider gender inclusive and mainstreaming approaches and support job creation in the renewable energy sector.

***The rationale for deploying decentralised renewable systems*:**

Evidence in the fragile and high-risk settings indicates that scaling up of renewable energy systems are more -cost-effective, practical and sustainable solution than the deployment of

[13] TERI.2018. Does access to energy cause human development? A Granger causality check https://www.teriin.org/article/does-access-energy-cause-human-development-granger-causality-check

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

centralized systems with inherent technical and other losses, and improves the resilience of energy systems for basic human needs. Decentralised renewable energy systems reduce reliance on centralized systems and eliminate the use of other backup/ alternate diesel generators (that are often targets during conflict and often unsustainable due to high costs) and allow democratization of power systems. Women, who are disproportionately affected by the lack of access to health and education services benefit from reliable energy services and new opportunities for livelihoods and jobs, and improved living standards. With a substantial decline in renewable energy costs combined with energy efficiency, they are increasingly affordable and competitive relative to alternative fossil fuels such as diesel generators. Solar energy alone has great potential in fragile settings due to geographic characteristics and its incremental scalability. However, other alternatives can be explored based on the local context.

### *Energy and UNDP: Priority and Lessons*

Energy remains one of UNDP's six signature solutions – alongside poverty and inequality, governance, resilience, environment, and gender equality - to support countries towards three directions of change: structural transformation, leaving no one behind and resilience. As per UNDP's new Strategic Plan 2022-2025, the first objective of UNDP is to increase energy access for those furthest behinds.

The project will leverage UNDP's more than two decades of work in the energy sector in diverse countries. It further builds on the lessons from the recent evaluation by UNDP- IEO. The findings of this evaluation reinforce the appropriateness of UNDP's deployment of a diverse range of mostly stand-alone energy technologies in crisis/post-crisis contexts since 2018 and the need for scaled-up support to deliver effective renewable solutions for managing energy challenges in fragile contexts has made significant impacts to date. UNDP has supported over 900 health centres and storage facilities with solar in Angola, Chad, Liberia, Libya, Namibia, Nepal, Sudan, South Sudan, Yemen, Zambia, and Zimbabwe, largely funded through the Global Fund to fight AIDS, Tuberculosis and Malaria (Global Fund). As a result, an estimated 34.5 million people now benefit from reliable health services in these countries.[14] UNDP has also partnered with KfW in similar areas[15].

### *UNDP in Energy Sector in Afghanistan*

In Afghanistan, UNDP has implemented renewable energy projects with its own funding, and with support from bilateral and others such as GCF. "ASERD" – Afghanistan Sustainable Energy for Rural Development with funding from Korea has demonstrated the feasibility of implementing solar – small hydro mini-grid providing electricity access to 18,000 people. The mini-grid is operated by a private sector company ASERD project has also provided solar electricity and hot water solution to 27 maternity clinics, supporting about 3,000 doctors, patients, and clinic staff. Emerging lessons are: a) local capacity in installing or constructing the solar electrical and hot water systems has improved as many Afghan-based companies have gained operational experience b) Users acceptance of new systems have increased c) prior community engagement and site assessments are key to proposing or designing the systems and its sustainability.

Specific to mini-grids and rural electrification, experience indicates that site selection needs to be more rational. Remote areas with poor roads and connectivity result in high installation as well as operational costs. As the ability of a household to pay for the electricity is limited in such remote locations, connectivity and load/energy demand profiles are other considerations. Design-Built-Operate-Maintain as a contracting modality has proved to be effective as it ensures payment based on guaranteed performance. If risks of the private sector are mitigated, the PPP modality can be leveraged for soliciting private investment. Engaging with the communities at every stage

[14] https://www.un.org/en/un-chronicle/solar-health-five-ways-solar-power-can-make-universal-healthcare-reality#_edn2
[15] https://intranet.undp.org/unit/pb/resmob/KfW/Home.aspx

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC


of mini-grid development and awareness training to the people in the project area needs to be included in the mini-grid planning. ASERD's scale-up has been conceptualised through the approved GCF project "AREMTI" – Afghanistan Rural Energy Market Transformation Initiative for improved renewable energy access and closing the energy gap which is on hold post-August 2021 crisis. There is also much learning from other projects implemented in Afghanistan. UNDP, under the technical assistance project of ADB, carried out a study (July – September 2022) on energy sector baseline assessments in Afghanistan[16]. Preliminary findings and consultations reaffirm the sectoral challenges. For distributed generation and use, there is a need to develop O&M services delivery models with an appropriate scale that could engage the private sector to provide energy services more sustainably.

Post-August 2021 crisis, UNDP has launched ABADEI, Area Based Approach to Development Emergency Interventions. The ABADEI is being regionally implemented and catalyses on a programme as well as a strategic framework within the four thematic areas of essential services provision, livelihood opportunities, climate-resilient infrastructure and social cohesion. Under ABADEI, the sub-projects in many end-use sectors mainstream energy interventions regionally with funding from other donors such as JSB. The proposed KfW-funded project complements ABADEI in its area-based approach by adopting a sector-wide approach to bring in scale and needed focus to address the overall challenges that the sector itself is facing concerning distribution generation, and applications including O& M, finance and commercial issues. While ABADEI works with communities more as a bottom-up approach, sectoral interventions are top-down and these complement both demand and supply side interventions.

### *Solar Vs. Renewable Energy Potential in Afghanistan*

Afghanistan is bestowed with very good solar insolation and receives about 4 to 6.5 kWh per square meter per day of solar insolation on average, with 300 sunny days a year. The estimate of solar power potential is 222 GW out of the 319.5 GW estimated from all renewable energy sources, namely, solar, wind, biomass and geothermal. They could be supplemented with potential energy efficiency measures as applicable such as replacement with efficient lighting and heating solutions besides retrofit measures for wiring and controls as necessary for optimal performance.

Figure 4: Afghanistan Solar Resource Potential

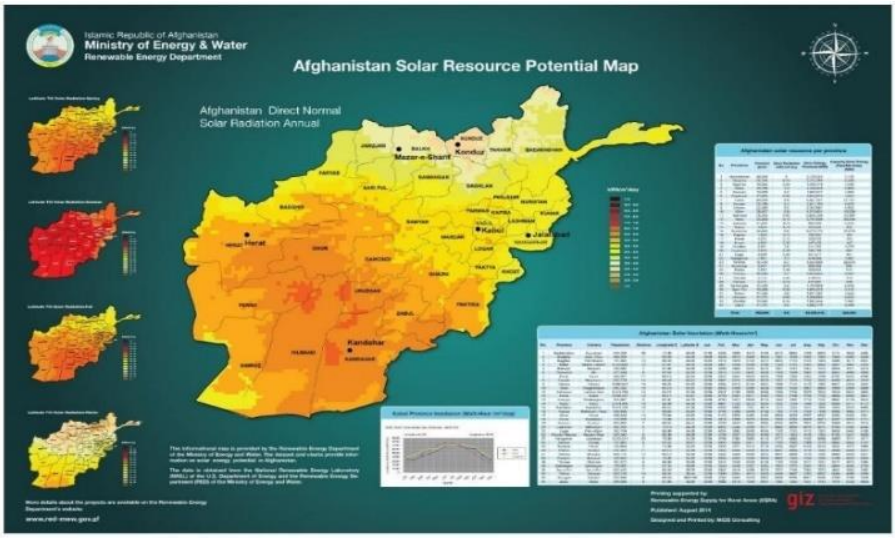


[16] Baseline report from ADB TA study is expected by September 2022

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

## III. RESULTS AND PARTNERSHIPS

### *Expected Results*

The project's objective is the adoption of renewable energy (and energy efficiency) measures in public facilities (primarily in the health and education sectors) for the sustained delivery of essential services for meeting basic human needs. Supplementing conventional sources of electricity with renewable energy-based electricity contributes to Afghanistan's energy security (with less reliance on imports), better resilience through reliable services and effective response to humanitarian and energy crises faced by poor and vulnerable Afghans.

Energy access enables improvements in infrastructure and essential services for meeting basic human needs. The project is conceptualised in the priority area of sustained essential services of the Strategic Framework for Afghanistan 2023-2025. It directly contributes to the two outcomes (out of the four) namely,

Outcome 1: By the end of 2025, more people in Afghanistan, particularly the most vulnerable and marginalized, including women and girls have their basic human needs progressively met through the sustained delivery of essential services.

Outcome 3: By the end of 2025, people in Afghanistan, especially women, youth, and other marginalized groups, and those at risk of being left behind benefit from a more equitable, inclusive, sustainable, and resilient employment-rich economy and shared economic opportunities with enhanced productive capacities for improved livelihoods and decent work.

### *Phased Implementation:*

The project will be implemented in two phases. The first phase of the project will focus on areas/provinces that are either not served or under-served by the regional/national grids with the average hours' supply of electricity between 0 - 6 hours. This will include an Inception Phase of six months that will further assess the project design and implementation approaches in detail for efficient and effective delivery of the results.The second Phase will target provinces between 7 -12 hours of average supply of electricity and forms the prioritization approach indicated in Table 1. Phase I will thus cover 16 provinces and Phase II, the remaining 18 provinces. The funding from KFW Development Bank (KFW) is envisaged initially for the first phase and based on the progress, funding for the subsequent phase will be ascertained by June 2023.

At the Outcome level, the project supports access to renewable energy for essential health coverage and education services measured for impacts through the following indicators (linked to Strategic Framework for Afghanistan):

- Increase in share of renewable energy in the overall energy mix for essential health services coverage
- The proportion of population/public facilities in health and education sectors with access to renewable electricity
- The proportion of individuals using digital tools/solutions

The project's interventions are in the following three areas that have been integrated into the results framework with three corresponding outputs:

1) Improving the supply of decentralised renewable energy-based electricity and energy efficiency measures for education facilities
2) Improving the supply of decentralised renewable energy-based electricity and energy efficiency measures for health facilities

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

3) Support to O&M of decentralised renewable energy systems through appropriate service delivery models and capacity building/ training, with a special focus on training for women in energy sectors.

***Project site selection:***

The provinces are targeted based on electricity access - Phase I with 0-6 hours and Phase -II with 7-12 hours of average supply or availability of electricity in different provinces and districts. This phased approach and prioritization of provinces based on the availability of hours of electricity was consented to by many stakeholders during preliminary discussions. A recent study based on the Night Lights Development Index points to the regions of poor energy access[17] and its consequences that necessitate urgent prioritization of provision of basis services in these regions.

Once the province is selected, a list of public facilities within the province will be screened based on the existing databases on schools and findings from surveys commissioned through other UN agencies such as Unicef. Based on desk analysis and through community engagement processes, representative facilities will be longlisted for conducting surveys for further shortlisting based on the key criteria (primary) and sub-criteria (secondary) highlighted in Table 1.

Following the survey of shortlisted facilities, the findings will be reviewed and vetted through a process of community engagement and stakeholder consultations and selected for the project interventions. Close coordination with other UN agencies such as UNICEF for accessing existing databases will be ascertained at all stages of screening, longlisting and shortlisting for finally targeting the facilities. This proposal already has referred to a database that was collected in January 2020 on electricity in schools in one province, Kapisa. Similarly, there is existing data for Health facilities, containing frequencies and percentages per province and per district on availability of electricity and availability of a generator for 1345 health facilities and this will be extended to reach approximately 2000. A sample visits of facilities have also been undertaken as part of this project development.

The shortlisted public facilities will be mapped and will be then subject to feasibility analysis. Every site would be assessed for solar insolation, load analysis, availability of suitable area, ESS, gender, security and other considerations. Most feasible sites will be selected for project interventions and will be standardised with technical packages for implementation. Given the higher number of installations of systems, the sites would be clustered and categorised for enabling procurement and installation, commissioning, and O&M with scale economies.

The actual implementation at the sites will be facilitated in close coordination with the regional teams of ABADEI.

[17] Preliminary findings of the draft report on “The economic and humanitarian consequences of electricity shortages following 15 August 2021, Afghanistan”, UNDP 2022 include:

a) A decreasing trend in NTL was evident within Afghanistan before 2021.
b) Following the events of 2021’s, including the country’s change of government, night light intensity per capita decreased; this is particularly pronounced in Kabul, and the southern, eastern and western regions of Afghanistan. This decrease suggests a drop in electricity consumption and consequently economic activity and living standards.
c) The five regions with the highest percentage decrease in NTL per capita are Farah, Kandahar, Paktika, Uruzgan, and Zabul.
d) The five districts with the highest percentage decrease in NTL per capita are Khulm, Sayyad, Rashidan, Qush Tepa, and Feroz Nakhchir.
e) Nighttime light intensity variations assist in identifying clusters of similar values and outliers, and facilitate the study of spillover effects. There is an agglomeration of districts between northern Kandahar, Zabul, Uruzgan, north Hilmand, Farah, and Hirat, that showcase clusters of decreased light intensity.
f) A decrease in NTL per capita is observed between July and September 2021, corresponding with the change in government. This has not been attributed to seasonal variations.
g) Negative NTL per capita variation is concentrated in urban areas. Overall, the variation is negative but with a higher magnitude in urban centers (-0.5% for rural vs -29% for urban).
h) The NTL per capita variation is negatively correlated with the presence of Diesel off-grid powerplants.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

Table 1: Prioritization matrix for installation of RE systems (indicative)

| **Primary Criteria** | **Secondary Criteria** | **Provinces (Indicative)** | |
|---|---|---|---|
| Ownership - Premises owned/ rented by the institution e.g. do not require land acquisition/ permissions and/ or enough space on the rooftop | Criticality of electricity in public facilities / Facilities running on diesel generator | Phase I (6 hrs of average supply of electricity) | Phase II (7 – 12 hours of average supply of electricity) |
| Availability of Suitable area - Not with shadows, structural safety etc. | Load profiles of public facilities and the impact of lack of electricity on the services Alternatives Solar insolation | 1. Khost<br>2. Paktika<br>3. Uruzgan<br>4. Zabul<br>5. Helmand<br>6. Farah<br>7. Kunar<br>8. Nuristan<br>9. Nimroz<br>10. Laghman<br>11. Bamyan<br>12. Ghor<br>13. Samangan<br>14. Panjshir<br>15. Daykundui<br>16. Farah<br>17. Badghis<br>18. Panjshir | 1. Kunduz<br>2. Logar<br>3. Nangarhar<br>4. Paktia<br>5. Parwan<br>6. Sar-e-Pol<br>7. Takhar<br>8. Wardak<br>9. Kabul<br>10. Kandahar<br>11. Ghazni<br>12. Balkh<br>13. Faryab<br>14. Baghlan<br>15. Herat<br>16. Jowzjan |
| Gender- Facilities are mainly accessible and used by women and vulnerable groups, and enhance the quality of service for them. | Footfall/enrolments | | |

The project's objective is to adopt renewable energy and energy efficiency measures in public facilities (primarily in the health and education sectors) for sustained delivery of essential services for basic human needs.

The Theory of Change is presented as follows:

***IF:***

Access to renewable energy and energy efficiency for meeting basic needs and services, especially for health facilities and educational institutions, is improved

Essential services become functional, reliable, efficient, sustained and expanded for women and men;


Investments in energy services delivery models are made for improved performance of infrastructure assets;

**THEN**

People in Afghanistan will be able to meet their basic human needs through sustained delivery of essential services

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

**Figure 5: Theory of Change**

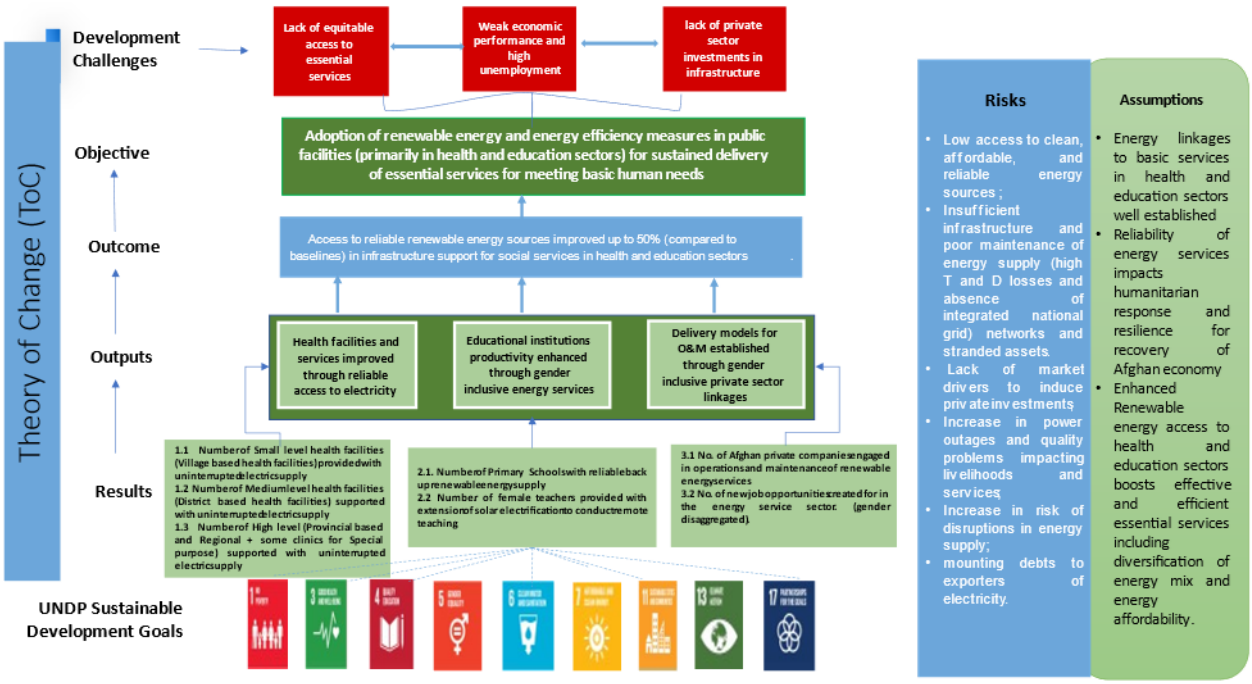


As in the Figure above, the results chain encompasses the following outputs and activities to achieve the stated objective and outcome.

**Output 1: Health facilities and services improved through reliable access to electricity**

The project covers approximately 10 -15 per cent of approx. 3,512 health facilities in 34 provinces that provide primary healthcare services to 30 million Afghans. It aims to address the lack of grid electricity access to an estimated 41% of the health facilities that rely on diesel generators; and provide power backup based on solar energy to the remaining 59% that have intermittent and unreliable electricity and puts many patients' lives at risk during as well as lack of treatments for want of electricity.

Energy audits, technical surveys and assessments would be carried out for devising appropriate solutions. Where feasible, turnkey solutions will be implemented within the agreed procurement approaches to determine solar power installation and battery backup capacity for reliable electricity supply to the public facilities. Load profiles would be developed for different appliances and equipment and critical loads will be identified based on a feasibility analysis that will take into account the ESS compliance requirements. These will be supplemented with energy efficiency measures and specific needs' for selective insulation and other winterization measures (not a focus and only for optimizing performance). The project estimates up to 10.56 MWp solar power - battery back-up systems to be installed for electrification of about 92 health institutions in phase I. While supporting health facilities, the project interventions will create access to services and new opportunities for women.

Different technical packages will then be designed based on the categories of health facilities as described in Table 2. This will be based on surveys and detailed assessments. A detailed feasibility study will determine the site requirements, contractual aspects and detailed specifications. The specifications drawn will be shared with the LTA holders or through competitive processes in line with the procurement strategy for receiving their offers and will be selected following standard UNDP procedures.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

Coordination meetings will be carried out by consultants/ contractors with hospital administrators and officials at the Ministry of Public Health to ensure access and follow the processes stipulated.

**Activity 1.1 Prioritise public facilities for installations through surveys and needs assessments**
The following specific tasks will be undertaken:

- Experts' advice and consultant support in providing engineering and technical expertise for scoping baselines through desk research, approaches on prioritization, determination of criteria, methodology, technical design, costing, ESS, including SEA, and screening and gender-responsiveness of the facility, etc for preparing a long-list of facilities
- Through contractual specialised services, assessment of the facilities will be done by applying technical criteria for preparing a shortlist of facilities and carrying out pre-feasibility for final selection. This will include recommended specifications for the short-listed facilities
- Project-related travel to the facilities prioritization, selection and assessments
- Meetings and consultation with stakeholders and beneficiaries including women and girls, and other vulnerable groups .

**Activity 1.2 Design, feasibility (including environmental, social and safety), installation and commissioning including O&M (procurement in stages/ turnkey)**
The following specific tasks will be undertaken:

- Coordination of the methodologies, design, specifications, etc. for evaluation/validation of pre-feasibility findings for the actual selection of the sites for project interventions
- Feasibility of the selected sites and Installation of Equipment, Commissioning, and operating and basic training cost up to 5 years (Years TBD) informed by the assessment.
- Project-related travel to the facilities

**Activity 1.3 Monitoring results and measuring/reporting impacts**
The following specific tasks will be undertaken:

- Independent monitoring/Third party monitoring, as well as UNDP's internal field monitoring.
- Travel related to monitoring of the sites (including field missions for reporting)

**Output 2: Schools/related educational institutions' productivity is enhanced gender-inclusive approaches to the provision of energy services**

The project will install up to 7 MWp in Phase I of solar power - battery back-up systems for electrification of approx. 700 educational institutions. Four categories of institutions have been identified (Refer to Table 2). Similar to Output 1, a turnkey solution approach will be adopted with checks at every stage.

Coordination meetings will be carried out by consultants/ contractors with school and university administrators and officials at the Ministry of Education and Ministry of Higher Education to ensure processes are adequately followed.

**Activity 2.1 Prioritise public facilities for installations through surveys and needs assessments**
The following specific tasks will be undertaken:

- Experts' advice and consultant support in providing engineering and technical expertise for scoping baselines through desk research, approaches on prioritization, determination of criteria, methodology, technical design, costing, ESS including SEA screening, , and gender-responsiveness of the facility, , etc. for preparing a long list of facilities

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

- Through contractual specialised services, assessment of the facilities (long list) by applying technical criteria for shortlisting of the facilities and carry out pre- feasibility for the shortlist for final selection including recommended specifications
- Project-related travel to the facilities
- Meetings and consultations with stakeholders, including women and girls.

**Activity 2.2 Design, feasibility, installation and commissioning including O and M (procurement turnkey)**

The following specific tasks will be undertaken:

- Coordination of the methodologies, design, specifications, etc. for evaluation/validation with support from short-term consultants or experts. These would entail the possible engagement of ITM, Copenhagen and other relevant units of UNDP outside of Afghanistan.
- Feasibility and Installation of Equipment, Commissioning, operating and basic training cost up to 5 years (Years TBD) informed by the assessment.
- Project-related travel to the facilities
- Training of the facility workers on the systems, processes and compliance requirements

**Activity 2.3 Monitoring results and measuring/reporting impacts**

The following specific tasks will be undertaken:

- Independent monitoring/Third party monitoring
- Travel related with monitoring

**Output 3: Delivery models for O&M through private sector linkages and gender inclusiveness are developed/ established**

This output will focus on exit strategy by facilitating appropriate delivery models for sustenance of the assets created through this project in public facilities. Improved private sector participation in energy ecosystems, after-sales services, maintenance would be considered. The project will strategize efforts in assessing the risks and possibilities to enhance private sector and women's participation in the upkeep of these systems through identifying appropriate business models. This would also assess the policies and regulations under the current regime and possible negotiations for market-driven approaches. Besides, the expertise of other knowledge partners such as IRENA will be sought for best practices or exchanges of experience. The role of IRENA will be further elaborated during the Inception Phase.

Managing supply chains require support from local Afghan renewable energy companies, vendors and manufacturers. They will be engaged to carry out site assessments, feasibility studies, technical designs, installations and O&M in other potential sites of educational institutions and health facilities. The engagement of the private sector will promote local manufacturing and strengthen the local economy, which has been impacted significantly following the crisis. The project interventions encompass efforts to create jobs for women and men in the renewable energy sector that will ease the levels of extreme poverty. The number of jobs to be created will be assessed during the project inception phase.

**Activity 3.1: Private sector platform for soliciting proposals for O&M beyond the project period**

The following specific tasks will be undertaken:

- Design exit strategies for operation and maintenance delivery models beyond the contractual phase (determined in outputs 1 & 2 as part of the project activity).

- Solicit proposals as per strategy from different interested groups for the sustenance of the project interventions including asset transfer mechanisms.
- Travel related with a visit to facilities and participation in workshops and meetings
- Workshop for the private sector and other institutions (CDC/RPs) engagement

**Activity 3.2: Execution of exit strategy/proposals implementation (including supply chain management and entrepreneurship promotion for installation, servicing, and maintenance of solar systems**

The following specific tasks will be undertaken:

- Evaluate and commission different delivery models
- Training on the sustenance of the project interventions

**Activity 3.3: Stakeholder engagement Plan (SEP)**

The following specific tasks will be undertaken across all activities under all the outputs:

- GRM, including SEA complaint, data base (Including running of the hotline, record keeping, connectivity cost etc.)
- Communication materials (leaflets, posters, social media)
- Training (Social issues, outreach, GRM, SEA etc.) for PIU, IPs

**Output 4: Project Management Support**

A dedicated team will be put in place for facilitating the implementation of the project activities under the overall organisation structure proposed. This would comprise members with engineering, procurement, environment and social safeguards expertise, energy and technical specialists, monitoring and reporting specialists, and communications and gender specialistsfor effective implementation of the project interventions. In addition, the project will synergise efforts through the engagement of knowledge partners such as IRENA, Responsible Parties (existing under ABADEI such as Actionaid, Care, etc.) and other UNDP units such as ITM, Copenhagen.

***Beneficiaries (tbc during the Project Inception Phase)***

The project aims to will reach approximately 0.5 million and 0.5 milion [18] people accessing health and education services respectively. Through the proposed investments, it would create direct employment for around 1000 people (which will be re-assessed during the project inception phase) across 34 provinces and trigger indirect employment, whichwill be much higher. These targets would be confirmed during the baseline assessment to be carried out during the Inception Phase.

| | Direct Beneficiaries | | | | Indirect Beneficiaries (as applicable) | | | |
|---|---|---|---|---|---|---|---|---|
| **Activity** | **Total** | **Women** | **Men** | **Other categories as relevant to Project design (e.g. age, refugees** | **Total** | **Relevant category (e.g. teachers)** | **Relevant other categories (e.g. community leaders)** | **Other categories as relevant (e.g. age, refugees)** |

[18] Revised for Phase I only based on the assumption of 6.7 million primary school enrolments (WB data for 2019) in approx.. 20,000 schools. 700 schools could cover approx. 335,000 enrolled students + teachers etc ~ say, 500,000 beneficiaries.

For health facilities, assuming @ 60% of Afghan people have access to health facilities, which is ~ 23 million people approx. and having access to 4,000 plus health facilities, which would be about 6,000 people having access per facility ~ 550,000 for Phase I (92 facilities) = tentative total target ~say, 1 million beneficiaries; the numbers will be firmed up during Inception Phase.

Note: sex ratios will be determined to contribute towards gender equality in the given context.

| | | | | | | | | |
|---|---|---|---|---|---|---|---|---|
| | | | | **etc)** | | | | |
| **Outcome 1:** | | | | | | | | |
| **Output 1: (Health)** | **0.5 million** | **0.25 million** | **0.25 million** | | | | | |
| **Output 2: Education** | **0.5 million** | **0.25 Million** | **0.25 million** | | | | | |
| **Output 3: delivery Models** | **Tbd** | | | | | | | |
| **Total incl. double counting** | **Tbd** | | | | | | | |
| **Total without double counting** | **Tbd** | | | | | | | |

### *Resources Required to Achieve the Expected Results*

The project will benefit from inhouse expertise at the country, regional and global levels. It will propose a dedicated team of interdisciplinary professionals covering aspects of clean and renewable energy technologies, financing, economics, the private sector, the environment, and gender. It will tap short-term need-based specialised experts from the Global Policy Network (GPN), a network of field-based and global technical expertise across a wide range of knowledge domains and in support of the signature solutions and organizational capabilities envisioned in the Strategic Plan. It will further tap resources of the newly set up Sustainable Energy Hub that will build on UNDP's existing Energy Portfolio, covering over 100 countries to harness clean energy and support the energy transition as well as on UNDP's Climate Promise, UNDP's Sustainable Finance Hub and UNDP's Digital offer. Key positions and roles are presented in Table 6.

### *Partnerships*

The partnerships at all stages of the project design until implementation are guided by all principles of the UN Transitional Engagement Framework (2022)[19] and the new strategic

[19] **Principles of the Transitional Engagement Framework (2022)**

**The Human Rights-Based Approach:** Ensure adherence to international human rights standards and principles to promote and protect human rights.

**Humanity:** Human suffering must be addressed wherever it is found, with particular attention to the most vulnerable populations, such as children, women, people with disabilities and the elderly. The dignity and rights of survivors must be respected and protected.

**Neutrality:** No participation individually or organizationally in hostilities or taking sides in controversies of a political, religious or ideological nature.

**Impartiality:** Assistance must be provided without discrimination on the basis ofbased on ethnic origin, political opinion, gender, nationality, race or religion. The provision of assistance is guided solely by needs, and priority is given to the most vulnerable cases.

**Operational independence**: Assistance must be autonomous from the political, economic, military or other objectives that any actor may hold with regard to areas where activities are being implemented.

**Centrality of Protection:** Protection shall be placed at the center of all actions, requiring that protection shall be mainstreamed throughout all sectors and activities for the affected population.

**Do no harm:** Assistance must strive to 'do no harm' or to minimize potential harm when being present and providing assistance. Safety audit will be integrated in the facility assessment and stakeholder engagement plan.

**Dignity:** People in need shall be respected as equal partners in action in all activities and their dignity as human beings will be maintained in all communications. People will have opportunity to express their concerns and complaints through Grievance response Mechanism (GRM).

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

framework for Afghanistan and Country Programme Document. As the project interventions are targeted in schools and health facilities, DFAs and local authorities would be engaged in coordination with the renewable energy contractors, community engagement and policy discussions. Their engagement will adhere to TEF guidance referred to in its section on 'UN Engagement with the de facto authorities that mainstreams the reinforcing principles as follows:

- No support will be provided directly or indirectly to the de facto authorities, whether in Kabul or at the local level.
- Support will be implemented free from the involvement of the de facto authorities concerning (hiring/recruitment) policy, implementation and management. Additionally, the de facto authorities may not influence the selection of beneficiaries, project locations or project partners. This also means that women staff should be able to continue to work.
- No support will be provided to structures that institutionalize discrimination and/or violate human rights.
- At a minimum, service providers should ensure that services are accessible to girls and women in an equal fashion. A flexible approach is required in the volatile situation where provinces, districts and communities have different dynamics[20]

**Leaving no one behind:** Commitment to eradicate poverty, end discrimination and exclusion, and reduce the inequalities and vulnerabilities that leave people behind. Hard to reach area, facilities available to ethnic minorities, and accessible to women and girls will be prioritized.

**Diversity**: Drive active and meaningful participation of religious and ethnic minorities, people with disabilities, and people who suffer discrimination based on sexual orientation and gender identity. Mentioned under "Leaving No One Behind"

**Resilience**: Promote integrated and cost-effective approaches informed by the UN Resilience Framework that reduce risks, mitigate displacement, and help people and communities anticipate, prepare, respond and recover from shocks and crises.

**Accountability** to the people of Afghanistan, including measures to build upon and extend greater transparency, and improved measurement and reporting on results. GRM and SEA action plan integrated into ESMP will further assure this accountability.

Primary stakeholders that the project's success will heavily rely on are the local administrators of schools and health facilities, and the Afghan renewable energy companies chosen for feasibility studies, installation and O&M. Intensive coordination shall take place at the project implementation level between UNDP's project management team, local authorities and the contractors. The second layer of partnership is at the ministerial level i.e. with the ministries of education, higher education and public health.

At the field level, the project will work closely with communities, local institutions and industry associations and energy stakeholders for need-based and demand-driven/responsive solutions to meet the local contexts.

For identifying appropriate solutions at scale, comprising of technology, financing, capacity building and marketplace opportunities, it will tap national as well as international organizations such as the International Renewable Energy Agency (IRENA), SE4ALL, International Solar Alliance, G7+ Fragility, etc. for accessing knowledge – global lessons learned, policies and tools,

---

**Gender equality: UNDP's global gender equality strategy linked to energy project will be adapted** to promote gender equality and women's empowerment , as well as adequate actions that does not exacerbate the risk of GBV aligned to UNDP's guidance on Gender Mainstreaming into Crisis and Recovery Toolkits. UNDP CO will have its internal gender action plan for this project.

International standards and principles to promote gender equality and the full realization of women's rights and freedoms will be integrated and mainstreamed across all activities.

**Cultural Sensitivity:** Local customs, cultures and religions are respected while simultaneously adhering to international humanitarian standards around gender and equality.

**Prevention of Sexual Exploitation and Abuse:** Create and maintain an environment in which sexual violence is not tolerated and prohibited for all interactions. SEA prevention, mitigation and response strategy and action plan will be integrated as part of overall ESMP.

[20] Central directions on policies and application of law from the de facto authorities, for example, are reflected unevenly across the provinces and districts which requires adaption for programme delivery. For more information on governance aspects see: Afghanistan Country focus. Country of Origin Information Report January 2022. European Union. European Asylum Support Office.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

best practices and carrying out capacity building of the targeted stakeholders to facilitate its implementation at the local level. Given the current context and the nature of interventions to speed up investment, especially for those hardest to reach and in crisis contexts, the project will leverage cooperation with the banking sector and with IFIs and donors.

Energy Think -Tanks in the region will be engaged for innovations, technical assistance and preparing the cadre of a new generation of energy enterprises and strengthening the existing energy networks. Through its ongoing UN-wide initiatives based on ABADEI, UNDP will be able to feed lessons, experience, and expertise of other partner UN agencies.

**Risks and Assumptions**

| Outputs and Activity results | Assumptions and Risks |
|---|---|
| Output 1: Health facilities and services improved through reliable access to electricity<br>Activity 1.1: Prioritise public facilities for installations through surveys and needs assessments<br>Activity 1.2: Design, feasibility (environmental, social and safety), installation and commissioning including O and M (procurement turnkey) | 1) Risks:<br>2) Low access to clean, affordable, and reliable energy sources,<br>3) Insufficient infrastructure and poor maintenance of energy supply (high T and D losses and absence of integrated national grid) networks and stranded assets<br>4) Lack of market drivers to induce private investments.<br>5) Increase in power outages and quality problems impacting livelihoods and services.<br>6) Increase in risk of disruptions in energy supply.<br>7) Mounting debts to exporters of electricity.<br>8) Barriers in promoting gender inclusivity<br>9) Biases to influence skill development or development of business models to benefit certain sections of the society<br><br>Assumptions:<br>1) Energy linkages to basic services in health and education sectors is well established.<br>2) Reliability of energy services impacts humanitarian response and resilience for recovery of Afghan economy<br>3) Enhanced renewable energy access to health and education sectors boosts effective and efficient essential services including diversification of energy mix and energy affordability<br>4) Stakeholder engagement will be carried out throughout the project according to the SEP<br>5) Exit strategy proposals will have a capacity development module and identify the entry points for the skill development programs |
| Output 2: Schools/related educational institutions' productivity through energy services enhanced (with gender inclusive approaches)<br>Activity 2.1: Prioritize public facilities for installations through surveys and needs assessments<br>Activity 2.2 : Design, feasibility, installation and commissioning including o and M (procurement turnkey) | |
| Output 3: Delivery models for O and M through private sector linkages and gender inclusion developed/established<br>Activity 3.1: Private sector platform for soliciting proposals for O and M beyond project time period<br>Activity 3.2: Execution of exit strategy/proposals implementation<br>Activity 3.3: Stakeholder Engagement Plan (SEP) | |

UNDP Afghanistan Country Office has set up a robust and dynamic risk management approach post-August 2021. Besides compliance with corporate systems such as Programme and Operations Policies and Procedures, Internal Control Framework, Enterprise Risk Management

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

Strategy and AML/CFT Policy, the following measures have been put in place (Annex 3 on Risk Analyses):

- Establishment of the Integrated Risk Management Unit (unique across UNDP globally) equipped with expertise in the different areas required to undertake thorough risk assessments (political, conflict sensitivity/do no harm/ fiduciary/programmatic/ML&FT/other areas and due diligence)
- Development of the UNDP Afghanistan Adaptive Risk Management and Mitigation Strategy
- Establishing partnerships with other UN Agencies regarding risk management information sharing and compliance with sanctions and AML/CFT.
- From January 2022 all partners are undergoing a thorough risk assessment and vetting against UNSC Sanctions, UN/WB debarments, and interim suspensions of partners under investigation Setting up the tools. In Afghanistan vetting has been extended to OFAC (US), EU and UK sanctions and financial restrictions.
- Development of a web-based platform to facilitate vetting, information sharing, depository of risk management information and identifying relationships between counterparties and associated individuals.

### *Stakeholder Engagement*

An initialStakeholder Engagement Plan (SEP) has been developed to identify different stakeholders and will be updated during the Inception Phase to develop an approach for reaching each of the sub-projects as part of UNDP SES and KfW requirements. The SEP will serve the following purposes: i) stakeholder identification and analysis; (ii) planning engagement modalities viz., an effective communication tool for consultations and disclosure; (iii) enabling platforms for influencing decisions; (iv) defining role and responsibilities of different actors in implementing the Plan; and (iv) grievance redress mechanism (GRM) and SEA risk prevention and mitigation plan.

Some of the key stakeholders identified for the Project relate to the following,

- Selected public facilities in the education and health sectors
- Project Workers
- Private Sectors
- Communities
- Donors
- Health and Educational Administrative Authorities
- Other UN Agencies
- Other National and International Organisations/Agencies

A plan of communication with the identified key stakeholders is provided within the SEP which will be implemented throughout the project life cycle.

Draft preliminary SEP has been attached as Annex 7. The preliminary SEP would be refined further during the Project Inception phase.

**South-South and Triangular Cooperation (SSC/TrC)**

- South-South and Triangular Cooperation (SSC/TrC) will be explored through tie-ups with academia, think tanks, NGOs and others for effecting technology transfer and innovations at local as well as international levels.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

**Digital Solutions**[21]

- Digital Solutions under the project potentially include load management, optimizing assets usage and sizing, digital controls for solar technologies, and thermal applications including cold chain (medicines) – temperature setting, technical monitoring, and performance management for extended life of the assets, remote servicing support and quality assurance, digital payments and online monitoring. The project will design a project management information system and dashboard for monitoring the implementation progress and impacts of this project. The project will also utilize the comprehensive, Afghanistan contextualized Information/Data Management System that will cover all aspects of project M&E and quality assurance. The system will be used to collect accurate information and generate detailed data analysis reports and visually appealing GIS-enabled analytical dashboards and maps. The digital system will capture all relevant information including but not limited to financials and documents, the images and GPS coordinates of field locations, beneficiaries, etc.

**Knowledge**

- The project will thrive on approaches to achieving the renewed target as per UNDP's new Strategic Plan 2022-2025 to increase access to clean and affordable energy for 500 million people. This builds the momentum for cross-learning among countries and partners with its primary objective of increasing energy access for those furthest behinds. UNDP's Africa Minigrids Programme for example and other energy initiatives are accelerating the transition to renewable energy through system changes that support inclusive, green economies, particularly in countries with low levels of renewable energy generation or poor energy-efficiency improvement rates. These will provide insights and experience for capitalizing on technological gains, clean energy innovations and new business models in the energy sector. Close cooperation and coordination with other UN agencies are considered for learning and insights into the implementation of the project components. The project will produce a detailed assessment in the form of a database of all health facilities and educational institutions in Afghanistan in collaboration with NFM (ADB TA).

**Sustainability and Scaling Up**

- Adopting a holistic and integrated approach to sustain the services for basic needs of the people is the backbone for sustainability of results for this project. Different energy services models will be explored and assessed for private sector participation and investments that would further stimulate the scaling up of project interventions and skillsets through employment generation. It will leverage existing community structures, including Community Development Councils (CDC) to create new mechanisms to deliver energy services sustainably. Capacities of civil society organizations (CSOs), community-based organizations (CBOs) and women and youth groups will also be strengthened as key players in the energy sector.

- Mobilizing local Afghan contractors for operation and maintenance for five years will ensure the sustainability and longevity of the project. In addition, the contractors will develop and submit a transition plan outlining proper training for electricians of educational institutions and health facilities. Throughout the project execution, emphasis will be on hiring Afghan

[21] *Please see the Guideline "Embedding Digital in Project Design".*

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

engineers, energy experts, and local companies to carry out the tasks of site assessments, technical design, installation, and O&M.

## IV. PROJECT MANAGEMENT

### *Cost Efficiency and Effectiveness*

The project will achieve cost efficiency through an effective procurement strategy in a potential collaboration with agencies such as Information and Technology Management (Green Team), Copenhagen and expert resources to consider economies of scale and quality standards. This is likely to reduce transaction and administrative costs. This project will work with 8 regional offices that are already set up with funding support from ABADEI and will enable cost-sharing arrangements. The project funding of EUR 59.99 million plans to target approx. 1 million beneficiaries with a unit cost of EUR 59 approximately per beneficiary. The project will benefit from the experience in Afghanistan through the ABADEI and ADB -TA projects and in other countries in the energy sector implemented by UNDP. This project will optimize available capacity and resources in IRMU, DEU and Policy units that are housed with UNDP Afghanistan CO.

### *Project Management*

A Project implementation unit will be established in line with Output 4. The details of the governance and management arrangements are presented with the structure. The project will be governed by a Project Board. The Project Board is responsible for making, by consensus, management decisions. The project team will be technically led by Renewable Energy Specialist (Technical Lead) under the strategic and overall guidance of the Senior Deputy Resident Representative, Programme. The project team will be based in Kabul. The Project Manager (Project Lead) will be overall responsible for the day-to-day Project management based out of Kabul and will collaborate with the eight field offices under ABADEI, while working in partnership with relevant partners and report to the Programme Advisor. Project teams are staffed with required management, technical, financial and monitoring capacities. (Refer to Budget under Output 4). The Project Manager will develop annual work plans to ensure the efficient implementation of the project. The Project Manager will inform the Project Board and the UNDP Country Office of any delays or difficulties during implementation, including the implementation of the Monitoring & Evaluation (M&E) plan so that appropriate support and corrective measures can be adopted. The Project Manager will also ensure that all project staff maintain a high level of transparency, responsibility and accountability in monitoring and reporting project results. S/he will be responsible for deliverables envisaged through the ToC and Results Matrix. The project team will comprise various experts and support staff to execute project activities, including day-to-day operations of the project, and the overall operational and financial management and reporting.

UNDP will perform the project assurance role. The ‘project assurance’ function of UNDP is to support the Project Board by carrying out objective and independent project oversight and monitoring functions. This role ensures appropriate project management milestones are managed and completed. Project assurance has to be independent of the Project Manager; therefore, the Project Board cannot delegate any of its assurance responsibilities to the Project Manager.

The UNDP will monitor the progress towards intended results, will ensure high-quality managerial, technical and financial implementation of the project, and will be responsible for monitoring and ensuring proper use of administrated funds to the assigned activities, timely reporting of implementation progress as well as the undertaking of mandatory and non-mandatory evaluations for each of their respective components. Project-level monitoring and evaluation will be undertaken in compliance with the UNDP POPP and the UNDP Evaluation Policy.

An inception workshop will be conducted after the signing of the project document to a) re-orient project stakeholders on the project strategy and discuss any changes in the overall context that influence project implementation; b) discuss the roles and responsibilities of the project team, including reporting and communication lines and conflict resolution mechanisms; c) review the

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

results framework, re-assess baselines as needed, and discuss reporting, monitoring and evaluation roles and responsibilities and finalize the M&E plan; d) review financial reporting procedures and mandatory requirements, and agree on the arrangements for the annual audit; e) plan and schedule Project Board meetings and finalize the first year annual work plan. The Project Manager will prepare the inception report no later than one month after the inception workshop. An independent mid-term review (MTR) process will be undertaken, and the findings and responses outlined in the management response will be incorporated as recommendations for enhanced implementation during the final half of the project's duration. The terms of reference, the review process and the final MTR report will follow the standard templates and guidance available at the UNDP Evaluation Resource Centre. UNDP will perform monitoring and reporting throughout the Reporting Period

***Visibility***

UNDP- KfW Visibility outputs and outreach evaluation measures

| Output | Frequency | Measuring outreach |
|---|---|---|
| Press release upon project signing and conclusion on UNDP Afghanistan Website | 1, upon signing the agreement, to be linked with other social media accounts available | # of impressions and engagements upon finalization of the project |
| Social media posting (Twitter) | < 2 per project year | # of impressions and engagements upon finalization of the project |
| Human interest/ success stories (Exposure) | < 2 per project year | # of impressions and engagements upon finalization of the project |
| Photo album of the project (Flickr) | <150 photos for the entire project duration | # of impressions and engagements upon finalization of the project |
| One video of the project (YouTube) | 1 for the entire project duration | # of impressions and engagements upon finalization of the project |
| Visibility product (s) | At least 1 visibility project, is to be discussed further with KfW | # products produced and distributed |

The partnership with KfW will be systematically mentioned in all high-level briefing opportunities, such as acknowledging donor contributions to funding reports or presentations.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

## V. RESULTS FRAMEWORK[22]

**Intended Outcome as stated in the UNSDCF/Country Programme Results and Resource Framework**

**Strategic Framework for Afghanistan 2023-25**

**Outcome 1:** By the end of 2025, more people in Afghanistan, particularly the most marginalized, can equitably access essential services that meet minimum quality standards.

**Outcome 2:** By the end of 2025, people in Afghanistan, especially women, youth, and other marginalized groups, and those at risk of being left behind, benefit from a more equitable, inclusive, sustainable, and resilient employment-rich economy and shared economic opportunities with enhanced productive capacities for improved livelihoods and decent work.

**UNDP CPRF 2022 Results:**

**Outcome 3**: Improved climate smart agriculture, access to renewable energy, and resilience to natural disasters
**Output 3.2:** Access to clean and affordable energy enhanced

**Outcome indicators as stated in the Country Programme [or Regional] Results and Resources Framework, including baseline and targets:**

UNDP SP[23] IRRF Indicator 5.1.1: Number of people, who gained access to clean, affordable and sustainable energy (disaggregated by sex)
UNDP SP IRRF Indicator 5.1.2: Number of people, who benefitted from services from clean, affordable and sustainable energy (disaggregated by sex)

**Applicable Output(s) from the UNDP Strategic Plan: (2022-2025): 5.1 Energy gap closed**

**Atlas Project Number: 00147445**

| EXPECTED OUTPUTS | OUTPUT INDICATORS[24] | DATA SOURCE | BASELINE | | | TARGETS (by frequency of data collection) | | | | | | DATA COLLECTION METHODS & RISKS |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | | | Value | Year | Year 1 | Year 2 | Year 3 | Year 4 | Year 5 | Year 6 | FINAL | |

[22] UNDP publishes its project information (indicators, baselines, targets and results) to meet the International Aid Transparency Initiative (IATI) standards. Make sure that indicators are S.M.A.R.T. (Specific, Measurable, Attainable, Relevant and Time-bound), provide accurate baselines and targets underpinned by reliable evidence and data, and avoid acronyms so that external audience clearly understand the results of the project.

[23] UNDP Strategic Plan (SP) Integrated Results and Resource Framework (IRRF)

[24] It is recommended that projects use output indicators from the Strategic Plan IRRF, as relevant, in addition to project-specific results indicators. Indicators should be disaggregated by sex or for other targeted groups where relevant.

| | | | | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| **Output 1:** Health facilities and services improved through reliable access to electricity | ***1.1 Number of Small level health facilities (Village based health facilities) provided with uninterrupted electric supply*** | *MoPH and NSIA* | 3512<br><br>(tbc) | 2022 | *20* | 51 | | | | | *71* | *M&E Reports, TPMA reports, Quarterly reports and Annual Report, National Statistics Yearbook by NSIA and MIS Data by MoPH* |
| | ***1.2 Number of Medium level health facilities (District based health facilities) supported with uninterrupted electric supply*** | *Site survey reports* | | | *5* | 6 | | | | | *11* | *Monitoring reports, Field Visit Reports, Technical reports, TPMA Reports* |
| | ***1.3 Number of High level (Provincial based and Regional + some clinics for Special purpose) supported with uninterrupted electric supply*** | | | | *5* | 5 | | | | | *10* | *Monitoring mission report and post intervention quick impact studies* |
| **Output 2** Schools/related educational institutions' productivity enhanced through gender inclusive energy services | ***2.1. Number of Primary Schools with reliable back up renewable energy supply*** | *MoE and NSIA* | *20,000*<br><br>*tbc* | 2022 | *50* | 500 | 150 | | | | *560* | *National Statistics Yearbook by NSIA and EMIS Data by MoE* |
| | ***2.2 Number of female teachers provided with extension of solar electrification to*** | | | | *7* | *130* | | | | | *140* | |

| | | | | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | ***conduct remote teaching.*** | | | | | | | | | | | |
| **Output 3**: Delivery models for O&M established through gender inclusive private sector linkages | **3.1 Number of Afghan private companies engaged in operations and maintenance of renewable energy services** | | | | | | | | | | | *Monitoring reports and project progress reports* |
| | **3.2 Number of new job opportunities created for in the energy service sector. (gender disaggregated).** | | | | | | | | | | | *Monitoring mission report and post intervention quick impact studies* |
| | | | | | | | | | | | | |
| **~~Output 4~~:** Project Management Support | **Baseline Study / Perception Survey** | | | | | | | | | | | |
| | **Project Offices established** | | | | | | | | | | | |
| | **Project staff recruited** | | | | | | | | | | | |
| | **Mid Term Evaluation** | | | | | | | | | | | |
| | **Terminal Evaluation** | | | | | | | | | | | |
| | **Impact Assessment** | | | | | | | | | | | |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

## VI. MONITORING PLAN

UNDP will integrate a systematic approach to the monitoring of project activities and results on an ongoing basis to ensure that activities are implemented, and results achieved and to enable an appropriate level of project oversight for quality assurance. The monitoring arrangement will function as a means of data collection that will contribute to quarterly and annual reporting. UNDP will report to the donor through quarterly and annual reports.

| Monitoring Activity | Purpose | Frequency | Expected Action | Partners (if joint) | Cost (if any) |
|---|---|---|---|---|---|
| **Track activity implementation and results progress** | Progress data against the results indicators in the RRF will be collected and analysed to assess the progress of the project in achieving the agreed outputs.<br><br>Progress against work plans and targets as well as risk management plans will be continuously checked throughout implementation and reported. | Monthly, quarterly, and annually | Slower than expected progress will be addressed by project management. | The project team in collaboration with local partners on the ground | Included in the project management |
| **Monitor and Manage Risk** | Identify specific risks that may threaten the achievement of intended results. Identify and monitor risk management actions using a risk log. This includes monitoring measures and plans that may have been required as per UNDP's Social and Environmental Standards. Audits will be conducted following UNDP's audit policy to manage financial risk. | Monthly, Quarterly | Risks are identified by project management and actions are taken to manage risk. The risk log is actively maintained to keep track of identified risks and actions taken. | The project team in collaboration with local partners on the ground | Included in the project management |
| **Learn** | Knowledge, good practices, and lessons will be captured regularly, as well as actively sourced from other projects and partners and integrated back into the project. | Quarterly and annually | Relevant lessons are captured by the project team and used to inform management decisions. | | Included in the project management |
| **Annual Project Quality Assurance** | The quality of the project will be assessed against UNDP's quality standards to identify project strengths and weaknesses and to inform management decision-making to improve the project. | Bi-Annually | Areas of strength and weakness will be reviewed by project management and used to inform decisions to improve project performance. | | |
| **Review and Make Course Corrections** | Internal review of data and evidence from all monitoring actions to inform decision-making. | Quarterly | Performance data, risks, lessons, and quality will be discussed by the project board and used to make course corrections. | | Included in the project management |
| **Project Report** | A progress report will be presented to the Project Board and key stakeholders, consisting of progress data showing the results achieved against pre-defined annual targets at the output level, the annual project quality | Quarterly and annually | Project progress reports will be produced highlighting progress data showing the results achieved against defined quarter | | Included in the project management |

| | | | | | |
|---|---|---|---|---|---|
| | rating summary, an updated risk long with mitigation measures, and any evaluation or review reports prepared over the period. | | and annual targets. | | |
| **Project Review (Project Board)** | The project's governance mechanism (i.e., project board) will hold regular project reviews to assess the performance of the project and review the Multi-Year Work Plan to ensure realistic budgeting over the life of the project. In the project's final year, the Project Board shall hold an end-of-project review to capture lessons learned and discuss opportunities for scaling up and to socialize project results and lessons learned with relevant audiences. | Annually or as required | Any quality concerns or slower than expected progress should be discussed by the project board and management actions agreed to address the issues identified. | | |

## VII. EVALUATION PLAN

| Evaluation Title | Partners (if joint) | Related Strategic Plan Output | Project (BMZ funding) / UNDAF/CPD Outcome | Planned Completion Date | Key Evaluation Stakeholders | Cost and Source of Funding |
|---|---|---|---|---|---|---|
| **Baseline Assessment** | | | | 1 Quarter 2023 | All partners and stakeholders in the project | KFW fund |
| **Mid-Term Evaluation** | | | | 2 Quarter 2025 | All partners and stakeholders in the project | KFW fund |
| **Final Evaluation** | | | | 4 Quarter 2027 | All partners and stakeholders in the project | KFW fund |

**Reporting:** The project team will report to the Project Board on a biannual basis to provide narrative and financial reports on its results and progress. Moreover, Project Quarterly progress reports and final project reports consisting of progress data showing the results achieved against pre-defined annual targets at the output level, the annual project quality rating summary, and an updated risk log with mitigation measures will be produced and shared with all relevant partners. In addition, a succinct monthly report (Annex 8.1) will be prepared to report progress against work plans, and procurement plans, and record any deviations, incidents, issues and risks perceived against trigger items provided by KFW.

**Quarterly Coordination Meetings:** To strengthen the results delivery and the monitoring and evaluation under this project, every quarter upon the submission of the quarterly report a quarterly coordination meeting will be organised by UNDP between the donor (KFW), and all relevant stakeholders including CSOs, implementing partners involved in the implementation. At these meetings, UNDP will present the achievements of each quarter, identify gaps and challenges and seek commitments from all participating members to overcome the challenges to ensure successful implementation and the delivery of results under this project.

**Evaluation Plan[25]**

| Evaluation Title | Partners (if joint) | Related Strategic Plan Output | UNSDCF/CPD Outcome | Planned Completion Date | Key Evaluation Stakeholders | Cost and Source of Funding |
|---|---|---|---|---|---|---|
| Mid-Term Evaluation | | **UNDP Strategic Plan Outcome:** Resilience built to respond to systemic uncertainty and risk | **Expected CPD Outcome(s):** Outcome 3: Improved climate smart agriculture, access to renewable energy, and resilience to natural disasters | After one year of project implementation | Schools, Health Facilities, Private sector, NGOs and other community organizations | USD 40,000 (KFW Project) |
| Terminal Evaluation | | **UNDP Strategic Plan Outcome:** Resilience built to respond to systemic uncertainty and risk | **Expected CPD Outcome(s):** Outcome 3: Improved climate smart agriculture, access to renewable energy, and resilience to natural disasters | After one year of project implementation | Schools, Health Facilities, Private sector, NGOs and other community organizations | USD 50,000 (KFW Project) |

[25] Optional, if needed

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

## VIII. MULTI-YEAR WORK PLAN [26][27]

| No | # | Description | Unit | # Units | Amount (Year-1,2,3,4,5 and6) | | | | | | Sub-Total amount | Total Budget (USD)* |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| **A=B+C+D** | **Total project input cost** | | | | | | | | | | | |
| **Gender Marker** | **Output 1** | **Output 1: Health facilities, and services, which are accessible to vulnerable people, including women and girls, improved through reliable access to electricity** | | | **Y-1** | **Y-2** | **Y-3** | **Y-4** | **Y-5** | **Y-6** | | |
| **Gen-2:** | **Activity 1.1** | **Prioritise public facilities for installations through surveys and needs assessments** | | | | | | | | | | |
| | Consultants/Experts | Experts' advice and consultant support in providing engineering and technical expertise for scoping baselines through desk research, approaches on prioritization, determination of criteria, methodology, technical design, costing, ESS, including SEA, screening, and gender-responsiveness of the facility, etc for preparing a Longlist of facilities | Individual | 2 | 160,000 | 160,000 | 160,000 | - | - | - | 480,000 | 480,962 |
| | Contractual service company | Assessing the facilities by applying technical criteria for shortlisting of the facilities and carry out pre- feasibility for the shortlist for final selection including the preparation of recommeded specifications | Service Company | 1 | 99,800 | - | - | - | - | - | 99,800 | 100,000 |
| | Travel | Project related travel to the facilities for prioritization, selection and assessments | Service | LSM | 25,891 | 25,891 | 25,891 | 25,891 | 25,891 | - | 129,456 | 129,715 |
| | Training and workshops | Meetings and consultation with stakeholders, especially women and girls,and other vulnerable groups .. | Service | LSM | 10,978 | 10,978 | - | - | - | - | 21,956 | 22,000 |
| | | | | **Activity 1.1** | **296,669** | **196,869** | **185,891** | **25,891** | **25,891** | **-** | **731,212** | **732,677** |

[26] Cost definitions and classifications for programme and development effectiveness costs to be charged to the project are defined in the Executive Board decision DP/2010/32

[27] Changes to a project budget affecting the scope (outputs), completion date, or total estimated project costs require a formal budget revision that must be signed by the project board. In other cases, the UNDP programme manager alone may sign the revision provided the other signatories have no objection. This procedure may be applied for example when the purpose of the revision is only to re-phase activities among years.

| | | | | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | **Activity 1.2** | **Design, feasibility (environmental, social and safety), installation and commissioning including o and M (procurement turnkey)** | | | | | | | | | - | - |
| **Gen-2:** | Consultants/Experts | Consultant for coordination of the methodologies, design, specifications, etc. for evaluation/validation of pre-feasibility findings for the actual selection of the sites for project interventions | Individual | 1 | 80,000 | 80,000 | - | - | - | - | 160,000 | 160,321 |
| | Contractual service company | Feasibility and Installatioin of Equipment, Commissioning, and operating and basic training cost up to 5 years (Years TBD) informed by the assessment | Service Company | 1 | 2,055,082 | 4,110,163 | 8,220,326 | 4,110,163 | 2,055,082 | - | 20,550,816 | 20,592,000 |
| | Travel | Project related travel to the facilities | Service | LSM | 3,114 | 6,228 | 12,455 | 6,228 | 3,114 | - | 31,138 | 31,200 |
| | | | | **Activity 1.2** | **2,138,195** | **4,196,391** | **8,232,781** | **4,116,391** | **2,058,195** | **-** | **20,741,954** | **20,783,521** |
| | **Activity 1.3** | **Monitoring results and measuring/reporting impacts** | | | | | | | | | - | - |
| **Gen-2:** | Monitoring | Independent monitoring/Third party monitoring as well as UNDP's internal field monitoring. | Service Company | 1 | - | 9,980 | 9,980 | 9,980 | 9,980 | 4,990 | 44,910 | 45,000 |
| | Travel | Travel related of field monitoring | Service | LSM | 5,000 | 5,000 | 5,000 | 5,000 | 5,000 | 2,500 | 27,500 | 27,555 |
| | | | | **Activity 1.3** | **5,000** | **14,980** | **14,980** | **14,980** | **14,980** | **7,490** | **72,410** | **72,555** |
| | **Technical Staff Cost** | | | | | | | | | | - | - |
| | Technical Staff Cost | Technical staff for design, quality assurance and monitoring of the project | Lump sum | 1 | 209,731 | 104,865 | 104,865 | 109,482 | 109,482 | - | 638,427 | 639,706 |
| | | | | **Technical Staff Cost** | **209,731** | **104,865** | **104,865** | **109,482** | **109,482** | **-** | **638,427** | **639,706** |
| | | | | **Sub-Total Output 1** | **2,649,595** | **4,513,105** | **8,538,518** | **4,266,744** | **2,208,549** | **7,490** | **22,184,002** | **22,228,459** |
| **Gen-2:** | **Output 2** | **Schools/related educational institutions' productivity through energy services enhanced (with gender inclusive approaches)** | | | | | | | | | - | - |
| | **Activity 2.1** | **Prioritise public facilities for installations through surveys and needs assessments** | | | | | | | | | - | - |

| | | | | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | Consultants/Experts | Providing engineering and technical expertise for scoping baselines through desk research, approaches on prioritization, determination of criteria, methodology, technical design, costing, ESS screening etc for preparing a long list of facilities | Individual | 3 | 240,000 | 240,000 | 240,000 | - | - | - | 720,000 | 721,443 |
| | Contractual service company | Assessing the facilities by applying technical criteria for shortlisting of the facilities and carry out pre- feasibility for the shortlist for final selection including the preparation of recommeded specifications | Service Company | 1 | 499,000 | - | - | - | - | - | 499,000 | 500,000 |
| | Travel | Project related travel to the facilities | Service | LSM | 25,891 | 25,891 | 25,891 | 25,891 | 25,891 | - | 129,456 | 129,715 |
| | Training and workshops | Meetings and consultation with stakeholders, especially women and girls, and other vulnerable groups . | Service | LSM | 80,838 | 80,838 | | | | - | 161,676 | 162,000 |
| | | | | **Activity 2.1** | **845,729** | **346,729** | **265,891** | **25,891** | **25,891** | **-** | **1,510,132** | **1,513,158** |
| **Gen-2:** | **Activity 2.2** | **Design, feasibility, installation and commissioning including o and M (procurement turnkey)** | | | | | | | | | **-** | **-** |
| | Consultants/Experts | Consultant for coordination of the methodologies, design, specifications, etc. for evaluation/validation | Individual | 1 | 80,000 | 80,000 | - | - | - | - | 160,000 | 160,321 |
| | Contractual service company | Feasibility and Installatioin of Equipment, Commissioning, and operating and basic training cost up to 5 years (Years TBD) | Service Company | 1 | 1,362,270 | 2,724,540 | 5,449,080 | 2,724,540 | 1,362,270 | - | 13,622,700 | 13,650,000 |
| | Travel | Project related travel to the facilities | Service | LSM | 25,891 | 25,891 | 25,891 | 25,891 | 25,891 | - | 129,456 | 129,715 |
| | Training and workshops | Training of the facility workers on the systems, processes and compliance requirements | Service | LSM | 18,363 | 36,726 | 73,453 | 36,726 | 18,363 | - | 183,632 | 184,000 |
| | | | | **Activity 2.2** | **1,486,524** | **2,867,158** | **5,548,424** | **2,787,158** | **1,406,524** | **-** | **14,095,788** | **14,124,036** |
| | **Activity 2.3** | **Monitoring results and measuring/reporting impacts** | | | | | | | | | - | - |
| | Monitoring | Independent monitoring/Third party monitoring as well as UNDP's internal field monitoring. | Service Company | 1 | - | 19,960 | 19,960 | 19,960 | 19,960 | 9,980 | 89,820 | 90,000 |
| | Travel | Travel related of field monitoring | Service | LSM | 10,000 | 10,000 | 10,000 | 10,000 | 10,000 | 5,000 | 55,000 | 55,110 |

| | | | | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | | | | | **Activity 2.3** | **10,000** | **29,960** | **29,960** | **29,960** | **29,960** | **14,980** | **144,820** | **145,110** |
| | **Technical Staff Cost** | | | | | | | | | | | - | - |
| | Technical Staff Cost | Technical staff for design, quality assurance and monitoring of the project | Lump sum | 1 | | 209,731 | 104,865 | 104,865 | 109,482 | 109,482 | - | 638,427 | 639,706 |
| | | | | | **Technical Staff Cost** | **209,731** | **104,865** | **104,865** | **109,482** | **109,482** | **-** | **638,427** | **639,706** |
| | | | | | **Sub-Total Output 2** | **2,551,984** | **3,348,712** | **5,949,141** | **2,952,491** | **1,571,858** | **14,980** | **16,389,167** | **16,422,011** |
| **Gen-2** | **Output 3** | **Delivery models for O and M through private sector linkages and gender inclusion developed/established** | | | | | | | | | | **-** | **-** |
| | **Activity 3.1** | **Private sector platform for soliciting proposals for O and M beyond project time period** | | | | | | | | | | **-** | **-** |
| | Consultants/Experts | Designing exit strategies for operation and maintenance delivery models beyond contractual phase (determined in output 1 & 2 as part of the project activity). | Individual | 2 | | 30,000 | 20,000 | 30,000 | - | - | - | 80,000 | 80,160 |
| | Contractual service company | The company will be engaged to solicit proposals as per strategy from different interested groups (for sustenance of the project interventions including asset transfer mechanisms). | Service Company | 1 | | - | - | 89,820 | 89,820 | - | - | 179,640 | 180,000 |
| | Travel | Project related to visit facilities and participation in workshops and meetings | Service | LSM | | 25,891 | 25,891 | 25,891 | 25,891 | 25,891 | - | 129,456 | 129,715 |
| | Training and workshops | Workshop for private sector and other institutions (CDC/RPs) engagement | Service | LSM | | - | - | 10,978 | 10,978 | 10,978 | - | 32,934 | 33,000 |
| | | | | | **Activity 3.1** | **55,891** | **45,891** | **156,689** | **126,689** | **36,869** | **-** | **422,030** | **422,876** |
| | **Activity 3.2** | **Execution of exit strategy/proposals implementation** | | | | | | | | | | **-** | **-** |
| | Contractual service company | Evaluate and comissioning of the different delivery models | Service Company | 1 | | - | - | 70,000 | 70,000 | 60,000 | - | 200,000 | 200,401 |
| | Training and workshops | Training on the sustenance of the project interventions | Service | LSM | | - | - | 27,944 | 27,944 | - | - | 55,888 | 56,000 |

| | | | | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | | | | | **Activity 3.2** | **-** | **-** | **97,944** | **97,944** | **60,000** | **-** | **255,888** | **256,401** |
| | **Activity 3.3** | **StakeHolder Engagement Plan (SEP)** | | | | | | | | | | **-** | **-** |
| | Grievance Resolution Mechanism (GRM), including SEA | Arrangements for hotline, database and database maintenance | Service Company | 1 | | 11,000 | 11,000 | 11,000 | 11,000 | 11,000 | - | 55,000 | 55,110 |
| | Training and workshops | Trainings (Social issues, outreach, GRM, SEA prevention and risk mitigation, etc.) for PIU, Ips | Service Company | 1 | | 41,517 | 83,034 | 41,517 | 41,517 | - | - | 207,584 | 208,000 |
| | Outreach & Printing of communication materials | Communication materials (leaflets, posters, social media) | Service Company | 1 | | 11,000 | 11,000 | 10,500 | 10,500 | 10,500 | - | 53,500 | 53,607 |
| | | | | | **Activity 3.3** | **63,517** | **105,034** | **63,017** | **63,017** | **21,500** | **-** | **316,084** | **316,717** |
| | **Technical Staff Cost** | | | | | | | | | | | - | - |
| | Technical Staff Cost | Technical staff for design, quality assurance and monitoring of the project | Lump sum | 1 | | 209,731 | 104,865 | 104,865 | 109,482 | 109,482 | - | 638,427 | 639,706 |
| | | | | | **Technical Staff Cost** | **209,731** | **104,865** | **104,865** | **109,482** | **109,482** | **-** | **638,427** | **639,706** |
| | | | | | **Sub-Total Output 3** | **329,139** | **255,790** | **422,515** | **397,132** | **227,852** | **-** | **1,632,429** | **1,635,700** |
| **E** | **Output 4** | **Direct Project Costs/ Project Management Support** | | | | | | | | | | **-** | **-** |
| | **Activity 4.1** | **Project Staffing & Running costs** | | | | | | | | | | **-** | **-** |
| | Project Management Cost | Project Coordinator (Project Manager) – P4 | Staff | 1 | | 296,048 | 296,048 | 296,048 | 296,048 | 296,048 | 148,024 | 1,628,262 | 1,631,526 |
| | Project Management Cost | Procurement Specialist - P3 | Staff | 1 | | 257,453 | 257,453 | 257,453 | 257,453 | 257,453 | - | 1,287,266 | 1,289,846 |
| | Project Management Cost | Procurement Specialist - P3 | Staff | 1 | | | | | 257,453 | 257,453 | - | 514,906 | 515,938 |
| | Project Management | Social and Environmental Safeguards Specialist - P3 | Staff | 1 | | 212,500 | 212,500 | 212,500 | 212,50 | 212,50 | - | 1,062,501 | 1,064,630 |

| | | | | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | Cost | | | | | | | 0 | 0 | | | |
| | Project Management Cost | GIS Specialist - P3 | Staff | 1 | 212,500 | 212,500 | 212,500 | 212,500 | 212,500 | - | 1,062,501 | 1,064,630 |
| | Project Management Cost | Energy Technical Specialist - P3 | Staff | 1 | 212,500 | 212,500 | 212,500 | 212,500 | 212,500 | - | 1,062,501 | 1,064,630 |
| | Project Management Cost | Social and Environmental Safeguards Specialist NPSA 9 | Staff | 1 | 48,807 | 48,807 | 48,807 | 48,807 | 48,807 | - | 244,035 | 244,524 |
| | Project Management Cost | Energy Specialist - NPSA 9 | Staff | 1 | 48,807 | 48,807 | 48,807 | 48,807 | 48,807 | - | 244,035 | 244,524 |
| | Project Management Cost | Procurement Analyst – NPSA 9 | Staff | 1 | 48,807 | 48,807 | 48,807 | 48,807 | 48,807 | - | 244,035 | 244,524 |
| | Project Management Cost | Administration and Finance Analyst NPSA 9 | Staff | 1 | 48,807 | 48,807 | 48,807 | 48,807 | 48,807 | 24,403 | 268,438 | 268,976 |
| | Project Management Cost | Project Associate NPSA 7 | Staff | 1 | 38,626 | 38,626 | 38,626 | 38,626 | 38,626 | 19,313 | 212,445 | 212,871 |
| | Project Management Cost | Monitoring & Evaluation and Reporting Specialist – NPSA 9 | Staff | 1 | 48,807 | 48,807 | 48,807 | 48,807 | 48,807 | 24,403 | 268,438 | 268,976 |
| | Project Management Cost | Energy Engineer - IUNV | Staff | 1 | 62,559 | 19,949 | | | | | 82,509 | 82,674 |
| | Project Management Cost | Administration and Finance Associate - NUNV | Staff | 1 | 15,403 | 15,403 | 15,403 | 15,403 | 15,403 | 7,702 | 84,719 | 84,888 |
| | Project Management Cost | Technical Associate - NUNV | Staff | 8 | 123,227 | 123,227 | 123,227 | 123,227 | 123,227 | - | 616,135 | 617,370 |
| | Project Management Cost | Office costs (office space, accommodation, security) | Service | 1 | 117,365 | 117,365 | 117,365 | 117,365 | 117,365 | 23,473 | 610,297 | 611,520 |
| | Project Management Cost | Laptops, Monitor screens, Memory Sticks, Wireless mouse & keyboard, Printer/Scanner, Router, Wi-Fi AP | Goods | 1 | 50,299 | - | - | - | - | - | 50,299 | 50,400 |
| | Project Management Cost | Communication Equipment | Goods | 1 | 21,500 | - | - | - | - | - | 21,500 | 21,543 |
| | Project Management | Video conferencing equipment (polystudio, projector, microphone, camera, etc.) | Goods | 1 | 2,994 | - | - | - | - | - | 2,994 | 3,000 |

| | | | | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | Cost | | | | | | | | | | | |
| | Project Management Cost | Software | Goods | 1 | 4,192 | 4,192 | 4,192 | 4,192 | 4,192 | 2,096 | 23,054 | 23,100 |
| | Project Management Cost | Connectivity Charges | Service | 1 | 32,694 | 32,694 | 32,694 | 32,694 | 32,694 | 16,347 | 179,820 | 180,180 |
| | Project Management Cost | IT supplies | Goods | 1 | 2,495 | 2,495 | 2,495 | 2,495 | 2,495 | 1,248 | 13,723 | 13,750 |
| | Project Management Cost | Office stationary, consumables | Goods | 1 | 2,994 | 2,994 | 2,994 | 2,994 | 2,994 | 1,497 | 16,467 | 16,500 |
| | Project Management Cost | Travel | Service | 1 | 57,585 | 57,585 | 57,585 | 57,585 | 57,585 | | 287,923 | 288,500 |
| | Project Management Cost | Utilities | Service | 1 | 67,864 | 67,864 | 67,864 | 67,864 | 67,864 | 33,930 | 373,250 | 373,998 |
| | Project Management Cost | Security | Service | 1 | 53,291 | 53,291 | 53,291 | 53,291 | 53,291 | 26,645 | 293,099 | 293,687 |
| | Project Management Cost | Vehicle Maintenance & fuel | Service | 1 | 23,952 | 23,952 | 23,952 | 23,952 | 23,952 | 11,976 | 131,736 | 132,000 |
| | Project Management Cost | Mid Term & Final Evaluation | Service | 1 | - | - | 99,800 | - | 99,800 | - | 199,600 | 200,000 |
| | Project Management Cost | Audit and Financial Spot Checks | Service | 1 | 20,000 | 20,000 | 20,000 | 20,000 | 20,000 | 20,000 | 120,000 | 120,240 |
| | Project Management Cost | Communications and Visibility | Service | 1 | 19,960 | 19,960 | 19,960 | 19,960 | 19,960 | 20,000 | 119,800 | 120,040 |
| | Project Management Cost | Bank Transfer fees | Service | 1 | 46,100 | 28,380 | 28,977 | 24,695 | 25,799 | 5,900 | 159,851 | 160,172 |
| | Project Management Cost | Miscellaneous Expenses | Service | 1 | 3,493 | 3,493 | 3,493 | 3,493 | 3,493 | 1,000 | 18,465 | 18,502 |
| **Activity 4.1** | | | | | **2,201,629** | **2,066,507** | **2,146,955** | **2,300,325** | **2,401,229** | **387,958** | **11,504,603** | **11,527,659** |
| **Sub-Total Output 4** | | | | | **2,201,629** | **2,066,5** | **2,146,95** | **2,300,3** | **2,401,2** | **387,9** | **11,504,603** | **11,527,659** |

| | | | | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | | | | | | **07** | **5** | **25** | **29** | **58** | | |
| **Direct Project Cost** | | | | | | | | | | | - | - |
| | Direct Project Cost (DPC) | IRMU cost | Lump sum | 1 | 65,693 | 65,693 | 65,693 | 65,693 | 65,693 | 32,846 | 361,311 | 362,036 |
| | Direct Project Cost (DPC) | Programme Management Cost | Lump sum | 1 | 124,784 | 124,784 | 124,784 | 124,784 | 124,784 | 62,392 | 686,313 | 687,688 |
| | Direct Project Cost (DPC) | Partnerships and communications cost | Lump sum | 1 | 65,693 | 65,693 | 65,693 | 65,693 | 65,693 | 32,846 | 361,311 | 362,036 |
| | Direct Project Cost (DPC) | Security cost | Lump sum | 1 | 29,546 | 29,546 | 29,546 | 29,546 | 29,546 | 14,773 | 162,501 | 162,826 |
| | Direct Project Cost (DPC) | Operations cost | Lump sum | 1 | 217,258 | 217,258 | 217,258 | 217,258 | 217,258 | 108,629 | 1,194,917 | 1,197,312 |
| | Direct Project Cost (DPC) | Procurement cost | Lump sum | 1 | 29,546 | 29,546 | 29,546 | 29,546 | 29,546 | 14,773 | 162,501 | 162,826 |
| | Direct Project Cost (DPC) | HR cost | Lump sum | 1 | 29,546 | 29,546 | 29,546 | 29,546 | 29,546 | 14,773 | 162,501 | 162,826 |
| | Direct Project Cost (DPC) | Finance cost | Lump sum | 1 | 25,694 | 25,694 | 25,694 | 25,694 | 25,694 | 12,847 | 141,316 | 141,599 |
| | Direct Project Cost (DPC) | ICT cost | Lump sum | 1 | 9,720 | 9,720 | 9,720 | 9,720 | 9,720 | 4,860 | 53,462 | 53,569 |
| | | **Total Direct Project Cost** | | | **597,479** | **597,479** | **597,479** | **597,479** | **597,479** | **298,739** | **3,286,132** | **3,292,718** |
| **F=(A+E)*8%** | | **UNDP Facilities and Management Fees (8%)** | | | **666,386** | **862,527** | **1,412,369** | **841,134** | **560,557** | **56,733** | **4,399,707** | **4,408,524** |
| **G=A+E+F** | | **Total Budget without levy** | | | **8,996,213** | **11,644,121** | **19,066,976** | **11,355,306** | **7,567,524** | **765,900** | **59,396,040** | **59,515,070** |
| | | | | | | | | | | | | - |
| **H=G*1%** | | **1% coordination levy to finance the United Nations Resident Coordinator System** | | | | | | | | | ***593,960*** | ***595,151*** |
| **I=G+H** | | **Total Budget including levy** | | | | | | | | | **59,990,000** | **60,110,220** |

DS


DS

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

## IX. GOVERNANCE AND MANAGEMENT ARRANGEMENTS

UNDP implements all its projects based on the Programme and Project Management (PPM) guidelines specified in the Programme and Operations Policies and Procedures (POPP) (UNDP - POPP). After the regime change in August 2021, UNDP changed all its projects' implementation modality to Direct Implementation Modality (DIM), where UNDP is the Implementing Partner, and thereby accountable for the overall management of project and achievement of results. In implementing its projects, UNDP may work with NGOs/CSOs, the private sector, academia, and UN Agencies among others.

The overall project management structure is presented as follows:

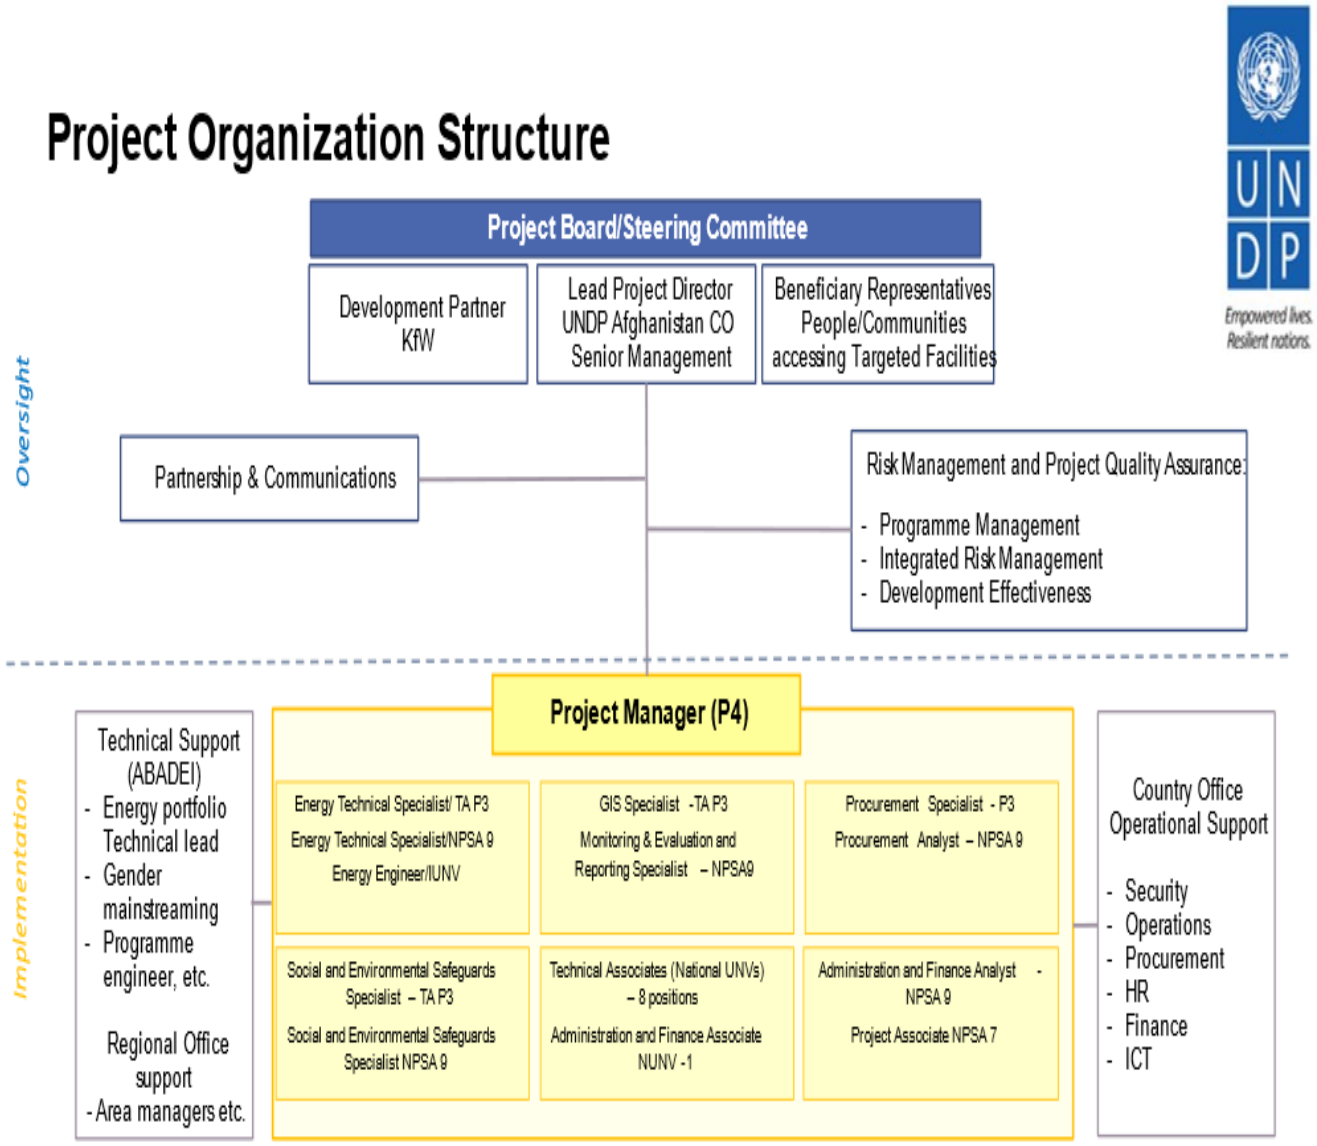


***The Project Board (PB)*** is the highest and final decision-making body for reporting, oversight, quality assurance and guidance on matters related to the project. The Project Board will consist of UNDP Senior Management (Resident Representative and Senior Deputy Resident Representative for Programme), Development Partner (KFW) and representatives from the beneficiary community.

Specific responsibilities of the Project Board include:

- Provide overall guidance and direction to the project, ensuring it remains within any specified constraints, and promote gender equality and social inclusion (LNOB) in the project implementation;
- Review project performance based on monitoring, evaluation and reporting, including standard quality assurance checks, progress reports, risk logs, spot checks/audit reports and the combined delivery report;
- Address any high-level project issues as raised by the project manager and project assurance;

- Provide guidance on emerging and/or pressing project risks and agree on possible mitigation and management actions to address specific risks (including ensuring compliance with UNDP's Social and Environmental Standards, Fraud/corruption, Sexual Exploitation and Abuse and Sexual Harassment);
- Agree or decide on project manager's tolerances as required, within the parameters set by UNDP (Manage Change in the PPM) and the donor, and provide direction and decisions for exceptional situations when the project manager's tolerances are exceeded;
- Advise on major and minor amendments to the project within the parameters set by UNDP and the donor;
- Provide high-level direction and recommendations to the project management team to ensure that the agreed deliverables are produced satisfactorily according to plans.
- Receive and address project level grievance, including overseeing whatever specific compliance and stakeholder response (or grievance) mechanisms have been put in place so that individuals and communities potentially affected by the project have access to effective mechanisms and procedures for raising concerns about the social and environmental performance of the project .
- Engage in the low value grant selection process where there is no Grant Selection Committee, as guided by the Low Value Grants – UNDP Operational Guide.
- Appraise the annual project implementation report, including the quality assessment rating report;
- Approve the Project Inception Report, Mid-term Review and Terminal Evaluation reports and corresponding management responses;
- Review the final project report package during an end-of-project review meeting to discuss lessons learned and opportunities for scaling up;

Project Board will follow the standard project board protocol as stipulated in Section IV of the UNDP Standard Terms of Reference (ToR) for the Project Board in POPP.

***Risk Management and Project Quality Assurance function*** (independent of the Project Manager) will support the Project Board to carry out objective and independent oversight. This function will ensure the necessary approvals of management and operational policy and procedures. They will ensure the quality implementation of activities and support the progress monitoring of the entire project. Under the Programme Management Unit, which comes directly under the purview of the Deputy Resident Representative-Programme provides programmatic and financial quality assurance. The Integrated Risk Management Unit (IRMU) will provide risk management support, including the screening of partners before engagement. Development Effectiveness Unit will provide support in compliance to the corporate programmatic policy and procedures. Project Assurance members, provide quality assurance of the documentation produced by the Project team and other assurance functions entrusted by the Project Board.

***Partnerships and Communications*** will provide support to the project team on partnerships building, donor relations, project visibility and knowledge sharing. The team will support in developing communication and partnership strategy for the project as per donor requirements, support in designing the contents, preparing appropriate narratives and lessons learnt for sharing with the key stakeholders.

***Project Manager*** will perform the overall programmatic, technical, and operational management role of the project including team management and day-to-day management operations to ensure that the project delivers and achieves its expected outputs specified in the workplan, to the required standard of quality, and in full alignment of UNDP's rules and regulations, fulfilling the duties as specified in its internal control framework. S/he will oversee all relevant project implementation activities in close collaboration with Technical Lead on Renewable Energy portfolio and various units of the UNDP Afghanistan office.

Project team led by the Project Manger is staffed with required operational, technical, financial and monitoring capacities which include the positions as listed below.

- Two Technical Specialist -Energy (P3 -TA and NPSA-9) with Energy Engineer (IUNV);
- GIS Specialist – (P3-TA) with M&E and Reporting Specialist (NPSA-9),
- Procurement Specialist (P3) with Procurement Analyst (NPSA 9),
- Two Social and Environmental Safeguards Specialist (P3-TA and NPSA-9)
- Eight Technical Associates (NUNVs) with one Finance and Administration Associate (NUNV)
- Administration and Finance Analyst (NPSA9) with Project Associate (NPSA 7)

Key responsibilities of these positions are summarised in Table 6

The ***Technical Leads on Renewable Energy*** and ***Gender Mainstreaming*** will be responsible for advising and guiding the project manager on critical technical matters and to ensure adequate progress in their assigned area. They will report on progress to UNDP senior management and support the development of solutions to emerging operational/contextual risk. Their contributions to progress monitoring will also inform programme adaptations.

The eight regional field offices headed by ***Regional Area Managers*** will provide implementation, operational and progress monitoring support on the ground working in partnership with local partners.

Project team will directly receive support on procurement, finance, ICT, administration and common services through the Country Office Operations Unit, which is directly overseen by the Senior Deputy Resident Representative-Operations.

**Table 2: Roles and Implementation responsibilities of Project Team members**

| Position/function (full- or part-time) | Main Responsibilities | Filled by existing staff or new hire |
|---|---|---|
| RE Specialist -P4 (Technical Lead)<br><br>Part-time | • To provide overall technical support for effective implementation of the project.<br>• To effectively coordinate project implementation with different stakeholders including KFW.<br>• To ensure quality assurance of project activities and reporting to the donor. | Existing |
| Project Manager – P4 (Project Lead)<br><br>Full time | • Effectively contribute to the successful implementation of project activities in different provinces.<br>• Coordinate project implementation with different stakeholders/actors on the ground.<br>• Contribute to the development of project AWP, procurement plan, M&E plan, QPR and annual reports.<br>• Liaise with relevant stakeholders including donors and present projects in different meetings and platforms | New |
| GIS Specialist TA P3 | • Support Project manager to integrate GIS tools in project identification, implementation and M&E.<br>• Supervising the spatial analysis of the project sites and their surroundings' demographic characteristics<br>• Responsible for the development of GIS tools to increase operational efficiency<br>• Responsible for developing a training module for GIS tools<br>• Supervise the preparation of all GIS maps and tools required for project implementation | New |
| Energy Technical Specialist/ TA P3<br><br>Full time | • Provide overall technical support to the project team in the successful implementation of project activities<br>• Provide technical inputs to the development of project annual work plan, procurement plan, and project progress reports including QPR and APR.<br>• Present project in the technical working group meetings with different stakeholders including donors and relevant actors working in the energy sector. | New |
| Energy Technical Analyst t NPSA 9 regular<br><br>Full time | • Provide overall technical support to the project team in successful implementation of project activities<br>• Provide technical inputs to the development of project annual work plan, procurement plan, and | New |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| | | |
|---|---|---|
| | project progress reports including QPR and APR.<br>• Present project in technical working group meetings with different stakeholders including donors and relevant actors working in the energy sector. | |
| Procurement Specialist - P3<br><br>Full time | • Provide overall procurement and contract management support to the project.<br>• Manage procurement of products and services for the project implementation.<br>• Effectively coordinate project procurement needs with the CO procurement unit on time deliver<br>• Ensure compliance with UNDP rules and regulations for procurement of supplies and services. | New |
| Procurement Specialist – P3 (Output 3) | • Provide procurement services for an exit strategy, in particular for Output 3 related project activities<br>• Manage procurement of products and services for the project's sustenance through identified delivery models<br>• Effectively coordinate project procurement needs with the CO procurement unit on time deliver<br>• Ensure compliance with UNDP rules and regulations for procurement of supplies and services | New |
| Procurement Analyst – NPSA 9<br><br>Full time | • Provide overall procurement and contract management support to the project.<br>• Manage procurement of products and services for the project implementation.<br>• Effectively coordinate project procurement needs with the CO procurement unit on time deliver<br>• Ensure compliance with UNDP's POPP and internal control mechanism for procurement of supplies and services. | New |
| Environment and Social Safeguards Specialist - TA P3<br><br>Full time | • Coordinate with experts for finalisation of ESMF/ESMP, GRM, SEP<br>• Review and follow up with vendors for ESMP implementation<br>• Monitor the overall ESS compliance<br>• Report on new risks, etc. | New |
| Social and Environmental Safeguards Analyst NPSA 9 | • Coordinate with experts for finalisation of ESMF/ESMP, GRM, SEP<br>• Review and follow up with vendors for ESMP implementation<br>• Monitor the overall ESS compliance<br>• Report on new risks, etc. | New |
| Administration and Finance Analyst NPSA 9 | • Provide overall administrative and financial management support to the project.<br>• Support the project in all operational processes including financial management, development of annual work plan, administrative, HR management, IT, and protocol.<br>• will ensure compliance of project implementation to the UNDP's POPP and internal control mechanism. | New |
| Project Associate NPSA 7 | • Provide overall administrative management support to the project. | New |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| | | |
|---|---|---|
| | • Support the project in all operational processes including financial management, development of annual work plan, administrative, HR management, IT, and protocol.<br>• will ensure compliance of project implementation to the UNDP's POPP and internal control mechanism. | |
| Monitoring & Evaluation and Reporting Analyst – NPSA9 | • Provide overall M&E and communications support to the project.<br>• M&E duties include project-related data collection from implementing partners' data analysis, conducting spot checks or site visits to provide quality assurance services and ensuring that required reports are well prepared and submitted on time on time.<br>• Support the project to deliver effective external communication including sharing success stories and highlighting progress to the relevant stakeholders. S/he will closely work with project field office staff, UNDP IRMU/DEU/PMU, and UNDP Partnership and communication team. | New |
| Energy Engineer - IUNV | • Support Inception Phase activities by providing technical support in collecting field data, analysis and coordination<br>• Inputs to the preparation of the procurement packages and tender documents for works to be contracted for experts, goods and services related to energy interventions .<br>• The Engineer will interact with stakeholders, other UN agencies, and partners as necessary as well as with engineering consultant companies and contractors/ specialized experts and support in preparation of the scope of work to be carried out with quality and timeliness, in line with UNDP standards and procedures.<br>• Providing inputs and technical support in creating a comprehensive overview of a good practices of solar-PV power plants in a local context. | New |
| Technical Associates National UNVs – 8<br>Administration and Finance National UNV – 1 | • Day-to-day coordination, research and monitoring and reporting at the field.<br>• Support to regional teams on administration and finance-related tasks (for meetings, missions, follow-ups, etc.) | New |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

## X. LEGAL CONTEXT

As UNDP Afghanistan currently does not have a Standard Basic Assistance Agreement (SBAA) with the current DFA, the project document shall be the instrument envisaged and defined in the Supplemental Provisions to the Project Document, attached hereto and forming an integral part hereof, as "the Project Document".

This project will be implemented by UNDP in accordance with its financial regulations, rules, practices and procedures only to the extent that they do not contravene the principles of the Financial Regulations and Rules of UNDP. Where the financial governance of UNDP apply and will provide the required guidance to ensure best value for money, fairness, integrity, transparency, and effective international competition..

## XI. RISK MANAGEMENT

1. UNDP as the Implementing Partner will comply with the policies, procedures and practices of the United Nations Security Management System (UNSMS.)

2. UNDP as the Implementing Partner will undertake all reasonable efforts to ensure that none of the [project funds][28] [UNDP funds received pursuant to the Project Document][29] are used to provide support to individuals or entities associated with terrorism , that the recipients of any amounts provided by UNDP hereunder do not appear on the United Nations Security Council Consolidated Sanctions List, and that no UNDP funds received pursuant to the Project Document are used for money laundering activities. The United Nations Security Council Consolidated Sanctions List can be accessed via https://www.un.org/securitycouncil/content/un-sc-consolidated-list. This provision must be included in all sub-contracts or sub-agreements entered into under this Project Document.

3. Social and environmental sustainability will be enhanced through application of the UNDP Social and Environmental Standards (http://www.undp.org/ses) and related Accountability Mechanism (http://www.undp.org/secu-srm).

4. UNDP as the Implementing Partner will: (a) conduct project and programme-related activities in a manner consistent with the UNDP Social and Environmental Standards, (b) implement any management or mitigation plan prepared for the project or programme to comply with such standards, and (c) engage in a constructive and timely manner to address any concerns and complaints raised through the Accountability Mechanism. UNDP will seek to ensure that communities and other project stakeholders are informed of and have access to the Accountability Mechanism.

5. In the implementation of the activities under this Project Document, UNDP as the Implementing Partner will handle any sexual exploitation and abuse ("SEA") and sexual harassment ("SH") allegations in accordance with its regulations, rules, policies and procedures.
6. All signatories to the Project Document shall cooperate in good faith with any exercise to evaluate any programme or project-related commitments or compliance with the UNDP Social and Environmental Standards. This includes providing access to project sites, relevant personnel, information, and documentation.
7. UNDP as the Implementing Partner will ensure that the following obligations are binding on each responsible party, subcontractor, and sub-recipient:
    a) Consistent with the Article III of the SBAA *[or the Supplemental Provisions to the Project Document]*, the responsibility for the safety and security of each responsible

[28] To be used where UNDP is the Implementing Partner
[29] To be used where the UN, a UN fund/programme or a specialized agency is the Implementing Partner

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

party, subcontractor and sub-recipient and its personnel and property, and of UNDP's property in such responsible party's, subcontractor's and sub-recipient's custody, rests with such responsible party, subcontractor and sub-recipient. To this end, each responsible party, subcontractor and sub-recipient shall:

i. put in place an appropriate security plan and maintain the security plan, taking into account the security situation in the country where the project is being carried;
ii. assume all risks and liabilities related to such responsible party's, subcontractor's and sub-recipient's security, and the full implementation of the security plan.

b) UNDP reserves the right to verify whether such a plan is in place, and to suggest modifications to the plan when necessary. Failure to maintain and implement an appropriate security plan as required hereunder shall be deemed a breach of the responsible party's, subcontractor's and sub-recipient's obligations under this Project Document.

c) Each responsible party, subcontractor and sub-recipient (each a "sub-party" and together "sub-parties") acknowledges and agrees that UNDP will not tolerate sexual harassment and sexual exploitation and abuse of anyone by the sub-parties, and other entities involved in Project implementation, either as contractors or subcontractors and their personnel, and any individuals performing services for them under the Project Document.

(a) In the implementation of the activities under this Project Document, each sub-party shall comply with the standards of conduct set forth in the Secretary General's Bulletin ST/SGB/2003/13 of 9 October 2003, concerning "Special measures for protection from sexual exploitation and sexual abuse" ("SEA").

(b) Moreover, and without limitation to the application of other regulations, rules, policies and procedures bearing upon the performance of the activities under this Project Document, in the implementation of activities, each sub-party, shall not engage in any form of sexual harassment ("SH"). SH is defined as any unwelcome conduct of a sexual nature that might reasonably be expected or be perceived to cause offense or humiliation, when such conduct interferes with work, is made a condition of employment or creates an intimidating, hostile or offensive work environment. SH may occur in the workplace or in connection with work. While typically involving a pattern of conduct, SH may take the form of a single incident. In assessing the reasonableness of expectations or perceptions, the perspective of the person who is the target of the conduct shall be considered.

d) In the performance of the activities under this Project Document, each sub-party shall (with respect to its own activities), and shall require from its sub-parties (with respect to their activities) that they, have minimum standards and procedures in place, or a plan to develop and/or improve such standards and procedures in order to be able to take effective preventive and investigative action. These should include: policies on sexual harassment and sexual exploitation and abuse; policies on whistleblowing/protection against retaliation; and complaints, disciplinary and investigative mechanisms. In line with this, sub-parties will and will require that their respective sub-parties will take all appropriate measures to:
(i) Prevent its employees, agents or any other persons engaged to perform any services under this Project Document, from engaging in SH or SEA;
(ii) Offer employees and associated personnel training on prevention and response to SH and SEA, where sub-parties have not put in place its own training regarding the prevention of SH and SEA, sub-parties may use the training material available at UNDP;

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

(iii) Report and monitor allegations of SH and SEA of which any of the sub-parties have been informed or have otherwise become aware, and status thereof;

(iv) Refer victims/survivors of SH and SEA to safe and confidential victim assistance; and

(v) Promptly and confidentially record and investigate any allegations credible enough to warrant an investigation of SH or SEA. Each sub-party shall advise UNDP of any such allegations received and investigations being conducted by itself or any of its sub-parties with respect to their activities under the Project Document, and shall keep UNDP informed during the investigation by it or any of such sub-parties, to the extent that such notification

(i) does not jeopardize the conduct of the investigation, including but not limited to the safety or security of persons, and/or (ii) is not in contravention of any laws applicable to it. Following the investigation, the relevant sub-party shall advise UNDP of any actions taken by it or any of the other entities further to the investigation.

e) Each sub-party shall establish that it has complied with the foregoing, to the satisfaction of UNDP, when requested by UNDP or any party acting on its behalf to provide such confirmation. Failure of the relevant sub-party to comply of the foregoing, as determined by UNDP, shall be considered grounds for suspension or termination of the Project.

f) Each responsible party, subcontractor and sub-recipient will ensure that any project activities undertaken by them will be implemented in a manner consistent with the UNDP Social and Environmental Standards and shall ensure that any incidents or issues of non-compliance shall be reported to UNDP in accordance with UNDP Social and Environmental Standards.

g) Each responsible party, subcontractor and sub-recipient will take appropriate steps to prevent misuse of funds, fraud, corruption or other financial irregularities, by its officials, consultants, subcontractors and sub-recipients in implementing the project or programme or using the UNDP funds. It will ensure that its financial management, anti-corruption, anti-fraud and anti money laundering and countering the financing of terrorism policies are in place and enforced for all funding received from or through UNDP.

h) The requirements of the following documents, then in force at the time of signature of the Project Document, apply to each responsible party, subcontractor and sub-recipient: (a) UNDP Policy on Fraud and other Corrupt Practices (b) UNDP Anti-Money Laundering and Countering the Financing of Terrorism Policy; and (c) UNDP Office of Audit and Investigations Investigation Guidelines. Each responsible party, subcontractor and sub-recipient agrees to the requirements of the above documents, which are an integral part of this Project Document and are available online at www.undp.org.

i) In the event that an investigation is required, UNDP will conduct investigations relating to any aspect of UNDP programmes and projects. Each responsible party, subcontractor and sub-recipient will provide its full cooperation, including making available personnel, relevant documentation, and granting access to its (and its consultants', subcontractors' and sub-recipients') premises, for such purposes at reasonable times and on reasonable conditions as may be required for the purpose of an investigation. Should there be a limitation in meeting this obligation, UNDP shall consult with it to find a solution.

j) Each responsible party, subcontractor and sub-recipient will promptly inform UNDP as the Implementing Partner in case of any incidence of inappropriate use of funds, or credible allegation of fraud, corruption other financial irregularities with due confidentiality.

k) Where it becomes aware that a UNDP project or activity, in whole or in part, is the focus of investigation for alleged fraud/corruption, each responsible party, subcontractor and sub-recipient will inform the UNDP Resident Representative/Head of Office, who will promptly inform UNDP's Office of Audit and Investigations (OAI). It will provide regular updates to the head of UNDP in the country and OAI of the status of, and actions relating to, such investigation.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

l) UNDP will be entitled to a refund from the responsible party, subcontractor or sub-recipient of any funds provided that have been used inappropriately, including through fraud corruption or other financial irregularities, or otherwise paid other than in accordance with the terms and conditions of the Project Document. Such amount may be deducted by UNDP from any payment due to the responsible party, subcontractor or sub-recipient under this or any other agreement.
Where such funds have not been refunded to UNDP, the responsible party, subcontractor or sub-recipient agrees that donors to UNDP (including the Government) whose funding is the source, in whole or in part, of the funds for the activities under this Project Document, may seek recourse to such responsible party, subcontractor or sub-recipient for the recovery of any funds determined by UNDP to have been used inappropriately, including through fraud, corruption or other financial irregularities, or otherwise paid other than in accordance with the terms and conditions of the Project Document.

*Note:* The term "Project Document" as used in this clause shall be deemed to include any relevant subsidiary agreement further to the Project Document, including those with responsible parties, subcontractors and sub-recipients.

m) Each contract issued by the responsible party, subcontractor or sub-recipient in connection with this Project Document shall include a provision representing that no fees, gratuities, rebates, gifts, commissions or other payments, other than those shown in the proposal, have been given, received, or promised in connection with the selection process or in contract execution, and that the recipient of funds from it shall cooperate with any and all investigations and post-payment audits.

n) Should UNDP refer to the relevant national authorities for appropriate legal action any alleged wrongdoing relating to the project or programme, the Government will ensure that the relevant national authorities shall actively investigate the same and take appropriate legal action against all individuals found to have participated in the wrongdoing, recover and return any recovered funds to UNDP.

o) Each responsible party, subcontractor and sub-recipient shall ensure that all of its obligations set forth under this section entitled "Risk Management" are passed on to its subcontractors and sub-recipients and that all the clauses under this section entitled "Risk Management Standard Clauses" are adequately reflected, *mutatis mutandis*, in all its sub-contracts or sub-agreements entered into further to this Project Document.

## ANNEXES

# Annexure 1: Project Quality Assurance Report

| PROJECT QA ASSESSMENT: DESIGN AND APPRAISAL | | | | |
|---|---|---|---|---|
| **OVERALL PROJECT** | | | | |
| **EXEMPLARY (5)** ◎◎◎◎◎ | **HIGHLY SATISFACTORY (4)** ◎◎◎◎○ | **SATISFACTORY (3)** ◎◎◎○○ | **NEEDS IMPROVEMENT (2)** ◎◎○○○ | **INADEQUATE (1)** ◎○○○○ |
| At least four criteria are rated Exemplary, and all criteria are rated High or Exemplary. | All criteria are rated Satisfactory or higher, and at least four criteria are rated High or Exemplary. | At least six criteria are rated Satisfactory or higher, and only one may be rated Needs Improvement. The Principled criterion must be rated Satisfactory or above. | At least three criteria are rated Satisfactory or higher, and only four criteria may be rated Needs Improvement. | One or more criteria are rated Inadequate, or five or more criteria are rated Needs Improvement. |

**DECISION**

- **APPROVE** – the project is of sufficient quality to be approved in its current form**.** Any management actions must be addressed in a timely manner.
- **APPROVE WITH QUALIFICATIONS** – the project has issues that must be addressed before the project document can be approved. Any management actions must be addressed in a timely manner.
- **DISAPPROVE** – the project has significant issues that should prevent the project from being approved as drafted.

**RATING CRITERIA**
**For all questions, select the option that best reflects the project**

**STRATEGIC**

| | |
|---|---|
| **1. Does the project specify how it will contribute to higher level change through linkage to the programme's Theory of Change?**<br>• **3:** The project is clearly linked to the programme's theory of change. It has an explicit change pathway that explains how the project will contribute to outcome level change and why the project's strategy will likely lead to this change. This analysis is backed by credible evidence of what works effectively in this context and includes assumptions and risks.<br>• **2:** The project is clearly linked to the programme's theory of change. It has a change pathway that explains how the project will contribute to outcome-level change and why the project strategy will likely lead to this change.<br>• **1:** The project document may describe in generic terms how the project will contribute to development results, without an explicit link to the programme's theory of change.<br>**Note: Projects not contributing to a programme must have a project-specific Theory of Change. See alternative question under the lightbulb for these cases.* | 3 **2** 1<br>**Evidence** Section II and III of the proposal provides the details |
| **2. Is the project aligned with the UNDP Strategic Plan?**<br>• **3:** The project responds to at least one of the development settings as specified in the Strategic Plan[30] and adapts at least one Signature Solution[31]. The project's RRF includes all the relevant SP output indicators. *(all must be true)*<br>• **2:** The project responds to at least one of the development settings as specified in the Strategic Plan[4]. The project's RRF includes at least one SP output indicator, if relevant. *(both must be true)*<br>• **1:** The project responds to a partner's identified need, but this need falls outside of the UNDP Strategic Plan. Also select this option if none of the relevant SP indicators are included in the RRF. | **3** 2 1<br>**Evidence** Section III and Annex I; linkages to the Strategic Plan 5.1/Signature Solution No. 5 on Energy |

[30] The three development settings in UNDP's 2018-2021 Strategic Plan are: a) Eradicate poverty in all its forms and dimensions; b) Accelerate structural transformations for sustainable development; and c) Build resilience to shocks and crises

[31] The six Signature Solutions of UNDP's 2018-2021 Strategic Plan are: a) Keeping people out of poverty; b) Strengthen effective, inclusive and accountable governance; c) Enhance national prevention and recovery capacities for resilient societies; d) Promote nature based solutions for a sustainable planet; e) Close the energy gap; and f) Strengthen gender equality and the empowerment of women and girls.

| | | |
|---|---|---|
| **3. Is the project linked to the programme outputs? (i.e., UNDAF Results Group Workplan/CPD, RPD or Strategic Plan IRRF for global projects/strategic interventions not part of a programme)** | **Yes** | **No** |
| **RELEVANT** | | |
| **4. Does the project target groups left furthest behind?**<br>• **3:** The target groups are clearly specified, prioritising discriminated and marginalized groups left furthest behind, identified through a rigorous process based on evidence.<br>• **2:** The target groups are clearly specified, prioritizing groups left furthest behind.<br>**1:** The target groups are not clearly specified.<br>*Note: Management Action must be taken for a score of 1. *Projects that build institutional capacity should still identify targeted groups to justify support* | 3 / 2 / **1** | **Evidence** Initial analysis included – to be defined during Inception Phase (Page# 35 – Beneficiaries); as agreed with donor |
| **5. Have knowledge, good practices, and past lessons learned of UNDP and others informed the project design?**<br>• **3:** Knowledge and lessons learned backed by credible evidence from sources such as evaluation, corporate policies/strategies, and/or monitoring have been explicitly used, with appropriate referencing, to justify the approach used by the project.<br>• **2:** The project design mentions knowledge and lessons learned backed by evidence/sources, but have not been used to justify the approach selected.<br>**1:** There is little or no mention of knowledge and lessons learned informing the project design. Any references made are anecdotal and not backed by evidence.<br>*Note: Management Action or strong management justification must be given for a score of 1 | 3 / **2** / 1 | **Evidence Section** Pls refer Page #12 - Energy and UNDP: Priority and Lessons |
| **6. Does UNDP have a clear advantage to engage in the role envisioned by the project vis-à-vis national/regional/global partners and other actors?**<br>• **3:** An analysis has been conducted on the role of other partners in the area where the project intends to work, and credible evidence supports the proposed engagement of UNDP and partners through the project, including identification of potential funding partners. It is clear how results achieved by partners will complement the project's intended results and a communication strategy is in place to communicate results and raise visibility vis-à-vis key partners. Options for south-south and triangular cooperation have been considered, as appropriate. *(all must be true)*<br>• **2:** Some analysis has been conducted on the role of other partners in the area where the project intends to work, and relatively limited evidence supports the proposed engagement of and division of labour between UNDP and partners through the project, with unclear funding and communications strategies or plans.<br>**1:** No clear analysis has been conducted on the role of other partners in the area that the project intends to work. There is risk that the project overlaps and/or does not coordinate with partners' interventions in this area. Options for south-south and triangular cooperation have not been considered, despite its potential relevance.<br>*Note: Management Action or strong management justification must be given for a score of 1 | 3 / **2** / 1 | **Evidence** Pls refer Page #40 - partnerships |
| **PRINCIPLED** | | |
| **7. Does the project apply a human rights-based approach?**<br>• **3:** The project is guided by human rights and incorporates the principles of accountability, meaningful participation, and non-discrimination in the project's strategy. The project upholds the relevant international and national laws and standards. Any potential adverse impacts on enjoyment of human rights were rigorously identified and assessed as relevant, with appropriate mitigation and management measures incorporated into project design and budget. *(all must be true)*<br>• **2:** The project is guided by human rights by prioritizing accountability, meaningful participation and non-discrimination. Potential adverse impacts on enjoyment of human rights were identified and assessed as relevant, and appropriate mitigation and management measures incorporated into the project design and budget. *(both must be true)*<br>• **1:** No evidence that the project is guided by human rights. Limited or no evidence that potential adverse impacts on enjoyment of human rights were considered.<br>*Note: Management action or strong management justification must be given for a score of 1 | 3 / **2** / 1 | **Evidence** Pls refer to #40 on TEF principles and Risk mitigation; besides the criteria to be set for targeting Public |

| | |
|---|---|
| | Facilities would align with HRB |
| **8. Does the project use gender analysis in the project design?**<br>• **3:** A participatory gender analysis has been conducted and results from this gender analysis inform the development challenge, strategy and expected results sections of the project document. Outputs and indicators of the results framework include explicit references to gender equality, and specific indicators measure and monitor results to ensure women are fully benefitting from the project. *(all must be true)*<br>• **2:** A basic gender analysis has been carried out and results from this analysis are scattered (i.e., fragmented and not consistent) across the development challenge and strategy sections of the project document. The results framework may include some gender sensitive outputs and/or activities but gender inequalities are not consistently integrated across each output. *(all must be true)*<br>• **1:** The project design may or may not mention information and/or data on the differential impact of the project's development situation on gender relations, women and men, but the gender inequalities have not been clearly identified and reflected in the project document.<br>*Note: Management Action or strong management justification must be given for a score of 1 | 3 **2** 1<br>**Evidence** Pls refer page # 16 gender mainstreaming into energy services and gender action plan proposed |
| **9. Did the project support the resilience and sustainability of societies and/or ecosystems?**<br>• **3:** Credible evidence that the project addresses sustainability and resilience dimensions of development challenges, which are integrated in the project strategy and design. The project reflects the interconnections between the social, economic and environmental dimensions of sustainable development. Relevant shocks, hazards and adverse social and environmental impacts have been identified and rigorously assessed with appropriate management and mitigation measures incorporated into project design and budget. *(all must be true)*.<br>• **2:** The project design integrates sustainability and resilience dimensions of development challenges. Relevant shocks, hazards and adverse social and environmental impacts have been identified and assessed, and relevant management and mitigation measures incorporated into project design and budget. *(both must be true)*<br>• **1:** Sustainability and resilience dimensions and impacts were not adequately considered.<br>*Note: Management action or strong management justification must be given for a score of 1 | 3 **2** 1<br>**Evidence** Section III The rationale for deploying decentralised renewable systems and overall project approach integrates resilience and sustainability aspects |
| **10. Has the Social and Environmental Screening Procedure (SESP) been conducted to identify potential social and environmental impacts and risks?** The SESP is not required for projects in which UNDP is Administrative Agent only and/or projects comprised solely of reports, coordination of events, trainings, workshops, meetings, conferences and/or communication materials and information dissemination. [if yes, upload the completed checklist. If SESP is not required, provide the reason for the exemption in the evidence section.] | **Yes** No<br>SESP Not Required |
| **MANAGEMENT & MONITORING** | |
| **11. Does the project have a strong results framework?**<br>• **3:** The project's selection of outputs and activities are at an appropriate level. Outputs are accompanied by SMART, results-oriented indicators that measure the key expected development changes, each with credible data sources and populated baselines and targets, including gender sensitive, target group focused, sex-disaggregated indicators where appropriate. *(all must be true)*<br>• **2:** The project's selection of outputs and activities are at an appropriate level. Outputs are accompanied by SMART, results-oriented indicators, but baselines, targets and data sources may not yet be fully specified. Some use of target group focused, sex-disaggregated indicators, as appropriate. *(all must be true)*<br>**1:** The project's selection of outputs and activities are not at an appropriate level; outputs are not accompanied by SMART, results-oriented indicators that measure the expected change and have not been populated with baselines and targets; data sources are not specified, and/or no gender sensitive, sex-disaggregation of indicators. *(if any is true)*<br>*Note: Management Action or strong management justification must be given for a score of 1 | 3 **2** 1<br>**Evidence**<br>Annex -1 |
| **12. Is the project's governance mechanism clearly defined in the project document, including composition of the project board?** | 3 **2** 1 |

| | |
|---|---|
| • **3:** The project's governance mechanism is fully defined. Individuals have been specified for each position in the governance mechanism (especially all members of the project board.) Project Board members have agreed on their roles and responsibilities as specified in the terms of reference. The ToR of the project board has been attached to the project document. *(all must be true)*.<br>• **2:** The project's governance mechanism is defined; specific institutions are noted as holding key governance roles, but individuals may not have been specified yet. The project document lists the most important responsibilities of the project board, project director/manager and quality assurance roles. *(all must be true)*<br>**1:** The project's governance mechanism is loosely defined in the project document, only mentioning key roles that will need to be filled at a later date. No information on the responsibilities of key positions in the governance mechanism is provided.<br>*Note: Management Action or strong management justification must be given for a score of 1 | **Evidence** Section VII |
| **13. Have the project risks been identified with clear plans stated to manage and mitigate each risk?**<br>• **3:** Project risks related to the achievement of results are fully described in the project risk log, based on comprehensive analysis drawing on the programme's theory of change, Social and Environmental Standards and screening, situation analysis, capacity assessments and other analysis such as funding potential and reputational risk. Risks have been identified through a consultative process with key internal and external stakeholders. Clear and complete plan in place to manage and mitigate each risk, reflected in project budgeting and monitoring plans. *(both must be true)*<br>• **2:** Project risks related to the achievement of results are identified in the initial project risk log based on a minimum level of analysis and consultation, with mitigation measures identified for each risk.<br>• **1:** Some risks may be identified in the initial project risk log, but no evidence of consultation or analysis and no clear risk mitigation measures identified. This option is also selected if risks are not clearly identified and/or no initial risk log is included with the project document.<br>*Note: Management Action must be taken for a score of 1 | **3** 2<br>1<br>**Evidence** Risk Management Page # 42-51 |
| **EFFICIENT** | |
| **14. Have specific measures for ensuring cost-efficient use of resources been explicitly mentioned as part of the project design? This can include, for example: i) using the theory of change analysis to explore different options of achieving the maximum results with the resources available; ii) using a portfolio management approach to improve cost effectiveness through synergies with other interventions; iii) through joint operations (e.g., monitoring or procurement) with other partners; iv) sharing resources or coordinating delivery with other projects, v) using innovative approaches and technologies to reduce the cost of service delivery or other types of interventions.**<br>*(Note: Evidence of at least one measure must be provided to answer yes for this question)* | **Yes (3)** Page # 40 – Cost Efficiency<br>No (1) |
| **15. Is the budget justified and supported with valid estimates?**<br>• **3:** The project's budget is at the activity level with funding sources, and is specified for the duration of the project period in a multi-year budget. Realistic resource mobilisation plans are in place to fill unfunded components. Costs are supported with valid estimates using benchmarks from similar projects or activities. Cost implications from inflation and foreign exchange exposure have been estimated and incorporated in the budget. Adequate costs for monitoring, evaluation, communications and security have been incorporated.<br>• **2:** The project's budget is at the activity level with funding sources, when possible, and is specified for the duration of the project in a multi-year budget, but no funding plan is in place. Costs are supported with valid estimates based on prevailing rates.<br>• **1:** The project's budget is not specified at the activity level, and/or may not be captured in a multi-year budget. | **3** 2<br>1<br>**Evidence** Annex 2 |
| **16. Is the Country Office/Regional Hub/Global Project fully recovering the costs involved with project implementation?**<br>• **3:** The budget fully covers all project costs that are attributable to the project, including programme management and development effectiveness services related to strategic country programme planning, quality assurance, pipeline development, policy advocacy services, finance, procurement, human resources, administration, issuance of contracts, security, travel, assets, general services, information and communications based on full costing in accordance with prevailing UNDP policies (i.e., UPL, LPL.)<br>• **2:** The budget covers significant project costs that are attributable to the project based on prevailing UNDP policies (i.e., UPL, LPL) as relevant.<br>• **1:** The budget does not adequately cover project costs that are attributable to the project, and UNDP is cross-subsidizing the project.<br>*Note: Management Action must be given for a score of 1. The budget must be revised to fully reflect the costs of implementation before the project commences. | **3** 2<br>1<br>**Evidence** Annex 2 |

| | | |
|---|---|---|
| **EFFECTIVE** | | |
| **17. Have targeted groups been engaged in the design of the project?**<br>• 3: Credible evidence that all targeted groups, prioritising discriminated and marginalized populations that will be involved in or affected by the project, have been actively engaged in the design of the project. The project has an explicit strategy to identify, engage and ensure the meaningful participation of target groups as stakeholders throughout the project, including through monitoring and decision-making (e.g., representation on the project board, inclusion in samples for evaluations, etc.)<br>• 2: Some evidence that key targeted groups have been consulted in the design of the project.<br>• 1: No evidence of engagement with targeted groups during project design. | 3 **2** 1<br>**Evidence** Annex – 7 Stakeholder Engagement Plan | |
| **18. Does the project plan for adaptation and course correction if regular monitoring activities, evaluation, and lesson learned demonstrate there are better approaches to achieve the intended results and/or circumstances change during implementation?** | **Yes (3)** | No (1) |
| **19. The gender marker for all project outputs are scored at GEN2 or GEN3, indicating that gender has been fully mainstreamed into all project outputs at a minimum.**<br>*Note: Management Action or strong management justification must be given for a score of "no" | **Yes (3)**<br>**Evidence** Page #16 and Annex -1 (Outputs 2 and 3**)** | No (1) |
| **SUSTAINABILITY & NATIONAL OWNERSHIP** | | |
| **20. Have national/regional/global partners led, or proactively engaged in, the design of the project?**<br>• **3:** National partners (or regional/global partners for regional and global projects) have full ownership of the project and led the process of the development of the project jointly with UNDP.<br>• **2:** The project has been developed by UNDP in close consultation with national/regional/global partners.<br>• **1:** The project has been developed by UNDP with limited or no engagement with national partners. | 3 **2** 1<br>**Evidence** Annex -7 Stakeholder Engagement Plan | |
| **21. Are key institutions and systems identified, and is there a strategy for strengthening specific/ comprehensive capacities based on capacity assessments conducted?**<br>• **3:** The project has a strategy for strengthening specific capacities of national institutions and/or actors based on a completed capacity assessment. This strategy includes an approach to regularly monitor national capacities using clear indicators and rigorous methods of data collection, and adjust the strategy to strengthen national capacities accordingly.<br>• **2:** A capacity assessment has been completed. There are plans to develop a strategy to strengthen specific capacities of national institutions and/or actors based on the results of the capacity assessment.<br>• **1:** Capacity assessments have not been carried out. | 3 2 **1**<br>**Evidence** Will be carried out during the Inception Phase once targeted Facilities are identified | |
| **22. Is there is a clear strategy embedded in the project specifying how the project will use national systems (i.e., procurement, monitoring, evaluations, etc.,) to the extent possible?** | **Yes (3)** | No (1) |
| **23. Is there a clear transition arrangement/ phase-out plan developed with key stakeholders in order to sustain or scale up results (including resource mobilisation and communications strategy)?** | **Yes (3)** | No (1) |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

# Annexure 2: Social and Environmental Screening Template

**UNDP Social and Environmental Screening Template (v. July 2022)**

*The completed template, which constitutes the Social and Environmental Screening Report, must be included as an annex to the Project Document at the design stage. Note: this template will be converted into an online tool. The online version will guide users through the process and will embed relevant guidance.*

## Project Information

| ***Project Information*** | |
|---|---|
| 1. Project Title | Sustainable Energy Services for Education and Health in Afghanistan (SESEHA) (in short: Renewable Energy Project Afghanistan) |
| 2. Project Number (i.e. Atlas project ID) | |
| 3. Location (Global/Region/Country) | Afghanistan |
| 4. Project stage (Design or Implementation) | Design |
| 5. Date | 10 August 2022 |

## Part A. Integrating Programming Principles to Strengthen Social and Environmental Sustainability

| **QUESTION 1: How Does the Project Integrate the Programming Principles in Order to Strengthen Social and Environmental Sustainability?** |
|---|
| ***Briefly describe in the space below how the project mainstreams the human rights-based approach*** |
| Afghanistan is currently coping with serious humanitarian crisis which has worsened further due to the COVID-19 pandemic and earthquake (2022). The proposed project aims at installing decentralized renewable energy applications (solar PV) and introducing energy efficiency measures to enhance services in public facilities of the education and health sectors and associated communities who are either not served or under-served (unreliable access) by the regional/national grids. The mainstreaming of the human rights-based approach is embedded in the project due to the nature of its activities being linked with basic services like education and health. The project aims at increasing access to sustainable energy by installation of solar panels for generating electricity. Most institutions and public facilities in the health and education sectors rely on polluting diesel generators or other sub optimal solutions that impact the reliance of these basic services. The project contributes to Afghanistan's energy security (with less reliance on imports), better resilience through reliable services and effective response to humanitarian and energy crisis faced by poor and vulnerable Afghans. The project will integrate the UNDP Overarching Principles of Engagement which ensures adherence to international human rights standards and principles to promote and protect human rights by aligning with new UN Transitional Engagement Framework (TEF) which represents the common basis for the United Nations and partners to deliver a coordinated and effective crisis response in Afghanistan after the powershift in August 2021. The project intends to have stakeholder engagement throughout the project cycle which will take all stakeholder considerations into account and will also have a project specific grievance redressal mechanism (GRM). |
| ***Briefly describe in the space below how the project is likely to improve gender equality and women's empowerment*** |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| |
|---|
| The project will serve as catalyst for strengthening health and education services provision and developing productive activities which will be specifically targeted to benefit women. Decentralized renewable energy systems coupled with battery/ DG sets and energy efficiency measures will help in upgrading the health and education related public services which have deteriorated in the recent times due to lack of access to energy/ electricity. The project also envisages establishment of delivery models for operation and maintenance (O&M) through private sector linkages and gender inclusion. At project level, all the activities will be coordinated with these ongoing programs as well as other donor led programs to draw synergies to roll out and scale up the interventions in the conflict sensitive context. The project thus seeks to remove barriers to women's economic empowerment; prevent and respond to GBV; promote women's health and catalyze active participation and leadership of women in community planning and decision making. It will carry out a gender analysis to determine existing gender inequalities, gender roles and norms and power balance in the areas of energy. The gender analysis will inform project implementation, monitoring, review and evaluation. Aligned with UNSDG standards, the project is being scored with Gender Equality Marker (GEM2) meaning that it 'make a significant contribution to gender equality and/or the empowerment of women (mainstreamed). A Gender Based Violence Action plan (GBV Action Plan) will also be prepared which will include specific and timebound actions to mitigate the Sexual Exploitation and Abuse and Sexual Harassment risks which will cover Codes of Conduct, and a responsive GRM where referrals will be made to pre-identified gender-based violence (GBV) service providers. |
| ***Briefly describe in the space below how the project mainstreams sustainability and resilience*** |
| The ongoing conflict coupled with the COVID-19 and earthquake (2022) has increased the high level of vulnerability and needs in the rural areas. Decentralized energy systems based on renewables are thus well suited in fragile, high-risk contexts and lead to the resilience of energy systems. The project interventions aim at installing solar PV and energy efficiency measures in public facilities related with education and health to enhance the energy access which would help the local population to address their basic needs while also contributing towards social cohesion and sustainable energy systems. The project will contribute towards energy security, better resilience and response to humanitarian and energy crisis faced by poor and vulnerable Afghans. |
| ***Briefly describe in the space below how the project strengthens accountability to stakeholders*** |
| The project envisages participatory approach by stakeholder engagement throughout the project cycle. The stakeholder engagement plan will be prepared during the project preparation phase. The project will also have a project specific GRM. The project team will ensure that the GRM is publicly accessible and that all grievances are addressed in a timely and acceptable manner in line with the UNDP SES. UNDP's Accountability Mechanism, which includes the Social and Environmental Compliance Review (SECU) and Stakeholder Response Mechanism (SRM) will also serve as an additional layer of grievance redress and empower stakeholders to push for accountability. |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

## Part B. Identifying and Managing Social and Environmental Risks

| **QUESTION 2: What are the Potential Social and Environmental Risks?** *Note: Complete SESP Attachment 1 before responding to Question 2.* | **QUESTION 3: What is the level of significance of the potential social and environmental risks?** *Note: Respond to Questions 4 and 5below before proceeding to Question 5* | | | **QUESTION 6: Describe the assessment and management measures for each risk rated Moderate, Substantial or High** |
|---|---|---|---|---|
| ***Risk Description (broken down by event, cause, impact)*** | ***Impact and Likelihood (1-5)*** | ***Significance (Low, Moderate Substantial, High)*** | ***Comments (optional)*** | ***Description of assessment and management measures for risks rated as Moderate, Substantial or High*** |
| Risk 1: Installation of solar PV projects with battery storage and DG sets as backup might have indirect environmental and/or social impacts<br>(Standard 1 ; 1.1)<br>(Standard 3 ; 3.1, 3.2, 3.3)<br>(Standard 7 ; 7.6) | I=3<br>L=3 | **Moderate** | The installation of solar PV with battery/ DG sets for power back up may have numerous environment and social impacts like land acquisition for setting up solar PV; stability of the building (in case of solar rooftop projects); the safe disposal and/or recycling of batteries and solar panels (hazardous waste)<br>after the end of their lifespan; the exhaust emissions of back-up diesel generators. | Since the location and size of the project inventions is yet to be identified through feasibility studies, an environmental and social management framework (ESMF) will be developed during project preparation stage and will be followed throughout the project cycle. The ESMF will include procedures for screening and categorization of E&S risks of subprojects, including the use of the screening tools and an exclusion list (comprising list of areas to avoid while undertaking the site selection). The ESMF would also include a generic Environment Social Management Plan (ESMP), which will be modified if required based on the findings of the feasibility study and screening results of identified sub project sites. A Stakeholder Engagement Plan (SEP)will also be developed during the project preparation phase to ensure a participatory process with the direct and indirect beneficiaries and stakeholders throughout the project cycle. The generic ESMP will be part of the relevant tender documents with the requirement of budgetary provisions for environmental and social risk management in relevant tender documents and construction contracts. |
| Risk 2: Lack of participation by stakeholders/ beneficiaries to voice their concerns in the programme | I = 2<br>L =2 | **Moderate** | Under the current political and socio-economic condition, the restrictive regime, public officials, | The stakeholder engagement plan and project specific |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| | | | | |
|---|---|---|---|---|
| (SES Principle P2, P10, P14) | | | private companies, local beneficiaries and other vulnerable groups may not have the opportunity to voice their concerns. | GRM will provide an opportunity for a participatory approach throughout the project cycle. The project team will ensure that all the grievances are addressed in a timely and acceptable manner in line with the UNDP SES. |
| Risk 3: Reduced participation of public officials in the program due to capacity constraints, current socio-political situation and security risk.<br>(SES Principle P3) | I = 3<br>L = 2 | **Moderate** | The various officials of the health and educational institutions and its associated facilities may not have the capacity to meet their obligations in the project in the current socio-political environment in Afghanistan. | The implementation will be guided by the principles of the UN Transitional Engagement Framework (2022) and will adhere to TEF guidance referred in its section on 'UN Engagement with the de facto authorities'. The project will aim to mainstream these principles by direct implementation. The stakeholder engagement plan and project specific GRM will provide an opportunity for a participatory approach throughout the project cycle. |
| Risk 4: Lack of participation of women/ risk of gender-based violence due to participation of women in the programme<br>(SES Principle P10 and 12) | I=3<br>L=4 | **Moderate** | Women in Afghanistan are not well represented within the country's working population and the situation has worsened in the current political context with large scale systematic gender-based discrimination and violence against women and girls. The project envisages establishment of delivery models for operation and maintenance (O&M) through private sector linkages and gender inclusion, which may trigger incidents of gender- based violence. | A GBV Action Plan is envisaged to be prepared during the project preparation phase as part of the ESMF which will include specific and timebound actions to mitigate the Sexual Exploitation and Abuse and Sexual Harassment risks which will cover Codes of Conduct, and a responsive GRM where referrals will be made to pre-identified gender-based violence (GBV) service providers. The SEP will establish approaches to ensure participation of the women throughout the project cycle |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| | | | | |
|---|---|---|---|---|
| Risk 5: Labour, occupational, health, safety standards during implementation and operation by the contractor selected for the project do not meet international labour commitments and global best practices<br>(Standard 7; 7.1, 7.2, 7.3, 7.5, 7.6) | I=3<br>L=3 | **Moderate** | Non-compliance towards Occupational, health, safety standards by the construction company. Also, workers may be exposed to discriminatory working conditions, include child labour and/or lack of equal opportunities | The ESMF will include a labor management plan and an Occupational Health and Safety (OHS) Plan to ensure that workers are safe during the retrofitting activities. All construction contracts will have the requirement of the contractor to develop a site-specific Environmental and Social Management Plan (ESMP) covering the project construction and operation. The generic ESMP will be a part of the bidding documents. The bids will be required to allocate financial resources towards mitigation measures/ compliance with the ESMF. |
| Risk 6: Improper disposal of solar PV panels, batteries and energy efficiency retrofitting activities will lead negative impacts on the water and air quality thus posing a risk to health of the population and other animals.<br>(Standard 3; 3.5)<br>(Standard 8; 8.1, 8.2) | I=3<br>L=3 | **Moderate** | The hazardous chemicals from the battery may leech to be ground water leading to soil and water pollution. The solar PV panels including broken panels also need to properly be disposed considering that more than 90% of their mass composed of glass, polymer and aluminium, which are non-hazardous wastes. However, trace amounts of tin and lead are used.<br>The proposed project also includes Energy Efficiency retrofitting activities which may lead to generation waste which has to be handled and disposed properly to ensure that hazardous material is not released into the environment | The ESMF will include<br>Waste Management Plan which will include the following provisions,<br>a) provisions for the original battery/equipment manufacturer (OEM) for transporting and recycling of used lead acid batteries.<br>b) Provisions of buy back policy with the vendors<br>c) Provisions for the OEM to dispose used equipment/ waste adequately and submit a proof of payment for the same<br>d) provisions for recycling of PV modules at the end of lifecycle. If there are broken modules, they should be stored safely on the site and should be covered, such that it does not impact soil or water and does not impact worker safety.<br>e) Provisions to ensure proper handling and disposal of retrofitted equipment |
| | **QUESTION 4: What is the overall project risk categorization?** | | | |

| | | | | | |
|---|---|---|---|---|---|
| | ***Low Risk*** | ☐ | | | |
| | ***Moderate Risk*** | X | With the development of the Exclusion List for the pre-selection of sub sites and the E&S Screening tool that would be implemented for all sites identified/selected, avoidance of sites which might trigger impacts on biodiversity/ecology, cultural heritage, physical and/or economic displacement and indigenous people would be ensured. In addition, a site specific ESMP (with guidance from the Project ESMF) would be developed for sub sites selected to minimize/mitigate any E&S risks and impacts envisaged during the screening process. Considering that adequate measures would be undertaken at every stage of site identification, selection. construction and operation of the project, hence the project has been provided an overall risk categorization of "moderate" risk. | | |
| | ***Substantial Risk*** | ☐ | | | |
| | ***High Risk*** | ☐ | | | |
| | **QUESTION 5: Based on the identified risks and risk categorization, what requirements of the SES are triggered? (check all that apply)** | | | | |
| | Question only required for Moderate, Substantial and High Risk projects | | | | |
| | ***Is assessment required? (check if "yes")*** | X | | | ***Status? (completed, planned)*** |
| | *if yes, indicate overall type and status* | | X | Targeted assessment(s) | Planned: Stakeholder Engagement Plan; Gender analysis; E&S Screening process for all identified sub-project sites as part of ESMF |
| | | | ☐ | ESIA (Environmental and Social Impact Assessment) | |
| | | | ☐ | SESA (Strategic Environmental and Social Assessment) | |
| | ***Are management plans required?*** | X | | | |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| | | | | | |
|---|---|---|---|---|---|
| | ***(check if "yes)*** | | | | |
| | *If yes, indicate overall type* | | **X** | Targeted management plans (e.g. GBV Action Plan, Emergency Response Plan, Waste Management Plan, etc) | Planned: GBV Action Plan, ERP, Waste Management Plan |

| | | | | | |
|---|---|---|---|---|---|
| | | | X | ESMF (Environmental and Social Management Framework which may include range of targeted plans) Procedures for screening and categorization of E&S risks of subprojects, including the use of the screening tools and exclusion list. Management Plans (including project specific SEP and GRM, Labor management plan, OHS Plan, waste management plan, security management plan, GBV action plan) will be included in the ESMF including generic ESMP. The ESMP would be customized during implementation based on site specific conditions identified during feasibility analysis prior to its installation, commissioning and O and M arrangements. | Planned: ESMF including a generic ESMP and customization during implementation based on site specific conditions |
| | | | | | |
| | ***Based on identified <u>risks</u>, which Principles/Project- level Standards triggered?*** | | **Comments (not required)** | | |
| | ***Overarching Principle: Leave No One Behind*** | | | | |
| | ***Human Rights*** | **X** | Participation of intended target groups may be impacted by the current socio-political situation in Afghanistan | | |
| | ***Gender Equality and Women's Empowerment*** | **X** | Participation of women and other vulnerable groups may be impacted by the current socio-political situation in Afghanistan | | |
| | ***Accountability*** | **X** | Capacities of the office bearers in the education, health related public institutions and other associated institutions may be limited due to the current socio-political situation in Afghanistan | | |
| | ***1. Biodiversity Conservation and Sustainable Natural*** | ☐ | The Exclusion List that would be developed as part of the ESMF would include a pre-selection criteria list | | |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| | | | |
|---|---|---|---|
| | ***Resource Management*** | | for selecting the sub-project/sites. The List would also include criteria wherein areas with biodiversity/ecological significance are to be avoided. In addition, the E&S screening process would also act as a tool to identify and assess the risks and impacts on ecology and biodiversity, so that impacts on this aspect can be avoided/ minimized. |
| | ***2. Climate Change and Disaster Risks*** | **X** | Through the proposed screening process that would be undertaken for the identified sub-projects, risks and impacts of climate change on the project would be assessed and appropriate mitigation measures would be recommended as part of the site specific ESMP. |
| | ***3. Community Health, Safety and Security*** | × | |
| | ***4. Cultural Heritage*** | ☐ | The pre-selection criteria would include criteria wherein areas with cultural/historical/religious significance are to be avoided. In addition, the E&S screening process would also act as a tool to identify and assess the risks and impacts on cultural heritage, so that impacts on this aspect can be avoided/ minimized. |
| | ***5. Displacement and Resettlement*** | ☐ | The pre-selection criteria would include criteria wherein areas which would trigger physical/ economic displacement are to be avoided. In addition, the E&S screening process would also act as a tool to identify and assess the risks and impacts on physical and/or economic displacement, so that impacts on this aspect can be avoided/ minimized. |
| | ***6. Indigenous Peoples*** | ☐ | The pre-selection criteria would include criteria wherein areas which might have an impact on land/rights/resources of indigenous people are to be avoided. In addition, the E&S screening process would also act as a tool to identify and assess the risks and impacts on indigenous people, so that impacts on this aspect can be avoided/ minimized. |
| | ***7. Labour and Working Conditions*** | × | |
| | ***8. Pollution Prevention and Resource Efficiency*** | × | |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

### Final Sign Off

*Final Screening at the design-stage is not complete until the following signatures are included*

| Signature | Date | Description |
|---|---|---|
| QA Assessor<br>**Usha Rao**<br>DocuSigned by: K. Usha Rao 9BAF891EF061460... | 13-Dec-2022 | UNDP staff member responsible for the project, typically a UNDP Programme Officer. Final signature confirms they have "checked" to ensure that the SESP is adequately conducted. |
| QA Approver<br>**Surayo Buzurukova**<br>DocuSigned by: Surayo Buzurukova C8F21608D8FA487... | 14-Dec-2022 | UNDP senior manager, typically the UNDP Deputy Country Director (DCD), Country Director (CD)**,** Deputy Resident Representative (DRR), or Resident Representative (RR). The QA Approver cannot also be the QA Assessor. Final signature confirms they have "cleared" the SESP prior to submittal to the PAC. |
| PAC Chair<br>**Surayo Buzurukova**<br>DocuSigned by: Surayo Buzurukova C8F21608D8FA487... | 14-Dec-2022 | UNDP chair of the PAC. In some cases, PAC Chair may also be the QA Approver. Final signature confirms that the SESP was considered as part of the project appraisal and considered in recommendations of the PAC. |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

## SESP Attachment 1. Social and Environmental Risk Screening Checklist

| **Checklist Potential Social and Environmental Risks** | |
|---|---|
| INSTRUCTIONS: The risk screening checklist will assist in answering Questions 2-6 of the Screening Template. Answers to the checklist questions help to (1) identify potential risks, (2) determine the overall risk categorization of the project, and (3) determine required level of assessment and management measures. Refer to the SES toolkit for further guidance on addressing screening questions. | |
| **Overarching Principle: Leave No One Behind**<br>**Human Rights** | **Answer (Yes/No)** |
| P.1 Have local communities or individuals raised human rights concerns regarding the project (e.g. during the stakeholder engagement process, grievance processes, public statements)? | No |
| P.2 Is there a risk that duty-bearers (e.g. government agencies) do not have the capacity to meet their obligations in the project? | Yes |
| P.3 Is there a risk that rights-holders (e.g. project-affected persons) do not have the capacity to claim their rights? | Yes |
| *Would the project potentially involve or lead to:* | |
| P.4 adverse impacts on enjoyment of the human rights (civil, political, economic, social or cultural) of the affected population and particularly of marginalized groups? | No |
| P.5 inequitable or discriminatory impacts on affected populations, particularly people living in poverty or marginalized or excluded individuals or groups, including persons with disabilities? [16] | No |
| P.6 restrictions in availability, quality of and/or access to resources or basic services, in particular to marginalized individuals or groups, including persons with disabilities? | No |
| P.7 exacerbation of conflicts among and/or the risk of violence to project-affected communities and individuals? | No |
| **Gender Equality and Women's Empowerment** | |
| P.8 Have women's groups/leaders raised gender equality concerns regarding the project, (e.g. during the stakeholder engagement process, grievance processes, public statements)? | No |
| *Would the project potentially involve or lead to:* | |
| P.9 adverse impacts on gender equality and/or the situation of women and girls? | No |
| P.10 reproducing discriminations against women based on gender, especially regarding participation in design and implementation or access to opportunities and benefits? | Yes |
| P.11 limitations on women's ability to use, develop and protect natural resources, taking into account different roles and positions of women and men in accessing environmental goods and services?<br>*For example, activities that could lead to natural resources degradation or depletion in communities who depend on these resources for their livelihoods and well being* | No |
| P.12 exacerbation of risks of gender-based violence?<br>*For example, through the influx of workers to a community, changes in community and household power dynamics, increased exposure to unsafe public places and/or transport, etc*. | Yes |

[16] *Prohibited grounds of discrimination include race, ethnicity, sex, age, language, disability, sexual orientation, gender identity, religion, political or other opinion, national or social or geographical origin, property, birth or other status including as an indigenous person or as a member of a minority. References to "women and men" or similar is understood to include women and men, boys and girls, and other groups discriminated against based on their gender identities, such as transgender and transsexual people.*

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| | | |
|---|---|---|
| **Sustainability and Resilience:** Screening questions regarding risks associated with sustainability and resilience are encompassed by the Standard-specific questions below | | |
| **Accountability** | | |
| *Would the project potentially involve or lead to:* | | |
| P.13 | exclusion of any potentially affected stakeholders, in particular marginalized groups and excluded individuals (including persons with disabilities), from fully participating in decisions that may affect them? | No |
| P.14 | grievances or objections from potentially affected stakeholders? | Yes |
| P.15 | risks of retaliation or reprisals against stakeholders who express concerns or grievances, or who seek to participate in or to obtain information on the project? | No |
| **Project-Level Standards** | | |
| **Standard 1: Biodiversity Conservation and Sustainable Natural Resource Management** | | |
| *Would the project potentially involve or lead to:* | | |
| 1.1 | adverse impacts to habitats (e.g. modified, natural, and critical habitats) and/or ecosystems and ecosystem services?<br>*For eg, through habitat loss, conversion or degradation, fragmentation, hydrological changes* | No |
| 1.2 | activities within or adjacent to critical habitats and/or environmentally sensitive areas, including (but not limited to) legally protected areas (e.g. nature reserve, national park), areas proposed for protection, or recognized as such by authoritative sources and/or indigenous peoples or local communities? | No |
| 1.3 | changes to the use of lands and resources that may have adverse impacts on habitats, ecosystems, and/or livelihoods? (Note: if restrictions and/or limitations of access to lands would apply, refer to Standard 5) | No |
| 1.4 | risks to endangered species (e.g. reduction, encroachment on habitat)? | No |
| 1.5 | exacerbation of illegal wildlife trade? | No |
| 1.6 | introduction of invasive alien species? | No |
| 1.7 | adverse impacts on soils? | No |
| 1.8 | harvesting of natural forests, plantation development, or reforestation? | No |
| 1.9 | significant agricultural production? | No |
| 1.10 | animal husbandry or harvesting of fish populations or other aquatic species? | No |
| 1.11 | significant extraction, diversion or containment of surface or ground water?<br>*For example, construction of dams, reservoirs, river basin developments, groundwater extraction* | No |
| 1.12 | handling or utilization of genetically modified organisms/living modified organisms?[17] | No |
| 1.13 | utilization of genetic resources? (e.g. collection and/or harvesting, commercial development) | No |
| 1.14 | adverse transboundary or global environmental concerns? | No |
| **Standard 2: Climate Change and Disaster Risks** | | |
| *Would the project potentially involve or lead to:* | | |

[17] See the Convention on Biological Diversity and its Cartagena Protocol on Biosafety.

[18] See the Convention on Biological Diversity and its Nagoya Protocol on access and benefit sharing from use of genetic resources.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| | | |
|---|---|---|
| 2.1 | areas subject to hazards such as earthquakes, floods, landslides, severe winds, storm surges, tsunami or volcanic eruptions? | Yes |
| 2.2 | outputs and outcomes sensitive or vulnerable to potential impacts of climate change or disasters?<br>*For example, through increased precipitation, drought, temperature, salinity, extreme events, earthquakes* | No |
| 2.3 | increases in vulnerability to climate change impacts or disaster risks now or in the future (also known as maladaptive or negative coping practices)?<br>*For example, changes to land use planning may encourage further development of floodplains, potentially increasing the population's vulnerability to climate change, specifically flooding* | No |
| 2.4 | increases of greenhouse gas emissions, black carbon emissions or other drivers of climate change? | No |
| **Standard 3: Community Health, Safety and Security** | | |
| *Would the project potentially involve or lead to:* | | |
| 3.1 | construction and/or infrastructure development (e.g. roads, buildings, dams)? (Note: the GEF does not finance projects that would involve the construction or rehabilitation of large or complex dams) | Yes |
| 3.2 | air pollution, noise, vibration, traffic, injuries, physical hazards, poor surface water quality due to runoff, erosion, sanitation? | Yes |
| 3.3 | harm or losses due to failure of structural elements of the project (e.g. collapse of buildings or infrastructure)? | Yes |
| 3.4 | risks of water-borne or other vector-borne diseases (e.g. temporary breeding habitats), communicable and noncommunicable diseases, nutritional disorders, mental health? | No |
| 3.5 | transport, storage, and use and/or disposal of hazardous or dangerous materials (e.g. explosives, fuel and other chemicals during construction and operation)? | Yes |
| 3.6 | adverse impacts on ecosystems and ecosystem services relevant to communities' health (e.g. food, surface water purification, natural buffers from flooding)? | No |
| 3.7 | influx of project workers to project areas? | No |
| 3.8 | engagement of security personnel to protect facilities and property or to support project activities? | No |
| **Standard 4: Cultural Heritage** | | |
| *Would the project potentially involve or lead to:* | | |
| 4.1 | activities adjacent to or within a Cultural Heritage site? | No |
| 4.2 | significant excavations, demolitions, movement of earth, flooding or other environmental changes? | No |
| 4.3 | adverse impacts to sites, structures, or objects with historical, cultural, artistic, traditional or religious values or intangible forms of culture (e.g. knowledge, innovations, practices)? (Note: projects intended to protect and conserve Cultural Heritage may also have inadvertent adverse impacts) | No |
| 4.4 | alterations to landscapes and natural features with cultural significance? | No |
| 4.5 | utilization of tangible and/or intangible forms (e.g. practices, traditional knowledge) of Cultural Heritage for commercial or other purposes? | No |
| **Standard 5: Displacement and Resettlement** | | |
| *Would the project potentially involve or lead to:* | | |
| 5.1 | temporary or permanent and full or partial physical displacement (including people without legally recognizable claims to land)? | No |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| | | |
|---|---|---|
| 5.2 | economic displacement (e.g. loss of assets or access to resources due to land acquisition or access restrictions – even in the absence of physical relocation)? | No |
| 5.3 | risk of forced evictions?[19] | No |
| 5.4 | impacts on or changes to land tenure arrangements and/or community based property rights/customary rights to land, territories and/or resources? | No |
| **Standard 6: Indigenous Peoples** | | |
| *Would the project potentially involve or lead to:* | | |
| 6.1 | areas where indigenous peoples are present (including project area of influence)? | No |
| 6.2 | activities located on lands and territories claimed by indigenous peoples? | No |
| 6.3 | impacts (positive or negative) to the human rights, lands, natural resources, territories, and traditional livelihoods of indigenous peoples (regardless of whether indigenous peoples possess the legal titles to such areas, whether the project is located within or outside of the lands and territories inhabited by the affected peoples, or whether the indigenous peoples are recognized as indigenous peoples by the country in question)?<br>*If the answer to screening question 6.3 is "yes", then Standard 6 requirements apply, and the potential significance of risks related to impacts on indigenous peoples must be Moderate or above.* [*] | No |
| 6.4 | the absence of culturally appropriate consultations carried out with the objective of achieving FPIC on matters that may affect the rights and interests, lands, resources, territories and traditional livelihoods of the indigenous peoples concerned? | No |
| 6.5 | the utilization and/or commercial development of natural resources on lands and territories claimed by indigenous peoples? | No |
| 6.6 | forced eviction or the whole or partial physical or economic displacement of indigenous peoples, including through access restrictions to lands, territories, and resources?<br>*Consider, and where appropriate ensure, consistency with the answers under Standard 5 above* | No |
| 6.7 | adverse impacts on the development priorities of indigenous peoples as defined by them? | No |
| 6.8 | risks to the physical and cultural survival of indigenous peoples? | No |
| 6.9 | impacts on the Cultural Heritage of indigenous peoples, including through the commercialization or use of their traditional knowledge and practices?<br>*Consider, and where appropriate ensure, consistency with the answers under Standard 4 above.* | No |
| **Standard 7: Labour and Working Conditions** | | |
| *Would the project potentially involve or lead to: (note: applies to project and contractor workers)* | | |
| 7.1 | working conditions that do not meet national labour laws and international commitments? | Yes |
| 7.2 | working conditions that may deny freedom of association and collective bargaining? | Yes |
| 7.3 | use of child labour? | Yes |
| 7.4 | use of forced labour? | No |
| 7.5 | discriminatory working conditions and/or lack of equal opportunity? | Yes |
| 7.6 | occupational health and safety risks due to physical, chemical, biological and psychosocial hazards (including violence and harassment) throughout the project life-cycle? | Yes |

[*] Note: revised July 2022 modifying presumption of risk significance from Substantial or higher to Moderate or higher.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

[19] Forced eviction is defined here as the permanent or temporary removal against their will of individuals, families or communities from the homes and/or land which they occupy, without the provision of, and access to, appropriate forms of legal or other protection. Forced evictions constitute gross violations of a range of internationally recognized human rights.

| **Standard 8: Pollution Prevention and Resource Efficiency** | | |
|---|---|---|
| *Would the project potentially involve or lead to:* | | |
| 8.1 | the release of pollutants to the environment due to routine or non-routine circumstances with the potential for adverse local, regional, and/or transboundary impacts? | Yes |
| 8.2 | the generation of waste (both hazardous and non-hazardous)? | Yes |
| 8.3 | the manufacture, trade, release, and/or use of hazardous materials and/or chemicals? | No |
| 8.4 | the use of chemicals or materials subject to international bans or phase-outs?<br>*For example, DDT, PCBs and other chemicals listed in international conventions such as the Montreal Protocol, Minamata Convention, Basel Convention, Rotterdam Convention, Stockholm Convention* | No |
| 8.5 | the application of pesticides that may have a negative effect on the environment or human health? | No |
| 8.6 | significant consumption of raw materials, energy, and/or water? | No |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

## Annexure 3: Risk Analysis.

The below matrix represents risks that may impact the project.

| RISKS | Risk Severity (Likelihood, Consequence and rating) | MITIGATION STRATEGY | Risk Owner |
|---|---|---|---|
| **Contextual Risks:** Existing and emerging uncertainties that could facilitate or hinder progress towards the development priorities of a given society. ERM considers contextual risk when these external uncertainties also present institutional or programmatic risks. | | | |
| Changes in the political landscape negatively may impact project implementation | Likelihood: moderately likely<br>Impact: intermediate<br>Risk rating: Moderate | • NDP CO liaises with UNCT, UNAMA, DPPAs and donors on the political situation to ensure consistency across the UN in matters related to the de-facto authorities<br>• egular Joint communique are issued by UNDP/UNCT/UNAMA on positioning concerning the de-facto authorities – (CO)<br>• RMU political situation assessment and information shared with CO Management and programme staff at Kabul and regional level<br>• RMU political situation assessment and information shared with CO Management and programme staff at Kabul and regional level<br>• lose collaboration across UN system organisations and timely information sharing<br>• ctive/passive defensive controls and monitoring, including robust cyber/information security management protocols. (UNDP CO) | Project Manager<br>(in collaboration with UNDP CO) |
| Harsh weather conditions may slow down project implementation | Likelihood: moderately likely<br>Impact: intermediate<br>Risk rating: Moderate | • detailed project implementation plan will be developed considering the weather and natural hazards (earthquakes).<br>• roject to remain flexible to respond to natural disasters.<br>• evelopment of a contingency plan with timelines and possible alternative locations to be put in place. | Project Manager<br>(in collaboration with UNDP CO) |
| The security situation may deteriorate due to increased terrorist activities or armed | Likelihood: moderately likely<br>Impact: intermediate | • The engaged vendor must ensure the safety and security of its staff personnel.<br>• Based on the security scenario, vendors should continue to | Project Manager<br>(in collaboration with UNDP CO) |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| RISKS | Risk Severity (Likelihood, Consequence and rating) | MITIGATION STRATEGY | Risk Owner |
|---|---|---|---|
| conflict | Risk rating: Moderate | communicate and seek alternative solutions to complete the project safely.<br>• Closely monitor the security situation in the project locations in collaboration with area security focal points, UNDP security and UNDSS.<br>• Deliver project activities based on the programme criticality assessment (updated regularly)<br>• Regular conflict sensitivity/do no harm risk analysis (IRMU) and timely relevant information sharing with regional offices<br>• Through the collaborative efforts under UNCT, CO with de-facto administration will advocate for the project, type of interventions, and protection of IPs and UN staff.<br>• Regular communication protocol and hotline with authorities at local, regional and central levels will be established. | |
| | | | |
| **Programmatic risks (as per the Results matrix):** Existing and emerging uncertainties that could facilitate or hinder the realization of programme or project objectives | | | |
| A weak banking system and existing restrictions may impact in-country financial transactions and access to funds | Likelihood: Highly likely<br>Impact: Extensive<br>Risk rating: Substantial | • NDP has been exploring the possibilities of other banks in addition to AIB. An assessment is ongoing.<br>• N will employ multiple money service providers through strict due diligence processes, and identify a variety of cash disbursement modalities.<br>• tilise overseas payments for international procurements | Project Manager<br>(in collaboration with UNDP CO) |
| Changes in import and exports policy and regulations influencing the supply chain | Likelihood: low<br>Impact: intermediate<br>Risk rating: Moderate | • ndp as other un agencies closely monitors the changes in policies by DFA<br>• losely engage and coordinate with DFAs on these issues<br>• scalate as necessary | Project Manager<br>(in collaboration with UNDP CO) |
| Possible increased pressure to access project resources or benefit from project interventions | Likelihood: highly likely<br>Impact: extensive<br>Risk rating: Substantial | • nsure compliance with principles of engagement as agreed across the UN under the Transitional Engagement Framework (TEF) or any other UN strategic planning beyond 2022. | Project Manager<br>(in collaboration with UNDP CO) |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| RISKS | Risk Severity (Likelihood, Consequence and rating) | MITIGATION STRATEGY | Risk Owner |
|---|---|---|---|
| | | • Set up clear and transparent criteria in selecting the location, and project health/education centres as direct beneficiaries of the project.<br>• Closely monitor the delivery of equipment/installation to the identified beneficiary, with a clear sustainability plan. | |
| Fiduciary risk<br>*that funds are not used for the intended purpose and/or are not properly accounted for, including* procurement Risks: (e.g., Price fixing, bid-rigging, market sharing, collusion, extorsion, false invoices shell companies; false financial statements, inaccurate qualifications and experience representation, bid security etc.) | Likelihood: Expected<br>Impact: Extensive<br>Risk rating: Substantial | • UNDP has a specialised team to conduct due diligence before engagement with contractors and Implementing partners, as well as throughout the implementation.<br>• Anti-fraud training (such as provided by the IRMU) to its counterparts including staff and contractors understand what constitutes fraud, what a zero-tolerance policy is, and employees know where to seek advice, should it be needed.<br>• UNDP has established processes and tools to communicate concerns about known or suspected fraud; introduce multiple reporting channels (e.g. independent, the third party means) such as telephone hotlines, email, and the provision of trusted local 'informants'<br>• Application of aggressive measures against fraudulent conduct; surprise visits, regular, special and forensic audits, investigations;<br>• Project management shall undertake continuous oversight of controls on procurement, accounts, transactions, and project results under the organization's requirements and additional risk mitigation measures, information sharing and face consequences of fraudulent behaviour.<br>• The project will undertake regular reviews on the risk of fraud and adjust the mitigation measures | Project Manager<br>(in collaboration with UNDP CO) |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| RISKS | Risk Severity (Likelihood, Consequence and rating) | MITIGATION STRATEGY | Risk Owner |
|---|---|---|---|
| | | accordingly.<br>• Market survey to be undertaken by the regional staff competition among retailers; monitor, identify and disqualify offending retailers<br>• Monitor to identify occasional or systematic abuse; disqualify if systematic abuse is found; review targeting and programmatic assumption<br>• Implement internal controls that promote transparency and accountability (e.g. penalties, civil society oversight, information verification)<br>• Implement robust risk management at all the levels – local, regional, and centre and through the processes<br>• Apply adaptive management based on timely, accurate and relevant risk information. | |
| Technical risks resulting in delays or shortfalls in targeted achievements due to factors such as non suitability of building structure or land available for installations of the systems | Likelihood: Highly likely<br>Impact: extensive<br>Risk rating: Substantial | • Site assessment will be conducted to the facilities before finalization of the list of facilities for installations;<br>• Robust screening criteria applying the priorities listed in the 'Technical Selection Criteria' will be applied for the selection of facilities. Facilities that do not meet the readiness criteria will be omitted.<br>• UNDP will launch a Expression of Interest (EOI) process among the potential vendors/contractors to identify the market capacity and select a list of qualified contractor.<br>• Using knowledge and experience from the past project/activities implementation, UNDP will include the 'Operation and Maintenance training' as a part of the contract during the supply and installations of equipment.<br>• Quality assurance and third party | Project Manager |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| RISKS | Risk Severity (Likelihood, Consequence and rating) | MITIGATION STRATEGY | Risk Owner |
|---|---|---|---|
| | | monitoring at every stage of project cycle will also enable timely mitigation of any potential deviation from realizing the targets | |
| Not enough suitable locations can be identified due to the lack of accessibility in the project locations, restrictions imposed by the DFA or any other political or security developments; the project may not meet the target/objectives leading to contractual issues; UNDP reputational damage, lack of trust and cost implications | Likelihood: Highly likely<br>Impact: extensive<br>Risk rating: Substantial | • During the inception phase, the project will critically review the site and facility identification criteria.<br>• ESMP implementation will be closely monitored by a team of experts.<br>• Depending on the site and identified challenges, engagement with the community groups would be undertaken as required.<br>• Raise project awareness at all levels.<br>• Apply an adaptive and flexible approach in the implementation of the project in close consultation with the donor. | Project Manager |
| **Risk of Elite Capture –** potential links between political/business/NGO communities | Likelihood: Highly likely<br>Impact: extensive<br>Risk rating: Substantial | • Strengthen monitoring mechanisms through field offices, community organizations, TPM and other tools.<br>• Sustained / Tailored risk management technical assistance to RP/IPs.<br>• IRMU has set up the tools and a network with internal (within the UN) and external partners on information sharing (formal and informal) to ensure verifications and data triangulation on hidden ownerships, money tracking, AML/CFT, compliance with sanctions regimes, etc, as well as gained access to restricted and confidential information. | Project Manager<br>(in collaboration with UNDP CO) |
| Limited pools of contractors/IPs | Likelihood: less likely<br>Impact: intermediate<br>Risk rating: Moderate | • UNDP maintains a roster of contractors, NGOs and consultants which have been assessed and screened by the IRMU to ensure compliance with sanctions regimes for Afghanistan.<br>• UNDP has access to UN-wide contractors that are being utilised by other UN Agencies in Afghanistan. | Project Manager<br>(in collaboration with UNDP CO) |
| Low quality or non-compliance of international quality assurance standards of | Likelihood: less likely<br>Impact: Minor | • Available technical experts in renewable energy, procurement, and the project team will establish requirements and technical specifications against international | Project Manager<br>(in collaboration with |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| RISKS | Risk Severity (Likelihood, Consequence and rating) | MITIGATION STRATEGY | Risk Owner |
|---|---|---|---|
| procured solarization systems | Risk rating: low | quality assurance standards (e.g., ISO, QMS, etc.)<br>• Data and reports from site visits will be incorporated into the solicitation document to ensure an effective and compliant procurement outcome<br>• Conduct pre-contract award meeting with the vendor to verify and streamline the understanding of requirements<br>• Third-party independent spot checks and quality inspection before receipt and payment of procured solarization systems | UNDP CO) |
| The possibility that the project may cause adverse negative impact/cause harm to people and the environment | Likelihood: moderately likely<br>Impact: intermediate<br>Risk rating: Moderate | • A continuous “dynamic impact, conflict & risk monitoring capacity” and adaptive management processes will be established.<br>• Activities which have the potential to capacitate or trigger human rights violations will be excluded.<br>• Risk will be jointly identified and endorsed, and the burden will be shared with key partners (donors).<br>• The CO will engage in gradual confidence building and discuss sensitive topics (such as training offered to Taliban middle-management that addresses HR considerations).<br>• Adhere to and uphold UNDP’s commitment to mainstream social and environmental sustainability (SES) in programme implementation as ESMF/ESMP and GRMs.<br>• Strictly apply SES procedure and key mechanisms to all sites. Minimize and mitigate negative impacts where avoidance is not possible<br>• Undertake a thorough analysis of conflict sensitivity and do-no-harm.<br>• Engage in technical experts (via regional LTA, expert roster, etc.) to support SES compliance through project design and implementation.<br>• Conduct site survey, pre-design, feasibility reports, etc. before solarization system implementation, and incorporate findings into a procurement solicitation document | Project Manager<br>(in collaboration with UNDP CO) |
| Project implementation may be delayed due to multiple risk drivers: | Likelihood: Moderately likely<br>Impact: Intermediate<br>Risk rating: | • IRMU, project and regional teams closely monitor political and security situations in the project locations<br>• Develop a contingency plan as an integral part of the project implementation plan.<br>• Ensure that hiring of the project | Project Manager<br>(in collaboration with UNDP CO) |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| RISKS | Risk Severity (Likelihood, Consequence and rating) | MITIGATION STRATEGY | Risk Owner |
|---|---|---|---|
| | Moderate | implementation is completed within the agreed timelines.<br>• Proactive engagement with the selected vendors/IPs and agreement on a mechanism of ensuring timely provision of services and completion of the project.<br>• UNDP and PIU regularly monitor the project progress and ensure that the implementation phases are completed within the agreed timeframe. | |
| **Institutional risks:** Existing and emerging uncertainties that could facilitate or hinder the efficiency and effectiveness of core operations within the organization | | | |
| The risk of not achieving project results as planned (in terms of time and quality) | Likelihood: Moderately likely<br>Impact: Intermediate<br>Risk rating: Moderate | • UNDP has adapted its approach to responding to the operational environment post 15 August 2021 through enhancing project monitoring, due diligence, risk management and compliance.<br>• A risk-based decision-making approach has been put in place.<br>• Systems for regular monitoring, data collection and quality assurance have been developed<br>• Compliance with donor reporting requirements and regular updates.<br>• Strengthened internal control and implementation of three lines of defence model (3LoD) are being implemented. | Project Manager<br>(in collaboration with UNDP CO) |
| UNDP may fail to meet donor contractual arrangements | Likelihood: Not likely<br>Impact: Minor<br>Risk rating: Low | • Close monitoring of the agreement and ensuring compliance with contractual obligations.<br>• Ensure quality of reporting and oversee data accuracy in donor reporting.<br>• Bring to the attention of the donor any challenges that may affect the timelines and the quality of the project deliverables. | Project Manager<br>(in collaboration with UNDP CO) |
| • Reputational:<br>• Possible Exposure to entities involved in money laundering and terrorism financing | • Low Likelihood<br>• Impact: Intermediate<br>• Risk rating: | • Assess all counterparties against ML/FT risk and escalate as necessary at the AML/CFT Corporate Unit<br>• Screen all counterparties and their associated individuals in the IRMU database which include the following sources: UNSC, EU, OFAC and UK | Integrated Risk Management Unit |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| RISKS | Risk Severity (Likelihood, Consequence and rating) | MITIGATION STRATEGY | Risk Owner |
|---|---|---|---|
| | Moderate | sanctions and restrictions; UN/WB debarments and UNDP interim suspensions<br>• Collect the necessary information by applying the Counterparties Information Form introduced to the UNDP AML/CFT Policy, and through open and restricted sourcesfor identification of beneficiary ownership. | |
| Procurement Risks: e.g., Price fixing, bid-rigging, market sharing, collusion, extorsion, false invoices shell companies; false financial statements, inaccurate experienced representation, bid security etc. | | | |
| Recipient/IP risk management procedures and/or failure to adhere to procedures (based on the partner assessments and risk assessments the partner risk rating remains significant to high) | Likelihood: less likely<br>Impact: intermediate<br>Risk rating: Moderate | • Enhanced due diligence through the establishment of the IRMU to support UNDP activities<br>• Introduction of additional controlling mechanisms through strengthening protocols, internal controls and three lines of risk management. Make increased use of common risk management tools (common minimum information tool end documentation submission by the contractors/RPs, CIMS, risk management and due diligence capacity building)<br>• Development of a UNDP Afghanistan Adaptive Management and Risk Mitigation strategy realigned with the UNDP ERM accountability mechanism and best practices from Afghanistan and other countries. | Project Manager<br>(in collaboration with UNDP CO) |
| Extensive links between political/business/NGO communities | Likelihood: Highly likely<br>Impact: extensive<br>Risk rating: Substantial | • Strengthen monitoring mechanisms through community organisations, TPM and other tools.<br>• Sustained / Tailored risk management technical assistance to RP/IPs. | Project Manager<br>(in collaboration with UNDP CO) |
| Limited pools of contractors/IPs | Likelihood: Highly likely<br>Impact: extensive<br>Risk rating: Substantial | • Information sharing between fund recipients of best practices in fraud detection/reporting and enhanced due diligence procedures (CIMS). | Project Manager (in collaboration with UNDP CO) |
| Low quality or non-compliance with international quality assurance standards of | Likelihood: less likely<br>Impact: intermediate | • Available technical experts in renewable energy, procurement, and the project team will establish requirements and technical specifications against international | |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| RISKS | Risk Severity (Likelihood, Consequence and rating) | MITIGATION STRATEGY | Risk Owner |
|---|---|---|---|
| procured solarization systems | Risk rating: Moderate | quality assurance standards (e.g., ISO, QMS, etc.)<br>• Data and reports from site visits will be incorporated into the solicitation document to ensure an effective and compliant procurement outcome<br>• Conduct pre-contract award meeting with the vendor to verify and streamline the understanding of requirements<br>• Third-party independent spot checks and quality inspection before receipt and payment of procured solarization systems | |
| The adverse negative impact on people and the environment | Likelihood: less likely<br>Impact: intermediate<br>Risk rating: Moderate | • Adhere to and uphold UNDP's commitment to mainstream social and environmental sustainability (SES) in programme implementation.<br>• Strictly apply SES procedure and key mechanisms to all sites. Minimize and mitigate negative impacts where avoidance is not possible<br>• Engage in technical experts (via regional LTA, expert roster, etc.) to support SES compliance through project design and implementation.<br>• Conduct site survey, pre-design, feasibility reports, etc. before solarization system implementation, and incorporate findings into a procurement solicitation document | |
| Security or political unrest caused stopping in work and implementation | Likelihood: Highly likely<br>Impact: extensive | • The engaged vendor must ensure the safety and security of its staff personnel.<br>• Based on the security scenario, vendorsshould continue to communicate and seek alternative solutions to complete the project safely. | Project Manager<br>(in collaboration with UNDP CO) |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

# Annexure 4: Capacity Assessment

Results of capacity assessments of Implementing Partner (including Partner Capacity Assessment Tool (PCAT) and HACT Micro Assessment)

**Not Applicable**

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

# Annexure 5: TORs of key management position

**Project Manager (ToRs)**

**Summary of Key Functions:**

**In this role the Project Manager will be responsible for project management ensuring quality and results by:**

- Overseeing and managing of the project on day-to-day basis;
- Overseeing monitoring and evaluation activities of the project;
- Managing partnerships, policy, resource mobilization and advocacy efforts, and;
- Facilitating knowledge management and sharing.

**Duties and Responsibilities:**

Under the overall strategic guidance of the Country Director, and the day-to-day supervision of the Deputy Country Director, the Project Manager has the following duties and responsibilities:

**Oversee and manage the project on day-to-day basis**

- Manage the project team (technical specialists, project officers, support staff, consultants) and ensure timely implementation, results –orientation and accountability for project results;
- Lead the development of annual programme/project delivery targets and guide the team to achieve the targets;
- Set direction for the team including roles and responsibilities, accountability and reporting ensuring that the work of the team is conducted in accordance with UNDP's relevant business processes and that high – quality outputs are delivered on time;
- Guide the project staff to perform project oversight, quality assurance, monitoring, reporting, field missions, audits, evaluations, formulations and project support services providing day-to-day guidance by enhancing team work within the project and with other Country Office units;
- Monitor the progress on agreed results framework and performance indicators and take action/decision and/or provide timely support to project staff;
- Undertake performance management of staff including establishment of annual results, on-going feedback and mid-term and final assessments in line with UNDP Rules and Regulations;
- Provide intellectual and strategic guidance in the area of economic empowerment and private sector development, prompting gender equality and inclusion of marginalized populations ensuring conflict – sensitivity and compliance with UNDP's Social and Environmental standards and other rules and regulations;
- Ensure project meets expectations with respect to quality, budget, delivery timelines, and strategy;
- Brief and consult with senior management on project progress and provide information and advice as required to contribute to the Country Office initiatives;
- Guide on ways to incorporate and apply HRB/RBM/M(S(DG) approaches as well as addressing cross cutting themes (e.g. gender) in project design and project activities;
- Identify areas of improvement by applying best practices/lessons learnt using UNDP corporate monitoring tools and corporate reports;
- Manage project budgets and ensure timely and accurate reporting, and;
- Undertake and supervise financial and administrative tasks including ATLAS transactions.

**Manage partnerships, policy, resource mobilization and advocacy efforts**

- Advise, guide and provide support in partnerships with the private sector and specific project partners;
- Seek engagement to promote social business opportunities in India;
- Provide policy advice to UNDP and the project to enable private sector engagement and Public

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

Private Dialogue;

- Set and manage donor expectations and manage day-to-day donor interaction;
- Seek and identify additional partnership and funding opportunities, and oversee the preparation of funding proposals, donor briefing and presentations in support of resource mobilization to advance UNDP's and the project goals;
- Mobilize, foster and strengthen strategic partnerships with UN agencies, and other relevant multilateral and bilateral organizations to advance and support the project;
- Foster and enhance collaboration with relevant Government bodies by working closely with Government counterparts and national partners;
- Establishes strong ties to and with national programmes, and relevant government ministries;
- Lead the analytical and policy development work of the project team;
- Contribute to the UNDP's work on economic empowerment and poverty reduction in support of UNDP's India country strategies, and;
- Promote the corporate social responsibility and the UN Global Compact.

**Oversee Monitoring and Evaluation activities of the project**

- Ensure close financial and procurement oversightand monitoring of all activities of the project;
- Set direction for monitoring and evaluation priorities in accordance to UNDP rules and regulations;
- Guide development of overall monitoring and evaluation systems for the project and put mechanisms in place for proper and timely reporting to the country office and the donor;
- Oversee relationships with external parties on M&E;
- Lead quarterly review meetings and annual project reviews by monitoring the progress of project implementation, assessing results and identifying areas of weaknesses to ensure the project achieves the planned results in accordance with relevant plans;
- Monitor and manage any strategic risks/issues facing the project; submit new risks/issues to the Board for consideration and decision on possible actions if required; update the status of these risks/issues by maintaining the Project Risks/Issues Log;
- Ensure project's procedural alignment with UNDP position, rules and regulations and mandate;
- Evaluate all key project deliverables, as well as final product to ensure traceability of requirements, high quality and client acceptance.

**Facilitate knowledge management and sharing**

- Ensure regular assessment of strategic, implementation, action plans identifying areas of emphasis to guide project improvements and future plans;
- Use sound judgment in all project communication and ensure that project communication meets needs of different audiences (government, private sector and so forth)
- Manage stakeholder expectations and participate in communication activities to inform stakeholders of progress and issues;
- Manage the formation of project panel of advisors to guide the work of the project
- Establish and maintain a usable, auditable and well-communicated records of the project;
    - Lead the process of knowledge creation and dissemination related to national, regional and global know-how in the subject area. In this context, partner with practitioners and members of the national think tanks, UNDP global networks, leadership of the practice and sub-practice teams in civil service, recruitment process, change management, HR policy and other related Bureaux on knowledge management services;
    - Ensure staff implementation of mandatory training and promote learning and development;
        - Ensure proper coordination with Regional Hubs and HQ;
        - Work closely and collaboratively with initiatives and institutes across UNDP systems, especially with the Istanbul Institute for Private Sector Development and UNDP's Global Alliance for Sustainable Employment (GASTE);

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

- Communicate progress, risks, expectations, timelines, milestones and other key project metrics to clients and team members;
- Organize internal and external networks or communities of practice covering prominent experts in government, non-government, think tanks, private companies, international development organizations and the UN system;
- Contribute to the development and maintenance of the programme knowledge networks and practices and development of knowledge products, and;
- Represent the project with donors, governments and national and international forums.

**Impact of Results:**

The key results of the role have an impact on the overall success of the project and directly contribute to the country office goals. In specific, the key results have an impact on design, operations and management of activities, creation of strategic long-lasting partnership as well as reaching overall project aims.

## Competencies

**Functional Competencies:**

**Job Knowledge and Technical Expertise**

- Demonstrates substantive and technical knowledge to meet responsibilities and post requirements with excellence;
- Possesses expert knowledge of advanced concepts in primary discipline, a broad knowledge of related disciplines, as well as in-depth knowledge of relevant organizational policies and procedures;
- Applies a broad knowledge of best management practices, defines objectives and workflows, positions reporting relationships in such a way as to obtain maximum effectiveness for the project;
- Keeps abreast of new developments in areas of professional discipline and job knowledge and seeks to develop her/himself personally;
- Demonstrates comprehensive knowledge of information technology and applies it in all work assignments;
- Responds flexibly & positively to change through active involvement;
- Possesses ability to lead strategic planning, result – based management and reporting;
- Possess excellent work/project planning skills;
- Demonstrates openness to change and ability to manage complex, ever-changing environments;
- Possesses ability to leadimplementation and monitoring of private sector development programmes and women empowerment programmes; and
- Possesses ability to formulate and manage budgets, and fundraise.

**Result Based Project Development and Management**

- Uses variety of UNDP resources to achieve results;
- Generates innovative, practical solutions to challenging situations
- Plans and produces quality results to meet established goals;
- Seeks and applies knowledge, information, and best practices from within and outside UNDP;
- Is highly motivated and results driven, and;
- Ensures the full implementation of project activities and financial resources to obtain results.

**Advancing a Policy – Oriented Agenda**

- Builds consensus concerning UNDP’s strategic agenda with partners on joint

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

initiatives;
- Dialogues effectively with national counterparts and other relevant stakeholders to strengthen advocacy and policy efforts, incorporating country, regional and global perspectives, and;
- Advocates for increasing priority given to human development and inclusive growth issues.

**Innovation and Judgment**
- Creates an environment that fosters innovation and creative thinking;
- Conceptualizes more effective approaches to project development, implementation and mobilization and use of resources;
- Conceptualizes and analyses problems to identify key issues, underlying problems and how they relate;
- Contributes creative, practical ideas and demonstrates sense of entrepreneurial initiative to deal with challenging situation, and;
- Strives for quality client-centered services (internal/external) when making decisions and taking action.

**Client Orientation**
- Demonstrates an understanding of client/partner/donor perspective;
- Anticipates constraints in the project delivery and identifies solutions or alternatives;
- Identifies, develops and discusses solutions for internal and external clients, and persuades management to undertake new project and services; and
- Advises and develops strategic and operational solutions with clients that add value to UNDP programmes and operations.

**Knowledge Management and Learning**
- Promotes UNDP as a learning organization;
- Participates effectively in a team-based, information-sharing environment, collaborating and cooperating with others
- Has excellent knowledge of monitoring best practices;
- Has excellent communication skills (written and oral) demonstrating sensitivity and responsiveness to all partners, and;
- Maintains respectful and helpful relationships with other UN agencies, national counterparts, civil society organizations, private sector and the donor.

**Building Strategic Partnerships**
- Makes effective use of UNDP's resources and comparative advantage to strengthen partnerships;
- Demonstrates experience of working with government counterparts especially on building successful partnerships;
- Creates networks and promotes initiatives with partner organizations, and;
- Has strong networking capabilities and ability to associate him/herself with a broad range of actors with a view to build relationships and facilitate links.

**Corporate Competencies:**
- Demonstrates integrity by modelling the UN's values and ethical standards;
- Promotes the vision, mission, and strategic goals of UNDP;
- Builds support and political acumen;
- Builds staff competences, creating an environment for creativity and innovation;
- Builds and promotes effective and emotionally intelligent teams;
- Adapts easily to rapidly changing, multiple pressing demand work context;
- Leverages conflict in the interest of UNDP and sets standards;
- Shares knowledge across the organization and builds a culture of knowledge sharing and learning;
- Examples fair and transparent decision making and calculated risk-taking, and;

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

- Displays cultural, gender, religion, race, nationality and age sensitivity and adaptability.

**Required Skills and Experience**

**Educational Qualifications:**

- Essential: Post Graduate degree (Masters) from a reputable institution preferably in business and/or economics, business administration, public policy or other related disciplines.

**Required Experience:**

- A minimum of 10 years of relevant, practical working experience within both public and private sector preferably in the Least Developed Countries (LDCs). Experience working in other Central Asian countries;
- Exposure to the design, implementation and management of pro-poor initiatives and development projects;
- Management experience of private sector development programmes or projects, and working with private foundations would be highly desirable;
- Experience working with government counterparts at high levels;
- Strong technical knowledge of at least two technical areas of the project would be desirable (skilling, job placement, women empowerment, entrepreneurship);
- Strong leadership, management and negotiation skills;
- Strong ability to work as part of a team and actively pursuing networking;
- Strong ability to lead and manage change environment;
- Experience with UNDP and a strong understanding of UNDP and its mandates, policies and procedures would be an advantage;
- Excellent computer skills and ability to use information technology as a tool and resource, and.
- Excellent analytical and problem solving skills.

**Language Required:**

- Excellent written and verbal communication skills in English.

[i] "Education." *UNICEF Afghanistan*, https://www.unicef.org/afghanistan/education.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



# Local Project Appraisal Committee Meeting (LPAC)

## Sustainable Energy Services for Education and Health in Afghanistan (SESEHA) (in short: Renewable Energy Project Afghanistan)

### Details

| | |
|---|---|
| **Programme/Project** | Sustainable Energy Services for Education and Health in Afghanistan (SESEHA) (in short: Renewable Energy Project Afghanistan) |
| **Date/Time/Location** | 08 November 2022 _ 09:00 a.m. – 10:00 a.m. (Qurban Ali Conference Room) |
| **Objective** | Adoption of renewable energy and energy efficiency measures in public facilities (primarily in health and education sectors) for sustained delivery of essential services for basic human needs in Afghanistan. |
| **Attendees** | In-Person (List provided below) |

### Attendees:

| SN | Member Name | Functional Title | Organization |
|---|---|---|---|
| **1** | Surayo Buzurukova | Senior Deputy Resident Representative (Prog.) | UNDP (Chair) |
| 2 | Usha Rao | Renewable Energy Programme Specialist | UNDP (Presenter) |
| 3 | Amanthi Wickramasinghe | Operations Manager | UNDP |
| 4 | Anisha Thapa | Quality Assurance Specialist | UNDP |
| 5 | Abdul Hameed Omar | Programme Specialist | UNDP |
| 6 | Fahad Bangash | M&E Expert | UNDP / ABADEI |
| 7 | Samila Daluwatte | SES Specialist | UNDP |
| 8 | Jesmin Aklima | Gender Specialist | UNDP / ABADEI |
| 9 | Merita Jorgo | Risk Management Advisor / Chair for LPAC | UNDP / IRMU |
| 10 | Mohammad Salim | Programme Analyst | UNDP / DEU |
| 11 | Akiko Hasegawa | Finance Specialist | UNDP / Finance |
| 12 | Syed Haroon Ahmadi | RBM Specialist (Ex-Officio) | UNDP / DEU |

**Chair:** Ms. Surayo Buzurukova Deputy Resident Representative (Programme), UNDP Afghanistan.

### Documents Submitted for LPAC Review

1. Draft Project Document
2. Design and Appraisal Project Quality Assurance (PQA) Report
3. Fragility, Conflict and Violence Matrix
4. UNDP Social and Environmental Screening Report
5. Stakeholder Engagement Plan (SEP),
6. Environment and Social Commitment Plan (ESCP)
7. Risk Analysis in the UNDP Risk register Template (Attached with Prodoc)
8. Budget and Timelines

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



## Meeting summary:

- Ms. Surayo Buzurukova thanked everyone for their contribution and Usha for taking the lead on this and moving this forward.
- Ms. Usha Rao presented the KFW Funded project on “Sustainable Energy Services for Education and Health in Afghanistan (SESEHA) (in short: Renewable Energy Project Afghanistan)”.

The presentation highlighted the following:

- Project Goals and Objectives.
- The project timeline is (from 2023 to 2028) The last six months will be for project closure.
- Project Linkage with UNDP Strategic Plan/Framework
- Project Output and activities including Theory of Change (ToC)
- Project Organizational Structure
- Baselines, Mid-Term and Terminal Evaluation
- Project budget (US $ 60.11 million).
- Preparatory work includes environmental and social management plan, Stakeholder Engagement Plan (SEP), Environment and Social Commitment Plan (ESCP) Risk Analysis in the UNDP Risk register Template

## Discussion

**Salim:**

1. The project document mentioned that the “stakeholder Engagement Plan (SEP) would be developed to identify different stakeholders and develop an approach for reaching each sub-projects as part of UNDP SES.” But the stakeholder engagement plan is already developed. Do you want to revise it, or do you like to correct the above paragraph?
2. No budget notes for each budget line are provided.
3. No Spot check and financial audit are mentioned in the project document as part of the quality assurance. However, the budget table has a USD 120,240 planned for spot check and financial audit.
4. Some of the tables are empty, for example, the direct and indirect beneficiary tables. When do you plan to collect data to fill them out?
5. Develop the ToRs of the relevant positions.

**Usha’s Response:**

1. The SEP will be updated at the time of Inception Phase once the public facilities are selected
2. The budget notes are included in the budget file.
3. Tentative beneficiaries are provided but will be assessed during the Inception Phase.
4. Draft TORs are being developed.

**Anisha**:

1. Results Matrix: I do see there is a baseline, the targets for multiple years is missing though. It is recommended to set targets, even tentative- required for ATLAS entry. You can provide targets only for 1st year.
2. Indicators for outputs are missing, she is ready to help-out on this.
3. On evaluation: at the end of phase one, is there any plan for a mid-term review?
4. Management Arrangement in the project document has missing link between Project Manager and the Board. Reporting lines of PM is not clear in the diagram.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



**Usha Rao Response:**

1. Noted on Results Matrix. Fahad will support in finalizing the same as per Anisha's inputs. However, it may be noted that the indicators might be updated based on Inception Findings.
2. Lessons learnt will be documented on continued basis and any unforeseen challenges during implementation could trigger a review as needed and not wait in terms of time frame. Also, there is a potential commitment for Phase -II (new funding) based on the Phase I implementation during the first six months. Hence, an interim review might be required to demonstrate the successes/ mitigate the challenges. The indicators are agreed with donors and are aligned with the current UNDP Strategic Plan. However, the project may include limited additional indicators as need be subject to validating during the Inception Phase.
3. Regarding the Management Arrangement/Organogram, currently it is aligned and agreed with donors, however, the UNDP approved format of organogram will be developed for internal use.

**Akiko Hasegawa**

1. The structure of the project organogram including reporting line and budget/costing of project-related staff should be aligned to avoid further confusion by the donor. (As an internal arrangement, Project Manager is not reporting to ABADEI Programme Manager, but Programme Advisor (P5) as confirmed by SDRRP).

**Usha Rao Response**

1. This organogram is as agreed with Donors, we will have one for UNDP aligned with UNDP reporting line.

**Amanthi:**

1. Is this a stand-alone project, and the project should be separated in two different phases and separate plan needs to be developed.
2. There are a couple of other legal requirements such as the legal text for DIM projects - Ops to follow up with on the requirements from internal perspective.
3. What about the project board for this upcoming project- how would the board arrangement look like?
4. Overall project document is very well developed and defined.

**Usha Rao Response**

1. Yes, this is a stand-alone project. This project document only presents the 1st phase (2023-28) as agreed with and having the commitment from KfW. The project will plan to get the procurement fast tracked and while the inception phase continues so as to seek potential commitment for Phase II (2024 – 2028). The decision on Phase II is dependent on the progress made in Phase I.
2. Project Board is not a requirement for KfW as the triggers for their attention are already agreed separately. We may however have the Project Board as part of our internal requirements.
3. The legal requirements and Risk Management such as legal text for DIM projects will be annexed to Prodoc

**Jesmin Aklima:**

1. During the project development phase gender and energy experts have already consulted and addressed many points. As situation here changes, therefore project level gender action plan has to be implemented and monitored.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



2. As the project claims to have gender marker 2 (Namely GEN2), this means it makes significant contribution to gender equality. To ensure that, the programme has to be gender responsive. Three questions should be considered for each activity implemented under each output: (i) Are we considering different needs, challenges, access and opportunities for women, men, girls, boys, ethnic and person with disabilities where we are aiming to intervene with renewable energy? (ii) Are we contributing to improve the situation from the current status quo? If yes, how? (iii) Are we substantiating the existing gender inequality, or making efforts against the odds?

## Conclusion

**Summary & Takeaways**

Following a detailed review of the project documents and its Annexes, the LPAC meeting positively appraised the project, and the Chair recommended its endorsement and approval. The revised document incorporating the changes as per the PAC minutes will be submitted for signing.
It is further noted that the revised document would incorporate the following:

- alignment of the project board diagram as per the corporate guideline,
- inclusion of the required legal annexes and
- sub indicators for Phase I

DocuSigned by:
Surayo Buzurukova
C8F21608D8FA487...

Ms. Surayo Buzurukova
Senior Deputy Resident Representative, Programme
UNDP Afghanistan

Date: 12 November 2022

**Enclosed:**

1. Project Presentation
2. Project Document – Revised
3. SESP
4. Budget
5. ESCP

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



**TEMPLATE**

**Version 2, July 2019**

# United Nations Development Programme (UNDP)
# Sustainable Energy Services for Education and Health in Afghanistan (SESEHA) (in short: Renewable Energy Project Afghanistan), 38345/201767185

## Draft

# ENVIRONMENTAL and SOCIAL COMMITMENT PLAN (ESCP)

## August 2022

**(Revised on October 26, 2022)**

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



## ENVIRONMENTAL AND SOCIAL COMMITMENT PLAN

1. The United Nations Development Programme (UNDP) Afghanistan will implement the Sustainable Energy Services for Education and Health in Afghanistan (SESEHA) (in short: Renewable Energy Project Afghanistan) (the **Project**) as the project implementing partner of **KfW Development Bank** (hereinafter KfW). KfW has agreed to provide financing for the Project.
2. UNDP will implement material measures and actions so that the Project is implemented in accordance with the UNDP's Social and Environmental Standards (SES) standards with KfW requirements. This Environmental and Social Commitment Plan (**ESCP**) sets out material measures and actions, any specific documents or plans, as well as the timing for each of these.
3. UNDP will also comply with the provisions of any other E&S documents required under the UNDP SES and KfW requirements referred to in this ESCP, such as Environmental and Social Management Framework (ESMF), Environmental and Social Management Plans (ESMP), and Stakeholder Engagement Plans (SEP), and the timelines specified in those E&S documents.
4. Implementation of the material measures and actions set out in this ESCP will be monitored and reported to KfW by UNDP as required by the ESCP and the conditions of the legal agreement, and KfW will monitor and assess progress and completion of the material measures and actions throughout implementation of the Project.
5. As agreed by KfW and UNDP, this ESCP may be revised from time to time during Project implementation, to reflect adaptive management of Project changes and unforeseen circumstances or in response to assessment of Project performance conducted under the ESCP itself. In such circumstances, UNDP will agree to the changes with KfW and will update the ESCP to reflect such changes. Agreement on changes to the ESCP will be documented in writing between KfW and UNDP. UNDP will promptly disclose the updated ESCP.
6. Where Project changes, unforeseen circumstances, or Project performance result in changes to the risks and impacts during Project implementation, UNDP shall ensure sufficient funds are available, if needed, to implement actions and measures to address such risks and impacts.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



| MATERIAL MEASURES AND ACTIONS | | TIMEFRAME | RESPONSIBILE ENTITY/AUTHORITY |
|---|---|---|---|
| **ASSESSMENT AND MANAGEMENT OF ENVIRONMENTAL AND SOCIAL RISKS AND IMPACTS** | | | |
| **1.1** | **ORGANIZATIONAL STRUCTURE**<br>Establish and maintain a Project Implementation Unit (PIU) with qualified personnel and resources to support management of Environmental, Social and Health & Safety (ESHS) risks and impacts of the Project.<br><br>The PIU will hire one Social and Environment Standard (SES) Specialist (International – P4) responsible for the Country Office's programme ESHS compliance/quality assurance. One SES Specialist (international – IPSA 10) responsible for coordinating the ESMF, SEP, GRM requirements and monitoring (incl. vendors) on and off site for the project will be hired and supported by the national level SES Specialist. Where necessary specific positions for ESHS management that are a part of the organizational structure and/or obtain external support (e. g. hiring of a dedicated E&S Specialist) will be identified. The Project Manager will have the overall oversight functions in cooperation with the Technical Lead. | *Prior to start of project implementation.*<br>*The organizational structure, including the specialists, should be maintained throughout Project implementation.* | UNDP<br><br>SES Specialist (International level – P3) will be overall responsible for CO programmes ESHS compliance/Quality Assurance at the CO level<br><br>SES Specialist (International Consultant) will be engaged to provide support in developing and coordinating ESMF, SEP, GRM requirements and monitoring (incl. vendors) on and off sites for this project. He or She will be supported by national SES Specialist (NPSA 9), SES Specialist (P3) and other relevant team members (technical specialist). Project Manager will have the overall oversight functions in cooperation with the Technical Lead |
| **1.2** | **ENVIRONMENTAL AND SOCIAL ASSESSMENT**<br>Scoping of key environmental and social (E&S) risks and impacts of the Project and identify appropriate mitigation measures to be included in the Environmental and Social Management Framework (ESMF) described in 1.3 and in line with UNDP SES and KfW requirements. The project-level ESMF will have specific requirements on the need for environmental and social risks and impacts identification, and management plans at project and sub-project levels. | *Develop ESMF by the end of inception phase for KfW's no-objection.*<br>*Implement mitigation measures as identified by the ESMF throughout the project life cycle.*<br>*Site- or subproject-specific E&S risk screening and impact assessment shall be conducted prior to commencement of sub-projects.* | UNDP<br><br>SES Specialist (International Consultant) would develop scoping of key E&S risks and impacts, E&S screening checklist and exclusion list to be included in the ESMF. |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



| MATERIAL MEASURES AND ACTIONS | | TIMEFRAME | RESPONSIBILE ENTITY/AUTHORITY |
|---|---|---|---|
| | Undertake site- or subproject-specific environmental and social risk screening using the screening tool and impact assessments for sub-projects as outlined in the ESMF in a phase wise manner.<br><br>Where legally required, UNDP will ensure that the contractor conduct Environmental and Social Impact Assessment (ESIA) for the subproject in accordance with the regulatory requirements and in-line with the international standards. | | Once sites are selected, screening would be undertaken in a phase wise manner wherein desktop review (by the national SES Specialist (NPSA 9) and SES Specialist (P 3) ) would be attempted first and followed by a site-specific assessment based on the risks and impacts.<br><br>Short term SES experts would be engaged for undertaking site or sub project specific environment and social risk screening and developing appropriate mitigation measures in line with the ESMF<br><br>Further, the SES Specialists (national SES Specialist (NPSA 9) and SES Specialist (P3)) would review the site-specific screening checklist and mitigation measures prepared by the short-term SES experts for the sub projects which will undergo a second level of review by the SES Specialist (International Consultant) to ensure it is in line with the ESMF and UNDP SES and KfW requirements. |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



| MATERIAL MEASURES AND ACTIONS | | TIMEFRAME | RESPONSIBILE ENTITY/AUTHORITY |
|---|---|---|---|
| | | | For sub-projects which might require permits/licenses, UNDP will ensure that Contractor undertakes the ESIA. SES Specialists (P3 and International Consultant) would review the ESIAs to ensure adequacy to UNDP SES and KfW requirements. |
| **1.3** | **MANAGEMENT TOOLS AND INSTRUMENTS**<br>Develop and implement the following safeguard documents and management plans for respective sub-projects, as applicable, in accordance with the Project-specific ESMF, and throughout Project preparation and implementation:<br>▪ Project-specific ESMF that is in-line with the UNDP's environmental and social risk management procedure and subject to KfW's no-objection. It should include, but not limited to the following:<br>- Project-specific organizational structure and resource planning;<br>- Overall project-wide E&S risks and impacts identification in-line with the UNDP SES and KfW requirements.<br>- Procedures for screening and categorization of E&S risks of subprojects, including the use of the screening tools (e.g. E&S Screening Checklist, UXO Clearance Form);<br>- Generic management and mitigation procedures for handling E&S risks of various categories.<br>- Labor Management Procedures including a workers' Grievance Redress Mechanism.<br>- Stakeholder Engagement Plan or Framework including a community Grievance Redress Mechanism.<br>- Waste Management Procedure (WMP); | *ESMF to be drafted and finalized at project inception, prior to start of project activities. Draft ESMF to be submitted to KfW for no-objection.*<br>*Sub-project level screening checklist should be completed when shortlisting the sub-projects.*<br>*Site/subproject - specific ESMPs shall be in place prior to start of site activities. Where contractors are involved, their requirements are to be included in the tender document and contract with the contractor.*<br>*ESMPs for the first 3 sub-projects should be submitted to KfW for their no-objection. KfW will retain the right of prior review and clearance of further sub-project ESMPs until the UNDP team can demonstrate its capacity to manage safeguards issues on its own.*<br>*Once approved, the ESMPs, the SEP and the GRM are to be carried out throughout Project implementation.* | UNDP<br><br>SES Specialist (International Consultant) would be responsible in developing the ESMF, SEP and GRM at the project inception stage.<br><br>Short term SES experts to complete the sub project level screening checklist and develop the site/sub project ESMPs and submit the same for review to SES Specialists (national SES Specialist (NPSA 9) and SES Specialist (P3)) which will undergo a second level of review by the SES Specialist (International Consultant) to ensure it is in line with the ESMF and UNDP SES and KfW requirements.<br><br>SES Specialist (International Consultant) will co-ordinate with the Project Manager to ensure that where contractors are involved, SES requirements are included in the tender document and contract. |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



| MATERIAL MEASURES AND ACTIONS | | TIMEFRAME | RESPONSIBILE ENTITY/AUTHORITY |
|---|---|---|---|
| | - Templates for site-specific mitigation measures to be included in ESMPs.<br>- Monitoring and reporting procedure.<br>- Exclusion List as part of site selection criteria.<br>- Security Management Plan.<br>▪ Filled-out Project E&S Screening Checklist following the E&S screening criteria defined by the ESMF for all sub-projects, screen project activities to determine sub-project-specific E&S risk level.<br>▪ Use UXO Clearance Form to conduct preliminary assessment on the UXO/ERW risks.<br>▪ Based on the outcome of the E&S Screening, draft, adopt, and implement the sub-project Environmental and Social Management Plan (ESMP) based on UNDP template. ESMP to be part of the tender document and contract with the contractor or implementation partner.<br>▪ The project-wide Stakeholder Engagement Plan (SEP) will be developed as part of the ESMF. However, where necessary, develop a SEP specific for a province, district or site, detailing structured approach on inclusive and participatory stakeholder engagement.<br>No civil work activities should start without having obtained confirmation of UXO/ERW clearance from a credible demining operator/UNMAS. | | First three sub project's E&S screening checklist will be reviewed by UNDP SES Specialist (national SES Specialist (NPSA 9) and SES Specialist (P3)) and thereafter undergo a second level of review by the SES Specialist (International Consultant) and then submitted for KfW review and no-objection to be obtained.<br>SES Specialist (P3 and NPSA 9) to ensure that the approved ESMP, SEP and GRM are implemented at the sub-projects throughout the project. |
| **1.4** | **MANAGEMENT OF CONTRACTORS**<br>UNDP, its contractors, implementing partners, and associated sub-contractors will comply with the ESMF and its corresponding E&S requirements per safeguard instruments related to the Project as defined in this ESCP.<br>Develop and implement procedures for managing contractors and subcontractors by the following: | *Prior to the preparation of procurement documents.*<br>*Supervise contractors throughout Project implementation.* | UNDP<br><br>SES Specialist (International Consultant ) would develop procedures relating to applicable E&S requirements to be included in the procurement and contracting process. |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



| MATERIAL MEASURES AND ACTIONS | | TIMEFRAME | RESPONSIBILE ENTITY/AUTHORITY |
|---|---|---|---|
| | • Applicable E&S requirements will be included in the procurement and contracting process including bidding documents (where applicable), for project activities.<br>• Relevant E&S requirements are included in contracts and subcontracts consistent with the requirements of UNDP SES policies and Code of Conduct.<br>• Code of Conduct are required for contractors, subcontractors, primary suppliers, and their workers. Labor Management Procedures as stipulated by the project ESMF should also apply.<br>• monitor contractor commitment and compliance with UNDP SES and KfW requirements ;<br>• providing grievance redress mechanisms (GRM) for contractors and subcontractors, affected communities and other stakeholders;<br>• Ensure contractor workforce have access to the project GRM. Make available an alternative avenue if contractor lacks the capacity to handle grievances.<br>• ensure contractors provide details on contractor's oversight on environmental, social, health and safety (ESHS) performance. | | The Contractors under the supervision of the SES Specialist (P3) would be responsible in implementation of the relevant E&S procedures onsite. The Specialist would also monitor the contractor's commitment and compliance with ESHS performance in coordination with the SES Specialist (NPSA 9) |
| **1.5** | **PERMITS, APPROVALS AND AUTHORIZATIONS**<br>UNDP through its contractors will ensure compliance all legally required permits and approvals for environmental and social clearance are obtained from relevant national authorities, pursuant to applicable national laws by the contractors. They include the clearance of unexploded ordinance (UXO) / explosive remnants of war (ERW). All permits or permissions shall be obtained before site activities begin, complying with national regulation. | *Prior to commencement of works or initiation of activities that require permits, consents and/or authorizations (confirmation sent to KfW).* | UNDP<br><br>SES Specialist (NPSA 9) in coordination with SES Specialist (P3) and Project Manager to ensure that the Contractors obtain the required permits, approvals and clearance prior to commencement of work (if in case required) at the sub project level. |
| **LABOR AND WORKING CONDITIONS** | | | |
| **2.1** | **LABOR MANAGEMENT PROCEDURES** | *Same timeframe as for the ESMF* | UNDP |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



| MATERIAL MEASURES AND ACTIONS | | TIMEFRAME | RESPONSIBILE ENTITY/AUTHORITY |
|---|---|---|---|
| | As part of the ESMF, a Labor Management Procedure (LMP) is to be developed in-line with the national legal framework and as well as the applicable UNDP policies and Code of Conduct.<br><br>LMP to be applied to project contractors and their workers.<br>Monitor and maintain compliance of the LMP throughout Project implementation. | | SES Specialist (International Consultant ) to develop the LMP and include it within the ESMF.<br><br>Once approved, the Contractor under the supervision of the Specialist (P3 and NPSA 9) to implement the LMP at all sub projects and monitor the compliance of the procedure throughout Project implementation. |
| **2.2** | **GRIEVANCE MECHANISM FOR PROJECT WORKERS**<br>Establish, maintain, and operate a grievance mechanism for Project workers (incl. community workers), as described in the LMP and SEP consistent with UNDP SES and KfW requirements. | *Grievance mechanism operational prior engaging Project workers and maintained throughout Project implementation.* | UNDP<br><br>Contractor's designated personnel to implement the GRM at the sub project level and coordinate with the SES Specialist (NPSA 9) for its adequate implementation. |
| **2.3** | **OCCUPATIONAL HEALTH AND SAFETY (OHS) MEASURES**<br>Ensure that Occupational, Health and Safety (OHS) measures specified in the ESMF and ESMP/ESCOP and developed in accordance to UNDP SES and KfW requirements are effectively communicated to the project workers and implemented. | *Same timeframe as for the implementation of the ESMP.* | UNDP<br><br>SES Specialist (International Consultant ) to develop the OHS measures.<br><br>Once approved by KfW, the SES Specialist (P3 and NPSA 9) to communicate the same to the contractors who in turn will provide dedicated trainings to the project workers. The Specialist (NPSA 9) will monitor the implementation of the OHS measures at the sub project level |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



| MATERIAL MEASURES AND ACTIONS | | TIMEFRAME | RESPONSIBILE ENTITY/AUTHORITY |
|---|---|---|---|
| **2.4** | **PROJECT WORKERS TRAINING**<br>Implement appropriate training of Project Workers designed to heighten awareness of site-specific health and safety risks and to mitigate impacts on local communities. | *Prior to commencement of works.* | UNDP<br><br>SES Specialist (P3 and NPSA 9) to provide trainings to Contractors who in turn will provide dedicated trainings and toolbox talks to project workers. |
| **RESOURCE EFFICIENCY AND POLLUTION PREVENTION AND MANAGEMENT** | | | |
| **3.1** | **WASTE MANAGEMENT PLAN**<br>As part of the ESMF, develop a Waste Management Procedure (WMP) covering both hazardous and non-hazardous wastes generated at the project sites. Requirements relevant for the Waste Electrical and Electronic Equipment (WEEE), in particular relating to solar photovoltaic (PV), will need to be considered in terms of infrastructure available at the site level and provisions of buy back policy with vendors to dispose used equipment/ waste adequately and submit a proof of payment for the same. Where applicable, incorporate the WMP into the ESMP . | Develop WMP in the same timeframe as development of the ESMF and ESMP. Implement throughout the Project. | UNDP<br><br>SES Specialist (International Consultant) to develop the WMP as part of the ESMF.<br><br>Contractors to develop site specific WMP based on infrastructure available at the site (and in line with ESMF) and provide the plan to SES Specialist (P3 and NPSA 9) for review. Vendor agreements to include provisions of buy back policy and disposal of used equipment/waste with adequate evidence which would be prepared by UNDP Country Office.<br><br>Contractors/Vendors to ensure WMP implementation in specific sub-projects. |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



| MATERIAL MEASURES AND ACTIONS | | TIMEFRAME | RESPONSIBILE ENTITY/AUTHORITY |
|---|---|---|---|
| | | | SES Specialist (P3) to ensure implementation of the WMP across all sub projects by the contractors by monitoring the same throughout the project implementation. |
| **COMMUNITY HEALTH AND SAFETY** | | | |
| **4.1** | **TRAFFIC AND ROAD SAFETY**<br>Where applicable and as part of the ESMP specified in 1.2 and based on site-specific E&S screening, develop and implement measures and actions to assess and manage traffic and road safety risks to address potential hazards for communities resulting from solar PV installation and maintenance activities. | *Same timeframe as for the implementation of the ESMP. Implementation throughout the project* | UNDP<br><br>SES Specialist (International Consultant) to develop the traffic and road safety measures as part of the ESMF.<br><br>The Contractors to develop and include site specific traffic measures in the ESMP and ensure its implementation.<br>SES Specialist (NPSA 9 and P3) to monitor that the Contractor is adequately complying with the measures across all sub projects throughout the project implementation. |
| **4.2** | **COMMUNITY HEALTH AND SAFETY**<br>Develop and implement measures and action to assess and manage specific risks and impacts to the community arising from Project activities, and include these measures in the ESMPs to be prepared in accordance with the ESMF, in-line with the international standards; this includes physical, chemical and biological hazards, litter (e.g. spread by wind), noise, dust and odours, impacts on ecosystem services such as groundwater. | *Same timeframe as for the implementation of the ESMP. Implementation throughout the project.* | UNDP<br><br>SES Specialist (International Consultant) to develop the community health and safety measures as part of the ESMF. |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



| MATERIAL MEASURES AND ACTIONS | | TIMEFRAME | RESPONSIBILE ENTITY/AUTHORITY |
|---|---|---|---|
| | | | Contractors to include the measures in the site specific ESMP and ensure implementation. SES Specialist (NPSA 9 and P3) to monitor that the measures are implemented by the contractors across all sub projects throughout the project implementation. |
| **4.3** | **GBV AND SEA RISKS**<br>.<br>Prepare, adopt, and implement a Gender-Based Violence Action Plan (GBV Action Plan), to assess and manage the risks of gender-based violence (GBV) and Sexual Exploitation and Abuse (SEA) and Sexual Harassment (SH) as part of the ESMF.<br><br>The GBV Action Plan shall include provision on GBV- sensitive grievance mechanisms (GMs) in compliance with UNDP SES and KfW requirements. GMs shall have multiple channels through which complaints can be registered in a safe and confidential manner for survivors of SEA/SH. | *Same timeframe as for the implementation of the ESMP. Implementation throughout the project.* | UNDP<br><br>UNDP Gender Specialist (Country Office) to develop the GBV Action Plan in coordination with SES Specialist as part of the ESMF.<br><br>SES Specialist (NPSA 9 and P3) to ensure implementation of the measures across all sub projects by the contractors by monitoring the same throughout the project implementation. |
| **4.4** | **UNEXPLODED ORDNANCES (UXO) AND DEMINING**<br>UNDP through its Contractors will ensure potential unexploded ordnance (UXO), or explosive remnants of war (ERW) risks are screened for all sub-projects using the UXO Clearance Form. Non-technical surveys (i. e. informal interviews with the community) would be conducted in parallel.<br>For sub-projects where UXO/ERW risks have been identified, UNDP through its contractor or implementing partner(s) (where applicable) will obtain reliable proof of UXO clearance (e. g. clearance certification or equivalent) from an accredited demining entity or will explore areas already cleared by UNMAS prior to commencement of any civil work activities. Information on UXO/ERW prevention and mitigation measures will be included in the site- or sub-project specific ESMP. | *Filled-out E&S Screening Checklists and UXO Clearance Form prepared for respective sub-projects prior to commencement of any project activities by qualified agency.*<br>*MRE is to be incorporated into the training plan of the sub-project and delivered prior to start of any commencement of project activities.* | Contractors engaged would undertake risk screening of potential unexploded ordnance (UXO), or explosive remnants of war (ERW) using the UXO Clearance Form for all sub-projects. UXO would also be responsible in providing Mine Risk Education (MRE) to all relevant project personnel for sub-projects where UXO risks have been identified, also for cases where UXO clearance certificates have been obtained |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



| MATERIAL MEASURES AND ACTIONS | | TIMEFRAME | RESPONSIBILE ENTITY/AUTHORITY |
|---|---|---|---|
| | Provide Mine Risk Education (MRE) to all relevant project personnel for sub-projects where UXO risks have been identified, also for cases where UXO clearance certificates have been obtained. MRE should be delivered by a qualified person or representative of a credible demining operator. | | The Contractor engaged will coordinate with demining agency to undertake the assessment and issue clearance certificate. |
| **4.5** | **SECURITY MANAGEMENT**<br>Where applicable, adopt and implement the Security Management Plan (SMP) to safeguard all project workers and project-affected parties as part of the ESMF. | *Maintained throughout Project implementation* | UNDP<br><br>SES Specialist (International Consultant) to develop the Security Management Plan as part of the ESMF with support from the UNDP CO Security Risk Specialist and Project Manager.<br><br>SES Specialist (NPSA 9 and P3) to ensure implementation of the measures in coordination with UNDP's security risk team across all sub projects by the contractors and monitor the same throughout the project implementation. |
| **LAND ACQUISITION, RESTRICTIONS ON LAND USE AND INVOLUNTARY RESETTLEMENT** | | | |
| **5.1** | **Land Acquisition and Livelihood Restoration**<br>The pre-selection criteria (exclusion list) would include criteria wherein areas which would trigger physical/ economic displacement are to be avoided. In addition, the E&S screening process would also act as a tool to identify and assess the risks and impacts on physical and/or economic displacement, so that impacts on this aspect can be avoided/ minimized. | *Sub-project level screening checklist should be completed when shortlisting the sub-projects and prior to selection of sites.* | UNDP<br><br>SES Specialist (International Consultant) to prepare pre-selection criteria (exclusion list) and the screening checklist as part of the ESMF. |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



| MATERIAL MEASURES AND ACTIONS | | TIMEFRAME | RESPONSIBILE ENTITY/AUTHORITY |
|---|---|---|---|
| | | | Short term SES experts to screen the sub projects/sites based on this checklist and negate the potential areas which might trigger this aspect. The screening checklist would be reviewed by SES Specialist (national SES Specialist (NPSA 9) and SES Specialist (P3)) which will undergo a second level of review by the SES Specialist (International Consultant) to ensure it is in line with the ESMF and UNDP SES and KfW requirements. |
| **BIODIVERSITY CONSERVATION AND SUSTAINABLE MANAGEMENT OF LIVING NATURAL RESOURCES** | | | |
| **6.1** | **Biodiversity Risks and Impacts**<br><br>The pre-selection criteria (exclusion list) would include criteria wherein areas which would trigger biodiversity/ecological risks and impacts are to be avoided. In addition, the E&S screening process would also act as a tool to identify and assess the risks and impacts on biodiversity and ecological aspects, so that impacts on this aspect can be avoided/ minimized. | *Sub-project level screening checklist should be completed when shortlisting the sub-projects and prior to selection of sites.* | UNDP<br><br>SES Specialist (International Consultant) to prepare pre-selection criteria (exclusion list) and the screening checklist as part of the ESMF. |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



| MATERIAL MEASURES AND ACTIONS | | TIMEFRAME | RESPONSIBILE ENTITY/AUTHORITY |
|---|---|---|---|
| | | | Short term SES experts to screen the sub projects/sites based on this checklist and negate the potential areas which might trigger this aspect. The screening checklist would be reviewed by SES Specialist (national SES Specialist (NPSA 9) and SES Specialist (P3)) which will undergo a second level of review by the SES Specialist (International Consultant) to ensure it is in line with the ESMF and UNDP SES and KfW requirements. |
| **INDIGENOUS PEOPLES/SUB-SAHARAN AFRICAN HISTORICALLY UNDERSERVED TRADITIONAL LOCAL COMMUNITIES** | | | |
| **7.1** | **INDIGENOUS PEOPLES PLAN**<br>The pre-selection criteria would include criteria wherein areas which might have an impact on land/rights/resources of indigenous people are to be avoided. In addition, the E&S screening process would also act as a tool to identify and assess the risks and impacts on indigenous people, so that impacts on this aspect can be avoided/ minimized. | *Sub-project level screening checklist should be completed when shortlisting the sub-projects and prior to selection of sites* | UNDP<br><br>SES Specialist (International Consultant) to prepare pre-selection criteria (exclusion list) and the screening checklist as part of the ESMF. |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



| MATERIAL MEASURES AND ACTIONS | | TIMEFRAME | RESPONSIBILE ENTITY/AUTHORITY |
|---|---|---|---|
| | | | Short term SES experts to screen the sub projects/sites based on this checklist and negate the potential areas which might trigger this aspect. The Screening Checklist would be reviewed by SES Specialist (national SES Specialist (NPSA 9) and SES Specialist (P3)) which will undergo a second level of review by the SES Specialist (International Consultant) to ensure it is in line with the ESMF and UNDP SES and KfW requirements. |
| **CULTURAL HERITAGE** | | | |
| **8.1** | **CHANCE FINDS**<br>The pre-selection criteria would include criteria wherein areas with cultural/historical/religious significance are to be avoided. In addition, the E&S screening process would also act as a tool to identify and assess the risks and impacts on cultural heritage, so that impacts on this aspect can be avoided/ minimized. | *Sub-project level screening checklist should be completed when shortlisting the sub-projects and prior to selection of sites* | UNDP<br><br>SES Specialist (International Consultant) to prepare pre-selection criteria (exclusion list) and the screening checklist as part of the ESMF. |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



| MATERIAL MEASURES AND ACTIONS | | TIMEFRAME | RESPONSIBILE ENTITY/AUTHORITY |
|---|---|---|---|
| | | | Short term SES experts to screen the sub projects/sites based on this checklist and negate the potential areas which might trigger this aspect. The Screening Checklist would be reviewed by SES Specialist (national SES Specialist (NPSA 9) and SES Specialist (P3)) which will undergo a second level of review by the SES Specialist (International Consultant) to ensure it is in line with the ESMF and UNDP SES and KfW requirements. |
| **FINANCIAL INTERMEDIARIES** | | | |
| **Not relevant** | | | |
| **STAKEHOLDER ENGAGEMENT AND INFORMATION DISCLOSURE** | | | |
| **10.1** | **STAKEHOLDER ENGAGEMENT PLAN**<br>As part of the ESMF, develop Stakeholder Engagement Plan (SEP) and summary reports of stakeholder consultations, prior to the commencement of the activities and at provincial or district level, embedded in E&S tools<br>The SEP will provide a guideline for meaningful consultations and engagement as well as Grievance Readiness Mechanism. | *Same timeframe as for the ESMF, prior to project work.*<br>*Prior to the commencement of project activities.* | UNDP<br><br>SES Specialist (International Consultant) to develop the SEP as part of the ESMF.<br><br>SES Specialist (P3 and NPSA 9) to ensure implementation of the SEP prior to commencement of project activities. |
| **10.2** | **PROJECT GRIEVANCE MECHANISM**<br>Prepare, adopt, maintain and operate a grievance mechanism, as described in the SEP and ESMF. | *Same timeframe as for the ESMF, prior to project implementation* | UNDP<br><br>PIU to establish the Grievance Mechanism in line with UNDP SES and KfW requirements. |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC



| MATERIAL MEASURES AND ACTIONS | | TIMEFRAME | RESPONSIBILE ENTITY/AUTHORITY |
|---|---|---|---|
| | | | SES Specialist (P3 and NPSA 9) to ensure implementation of the mechanism at the sub project level by the contractors by monitoring the same throughout the project implementation. |
| **CAPACITY SUPPORT (TRAINING)** | | | |
| **CS1** | Conduct capacity building in-line with the training plan per ESMF. It includes trainings of UNDP project team, contractors, monitoring & evaluation staffs, as well as the awareness raising on UXO and mine risks (in coordination with UNMAS). Topics on GBV and SEA should be incorporated where applicable. | *Prior to the start of project activities and during onboarding of new project staff. Conduct refresher trainings throughout the project implementation.* | UNDP<br><br>SES Specialist (P3 and NPSA 9 ) with support from SES Specialist (International Consultant) in coordination with Contractors |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

# United Nations Development Programme (UNDP)

# Sustainable Energy Services for Education and Health in Afghanistan (SESEHA) (in short: Renewable Energy Project Afghanistan)
# 38345/201767185

**DRAFT**

**PRELIMINARY STAKEHOLDER ENGAGEMENT PLAN (SEP)**

**05 September 2022** **(revised on 26.10.2022)**

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

# Table of Contents

1 INTRODUCTION/PROJECT DESCRIPTION ..... 1

**1.1 Project Background ..... 1**

**1.2 Purpose of the SEP ..... 2**

**1.3 About the Project ..... 2**

**1.4 Project Beneficiaries ..... 4**

**1.5 Potential Environmental and Social Risks and Management Measures ..... 4**

1.5.1 Environmental Risks ..... 4

1.5.2 Social Risks ..... 5

1.5.3 Environmental and Social Instruments ..... 5

**1.6 Scope and Structure of the SEP ..... 5**

2 BRIEF SUMMARY OF PREVIOUS STAKEHOLDER ENGAGEMENT ACTIVITIES ..... 6

3 REGULATORY FRAMEWORK ..... 15

**3.1 World Bank ESF Framework on Stakeholder Engagement ..... 15**

**3.2 UNDP's Social and Environmental Standards Requirements Related to Stakeholder Engagement ..... 16**

**3.3 Legal Framework ..... 17**

4 STAKEHOLDER MAPPING AND ANALYSIS ..... 19

**4.1 Stakeholder Mapping and Analysis ..... 19**

**4.2 Project-Affected Parties ..... 19**

**4.3 Other Interested Parties ..... 20**

**4.4 Disadvantaged / Vulnerable Individuals and Groups ..... 21**

**4.5 Summary of Project Stakeholder Needs ..... 23**

5 STAKEHOLDER ENGAGEMENT PROGRAM ..... 25

**5.1 Purpose and Timing ..... 25**

**5.2 Plan for Information Disclosure ..... 26**

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

**5.3 Plan for Consultations ..... 28**

**5.4 Timeline ..... 29**

**5.5 Reviews of Comments ..... 30**

6 RESOURCES AND RESPONSIBILITIES FOR IMPLEMENTING THE SEP ..... 30

7 GRIEVANCE REDRESS MECHANISM ..... 31

**7.1 Objective ..... 31**

**7.2 Principles ..... 31**

**7.3 GRM Structure for the project ..... 32**

**7.4 Channels for submitting the requests: ..... 33**

**7.5 Grievance Redressal Committees Terms of Reference ..... 34**

**7.6 GRM for SEA/SH grievances ..... 35**

**7.7 Capacity building/ Awareness ..... 35**

**7.8 GRM Reporting ..... 36**

8 MONITORING AND REPORTING ..... 37

**8.1 Involvement of Stakeholders in Monitoring Activities ..... 37**

**8.2 Reporting Back to Stakeholder Groups ..... 37**

**8.3 Reporting to the KfW ..... 37**

9 ESTIMATED BUDGET ..... 37

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

## List of Acronyms and Abbreviations

| | |
|---|---|
| AREU | Afghanistan Renewable Energy Union |
| AUB | Afghanistan United Bank |
| ABADEI | Area Based Approach to Development Emergency Interventions |
| ADB | Asian Development Bank |
| CEO | Chief Executive Officer |
| CO | Country Office |
| DABS | Da Afghanistan Breshna Sherkat |
| E&S | Environment and Social |
| ESCOP | Environment and Social Code of Practice |
| ESMF | Environment and Social Management Framework |
| ESMP | Environment and Social Management Plan |
| ESCP | Environmental and Social Commitment Plan |
| EHSG | Environmental, Health and Safety Guidelines |
| GBV | Gender Based Violence |
| GIIP | Good International Industry Practice |
| GRC | Grievance Redressal Committee |
| GRM | Grievance Redressal Mechanism |
| IP | Implementation Partners |
| IRMU | Integrated Risk Management Unit |
| ITA | Interim Taliban Administration |
| IDPs | Internally Displaced Populations |
| IRENA | International Renewable Energy Agency |
| LTA | Long Term Agreement |
| MEW | Ministry of Energy and Water |
| M&E | Monitoring and Evaluation |
| O&M | Operation and Maintenance |
| PMO | Program Management Office |
| PIU | Project Implementation Unit |
| QRTDW | Quadardan Rural Technology & Development Workshop |
| SEA/SH | Sexual Exploitation and Abuse/Sexual Harassment |
| SES | Social and Environment Standard |
| SEP | Stakeholder Engagement Plan |
| TPMA | Third-Party Monitoring Agent |
| UNCT | United Nations Country Team |
| UNDP | United Nations Development Programme |
| WMP | Waste Management Plan |
| ESS | World Bank's Environment and Social Safeguards |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

# 1 INTRODUCTION/PROJECT DESCRIPTION

## 1.1 Project Background

Afghanistan's per capita electricity consumption is at approximately 100 kWh, which is less than a tenth of the levels of neighbouring countries, which in turn is much lower than the world's average and lower than the IEA recommended provision of at least 150 kWh per person per year. Afghanistan is one of the poorest counties in terms of Multidimensional Energy Poverty[1] (Abbas et al. 2020) and remains lowest among the countries in the region. Nearly 24.5 million people in Afghanistan are not connected to the national grid, energy efficiency is significantly below the global average (1.8 vs 4.8 MJ per US$ PPP 2017), 36 percent of the population has access to clean cooking (2019), and 21 percent of the final energy consumed is from renewable sources (2018).

Energy poverty affects the quality of lives of women and men differently in varying degrees and impacts their health, employment and many basic services. Although there is lack of data on the energy poverty and its negative consequences for women and men in Afghanistan followed by August 2021; it can be assumed that women are the poorest among the poor: majority of the crisis affected population from the 24.5 million who need humanitarian assistance are women and children (UN TEF), and 85% women-headed households turned into negative coping strategies to meet their basic human needs in 2022 compared to 62% households headed by man[2]. Currently the demand for energy in the country far exceeds its supply, the transmission and distribution grid are unreliable, load shedding and outages of electricity supply are common. Many provinces[3] are not connected to the grid and are therefore largely served through local diesel generating units that increases the costs of supply. Thus, lack of access is linked to affordable energy and impedes economic, social and educational opportunities for the poor and rural residents.

Afghanistan's electricity demand is projected to grow at 12-15% annually over the next decade[4] resulting in a supply shortfall of over 6,000 MW by 2032. In the absence of an integrated/ synchronized national grid, Afghanistan is constrained to access energy sources from its different regions due to technical limitations. Improvement of the national grid will have its own benefits, but strengthening it is a long drawn and expensive (capital intensive) process. It will be necessary to supplement the grid system with expanding distributed and decentralized energy generation systems based on renewable energy sources in a context where poverty and people's ability to meet basic human needs are real. This will have both medium and longer term implications for meeting the basic needs of Afghan people sustainably, in particular, health and education as it transcends to food security and provision of other essential services (e.g., water supply).

[1] A household is identified as multidimensionally energy-poor if: (1) deprivation occurs in three of the four dimensions of indoor air pollution, education/entertainment, household appliances, and telecommunications; (2) there is also deprivation in cooking and lighting; and if (3) it is deprived in one of the two dimensions of lighting and cooking, in addition to one of any other dimensions.
2 forthcoming Rapid Gender Analysis 2022 of Gender in Humanitarian Action Group in Afghanistan, as cited in the Gender Alert 2, UN Women.
[3] The Provinces which are not connected to the National Grid and the main source of energy is mini-grids and diesel Generator are: Nooristan, Kunar, Paktika, Zabul, Orozgan, Farah, Daindi and Ghor.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

Renewable energy and energy efficiency solutions for resilience in basic services in educational and health institutions addresses the challenges of access to reliable electricity in public facilities in the education and health sectors and associated communities through the provision of decentralized and distributed renewable energy technologies and services. The proposed interventions consider gender sensitive elements as well as support job creation in renewable energy sector.

The projects' interventions will be designed to cater to the electricity needs of the targeted public facilities in education and health sectors. Educational institutions, hospitals, hostels, and community establishments would be the primary targets. All these institutions require electricity that can be met with solar energy. The size of the solar systems is estimated in the range of 5 to 650 kW, depending on the availability of hours of electricity. This would take into account energy efficiency measures such as efficient lighting, heating and other appliances. If the facilities offer potential for extending electrification to communities, this would be considered with microgrids or battery charging stations.

The Project intends to provide electricity to approximately 20,000 educational facilities and approximately 3,512 health facilities across the 8 regions and 34 provinces of Afghanistan. The project aims to benefit approximately 1.4 million and 1.68 million number of people accessing health and education services respectively and create direct employment for around 1000 people (will be re-assessed during project inception phase) across 34 provinces and trigger indirect employment. These targets would be conformed during the baseline assessment to be carried out during Inception Phase. Implementation is planned in two phases of 5 years duration each.

## 1.2 Purpose of the SEP

The purpose of Stakeholder Engagement Plan (SEP) is to identify different stakeholders and develop an approach for reaching each of the sub-projects. In simpler terms, it provides an appropriate approach for consultations and disclosure. These in turn are expected to create an atmosphere of understanding that actively involves project-affected people and other interested parties, reaching out to them in a timely manner so that each stakeholder within sub project is provided opportunities to voice their opinions and concerns. Overall, SEP serves the following purposes: i) stakeholder identification and analysis; (ii) planning engagement modalities viz., effective communication tool for consultations and disclosure; (iii) enabling platforms for influencing decisions; (iv) defining role and responsibilities of different actors in implementing the Plan; and (iv) grievance redress mechanism (GRM).

## 1.3 About the Project

The project's objective is to provide renewable energy and energy efficiency measures to public facilities (primarily in health and education sectors) for improved basic services and community resilience. Supplementing conventional sources of electricity with renewable energy-based electricity contributes to Afghanistan's energy security (with less reliance on imports), better resilience through reliable services and effective response to humanitarian and energy crisis faced by poor and vulnerable Afghans.

The Project encompasses the following outputs and activities to achieve the stated objective and outcome.

**Output 1: Health facilities and services improved through reliable access to electricity**

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

The project covers approximately 10 -15 percent of approx. 3,512 health facilities in 34 provinces that provide primary healthcare services to 30 million Afghans. It aims to address the lack of grid electricity access to an estimated 41% of the health facilities that rely on diesel generators; and provide power backup based on solar energy to the remaining 59% that have intermittent and unreliable electricity and puts many patients' lives at risk during as well as lack of treatments for want of electricity.

Energy audits, technical surveys and assessments would be carried out for devising appropriate solutions. Where feasible, turnkey solutions will be implemented within the agreed procurement approaches to determine solar power installation and battery backup capacity for reliable electricity supply to the public facilities. Load profiles would be developed for different appliances and equipments and critical loads will be identified based on feasibility analysis that will take into account the Social and Environment Standards compliance requirements. These will be supplemented with energy efficiency measures and specific needs for selective insulation and other winterization measures (not a focus and only for optimizing performance). The project estimates up to 10.5 MWp solar power - battery back-up systems to be installed for electrification of about 92 health institutions in respective phases. While supporting health facilities, the project interventions will create access to services and new opportunities for women.

Different technical packages will then be designed based on the categories of health facilities will be based on surveys and detailed assessments. Detailed feasibility study will determine the site requirements, contractual aspects, and detailed specifications. The specifications drawn will be shared with the Long-Term Agreement (LTA) holders or through competitive processes in line with the procurement strategy for receiving their offers and will be selected following standard UNDP procedures.

Coordination meetings will be carried out by consultants/ contractors with hospital administrators and officials at the Ministry of the Public Health to ensure access and follow processes stipulated.

Activity 1.1 Prioritise public facilities for installations through surveys and needs assessments
Activity 1.2 Design, feasibility, installation and commissioning including O&M (procurement in stages/ turnkey)
Activity 1.3 Contracting of services in line with the TEF arrangements (ownership, transfer and sustenance)
Activity 1.4 Monitoring results and measuring/reporting impacts

**Output 2: Schools/related educational institutions' productivity enhanced through gender inclusive energy services**

The project will install up to 7 MWp of solar power - battery back-up systems for electrification of approx. 700 educational institutions. Four categories of institutions have been identified wherein a turnkey solution approach will be adopted with checks at every stage.

Coordination meetings will be carried out by consultants/ contractors with school and university administrators and officials at the Ministry of the Education and Ministry of Higher Education to ensure processes are adequately followed.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

Activity 2.1 Prioritise public facilities for installations through surveys and need assessments
Activity 2.2 Design, feasibility, installation and commissioning including O & M (procurement turnkey)
Activity 2.3 Contracting of services in line with the TEF arrangements (ownership, transfer and sustenance)
Activity 2.4 Monitoring results and measuring/reporting impacts

**Output 3: Delivery models for O&M established through gender inclusive private sector linkages**

Improved private sector participation in energy ecosystems, after sales services, maintenance would be crucial for sustained use of the assets created through this project in various public facilities. The project will strategize efforts in assessing the risks and possibilities to enhance private sector and women's participation in the upkeep of these systems through identifying appropriate business models. This would also assess the regulations under the current regime and possible negotiations for market driven approaches.

Managing supply chain require support to local Afghan renewable energy companies, vendors and manufacturers. They will be engaged to carry out site assessments, feasibility studies, technical designs, installations and O&M in other potential sites of educational institutions and health facilities. The engagement of the private sector will promote local manufacturing and strengthen the local economy. As a result, thousands of jobs will be created that will ease the levels of extreme poverty.

Activity 3.1: Private sector platform for soliciting proposals for O&M beyond project time period
Activity 3.2: Market and capacity development for supply chain management and entrepreneurship for installation, servicing, and maintenance of solar systems

**Output 4: Project Management Support**

A dedicated team will be put in place for facilitating the implementation of the project activities under the overall organisation structure proposed. This would comprise members with engineering, procurement, environment and social safeguards expertise, monitoring and reporting specialists for effective implementation of the project interventions.

## 1.4 Project Beneficiaries

The project aims to reach approximately 0.5 million and 0.5 million beneficiaries accessing health and education services respectively. Through the proposed investments, it would create direct employment around 1000 people (will be re-assessed during project inception phase) across 34 provinces and trigger indirect employment will be much higher. These targets would be conformed during the baseline assessment to be carried out during Inception Phase.

## 1.5 Potential Environmental and Social Risks and Management Measures

### 1.5.1 Environmental Risks

Potential environmental risks are considered moderate given that the project is designed to cater to the electricity needs of the targeted public facilities in education and health sectors. The Project will focus on

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

educational institutions, hospitals, hostels, and community establishments as primary targets. All these institutions require electricity that can be met with solar energy. The size of the solar systems is estimated in the range of 5 to 650 kW, depending on the availability of hours of electricity. This would take into consideration energy efficiency measures such as efficient lighting, heating and other appliances. If the facilities offer potential for extending electrification to communities, this would be considered with microgrids or battery charging stations. The Project's adverse environmental risks and impacts are: i) risk of generation of battery waste and e-waste; and ii) risk of improper disposal of solar PV panels. With the development of Environment and Social Management Framework (ESMF), it is anticipated that risks and impacts identified would be mitigated with adequate measures in compliance with UNDP Social and Environment Standards (SES) and KfW requirements.

### 1.5.2 Social Risks

The social risks and impacts are moderate, given that it is the aim of the project to reach approximately 0.5 million and 0.5 million number of people accessing health and education services respectively and create direct employment around 1000 people (will be re-assessed during project inception phase) across 34 provinces and trigger indirect employment as well. The Project's adverse social risks and impacts are: i) triggers of impacts on land related aspects (during identification of sites) ii) discrimination of potential beneficiaries (women); ii) risk of sexual exploitation and abuse and sexual harassment (SEA/SH); iii) risk of non-compliance of labor and working conditions; iv) risk of spreading of communicable diseases especially Covid 19; and (v) Possible occurrence of conflict (including armed conflict) near identified project sites and/or terrorist attacks on project staff is also an important contextual risk that may affect safety of the project staff. Overall, the project will have significant positive benefits in the form of providing electricity needs to the targeted public facilities in education and health sectors.

### 1.5.3 Environmental and Social Instruments

The Project entails certain environmental and social (E&S) risks and potential adverse impacts. The project is assigned a Moderate Risk rating based on the environmental and social risk classification procedure. E&S risk mitigation measures will be detailed in ESMF which will include Procedures for screening and categorization of E&S risks of subprojects, including the use of the screening tools; Generic management and mitigation procedures for handling E&S risks of various categories; Labor Management Procedures including a workers' Grievance Redress Mechanism; Stakeholder Engagement Plan or Framework including a community Grievance Redress Mechanism; Waste Management Procedure (WMP); Templates for site-specific mitigation measures to be included in ESMPs/ESCOPs; Monitoring and reporting procedure; Security Management Plan and GBV Action Plan. As outlined in the Environmental and Social Commitment Plan (ESCP), these plans will be developed and implemented to ensure consistency with the UNDP's SES, KfW requirements, the Environmental, Health and Safety Guidelines (EHSGs), and other relevant Good International Industry Practice (GIIP). The E&S requirements/obligations mentioned as part of the plans are to be incorporated in the contractual agreements, responsible party agreements and consultancy Terms of Reference.

## 1.6 Scope and Structure of the SEP

Scope of the SEP shall be as outlined in the World Bank's ESS10 (as followed by KfW). The World Bank's Environment and Social Standard 10 sets out that a Borrower has to engage with stakeholders as an

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

integral part of a Project's environmental and social assessment and project design and implementation. The nature, scope and frequency of the engagement should be proportional to the nature and scale of the Project. Consultations with stakeholders have to be meaningful and be based on stakeholder identification and analysis, plans on how to engage stakeholders, disclosure of information, actual consultations, as well as responses to stakeholder grievances, and reporting back to stakeholders.[5]

In addition, the project applies UNDP's Social and Environmental Standards (www.undp.org/ses), including commitments and requirements related to meaningful, effective and informed stakeholder engagement.[6]

This document has 9 chapters which are outlined below:

- Chapter 1- This chapter serves as an Introduction. It provides a brief about the Project and the context in which the SEP is being prepared.
- Chapter 2 - A summary of the consultations held so far is presented in Chapter 2.
- Chapter 3 - Chapter 3 lists the regulatory framework UNDP (including WB ESF requirments on stakeholder engagement), which provides legitimacy for SEP. Stakeholder Mapping and Analysis is elaborated in the chapter
- Chapter 4 – Presents the stakeholder mapping and analysis
- Chapter 5 - Provides the Stakeholder Engagement program
- Chapter 6 - Details the resources and responsibilities for implementing the SEP
- Chapter 7 – Presents the Grievance Redress Mechanism (GRM)
- Chapter 8 – Details the Monitoring and reporting component of the SEP
- Chapter 9 - Presents the estimated budget of the SEP.

# 2 Brief Summary of Previous Stakeholder Engagement Activities

Under the UNDP-ADB partnership, a baseline study was undertaken by third party consultants for the recently launched $405 million grant for the "Sustaining Essential Services Delivery Project" (Support for Afghan People). As part of the baseline study, consultations were undertaken with stakeholders on the current status and challenges including opportunities and needs. The inputs from these consultations have been used to strengthen the development of the proposed approach and activities of the Project.

*Table 1. Previous Stakeholder Consultations*

[5] World Bank, Environmental and Social Framework. Setting Environmental and Social Standards for Investment Project Financing, August 2016.
[6] UNDP, Social and Environmental Standards (www.undp.org/ses), 1 January 2021 version.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| Organizations | Role | Date | Participants | Key discussion points |
|---|---|---|---|---|
| Ministry of Energy and Water (MEW) | Policy Maker and regulatory.<br>Projects design and implementation.<br>Issuing licenses and setting the tariff for IPPs and DABS. | 17 July 2022 | • DG Energy Services Regulatory<br>• Energy Programs Director<br>• Commercial Director<br>• Energy Policy Advisor<br>• Energy PPP Specialist<br>• Energy Specialist | • Overall picture of the energy sector and way forward after 15 August. Mini-Grids and community led Energy Projects and its operation and maintenance.<br>• MEW support in the overall study.<br>• Donor's support and willingness to restart the energy projects, after August 15.<br>• Licenses for new projects in all sectors i.e. Generation, Transmission and Distribution.<br>• Rooftop solar and mini-grids: MEW supports the mini-grids, but not community led mini-grid projects. Because in the past community led infrastructure projects failed due to technical issues and proper operation and maintenance issues.<br>• Current legal framework for the energy sector<br>• Stranded projects after 15 August, where in total 47 projects are stand-by due to the funding issues. MEW has start work on Kandahar Ghazni and Kajaki transmission lines, through the national budget. Due to the budget constraints, they are not able to restart other priority projects. |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| Organizations | Role | Date | Participants | Key discussion points |
|---|---|---|---|---|
| Da Afghanistan Breshna Sherkat (DABS) | Power Utility owned by the government and working under the MEW.<br>Project Implementation, Ownership and control the whole electricity network of the Country.<br>Purchasing electricity from the neighboring countries and IPPs | 20 July 2022 | • Director for Renewable Energy<br>• Energy Efficiency Manager<br>• Renewable Energy Manager | • Stranded projects and way to move forward<br>• Land allocation and legal framework for all type of energy projects<br>• Private sector engagement<br>• Budget deficit for starting new projects funded by government<br>• Incentives for private investment, investing in renewable energy<br>• Environment, risks and challenges for net metering and grid condition<br>• New five years plan which will be prepared based on current situation and grid analysis and based on that new projects will be selected.<br>• Community led and mini-grids energy projects. Risks and challenges and O&M |
| DABS | Power Utility owned by the government and working under the MEW.<br>Project Implementation, Ownership and control the whole electricity network of the Country.<br>Purchasing electricity from the neighboring countries and IPPs | 21 July 2022 | • Policy and Plan Director<br>• Deputy PMO | • Stranded Projects and reengagement of donors<br>• Affects of stranded projects on long term PPAs with neighbouring countries and regional projects and cooperation<br>• Current status of stranded projects and effect of not starting of the projects on the work which is previously done (the stranded projects are affected and all the |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| Organizations | Role | Date | Participants | Key discussion points |
|---|---|---|---|---|
| | | | | money spent on the projects will be waste due to current vandalism)<br>• Challenges for private sector for the investment in energy projects<br>• Legal framework and budget availability for the stranded projects<br>• DABS financial health and effect of political changes on DABS Operation and financial situation (Revenue, Liabilities, payments to the neighbouring countries and IPPs, DABS arears and collections etc.)<br>• Sustainability of starting new projects<br>• One national tariff for all provinces |
| Ministry of Public Health | Policy Maker and Regulatory body for the health sector,<br>Oversight on the whole health sector of the country.<br>Owner of all the government health facilities. | 5 – Sep – 2022 | • Policy and Plan Director General<br>• Hospitals Director<br>• PPP Head | • Land allocation, site identification and sustainability of the projects<br>• Past experiences and the reasons for the failure of such projects<br>• Importance of government involvement<br>• Importance of Energy for the health sector<br>• Transparency and accountability during project implementation |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| Organizations | Role | Date | Participants | Key discussion points |
|---|---|---|---|---|
| | | | | • Support required and data from the government side |
| Afghanistan Renewable Energy Union (AREU) | Promote the use of Renewable Energy (RE) in Afghanistan. To act as a lobbying union to establish Renewable Energy as a permanent pillar of Afghanistan's national energy industry. | 20 July 2022 | • AREU Manager<br>• Member AREU | • Focus of renewable energy and rooftop solar<br>• Policies and regulation for the private investment<br>• Engagement of private sector for energy sector, expectations and risks and challenges<br>• Quality assurance and operation and maintenance of rooftop and renewable projects<br>• Proper guarantee mechanisms for payments and investment for the renewable projects |
| Zolaristan | Private Company and investor in the solar projects in Afghanistan. | 21 July 2022 | • CEO<br>• Project Manager | • Current Status of Kandahar 15 MW Solar, Mazar 40 MW Solar and 20 MW Floating solar in Naghlu<br>• Willingness to restart the investment on Mazar 40 MW and Naghlu floating solar<br>• Risks and challenges faced in the implementation of Kandahar 15 MW Solar<br>• Payments for the electricity from DABS after August 15<br>• Future investment appetite and opportunities in Afghanistan |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| Organizations | Role | Date | Participants | Key discussion points |
|---|---|---|---|---|
| | | | | • Expectations from defacto and the donors' community |
| 77 Construction USA Corps | Private Investor in some solar and hydro projects and selling the electricity to the DABS | 22 July 2022 | • Project Manager | • Current status of Kajaki II, Kandahar 15 MW Solar IPP and 25 MW wind project in Herat Province.<br>• Willingness to restart the work and investment for 25 MW wind project in Herat<br>• Risks and challenges currently faced in the implementation of the IPPs<br>• Payments for the electricity from DABS after August 15<br>• Future investment appetite and opportunities in Afghanistan<br>• Expectations from defacto and the donors' community |
| Badakhshan Energy | Private investor which is responsible for whole Badakhshan electrification including generation and distribution | 22 August 2022 | • CEO<br>• Deputy CEO | • Current status of BEC Project<br>• Risks and challenges currently faced in the implementation<br>• Future investment appetite and opportunities in Afghanistan<br>• Expectations from defacto and the donors' community |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| Organizations | Role | Date | Participants | Key discussion points |
|---|---|---|---|---|
| Quatro | Private Investor in some solar and hydro projects and sells electricity to DABS | 23 July 2022 | • CEO | • Current status of Herat tracking solar, funded through USAID VGF<br>• Willingness to restart the work and investment for 25 MW tracking solar project in Herat<br>• Risks and challenges currently faced in the implementation of the IPPs<br>• Payments for the electricity from DABS after August 15<br>• Future investment appetite and opportunities in Afghanistan<br>• Expectations from defacto and the donors' community |
| UNDP Mini-Grid Team | UNDP Team members that were engaged in various projects pertaining to mini grids in Afghanistan; project implementation support/monitoring/oversight | 21 July 2022 | - | Background of ASERD, experiences of Clean Cook stoves, solar dryers and citizen's charter pilots, discussions on Shemol mini grid challenges and opportunities, planning for sustainability of future mini grids, plan for transfer of ownership, status of CF project |
| KPTL - RGM JV (Transmission Line Contractor) | Engineering, Procurement and Construction (EPC) company undertaking installation of transmission line in the Dashti Alwan to Arghandi 500 kV Transmission Line. | 22 July 2022 | • Country Manager | Status of Dashti Alwan to Arghandi 500 kV Transmission line, pressing issues in resuming project implementation, outstanding payments, storage of equipment and construction materials, banking issues, subcontracting to locals, |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| Organizations | Role | Date | Participants | Key discussion points |
|---|---|---|---|---|
| | | | | timeline for completing the remaining work |
| KEC International (Transmission Line Contractor | Private Investor invested in few donor funded contracts for grids and transmission lines and substations | 23 July 2022 | • Project Manager | • Status of Sheberghan to Dashti Alwan 500 kV Transmission line, CASA1000 lot 2 and 3, Doshi to Bamyan 220 kV transmission line projects.<br>• Pressing issues in resuming project implementation, outstanding payments, storage of equipment and construction materails, banking issues, subcontracting to locals, timeline for completing the remaining work |
| State Corps (Substation Contractor) | Private Investor invested in few donor funded contracts for grids and transmission lines and substations | 23 July 2022 | • CEO | • Status of Herat four substations in Obai, Karukh, Pashton Zarghun, Chist, and Jalalabad 220 kV substation.<br>• Pressing issues in resuming project implementation, outstanding payments, storage of equipment and construction materials, banking issues, subcontracting to locals, timeline for completing the remaining work |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| Organizations | Role | Date | Participants | Key discussion points |
|---|---|---|---|---|
| Ministry of Energy and Water | Same as above | 26 July 2022 | • DG Energy Services Regulatory | Latest updates about the legal framework of the energy sector, changes, amendments in laws, regulations and policies of MEW. De Facto Authorities policy about IPPs |
| Program Management Office of DABS | Same as above | 27 July 2022 | • Director of PMO | Status of stranded projects of ADB, World Bank, USAID and KfW. New changes in PMO's structure. Outstanding payment. Legal and contractual implications of stranded projects. |
| Ministry of Mines and Petroleum | Manager of all-natural resources in Afghanistan and committed to performing its responsibilities for sustainable usage of the resources (Minerals and Hydrocarbons) to sustain financial growth and the balance payment. | 28 July 2022 | • TAPI Gas pipeline Focal Point | Status of TAPI Gas pipeline, updates on host government agreements. Land acquisition. Commencement of work for from Torghundi to Herat city. |
| Shemol community | Experience of the beneficiaries of Shemol mini grid project | 27 July 2022 | • Village Elders | Experience sharing of communities on use of electrical appliances, visit to a household to see the appliances, satisfaction with the electrification, demand to extend to unserved villages |
| Expert | Experienced personnel well versed with GIZ energy portfolio in the pre-Taliban regime; share lessons learned and good practices | 20 July 2022 | • Ex-Deputy CD- GIZ, Current CD-Phelan Energy | GIZ's energy portfolio pre-Taliban regime, discussion on GIZ's capacity building, policy and planning initiatives, experience with MHPs and small scale solar, challenges faced by Phelan as private sector |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| Organizations | Role | Date | Participants | Key discussion points |
|---|---|---|---|---|
| Expert | Experienced personnel well versed with the regulatory requirements and mechanism to engage with donors and private sectors share lessons learned and good practices | 19 July 2022 | • Ex-CEO DABS | Amendments in the Laws, mechanism to engage with donors and private sector |
| Envirofit India Pvt Ltd | Social enterprise institution experienced in providing clean cooking appliances to communities in Afghanistan as part of UNDP's project. | 09 August 2022 | • CEO | Discussions about UNDP's pilot clean cook stove project, plan for JV with local company |
| Afghanistan United Bank | Commercial bank of Afghanistan that provides investment to energy projects | 22 August 2022 | • CEO | Interest of AUB to support private sector in energy projects particularly in overseas payments, LCs etc. Plea to the donors to start infrastructure projects so that lending, deposits etc. |
| Quadardan Rural Technology & Development Workshop (QRTDW) & Ludin Consulting | Development center for local people of Afghanistan in order to familiarize technology amongst them | 25 July 2022 | • CEO<br>• MD | Challenges and opportunities for local RE industry in Afghanistan, potential projects for small scale RE and for economic development |
| Expert | Experienced personnel working on solar projects in Afghanistan -share lessons learned and good practices | 17 July 2022 | • Technical Expert | Status and challenges for solar projects in Afghanistan with focus on Kandahar IPPs and roof top solar |

# 3 Regulatory Framework

Considering that KfW follows World Bank ESF Framework as part of their Environment and Social Sustainability requirement, compliance to World Bank ESF Framework has been considered in the preparation of the SEP.

## 3.1 World Bank ESF Framework on Stakeholder Engagement

The World Bank Environmental and Social Standard (ESS) 10, "Stakeholder Engagement and Information Disclosure", recognizes "the importance of open and transparent engagement between the Borrower and

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

project stakeholders as an essential element of good international practice" (World Bank, 2017: 97). Specifically, the requirements set out by ESS10 are the following:

- Borrowers will engage with stakeholders throughout the project life cycle, commencing such engagement as early as possible in the project development process and in a timeframe that enables meaningful consultations with stakeholders on project design. The nature, scope and frequency of stakeholder engagement will be proportionate to the nature and scale of the project and its potential risks and impacts.
- Borrowers will engage in meaningful consultations with all stakeholders. Borrowers will provide stakeholders with timely, relevant, understandable, and accessible information, and consult with them in a culturally appropriate manner, which is free of manipulation, interference, coercion, discrimination, and intimidation.
- The process of stakeholder engagement will involve the following, as set out in further detail in this ESS: (i) stakeholder identification and analysis; (ii) planning how the engagement with stakeholders will take place; (iii) disclosure of information; (iv) consultation with stakeholders; (v) addressing and responding to grievances; and (vi) reporting to stakeholders.
- The Borrower will maintain and disclose as part of the environmental and social assessment, a documented record of stakeholder engagement, including a description of the stakeholders consulted, a summary of the feedback received and a brief explanation of how the feedback was taken into account, or the reasons why it was not." (World Bank, 2017: 98).

A Stakeholder Engagement Plan proportionate to the nature and scale of the project and its potential risks and impacts needs to be developed by the Borrower. It has to be disclosed as early as possible, and before project appraisal, and the Borrower needs to seek the views of stakeholders on the SEP, including on the identification of stakeholders and the proposals for future engagement. If significant changes are made to the SEP, the Borrower has to disclose the updated SEP (World Bank, 2017: 99). KfW will be consulted post appraisal stage, on the disclosure modalities to be adopted for this project and align it with the requirements of UNDP. According to ESS10, the Borrower should also propose and implement a grievance mechanism to receive and facilitate the resolution of concerns and grievances of project-affected parties related to the environmental and social performance of the project in a timely manner (World Bank, 2017: 100).

For more details on the WB Environmental and Social Standards, please follow the below links:

www.worldbank.org/en/projects-operations/environmental-and-social-framework/brief/environmental-and-social-standards and http://projects-beta.vsemirnyjbank.org/ru/projects-operations/environmental-and-social-framework/brief/environmental-and-social-standards

## 3.2 UNDP's Social and Environmental Standards Requirements Related to Stakeholder Engagement

The UNDP Social and Environmental Standard (SES), Part C, on Social and Environmental Management System requires meaningful, effective and informed participation of stakeholders in the formulation and implementation of UNDP programmes and projects. Stakeholder engagement is an ongoing process that may involve, to varying degrees, the following elements: stakeholder analysis and planning, disclosure and dissemination of information, consultation and meaningful participation, dispute resolution and

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

grievance redress, ongoing reporting to affected communities and stakeholders, and inclusion of stakeholders in monitoring and evaluation.

Stakeholder analysis and engagement is to be conducted in a gender-responsive, culturally sensitive, non-discriminatory and inclusive manner, ensuring that potentially affected vulnerable and marginalized groups are identified and provided opportunities to participate. Measures are to be undertaken to ensure that effective stakeholder engagement occurs where conditions for inclusive participation are unfavorable.

Meaningful, effective and informed stakeholder engagement and participation is to be undertaken that seeks to build and maintain over time a constructive relationship with stakeholders, with the purpose of avoiding or mitigating any potential risks in a timely manner. The scale and frequency of the engagement should reflect the nature of the activity, the magnitude of potential risks and adverse impacts, and concerns raised by affected communities.

Meaningful, effective and informed consultation processes in UNDP programmes and projects aims to identify priorities of stakeholders and provide them with opportunities to express their views at all points in the programme and/or project decision-making process on matters that affect them and allows the programme and/or project teams to consider and respond to them.

Consistent with UNDP's Information Disclosure Policy, UNDP is also committed to ensuring that relevant information about UNDP programmes and projects is disclosed to help affected communities and other stakeholders understand the opportunities, risks and impacts of the proposed activities.

UNDP ensures that information on programmes and/or project's purpose, nature and scale, and duration, and its risks and potential impacts, is made available in a timely manner, in an accessible place, and in a form and language understandable to affected persons and other stakeholders, including the general public, so they can provide meaningful input into programme and/or project design and implementation.

For more details on UNDP's Social and Environmental Standards, please follow the below link:

https://www.undp.org/SES

## 3.3 Legal Framework

***Power Services Regulation Act, 2016***

The Power Services Regulation Act, 2016 has been enacted in light of the provision of Article 10 of the Afghan constitution. The Objective of the Act is,

- To supply electrical energy from natural resources of the country and imported energy.
- To improve the quantity and quality of energy services, and its development and promotion.
- Economic growth and development as well as public welfare.
- Public access to the electricity energy services in exchange to a fair price.
- Non-discriminatory access of the electricity energy service providers to the market.
- Regulation of electricity related affairs throughout the country.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

The Ministry of Energy and Water is responsible in implementing the provisions of this Act at the state level and provide electric energy services by itself or through other government institutions, foreign and domestic private sector or in a joint manner. In order to achieve the objectives stated in the Act and for effective and better electricity service delivery, the Energy Services Regulation Department functions within the Ministry of Energy and Water and cumulatively termed as the 'Authority'. One of the Authority's role and responsibility is to register, issue, extend, suspend, and revoke the activity licenses.

As per Article 8, Chapter 2 of the Act, it has been mentioned that without obtaining the license and concluding contract, no one shall take action on construction, installation and assembly of the equipment, production facilities, transmission, distribution, import and export of Electricity power. In addition, real or legal persons/entities that avail the means of production of the electrical energy for their personal usage shall be exempted from the provisions of the Article, provided that the technical conditions have been adhered in accordance with the acceptable national and international standards (published in the area of electricity power). Further, energy services up to one hundred (100) kilowatts supplied for rural areas by the real and legal entities are exempted from obtaining permits under this Article.

According to Article 10 and 11 of the said Act, five types of licenses (and validity) are issued under this Act, namely,

- Electricity Generation License for a maximum of 25 years
- Electricity Transmission License for a maximum of 25 years
- Electricity Distribution License for a maximum of 20 years
- Electrical Energy Import License for a maximum of 15 years
- Electrical Energy Export License for a maximum of 15 years

At this stage, it is unclear if the proposed sub projects would require permits to be obtained from the Energy Services Regulation Authority. Further clarification on the qualification for permit applicant will be sought during the Project Inception phase, post which adequate measures would be accordingly implemented.

***Islamic Republic of Afghanistan, Environmental Law, 2007***

Environmental Law, 2007 in the Islamic Republic of Afghanistan provides for the management of issues relating to rehabilitation of the environment and the conservation and sustainable use of natural resources, living organisms and non-living organisms. Article 14, Chapter 3 of the Act states that a person proposing to undertake a project, plan, policy or activity shall submit to the National Environmental Protection Agency (NEPA) accurate information to all the NEPA to determine the potential adverse effects and positive impacts of the project, plan, policy or activity.

Post review of the brief and acting on the advice of the EIA Board of Experts that has been established under Article 20, NEPA may authorize the project, plan, policy or activity, with or without conditions, provided that the potential adverse effects of the project, plan, policy or activity on the environment are unlikely to be significant. If NEPA considers that the potential adverse effects on the environment are likely to be significant, it may require the proponent to submit to the NEPA as prescribed an environment impact statement or a comprehensive mitigation plan in accordance with the Act.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

At this stage, it is unclear if the proposed sub-projects would be exempted from this criterion as defined by the Act or whether site specific environment impact statement and mitigation plans would be required to developed and submitted to the NEPA for clearance. Clarification on this aspect will be further explored during the Project's Inception phase.

# 4 STAKEHOLDER MAPPING AND ANALYSIS

## 4.1 Stakeholder Mapping and Analysis

ESS 10 recognizes two broad categories of stakeholders: 1) those likely to be affected by the Project because of actual impacts or potential risks to their physical environment, health, security, cultural practices, well-being, or livelihoods (project affected parties), and 2) other interested parties. Stakeholders for the project are categorized accordingly and summarized below

For the renewable energy and energy efficiency solutions for resilience in basic services in educational and health institutions Project in Afghanistan, 'affected parties' will primarily be the targeted beneficiaries, specifically the identified educational and health institutions.

## 4.2 Project-Affected Parties

*Table 2. List of Project Affected Parties*

| Stakeholder | Description |
|---|---|
| Selected public facilities in education and health sectors | The following selection criteria would be adopted in the identification and selection of the education and health facilities.<br>1. (un)- availability of grid and reliance on diesel<br>2. Geographical coverage of the institution and population served<br>3. Availability of basic facilities and equipment that can be powered effectively by solar electricity<br>4. Suitability of the building, facility to install solar system<br>5. Ownership and management of the facility to ensure smooth asset transfer<br>6. Presence of other UNDP's program to draw synergies<br><br>The priority sites (selected) would be further synergized with the ongoing UNDP projects and programmes (linking as a sectoral programme to ABADEI) in the eight regions. It would be matched for the Night Lights Development Index that highlights the regions of poor energy access.<br><br>Once the target facilities are selected, steps will be initiated for designing the technical packages. Standardization of technical packages based on categorisation of facilities will be attempted. Site specific detailed feasibility will be proposed by clustering public facilities of different categories for implementation at scale. |
| Project Workers | Project workers (including project workers from UNDP, contractors, responsible parties, targeted facilities) may also be affected given potential impacts and risks related to the delivery of the project. Labour Management Procedures and workplace grievance mechanisms will be in place. |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

## 4.3 Other Interested Parties

*Table 3. List of Other Interested Parties*

| Stakeholder | Description |
|---|---|
| KfW | As the donor for the project, KfW is a key stakeholder in the project. |
| UN agencies | UNDP Country Office will liaise with UNCT, UNAMA, DPPAs and donors on the political situation to ensure consistency across the UN in matters related to the de-facto authorities |
| Interim Taliban Administration (ITA) | The ITA and their central and provincial authorities are interested parties and can influence this project. |
| Ministry of Energy and Water | Inputs from the Ministry of Energy and Water will be essential especially in relation to permits and approvals required (if in case) to install and operation the solar projects in the selected facilities. |
| Ministry of Public Health | Coordination meetings will be carried out by consultants/ contractors with hospital administrators and officials at the Ministry of the Public Health to ensure access and follow processes stipulated. |
| Ministry of the Education and Ministry of Higher Education | Coordination meetings will be carried out by consultants/ contractors with school and university administrators and officials at the Ministry of the Education and Ministry of Higher Education to ensure processes are adequately followed. |
| DABS | Inputs from DABS is crucial to understand the current status and challenges faced in terms of setting up of solar projects and details surrounding the generation, distribution and supply related aspects. |
| Afghanistan Renewable Energy Union | Afghanistan Renewable Energy Union (AREU) role with representation of over 100 companies in the energy sector will be beneficial in seeking information for potential support in the operation and maintenance phase of the solar projects. In addition, AREU's interest to establish Renewable Energy as a permanent pillar of Afghanistan's national energy industry will help the project to gain potential interest in the country. |
| ABADEI | The ABADEI, Area Based Approach to Development Emergency Interventions launched by UNDP, will help strategize and catalyze the programme framework that mainstreams renewable energy and energy efficiency interventions for essential services, livelihoods and resilient infrastructure support. |
| Community members and leaders | With formal administration systems in question under the present circumstances, community leaders including clan and religious leaders play a vital role in dissemination of information about the project to the wider community and the attainment and social license to operate. |
| National and International Organisations/ Agencies | National and International Organisations/Agencies such as International Renewable Energy Agency (IRENA), SE4ALL, International Solar Alliance, G7+ Fragility knowledge would be used for technology, financing, capacity building and marketplace opportunities for identifying solutions to the project |
| Private Sector | The engagement of the private sector will promote local manufacturing and strengthen the local economy. Delivery models for O&M established through gender inclusive private sector linkages would be initiated as part of the Project's output. |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

## 4.4 Disadvantaged / Vulnerable Individuals and Groups

The Project will focus on targeting support to a number of public facilities (Targeted 792 in Phase I and 2349 in Phase II) based on electricity access and phased for implementation for 0-6 hours and 7-12 hours of average supply or availability of electricity. The project will also prioritize with the highest levels of vulnerabilities. Therefore, vulnerability factors will inform the project site selection and prioritization of provinces. Primary schools and clinics that provide services to girls and women, will be prioritized during project implementation.

*Table 4: Engagement of vulnerable persons and groups*

| No. | Vulnerable Group and Individuals | Characteristic/Needs | Preferred Needs of Notification/Consultation | Additional Resources Required |
|---|---|---|---|---|
| 1 | Women and Girls | There is gender-specific protection and inclusion concerns particularly among rural and urban populations. In terms of livelihoods, women dominate in many aspects. Although women play a critical role in the maintenance of household livelihoods, they generally have less access to productive resources, services and employment opportunities, contributing to a significant gap between men and women's productivity. Given the protracted conflict situation, there are serious GBV concerns across Afghanistan. | Individual consultation. Engage a dedicated female liaison officer from the Country Office with support from the Gender Specialist to liaise with the women and girl group.<br>Use specially designed print media. | Meetings to be separately at convenient time |
| 2 | Persons living below poverty line | Almost 70 percent of the rural population depends on agriculture. Crops are mainly rain-fed, which makes agriculture a vulnerable livelihood. Livestock levels have fluctuated due to droughts. Generally, droughts as well as flooding, and years of protracted conflict has resulted in high levels of poverty of rural households.<br>Urban growth has significantly increased in Afghanistan over the last couple of decades. In 2020, the WB recorded 3.4 percent of urban growth. The urban population accounted for over 10 million people in | Community radio, community meetings, notice boards, community mobilizers to reach out | May require special assistance to attend community meetings, may not have access to electronic means |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| No. | Vulnerable Group and Individuals | Characteristic/Needs | Preferred Needs of Notification/Consultation | Additional Resources Required |
|---|---|---|---|---|
| | | the country. This has come along with increased poverty, many urban poor households living in slums due to disorganized urban growth. | | |
| 3 | IDPs | Suffering from protracted conflict, Afghanistan has been subject to an acute internal displacement crisis. Since the US withdrawal from the country, more than 240,000 Afghans have been internally displaced. An estimated 3.5 million are displaced in total. IDPs often constitute the most vulnerable populations in urban as well as rural environments, given their lack of access to livelihoods, loss of homes, and lack of a social infrastructure. Due to the low level of education prevalent amongst the affected persons, this Group focusses on informal sector business and other activities. | Individual and group consultations, leaflets and information through information cell | Need special attention through support from CO dedicated community engagement specialist |
| 4 | Ethnic and Religious Minorities | Afghanistan is made up of various ethnic and religious groups with a number of ethnic and religious minorities living in a precarious condition post takeover of Afghanistan by the Taliban in August 2021. These groups usually comprise of individuals with low level of education and are reluctant to participate in consultations. | Community radio, community meetings, notice boards, community mobilizers to reach out | Mobilize external resource agencies to create outreach with these target groups |
| 5 | Vulnerable households lacking abled bodied members in urban areas | The most vulnerable households lack any abled bodied members that could potentially participate in cash for work schemes. These include, for example, female-headed households, children-headed households, or households only consisting of elderly people. | Individual and group consultations, leaflets and information through information cell | Use community groups to disseminate information |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

## 4.5 Summary of Project Stakeholder Needs

*Table 5. Project Stakeholder Needs*

| Community | Stakeholder Group | Key Characteristics | Language needs | Preferred notification means (email, radio, phone, letter) | Specific needs (accessibility, large print, childcare, daytime meetings etc.) |
|---|---|---|---|---|---|
| **Provincial Level** | Selected health and educational facilities | • Selection based on assessment of priority criteria<br>• Experience in working with most vulnerable communities in prioritized provinces | Pashto/Dari and/or the third official languages in areas where the majority uses for communication. | Email, internet, radio, mobile phone, social media, individual meetings | Ensure that the facilities selected receive 0-6 hours and 7-12 hours of average supply or availability of electricity are considered for engagement<br><br>Gender disaggregated consultations, Inclusion in project benefits and access to GBV services as required |
| | Vulnerable Communities | Vulnerable and little access to assistance | Pashto/Dari and/or the third official languages in areas where the majority speaks to them. | Community radio, community meetings, notice boards, community mobilizers to reach out | May require special assistance to attend community meetings, may not have access to electronic means |
| | Community Leaders and Members | Their authority will depend on the presence and strength of community leaders of other groups; leaders can have significant influence in the communities | Pashto/Dari and/or the third official languages in areas where the majority speaks to them. | Community meetings, individual meetings, notice boards, social media, community radio, TV | They can also be used as a means to reach the vulnerable communities including support in stakeholder engagements and information dissemination. |
| **Regional Level** | Agencies operating at regional level | Use of existing network in mapping the health and education facilities | Pashto/Dari and/or the third official languages in areas where the majority uses for communication. | Community meetings, individual meetings, notice boards, social media, community radio, TV | They can also be used as a means to reach the broader health and education facilities and in information dissemination. |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| Community | Stakeholder Group | Key Characteristics | Language needs | Preferred notification means (email, radio, phone, letter) | Specific needs (accessibility, large print, childcare, daytime meetings etc.) |
|---|---|---|---|---|---|
| **National Level** | UN agencies, international/national organisations, bilateral donors | Established UN, organisations/agencies and donor coordination mechanisms | English | Internet/email, UNCT | Preparation and implementation support. |
| | Other Agencies operating at national level | Good capacity | English | Internet/email, individual meetings, telephone | Preparation and implementation support. |
| | Contractors | • Qualified staff in carrying out implementation of the project<br>• Experience in undertaking similar projects<br>• Proven track record of implementing similar projects | English; Pashto/Dari and/or the third official languages | Internet/email, individual meetings, telephone | Preparation and implementation support |
| | Private Sectors | • Discussion with private sectors on collaboration in regards with project implementation | English | Internet/email, individual meetings, telephone | Preparation and implementation support |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

# 5 STAKEHOLDER ENGAGEMENT PROGRAM

## 5.1 Purpose and Timing

The SEP defines a structured, purposeful and culturally appropriate approach to consultation and disclosure of information, in accordance with ESS 10 and UNDP's social and environmental standards (SES). UNDP recognises the diverse and varied interests and expectations of project stakeholders and seeks to develop an approach for reaching each of the stakeholders in the different capacities at which they interface with the Project. The aim is to create an atmosphere of understanding that actively involves project-affected people and other stakeholders leading to improved decision making.

Overall, this SEP will serve the following purposes:

- Define a plan for stakeholder engagement, including information disclosure and consultation, throughout the project lifespan
- Stakeholder identification and analysis
- Planning engagement modalities through effective communication, consultations, and disclosure
- Provide enabling platforms for influencing decisions
- Define roles and responsibilities for the implementation of the SEP
- Define reporting and monitoring measures to ensure the effectiveness of the SEP and periodical reviews of the SEP based on findings
- Elaborate on the Project Grievance Redress Mechanism (GRM)

The purposes of consultations and information dissemination in the Renewable energy and energy efficiency solutions for resilience in basic services in educational and health institutions Project in Afghanistan are: (a) mapping the health and education facilities to understand the current situation which will be critical to design both immediate and mid-term interventions; (b) supplementing conventional sources of electricity with renewable energy-based electricity contributes to Afghanistan's energy security (with less reliance on imports), better resilience through reliable services and effective response to humanitarian and energy crisis faced by poor and vulnerable Afghans; (d) support to O&M of decentralized renewable energy systems through appropriate service delivery models and capacity building/ training; (e) support to local Afghan renewable energy companies, vendors and manufacturers, and; (f) enhance coordination structures on renewable energy at both national and provincial levels, tapping into the existing coordination body and also coordinating with other efforts made by UNCT. To ensure this, a Grievance Redress Mechanism is included below, which will be rolled out at the provincial, regional and national level. Efforts will be made to collaborate with existing channels of grievance mechanism available at the provincial level and route it to the Project's regional and national level mechanism. This will allow affected individuals and groups to report on project-related grievances or can provide comments and feedback.

In consideration of Covid-19 restrictions, the project will follow existing guidelines on community consultation under Covid-19. This means effective and meaningful consultations to meet project and stakeholder needs and adhere to the restrictions put in place by the Interim Taliban Administration (ITA) to contain virus spread. Representatives of particular community groups will be consulted. Strategies will be employed to include smaller meetings, small focus group discussions to be conducted as appropriate taking full precautions on staff and community safety. Where meetings are not permitted, traditional channels of communications such as radios and public announcements will be implemented. Other strategies will include one on one meetings through phones for community representatives other interests' groups.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

Given the current political context, stakeholder engagements with the ITA will be avoided to the extent possible. Engagements will be undertaken directly by the above listed implementers (UNDP and ABADEI including contractors). Implementers will focus on the existing network as a key vehicle for information dissemination and consultations at the regional and provincial level. Consultations with higher level partners will be undertaken directly by UNDP.

## 5.2 Plan for Information Disclosure

Information disclosure to the health and education facilities (beneficiaries) will rely on the following key methods: email, internet, radio, mobile phone, social media and individual meetings. Support from community members and leaders would also be explored as a means to reach the broader health and education facilities in information dissemination. At the national level information will be disclosed mainly by email and through social media. Information will be disclosed in Pashtu/Dari, English or respective local languages.

*Table 6 Plan for Information Disclosure*

| Project Stage | List of information to be disclosed | Methods proposed | Timelines: locations / dates | Target Stakeholders | Responsibilities |
|---|---|---|---|---|---|
| **Project Design** | Draft Project Document discussion (including SEP and GRM) and to seek feedback and opinions from stakeholders | Coordination Meetings / telephone / notice boards | TBC | - Ministry of Public Health and Ministry of the Education and Ministry of Higher Education at national level and in major provincial capitals<br>- Private Sectors<br>- Relevant Government Departments | UNDP CO |
| | | Separate consultations with women groups, including online | TBC | Health and education facilities catering to women health and education at national level and in major provincial capitals | UNDP CO |
| | | Email | TBC | Select health and education facilities; private sectors | UNDP CO |
| | | Websites –UNDP | TBC | National and Regional Level | UNDP CO |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| Project Stage | List of information to be disclosed | Methods proposed | Timelines: locations / dates | Target Stakeholders | Responsibilities |
|---|---|---|---|---|---|
| | Final Project Document and action items including (LMP with GBV Action Plan) | Inception workshops | TBC | National and Regional Level | UNDP CO |
| | | Separate Inception workshops for women groups | TBC | National and Regional Level | UNDP CO |
| | | Email | TBC | Select health and education facilities | UNDP CO |
| | | Websites - UNDP | TBC | National and Regional Level | UNDP CO |
| **Project Implementation** | Priority criteria in selection of Health and Education facilities – discussion and feedback | Meetings / telephone / notice boards | TBC | National and Regional Level | PIU/UNDP |
| | | Email | TBC | National and Regional Level | PIU/UNDP |
| | Draft Health and education facilities mapping and selection criteria | Stakeholder meetings / telephone / notice boards/separate meetings for women groups | As needed | National and Regional Level | PIU/UNDP |
| | | Email | As needed | National and Regional Level | PIU/UNDP |
| | | Websites - UNDP | As needed | National and Regional Level | PIU/UNDP |
| | Any proposed substantive revisions to Project Document or Plans | Stakeholder meetings / telephone / notice boards/separate meetings for women groups | As needed | Selected Health and Education Facilities | PIU/UNDP |
| | | Meetings/ telephone / notice boards | As needed | National and Regional Level | PIU/UNDP |
| | | Email | As needed | Selected Health and Education Facilities | PIU/UNDP |
| | | Websites - UNDP | As needed | Selected Health and Education Facilities | PIU/UNDP |
| | Information about Project | Stakeholder meetings / telephone / notice boards | Continuous | Local affected people | PIU/UNDP and Selected Health and Education Facilities |
| | | Radio | Continuous | Local affected people | PIU/UNDP and Selected Health |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| Project Stage | List of information to be disclosed | Methods proposed | Timelines: locations / dates | Target Stakeholders | Responsibilities |
|---|---|---|---|---|---|
| | | | | | and Education Facilities |
| | | Mobile phone | Continuous | Local affected people | PIU/UNDP and Selected Health and Education Facilities |
| | | Email | Continuous | Local affected people | PIU/UNDP and Selected Health and Education Facilities |
| | GRM | Community meetings / notice boards | Continuous | Affected people | PIU/UNDP |
| | | Project worker/staff training and inception | At inception and continuous | Affected people (project workers) | PIU/UNDP |
| | | Radio | Continuous | Affected people | PIU/UNDP |
| | | Mobile phone | Continuous | Affected people | PIU/UNDP |
| | | Website - ACBAR, WB, UNDP | Continuous | Affected people | PIU/UNDP |
| | Capacity building trainings | Selected health and education facilities meetings / telephone / notice boards | As needed | National and Regional Level | PIU/UNDP |
| | | Email | As needed | National and Regional Level | PIU/UNDP |

## 5.3 Plan for Consultations

This plan lays out the overall consultative processes of the Project with its different stakeholders. In principle, the PIU including other partners implementing activities underlined in the output, will follow their existing participatory engagement and consultation methods. However, throughout the mapping process, SEP-related activities will be included, and other partners will be called upon to budget for SEP-related activities that are under their responsibility.

The GRM is another means of engagement with beneficiaries/stakeholders, as complaints received will be filed, assessed and responded to (see below).

*Table 7 Plan for Consultations*

| Project stage | Topic of consultation | Suggested Method (will be refined by PMU) | Target stakeholders | Responsibilities |
|---|---|---|---|---|
| **Project Design** | Overall Project activities and | Stakeholder meetings, email, social media | Selected health and education facilities | PIU |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| Project stage | Topic of consultation | Suggested Method (will be refined by PMU) | Target stakeholders | Responsibilities |
|---|---|---|---|---|
| | E&S risks and impacts | Stakeholder meetings, email | Ministry of Public Health and Ministry of the Education and Ministry of Higher Education at national level and in major provincial capitals | PIU |
| | | Stakeholder meetings, email | Private Sectors | PIU |
| | | Email | National level stakeholders | PIU |
| **Project Initiation and Implementation** | Mapping exercise | Stakeholder meetings, email | National, Regional and Provincial Level stakeholders | PIU |
| | Details project activities | Stakeholder meetings of health and education facilities, mobile phone | Selected health and education facilities | PIU |
| | ESMF<br><br>E&S risks and impacts and mitigation measures | Stakeholder meetings, email, social media | Selected health and education facilities | PIU |
| | Capacity building plan | Meetings, email, mobile, | Selected health and education facilities | PIU |
| | Co-ordination amongst selected health and education facilities | Stakeholder meetings, email | National, Regional and Provincial Level health and education facilities | PIU |
| | GRM | Mechanism set up | Selected health and education facilities including health and education facilities at the national, regional and provincial level | PIU |

## 5.4 Timeline

The Project is planned for two phases of 5 years each. Information disclosure and consultations are relevant throughout the entire life cycle of the Project. Project design will therefore be based on national-level and regional level consultations of Ministry of Public Health and Ministry of the Education and Ministry of Higher Education at national level and in major provincial capitals and health and education facilities administration. Activities under each output will include further consultations prior to their commencement, to ensure transparency and accountability on project modalities, and allow stakeholder voices to form the basis for the concrete design of every intervention; consultations will continue throughout the project cycle. Initial consultations will be held during the design and preparation phase of the project, in the months post project appraisal. This SEP will be updated during the implementation phase, based on in-depth consultations with the various stakeholders.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

### 5.5 Reviews of Comments

The UNDP will gather all comments and inputs originating from community meetings, GRM outcomes, SMS, emails and other communication modalities. The information gathered will be submitted to the SES Specialists in the PIU, to ensure that the Project has general information on the perception of the stakeholders, and that it remains on target. It will be the responsibility of the PIU to respond to comments and inputs, and to keep open a feedback line to the stakeholders. Training on environmental and social standards facilitated by KfW will be provided soon after the Project becomes effective to ensure that all the staff from the PIU are equipped with the necessary skills.

This SEP provides the overarching guidelines for the rolling out of stakeholder engagements. The PIU will monitor the capacity of the E&S safeguards staff (including contractors), and recommend and implement appropriate actions, e.g., refresher trainings.

## 6 RESOURCES AND RESPONSIBILITIES FOR IMPLEMENTING THE SEP

The overall responsibility for the implementation of the SEP lies with the Technical Lead/Project Manager in UNDP through the PIU. The PIU along with the Technical Lead will be supported by the SES Specialist (international and national) and Gender Specialist (support from CO) in the implementation of the SEP at the national level. In the sub-national/regional level, UNDP will leverage its capacities in the eight regional offices/hubs in the implementation of the Project, including the Area Managers who are heading the sub-offices, and the National Programme Officers. In addition, UNDP will provide oversight and assurance capacity through its Afghanistan Country Office, including a SES Specialist. Additional UNDP CO, regional and global social and environmental safeguards oversight capacity will be made available to the project as needed.

The Integrated Risk Management Unit (IRMU) of UNDP Country Office will be used to lead the UNDP's risk management efforts, including the screening of partners prior to engagement. The SES Specialists and Gender Specialist will be responsible in overseeing all SEP-related activities and will provide continuous expert inputs into the refinement of the SEP.

The SES Specialist (national) maintains a stakeholder database for the overall project and leads a commitment register. However, while the PIU will oversee all coordination and disclosure-related consultations, ABADEI will support the PIU in coordination and implementation of the SEP at the national and regional levels in their respective operational areas and report on their activities to the PIU SES Specialist (national) on a monthly basis. Where UNDP implements activities directly, UNDP will be responsible for all local stakeholder engagement. The PIU will engage short term SES experts to undertake verification activities of the selected health and education facilities jointly with the responsible parties – at least every other month, or during planned events.

Implementation Partners (IPs) (including responsible parties and contractors) will identify staff responsible for the implementation of E&S measures, including this SEP. Staff names are to be submitted to the PIU SES Specialist. IPs also commit to communicate the stakeholder engagement strategies to their respective networks and internally.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

# 7 GRIEVANCE REDRESS MECHANISM

## 7.1 Objective

The objective of a Grievance Redress Mechanism (GRM) is to assist in resolving complaints in a timely, effective and efficient manner. Project-level GRMs can provide the most effective way for stakeholders to raise issues and concerns about the project that affect them. The GRM provides a transparent and credible process for fair, effective and lasting outcomes. It also builds trust and cooperation as an integral component of broader stakeholder engagement, that facilitates corrective actions and helps the community to have ownership of the project. The GRM for this project is designed in accordance with World Bank's ESS10 and UNDP's SES for the benefit of all project affected persons, including workers and other stakeholders. The GRM would also provide for handling of grievances related to SEA/SH.

The GRM provides an avenue for stakeholder engagement and the management of social and environmental risks and impacts. However, it is not a substitute for proactive outreach to stakeholders to inform them about the Project, seek their input, and respond to their suggestions and concerns regarding social and environmental benefits, risks and impacts.

UNDP corporate Accountability Mechanism (www.undp.org/secu-srm) provides additional recourse for complainants who are not satisfied with the response they have received from the Project GRM or who are concerned about an adverse response if they raise concerns with the Project GRM.

## 7.2 Principles

The project-level GRM would be designed in a culturally appropriate way so as to effectively respond to the needs and concerns of all parties involved.

- The GRM would be well-publicized and known to all stakeholders. The implementing agency will ensure that the GRM is widely publicized and will also conduct awareness campaigns in this regard among the selected and wider network of educational and health institutions. Implementing agencies will brief target stakeholders about the scope of the mechanisms, the safety of the complainant, time of response, the referral and appeal processes.
- Accessibility - The GRM will be clear, accessible to all levels of health and education facilities based at national, regional and provincial level.
- The Mechanism would allow for multiple avenues of uptake of grievances.
- The system would be sensitive to women, men, boys and girls, as well as vulnerable populations such as women headed households, elderly, displaced persons and other marginalized groups.
- Confidentiality and prevention against retaliation.
- The GRM would be designed to protect beneficiaries and stakeholder's rights to comment and complain, and even raise their complaints to higher management if they are not satisfied with services or receive insufficient solutions. The mechanism would facilitate their sharing of concerns freely with understanding that no retribution will be exacted for their participation. To create a safe space, anonymous complaints will also be allowed.
- The GRM shall provide for relaying regular information and feedback regarding the redressal of the grievance to the aggrieved.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

- The Mechanism shall be responsive in redressal of grievances by facilitating resolution with the concerned actor in the implementing chain.
- The GRM would be based on transparency and accountability. All complainants will be heard, taken seriously, and treated fairly. The community and stakeholders will be aware of the expectation from the project; the GRM procedures; understand its purpose, have sufficient information on how to access it.
- The GRM will have provisions to appeal if the grievances are not resolved satisfactorily
- The GRM would not prevent access to judicial and administrative remedies.
- The mechanism would provide for prompt time-bound redressal of grievances.
- For SEA/SH cases, guiding principles of confidentiality, survivor centricity, non-discrimination, respect, access to services and survivor safety are to be applied to specific cases of SEA/SH cases as per the UNDP's guidance. Reporting mechanisms will enable complainant to report SEA/SH cases without being publicly identified given the risk of stigma, reprisals, and rejection associated with sexual exploitation and abuse and sexual harassment.

## 7.3 GRM Structure for the project

The Project consists of a three-tiered GRM system with Grievance Redressal Committees (GRCs) would be established. Established available UNDP GRM will also be explored to be adopted to this project during the Project Inception stage.

GRCs will be comprised of network of educational and health facilities at regional level, education and health facilities at national level and UNDP- PIU GRC. It is proposed that the regional and national level GRCs would be operated by the existing UNDP networks with support from UNDP Provincial Hubs and Kabul. There would be a provision for appeals and any aggrieved party would be able to directly approach the national level GRC or directly to the UNDP-PIU central office as well. The formation of the GRCs would be completed prior to the commencement of project activities.

The complainants will have the option to report their complaints/feedback to the following committees:

**Existing UNDP networks at regional level GRC (8 regions).** The members will comprise, networks Head, networks Secretary, UNDP Provincial Hubs and female advocates. The grievance focal point (GFP) (from CO) will be responsible to maintain record of grievances in a logbook. If the issue cannot be resolved at the regional network level, then the GRC will immediately escalate it to a higher level, i.e., either to the GRC at the national networks level and/or directly to the UNDP-PMU central office. Each network (including selected facilities) will have a complaint box and the network GRC to check the box at least once a week or if they know a grievance has been put. The person(s) can put a complaint anonymously. If they wish, individuals or groups can also hand a complaint to the existing network Committee. The regional networks GRC will address complaint/feedback within 10 days.

**Existing UNDP networks at national level GRC.** The timeline for complaint registration at national networks level is 10 days. The national level GRC will consist of members from health and educational facilities network at national level and UNDP national Hub (Kabul). Ideally, there should be an equal number of men and women

**UNDP-PIU level GRC**. The GRC members will comprise UNDP-PIU-manager, SES expert and gender and SEA/SH expert. The timeline for complaint resolution at the UNDP-PIU central office level will be 15 days upon receipt of the complaint. The complainant will be informed of the outcome immediately and at the latest within 5 days of the decision.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

## 7.4 Channels for submitting the requests:

Stakeholder can submit their grievances regarding any element of the project without any restriction through a variety of means as listed below:

- Suggestion Boxes: Will be in a visible place in each of the selected facilities, and at the existing network at national level.
- Personal Visit: Complainants can personally submit his/her grievance to one of the relevant Grievances Redressal Committees (including oral or written communications received during field meetings).
- Telephone Hotline: The complainant can report his/her grievance verbally to a dedicated telephone hotline (the number of which will be disseminated in the Project areas).
- Petition: Complainant can submit his/her written petition directly to one of the grievance handling committees (existing network at regional and national level and UNDP- PIU GRC).
- Email: Those complainants can also send their grievances to emails address that will be disseminated in the Project area.
- UNDP website (complaints and inquires).

UNDP will also explore grievance uptake channel already in existence to boost the grievance mechanism proposed, including the uptake channel at regional and national level under ABADEI Programme and partners (responsible parties) and the UNDP AFG Country Office GRM and CHM (Compliant Handling Mechanism). While the existing mechanisms would be leveraged for this project, in order to address other requirements of UNDP, the system would be augmented for the purposes of this project in accordance with the principles given above and the following steps:

- **Step 1**: **Uptake** – Project stakeholders will be able to provide feedback and report complaints through several channels. The aggrieved party must be able to select the most efficient institution, the most accessible means of filing a grievance, and must be able to circumvent partial stakeholders in the Project, which may be implicated in the complaint. He or she must further be able to bypass some grievance channels that are perceived as potentially not responsive or biased. The means to file a grievance would include a toll-free hotline, SMS, email, filling up grievance forms, verbally, sending a letter, to implementing agencies, via the implementing institutions' websites, helpdesks and collection boxes stipulated for walk-ins at the sites of project activities. Anonymous grievances can also be raised. All uptake channels should permit for grievances in Dari and Pashto as well.

  A help desk will also be set up by the Project during the implementation of activities at the regional level. At the help desk, aggrieved parties can inquire about project activities, or they can file a grievance directly with the person manning the desk. Grievances can be filed in writing or verbally at the Help Desk.

  The staff managing help desks and those operating the toll-free hotline number would be trained by the PIU for (a) the registration of a grievance; (b) the interaction with complainants; (c) appropriate responses to SEA/SH issues; (d) grievances of workers; and (e) Project components and Implementing Partners.

- **Step 2: Sorting and processing** – All grievances received will be transferred to the GRM Focal Point at the PIU based at the Country Office. The GRM focal point will categorize the complaint and forward it to the responsible unit. The GRM focal point will also record the grievance in the same format as would be used at the PIU.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

- **Step 3: Acknowledgement and follow-up** – Within three (3) days of the date a grievance is submitted, the GRM focal point will communicate with the aggrieved and provide information on the likely course of action and the anticipated timeframe for resolution of the grievance. The information provided to aggrieved would also include, if required, the likely procedure if the grievance had to be escalated outside the unit and the estimated timeline for each stage.

- **Step 4: Verification, investigation, action and documentation** – This step involves gathering information about the grievance to determine the facts surrounding the issue and verifying the validity of the grievance, and then developing a proposed resolution. It is expected that many or most grievances would be resolved at this stage. All activities taken during this and the other steps will be fully documented, and any resolution logged in the register. In case the grievance is not resolved at this stage, it would be escalated to the next tier.

- **Step 5: Monitoring, Evaluation and Reporting** – Monitoring refers to the process of tracking grievances and assessing the progression toward resolution. Each implementing agency would develop and maintain a grievance register and record of all steps taken to resolve grievances or otherwise respond to feedback and questions. GRM data would be collated and reported monthly at all levels.

  The Third-Party Monitoring Agent (TPMA) (TBD) will provide independent operational review of overall project implementation and project results, including the implementation of the SEP and GRM. The PIU will synthesize all reporting by TPMA, as well as its own findings, and produce an overall environment and social progress report with a distinct section on stakeholder engagement in line with a template to be provided. The project provides for quarterly reporting.

- **Step 6: Providing Feedback** – This step involves informing those who have raised complaints, concerns or grievances the resolutions to the issues they have raised. Whenever possible, complainants should be informed of the proposed resolution in person, which gives them the opportunity to ask follow-up questions. If the complainant is not satisfied with the resolution, he or she will be informed of further options. The GRM would not prevent access to judicial and administrative remedies. Each complaint must be closed within thirty (30) days of receipt - either resolved, withdrawn or escalated.

## 7.5 Grievance Redressal Committees Terms of Reference

The formed Committee will have the following tasks to perform:

- To receive and register all incoming grievances into the Grievance Registration Book (grievance logbook and central grievance excel-sheet).
- To analyze the grievances in order to understand the nature of grievances and an appropriate way to deal with them
- To categorize all incoming grievances
- To refer the analyzed grievances to the related committees/entities for resolution, and complainants, if they wish to come forward should be able to explain
- To follow up on the grievances with the responsible committees/entities to speed up the process and reach the result (timeline based)
- To hold periodic Grievance Redressal Committee's meeting, as required
- To feed the result back to the complainant
- To check the complaints box and address the incoming complaints.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

## 7.6 GRM for SEA/SH grievances

SEA/SH related grievances are handled through a survivor-centered approach. All grievance uptake channels can be used to report on SEA/SH issues. No grievance uptake mechanism can reject such grievances, and all personnel directly receiving grievances will be trained in the handling and processing of SEA/SH-related grievances. Any recipients of the grievance should, with the survivor's informed consent, report the case to one of the Project's formal grievance recipients. A survivor can ask someone else to act as a survivor advocate and report on her/his behalf.

Absolute confidentiality would be maintained for all grievances related to SEA/SH issues. This means that no information shall be disclosed at any time to any party without the informed consent of the person concerned. The survivor's consent would also be sought for undertaking any action on the grievance. Under no circumstances should the survivor be pressured to consent to any conversation, assessment, investigation or other intervention with which they do not feel comfortable. A survivor can withdraw such consent at any time as well. If a survivor does not consent to sharing information, then only non-identifying information can be released or reported on. In the case of children, informed consent is normally requested from a parent or legal guardian and the children.

Data on GBV cases recorded will only include the nature of the complaint (what the complainant says in her/his own words), whether the complainant believes the perpetrator was related to the project and additional demographic data, such as age and gender, will be collected and reported, with informed consent from the survivor. The GRM provides for offering the survivor referral to pre-identified GBV Service Providers in the area. Services can include health, psycho-social, security and protection, legal/justice, and economic reintegration support. This would be offered even if the survivor does not wish to file a formal complaint or if the complaint is not related to the project before closing the case. The ESMF will incorporate measures to assess and manage risks related to SEA and SH and will include a list of referral services in the different Project areas.

Where SEA/SH grievances have been allegedly committed by a Project worker, the grievance will also be reported to the respective employing agency. The PIU SES Specialist (national level) will follow up and determine jointly with the GRM Focal Point of the respective partner the likelihood that the allegation is related to the Project. The Gender Specialist will follow up and ensure that the violation of the Code of Conduct is handled appropriately. The responsibility to implement any disciplinary action lies with the employer of the perpetrator, in accordance with local labor legislation, the employment contract, and the code of conduct. The GRM focal point will report back to the survivor on any steps undertaken and the results.

All SEA/SH incidents would be reported to the KfW in accordance with the project Environmental and Social Commitment Plan (ESCP). UNDP-PIU will notify the KfW of any incident, including SEA/SH incidents within 48 hours after taking notice of the project-related incident. They will provide incident investigation report to the KfW within 45 days from the time of incident was reported to KfW.

## 7.7 Capacity building/ Awareness

The dedicated SES (national) Specialist including GRM focal point (TBD) will conduct capacity building and awareness raising of the GRCs and relevant staff. The incumbent will train the national and regional GRCs (networks). The SES (national) Specialist and GRM focal point and the GRCs will be responsible to disseminate the GRM information in the project areas to inform stakeholders/beneficiaries about GRM service.

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

## 7.8 GRM Reporting

The project will also continuously monitor the functioning of the GRM, and the types of complaints registered, as well as beneficiary feedback.

The UNDP-PIU SES (national) Specialist and GRM focal point will provide updates on grievances registered in the grievance logbooks and central GRM excel-sheet.

The quarterly report will include following GRM details:

- How many complaints were received from communities (men and women)?
- Of the grievances (not suggestions or inquiries or comments), what category of grievance raised most frequently (#1, 2, and 3) with most frequent sub-categories included
- What category of grievance raised the least frequent (# 1, 2, and 3)?
- Of each Grievance category, which sub-categories have the most grievances?
- Report number of Grievances by regions

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

# 8 MONITORING AND REPORTING

## 8.1 Involvement of Stakeholders in Monitoring Activities

The Project will involve project stakeholders in monitoring of project activities, in particular selected health and education facilities receiving support will be directly involved in monitoring of stakeholder engagement activities.

At this stage it is also anticipated that a TPMA (TBD) will be deployed in order to monitor project performance and E&S risks and impacts at all levels. The TPMA will submit monitoring reports directly to the UNDP PIU and the KfW.

## 8.2 Reporting Back to Stakeholder Groups

The above listed plan for information dissemination to the stakeholders also includes the information dissemination and disclosure of Project monitoring results. The SES (national) Specialist and GRM Focal Point (TBD) will ensure that monitoring results on Project performance as well as E&S risks and impacts and implemented mitigation measures will be made available to the above identified stakeholders at the provincial, regional and national level. The implementation of the stakeholder consultation plan (see above), in turn, will allow the key stakeholders to react and voice their feedback with regards to the monitoring results. Information dissemination will always include information on the available Project GRM and its different channels to file a grievance or provide feedback.

## 8.3 Reporting to the KfW

The PIU will provide quarterly Project Progress Reports to the KfW. These Quarterly reports will consist of project performance and results; financial and procurement information; risk management progress, including progress on implementation of the ESMF. The PIU will receive monthly and quarterly inputs from selected health and education facilities and responsible parties prior to the preparation of the Quarterly Reports and will include those inputs in the Quarterly Report. The Quarterly Report will further contain a section on stakeholder engagement initiatives undertaken in the Quarter, as per this SEP, as well as a section reflecting on the results of stakeholder consultations. A synthesis report and analysis of grievances filed under the Project GRM and the workers' GRM will be included.

# 9 ESTIMATED BUDGET

The below table presents an estimated budget for the implementation of the SEP for Phase I (5 years) of the Project. It should be noted that budgets for selected health and educational facilities, contractors, and responsible parties should include the costs of SEP implementation, in view of activity specific stakeholder consultations and information dissemination. The budget presented here concerns the Project level implementation (Phase I) of the SEP through the PIU. The source of funding is the Project budget.

*Table 8 Estimated Budget for SEP implementation*

| Stakeholder Engagement Activities | Q-ty/per years (months) | Unit Cost, USD | # of months | Total cost (USD) |
|---|---|---|---|---|
| Environment and Social Safeguards Specialist (international), Social and Environmental Safeguards Specialist (national), Gender | | | | Included in PIU staff costs |

DocuSign Envelope ID: 9F9C5961-86FC-408E-9E66-1E11FAC7C5DC

| **Stakeholder Engagement Activities** | **Q-ty/per years (months)** | **Unit Cost, USD** | **# of months** | **Total cost (USD)** |
|---|---|---|---|---|
| Specialist (International) (PIU) from country office, GRM Focal Point (TBD), TPMA (TBD) | | | | |
| GRM, data base (Including running of hotline, record keeping, connectivity cost etc.) | 12 | 1,000.00<br>Per month | 60 | 55,000.00 |
| Operational Costs (Travel, Logistic Support, Security, Transportation & Accommodation). | | | | Included in PIU staff travel costs |
| Communication materials (leaflets, posters, social media) | 5 | 10,500.00 per year | 60 | 53,500.00 |
| Trainings (Social issues, outreach, GRM, etc.) for PIU, IPs | 5 | 40,000 per year | 60 | 207,584.00<br>+ integral to Project's capacity building activities/budget |
| **Total Budget** | | | | **316,084.00** |

DocuSign

## Certificate Of Completion

Envelope Id: 9F9C596186FC408E9E661E11FAC7C5DC
Subject: Please DocuSign: KFW RE Pro Doc
Source Envelope:
Document Pages: 144
Certificate Pages: 2
AutoNav: Enabled
EnvelopeId Stamping: Enabled
Time Zone: (UTC-08:00) Pacific Time (US & Canada)

Signatures: 7
Initials: 5

Status: Completed




Envelope Originator:
Anisha Thapa
One United Nations Plaza
New York, NY 10017
anisha.thapa@undp.org
IP Address: 103.13.66.66

## Record Tracking

Status: Original
12/13/2022 1:49:47 AM

Holder: Anisha Thapa
anisha.thapa@undp.org

Location: DocuSign

| Signer Events | Signature | Timestamp |
|---|---|---|
| Usha Rao<br>usha.rao@undp.org<br>Portfolio Specialist (Sust/SDRRP OiC<br>UNDP BPPS / GEF<br>Security Level: Email, Account Authentication (None)<br><br>**Electronic Record and Signature Disclosure:**<br>Not Offered via DocuSign | DocuSigned by:<br>  <br>9BAF891EF061460...<br><br>Signature Adoption: Drawn on Device<br>Using IP Address: 103.28.133.143<br>Signed using mobile | Sent: 12/13/2022 2:11:03 AM<br>Viewed: 12/13/2022 2:39:30 AM<br>Signed: 12/13/2022 2:40:56 AM |
| Anisha Thapa<br>anisha.thapa@undp.org<br>RBM Specialist<br>UNDP Headquarters<br>Security Level: Email, Account Authentication (None)<br><br>**Electronic Record and Signature Disclosure:**<br>Not Offered via DocuSign | DocuSigned by:<br>  <br>9E2F629C547F485...<br><br>Signature Adoption: Pre-selected Style<br>Using IP Address: 152.36.212.13 | Sent: 12/13/2022 2:41:08 AM<br>Viewed: 12/13/2022 2:52:23 AM<br>Signed: 12/13/2022 2:52:45 AM |
| Akiko Hasegawa<br>akiko.hasegawa@undp.org<br>Finance Specialist / Head of Finance<br>UNDP Afghanistan Country Office<br>Security Level: Email, Account Authentication (None)<br><br>**Electronic Record and Signature Disclosure:**<br>Not Offered via DocuSign | DocuSigned by:<br>  <br>9205090886DE4C3...<br><br>Signature Adoption: Uploaded Signature Image<br>Using IP Address: 152.36.212.13 | Sent: 12/13/2022 2:52:54 AM<br>Viewed: 12/14/2022 2:44:20 AM<br>Signed: 12/14/2022 2:46:21 AM |
| Surayo Buzurkova<br>surayo.buzurukova@undp.org<br>SDRR-P UNDP Afghanistan<br>UNDP Yemen<br>Security Level: Email, Account Authentication (None)<br><br>**Electronic Record and Signature Disclosure:**<br>Not Offered via DocuSign | DocuSigned by:<br>  <br>C8F21608D8FA487...<br><br>Signature Adoption: Pre-selected Style<br>Using IP Address: 185.159.156.17<br>Signed using mobile | Sent: 12/14/2022 2:46:29 AM<br>Viewed: 12/14/2022 4:17:37 AM<br>Signed: 12/14/2022 4:18:01 AM |

| In Person Signer Events | Signature | Timestamp |
|---|---|---|

| Editor Delivery Events | Status | Timestamp |
|---|---|---|

| Agent Delivery Events | Status | Timestamp |
|---|---|---|

| Intermediary Delivery Events | Status | Timestamp |
|---|---|---|

| Certified Delivery Events | Status | Timestamp |
|---|---|---|

| Carbon Copy Events | Status | Timestamp |
|---|---|---|

| Witness Events | Signature | Timestamp |
|---|---|---|

| Notary Events | Signature | Timestamp |
|---|---|---|

| Envelope Summary Events | Status | Timestamps |
|---|---|---|
| Envelope Sent | Hashed/Encrypted | 12/13/2022 2:11:03 AM |
| Certified Delivered | Security Checked | 12/14/2022 4:17:37 AM |
| Signing Complete | Security Checked | 12/14/2022 4:18:01 AM |
| Completed | Security Checked | 12/14/2022 4:18:01 AM |

| Payment Events | Status | Timestamps |
|---|---|---|
