UNITED NATIONS DEVELOPMENT PROGRAMME

Empowered lives.
Resilient nations.

PROJECT DOCUMENT
[UNDP Iraq]

Project Document Revision Cover Page

Project Title: Iraq Crisis Response and Resilience Programme

Project Number: 00085156

Implementing Partner: United Nations Development Programme

Start Date: 1 October 2014 **End Date:** 31 December 2024 **PAC Meeting date:**

Brief Description

The Iraq Crisis Response and Resilience Programme (ICRRP) was designed in 2014 to enable UNDP Iraq to provide immediate support in response to the crisis-situation following the Islamic State of Iraq and the Levant (ISIL), taking control of several locations of the country. ICRRP was originally designed to work under 5 thematic areas: 1) Government coordination, 2) Basic services, 3) Livelihood recovery, 4) Protection and 5) Social cohesion, to support the internally displaced persons, returnees, Syrian refugees and host communities in the Kurdistan Region of Iraq (KRI).

Since its design, ICRRP managed a level of flexibility enabling a structured response to the fast-evolving country context to address the most urgent needs. It adopted a holistic, integrated and community driven approach with an emphasis on gender and women to set the stage for Iraq's full recovery and economic development. In 2017, major changes were observed in the country context where the Government of Iraq made considerable progress recapturing areas under the control of ISIL. Consequently, ICRRP's geographical focus was expanded to cover some of the urgent needs of returnees to the newly liberated areas (NLAs), in tandem with the UNDP Funding Facility for Stabilization (FFS). With the approval of the Project Board, from 2018 onwards, ICRRP implementation covered Dohuk, Erbil and Sulaymaniyah Governorates in KRI and Baghdad, Diyala, Ninewa, Salah al-Din, Kirkuk, Basra, Najaf and Karbala in Federal Iraq. To accommodate the response to new shocks, namely COVID-19 and associated high youth unemployment, the project document was also revised in 2021 and extended to 31 Dec 2022. ICRRP continued to focus on the five original thematic areas however with a tailored approach relying on the provision of livelihoods and economic recovery activities to enable the humanitarian-development-peace nexus.

Responding to the development of the country context, in particular the humanitarian exit and the handover timeline of all clusters to the Iraqi Government by December 2022, the political instability, and the unprecedented, recorded impact of climate change in Iraq, the Project Board endorsed an overall revision in addition to the extension of the project duration to 31 Dec 2024.

The updated ICRRP project document outlines the implementation strategy, governance structure, the programmatic and geographic realignment as well as the results framework. Going forward ICRRP will focus on 3 integrated multi-dimensional thematic areas: 1) Resilient livelihoods solutions, 2) Community social cohesion, and 3) Climate change action, and will cover all Governorates of Iraq in close collaboration and partnership with various stakeholders.

Contributing Outcome (UNSDCF (2020-2024)/CPD):
1.3: People in Iraq participate in and benefit from effective mechanisms – at national, subnational and community levels – that prevent, mitigate and manage conflict, and contribute to social cohesion and peaceful coexistence, with particular focus on women and youth leadership in decision- making, peace-building and reconciliation processes
2.1: Improved people-centred economic policies and legislation contribute to inclusive, gender sensitive and diversified economic growth, with focus on increasing income security and decent work for women, youth and vulnerable populations
4.2: Increased engagement of the people of Iraq, sub-national institutions, civil society, and private sector to ensure more responsible, inclusive, accountable and transparent management of natural resources and the environment

Total resources required (USD)	307,177,525.00[1]	
Total resources allocated (USD):	185,618,532[2]	
	UNDP TRAC:	1,463,919
	Donor:	184,154,613
	Government:	
	In-Kind:	
Unfunded (USD):	121,558,994[3]	

Agreed by

UNDP
Print Name: Zena Ali Ahmad Resident Representative UNDP Iraq

[1] Estimated values.

[2] Estimated values, subject to change based on exchange rates.

[3] Estimated values, subject to change based on exchange rates.

SITUATION ANALYSIS

Project Background

From 2014 to 2017, ISIL occupied territory in the Governorates of Anbar, Diyala, Ninawa, Salah-al-Din, and Kirkuk, dismantled the Government of Iraq's (GoI) control over resources and public infrastructure, and led to the temporary dissolution of several units of the Iraqi Security Forces. Iraq's largest cities, notably Mosul, Ramadi, and Tikrit, were controlled by ISIL for over two years, leading to widespread damage to infrastructure, private homes, and businesses. During this period, Iraq faced one of the biggest humanitarian crises. The GoI was responsible for supporting more than six million Internally Displaced Persons (IDPs)[4] and 250,000 Syrian refugees while undertaking a difficult military campaign. The fight to liberate occupied areas led by the Iraqi Security Forces, with the support of the Global Coalition to Defeat Daesh resulted in further damage, taxing the GoI's limited resources at a time when global oil prices dropped drastically.

In response to this, in 2014, UNDP with financial contributions from the Governments of Austria, France, Japan, Germany, the United States, and the United Kingdom developed ICRRP initially for two years (2014-2015). The project supported the GoI's efforts to prevent and respond to crises and played a catalytic role in developing resilience against shocks that stemmed from renewed violence and instability. The project served as the platform for providing emergency, early recovery, and resilience support. It initially focused on geographical locations that were not at the time sufficiently supported by the humanitarian clusters or agencies and as such concentrated on the Kurdistan Region of Iraq.

The project complemented the primarily life-saving and shorter-term activities carried out by other partners through the project's multi-sectoral strategy with sustainability at its core. ICRRP covered five thematic areas, namely 1) Government coordination, 2) Basic services, 3) Livelihood recovery, 4) Protection, and 5) Social cohesion, to support IDPs, returnees, Syrian refugees, and host communities.

In December 2017, the GoI declared victory over ISIL, marking the end of the military operations in the country. ICRRP quickly adapted and expanded its geographical coverage to address the urgent needs identified in the newly liberated areas (governorates of Anbar, Diyala, Kirkuk, Ninawa and Salah-al-Din). ICRRP activities focused on the construction/light-rehabilitation/maintenance of critical infrastructure (e.g., schools, roads, public offices, public gardens, etc.) using emergency short-term job creation opportunities (Cash For Work), transition livelihood interventions to promote economic recovery (e.g., asset recovery grants, start-up grants, job placement, and vocational training), and training on peacebuilding and conflict prevention for community leaders, academics, and youth. These interventions complemented those supported by UNDP Iraq's Funding Facility for Stabilization (FFS).

In 2019, UNDP with continued financial support from the Governments of Germany and the United Sates expanded the project to other governorates, starting with Basra, as a response to the crisis which broke out in 2018. Economic, social, and environmental vulnerabilities increased in Basra due to high youth unemployment and degradation of basic services following the pollution of the Shatt Al Arab River. ICRRP continued to implement activities in 2020 under the 5 thematic areas. The support became even more critical during the COVID-19 pandemic and the subsequent lockdowns across Iraq.

Since the inception of ICRRP, the country's context has been fluid and complex, requiring a highly flexible approach. In 2021, the Project Board made a programmatic shift positioning ICRRP to focus on two main thematic areas: 1-Basic Services and 2- Livelihoods and Economic Recovery both contributing to community social cohesion. The project, with the approval of the Board was extended to 31 December 2022 and added the Ministry of Labour and Social Affairs (MOLSA) in Federal Iraq as a member of the project's governance structure.

[4] In 2014, 2.5 million civilians were displaced inside Iraq; in 2015, more than one million people fled their homes; in 2016, an additional 700,000 people fled and in 2017, 1.7 million civilians were newly displaced.

Context

Overall, the situation in Iraq has been fluid for several years. Five years after the defeat of ISIL in 2017, political instability, weak governance, and widespread corruption in public institutions are blocking structural reforms for an inclusive and resilient socio-economic recovery in Iraq. Poverty and inequality remain widespread across the country. In 2021, around 29% of the population were living under the national poverty line (monthly poverty line 115,000 IQD: 1 USD = 1470 IQD. Equal US$2.6/day). In 2020, around 14% of the population was living below the lower income middle class international poverty line of US$ 3.2/day. The coverage of social security programs is modest. Less than 5% of the population was included in 2019.[5]

ISIL control, conflict, violence, forcing displacement and ceasing agriculture production in the occupied governorates, heavily affected the population vulnerable to undernourishment. The Prevalence of Undernourishment (POU) is extremely high for an upper middle-income country. In 2019, it accounted for 37.5% of the population. In 2008, POU was 24.9% compared to an average of 11% in the Arab region, indicating a structural challenge in nutrition and food systems even before the last global food crisis in 2008[6]. COVID-19 containment measures and associated impacts on livelihoods have also played a crucial role. Inflation of food prices has been significantly increasing. Cost of food increased by 8.54% in May 2022 over the same month in the previous year.[7]

Conflict and multi-dimensional crises also restricted economic growth and limited job creation and decent job opportunities. In 2020, the unemployment rate was 14%[8], 27.7% in youth age groups[9] and 38.6% for women. Gender based violence, early marriage (28% of women married before age of 18)[10], and lack of women's economic participation are widespread. The ratio of female to male labour force participation rate accounted for 17% in 2020. Decentralization efforts and plans have not yielded strong governance and direction of resources to serve the vulnerable population. Electricity and water access (for domestic and irrigation) are still largely subsidized. Lack of access to both basic services is causing significant disruptions in productive sectors. Power outages in Iraq remain a daily occurrence for most households, as increasing generating capacity has been outrun by the increasing demand for electricity, spurred by greater cooling needs in the peak summer months. Rising demand is widening this gap, with Iraq's population growing at a rate of over 1 million per year.

The Gross Domestic Product (GDP) contracted 11.3% in 2020 due to fluctuations in oil prices and a difficult fiscal environment. GDP grew by 1.3% in 2021[11]. Favourable oil market conditions have recently pushed Iraq's fiscal balance into a surplus. However, a high budget spent on wages/pensions and the subsidization of basic services limit the ability of the government to stimulate the economy. Oil generates up to 99% of Iraq's exports, makes up 90% of government budget, contributes to 58% of GDP, but creates only 1% of total employment[12]. This has produced a fragile economy with low resilience to internal or external shocks.

In 2020, agriculture contributed to 5.89% of Iraq GDP[13]. In 2021, agriculture value added was contracted by 3.3% due to unusual low rainfall, the second lowest in 40 years. This has impacted the production of

[5] Ministry of Planning, GOI, The second National Voluntary Review Report on the Achievement of the sustainable development goals, 2021
[6] World Bank Open Data, Prevalence of Undernourishment (% of Population)- Iraq
[7] Central Bank of Iraq 2022
[8] World Bank Open Data, Unemployment, total (% of total labor force) (modeled ILO estimates)- Iraq
[9] 15–24-year-old
[10] Ministry of Planning, GOI, The second National Voluntary Review Report on the Achievement of the sustainable development goals, 2021
[11] World Bank, Iraq, overview, Context, June 2022
[12] Iraq systematic country diagnostic 2017, the World Bank
[13] World Bank Open Data, Agriculture, forestry, fishing, value added (% of GDP) =- Iraq

strategic crops (wheat and barley) at a national scale. Historically, the Tigris and Euphrates rivers provided 98% of Iraq surface water. However, reduced water flow, due to mismanagement and handling of upstream dams and groundwater in addition to salination, will increase water scarcity in the short to medium terms.

The agriculture sector generates 18% of total employment and is concentrated in rural areas[14]. The real potential of the agriculture sector has not been fully leveraged. Iraq imports 50% of its food needs. Arable land represented 11.5% of land area in 2018[15]. Agriculture production consumes 75% of total water resources. Ninety-one percent of water withdrawal is used for agriculture and flood irrigation is still the predominant system for open field production (more than 60% of irrigated land). Both water efficiency and productivity in the agriculture sector are very low accounting for less than 40%. Subsidies for the agriculture sector have been gradually lifted to very minimal support limiting their role in maintaining production and increasing productivity. The public sector contributes to 39% of total employment and there are limited opportunities in the private sector due to years of conflict and political instability. A weak enabling environment and inadequate infrastructure prevent small and medium enterprises growth. This is limiting market-oriented recovery to enable sustainable job creation.

The informal economy plays a large role in Iraq. In a recent labour market assessment conducted by ILO in partnership with UNDP, findings showed that no more than 14% of employees reported to have written contracts compared to 37% who have an oral agreement. Overall, 96% of respondents had no health insurance coverage and 91% had no social security[16].

Iraq has been one of the hardest hit countries by climate change with an annual mean temperature increasing by 1-2 degrees Celsius between 1970 and 2004, resulting in higher frequency of droughts. Average annual precipitation is decreasing. By 2050, a temperature increases of 1 degree Celsius, and a precipitation decrease by 10% will cause a 20% reduction of available freshwater resources. Under this scenario, nearly one-third of the irrigated land in Iraq will have no water by the year of 2050[17]. This will have a serious impact on food security. In 2020, the annual population growth rate was 2.4%[18]. In this regard, climate change is already impacting social and economic conditions in the country, and, if not addressed urgently, might be a conflict trigger due to climate-induced migration, and competition over scarce resources.

As of June 2022, around 1.17 million remain internally displaced and 4.96 million have returned to their areas of origins. More than 90% of IDPs and returnees are in central and north Iraq (Anbar, Diyala, Kirkuk, Ninewa and Salah al-Din)[19]. Although major efforts have and will continue to be made by the GoI to incentivize returns, many vulnerable families will be unable to return without special assistance. With the closure of camps, those families risk facing a second displacement. Displaced families living in camps and substandard accommodation will also remain highly vulnerable. The country also continues to host approximately 250,000 Syrian refugees requiring continuous assistance to avoid negative coping mechanisms.

The COVID-19 pandemic exacerbated the vulnerability of all these groups. In 2021, around 18% of IDPs, 33% of refugees, and 20% of returnees had insufficient food consumption level. Out of the 2.5 million People in Need (PIN), Iraq Humanitarian needs overview estimated around 750,000 PIN facing challenges to meet their daily food needs and around 632,000 PIN require emergency livelihoods

[14] World Bank Open Data: Employment in agriculture (% of total employment) (modeled ILO estimate) ILO

[15] World Bank Open Data: Arable Land (% of land area)- Iraq

[16] ILO 2021. A diagnostic of the informal economy in Iraq

[17] World Bank 2021. IRAQ economic monitor: the slippery road to economic recovery

[18] Work Bank open data- 2020. Population growth (annual percentage)- Iraq

[19] IMO 2022. Displacement tracking matrix- IRAQ. https://iraqdtm.iom.int/

assistance in 2022. IDPs and returnees continue to have difficulty accessing livelihood opportunities and basic services[20].

The Ukraine-Russia war increased the price of essential food commodities in Iraq and had a direct impact on the purchasing power of the vulnerable. The financial gains from higher oil price were offset by an increased import bill. Wage rates were not revised over the past 2 years and the war is exacerbating the already deteriorating food security situation in the country. The GoI faces challenges in the implementation of the Public Distribution System (PDS), one of the largest food subsidies programs providing six essential food commodities to vulnerable Iraqis[21].

Recovery is still blocked by structural, institutional and finance challenges including conflict related damage to productive infrastructure, lack of access to income generating activities, in addition to safety and security issues. Rebuilding trust within and between communities and between communities and the government requires a considerable and sustained effort to support social and economic resilience in the society, preventing the re-emergence of violence. As already outlined, the people of Iraq have been for many years facing numerous challenges including social ones (sectarianism, extremism and repeated waves of violence) which were exacerbated by the 2014 conflict. The ISIL caused massive displacements negatively impacted Iraq's social structures, especially between different sects and amongst Iraq's religious minorities. There was an increase in the number of armed groups that helped in the fight against ISIL but are now aligned to different political agendas and posing a challenge to community cohesion.

Unemployed youth remain the most vulnerable social group to radicalization – with analysis indicating that the concentration of unemployed or disenfranchised youth was the only socioeconomic demographic to which violence was consistently and strongly correlated in the period of 2004-2015. In addition, the perpetrators of ethnic violence are overwhelmingly within the 15-25 age range and are from lower-middle class socio-economic backgrounds (within the fourth quartile of individual income). Such phenomena imply that Iraq risks falling into dangerous cycles of violence, radicalization of certain social groups, particularly the youth, succumbing to propaganda from extremist groups and undertaking violent acts.

Additionally, while Central and Northern Iraq were directly impacted by the ISIL conflict, the Southern Governorates have also been indirectly impacted and require concerted support. The GoI focus on the areas of Central and Northern Iraq that were devastated by the conflict with ISIL meant that development and basic services deteriorated significantly in Iraq's Southern Governorates. These regions were also areas where communities answered the public calls to join the Iraqi Security Forces (ISF) and Popular Mobilization Forces (PMF), which helped defeat ISIL militarily.

Demands for reforms by the people of Iraq, especially youth, are increasing. The popular protests that began in October 2019 and continued to 2020, until the global pandemic of COVID-19 that caused the GoI to declare nationwide curfews and lockdowns signify the country's underlying problems. The protesters' demands for substantial political, economic and social reforms attest to the lack of progress in income equality, and the growing disparity between the centre and the periphery, and urban and rural areas.

Following the ratification of the parliamentary election results at the end of December 2021, the newly elected parliament met for the first time in the Green Zone on 9 January 2022 to elect the parliament speaker and two deputies. However, the next step in the process, the election of a President, is in abeyance as the necessary parliamentary quorum has not been reached yet. Once the President is elected, he or she will then charge the nominee of the largest parliamentary bloc with the formation of a council of ministers, to be endorsed by Parliament. The stagnant government formation process following

[20] Humanitarian Needs Overview- Iraq 2022. Humanitarian program Cycle Feb 2022

[21] WFP 2022. Iraq market monitor report, issue #31, March 2022

Iraq's peaceful elections last October 2021 is stalling urgently needed reforms, such as the implementation of the White Paper for Economic Reform and creating a dangerous political and security vacuum that could be exploited by ISIL.

The United Nations Sustainable Development Cooperation Framework (UNSDCF) of Iraq (2020-2024) prioritizes support to Iraq to grow its economy for all through improving people-centred economic policies and legislation that will contribute to inclusive, gender-sensitive and diversified economic growth, with a focus on increasing income security and decent work for women, youth and vulnerable populations. The framework is multidimensional and considers short- and long-term impediments including community social insecurity, lack access to services, and climate change effects.

UNDP's Strategic Plan 2022 – 2025 adopts an integrated development solution addressing poverty and inequality and strengthening the resilience of communities by helping countries and stakeholders increasing access to renewable energy, improving their governance system, and putting nature and environment at the heart of national economies and planning to protect natural resources. This is enabled through 3 directions of systematic change: building resilience, leaving no one behind, and structural transformation (green, inclusive and digital transitions).

UNDP Iraq's Country Programme 2020 – 2024 puts in place a sustainable livelihoods framework that aims to support Iraq to strengthen businesses ecosystems, especially in high-impact, labour-intensive productive sectors and improve access to markets and finance through innovative financing options. UNDP will also work on establishing small and medium enterprises (SMEs) and start-ups; promote skills development and job placement; and set up a system for asset grant replacement.

STRATEGY AND RESULTS

Against this multi-dimensional challenging context, ICRRP will support the GoI vision for a sustainable peaceful Iraq through an integrated approach that strengthens societal resilience to deal with social, economic, environmental, and political shocks and stresses, while addressing risk drivers.


In this regard, ICRRP will:

- aim to strengthen local government capacities for inclusive green economic development; support innovative solutions through public-private partnerships that stimulate local economic development; provide income and employment opportunities for vulnerable groups and promote social cohesion and environment-friendly business practices, especially in growth-promising economic sectors that have a high impact on employment creation. UNDP will support both the central level and underserved regions, especially those liberated from ISIL, southern governorates and the Baghdad belt.
- support resilient, low-emission, development pathways to cope with climate change and environmental risks and exposures. Key elements will include prompting sustainable water governance, sustainable practices of wastewater and solid waste management; improving access to clean renewable energy; and strengthening resilient climate smart agriculture and biodiversity. To restore citizens' confidence in governance institutions and state legitimacy,
- support accountable, transparent, efficient institutions able to deliver basic services, through support to policies and actions for inclusive, participatory and responsive planning, budgeting and decision-making processes that reflect the needs and priorities of vulnerable groups.

The project will continue to focus on vulnerable Iraqi populations, including **internally displaced persons, returnees, and disengaged former fighters, and host communities**, with a special emphasis on women and youth; and identify the support requirements for particularly vulnerable groups (i.e., minority groups, and victims of GBV).

Geographically, the project will target all governorates of Iraq, with a special emphasis on the most vulnerable localities. ICRRP will tailor the response to address the needs of the people of Iraq based on identified shocks, assets (human, social, financial, natural, and physical), institutional capacities and processes and available opportunities in target communities.

To this end, ICRRP will work on three integrated and multi-dimensional thematic areas of focus with various sub-targets and components to strengthen resilience:

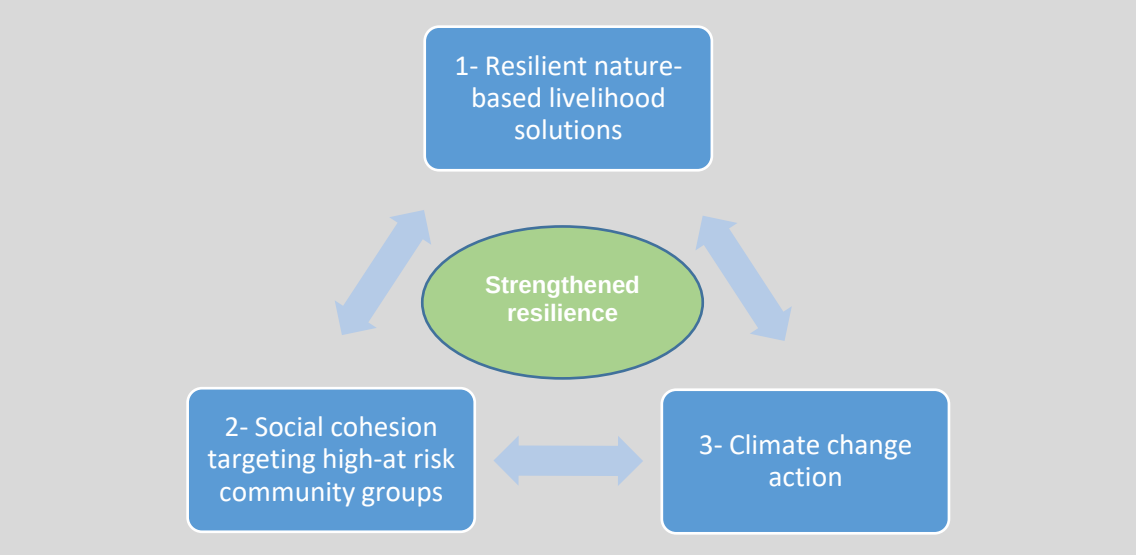


ICRRP will continue to ensure community engagement across thematic areas, and serve as a platform that links the community with other stakeholders, such as local authorities, private sector, academia, other development organizations, etc. It will also **continue to engage Iraqi Civil Society Organizations** (where relevant and suitable) to **empower and strengthen** their capacities to lead community level processes for policy advocacy, and peace- building in the longer term, and to implement defined activities.

ICRRP will focus **on medium to long-term interventions** to support meaningful recovery and resilience processes and build peaceful communities to lay a strong foundation for sustainable development of Iraq.

ICRRP will maintain a **flexible approach** to programming and will mainstream conflict-sensitive approaches in the three thematic areas to address the underlying challenges of exclusion, marginalization and societal divisions. Gender and youth will remain important elements of implementation. Emphasis will also be done to mainstream environmental sustainability considerations in all activities.

Guiding Principles

ICRRP is guided by the following principles.

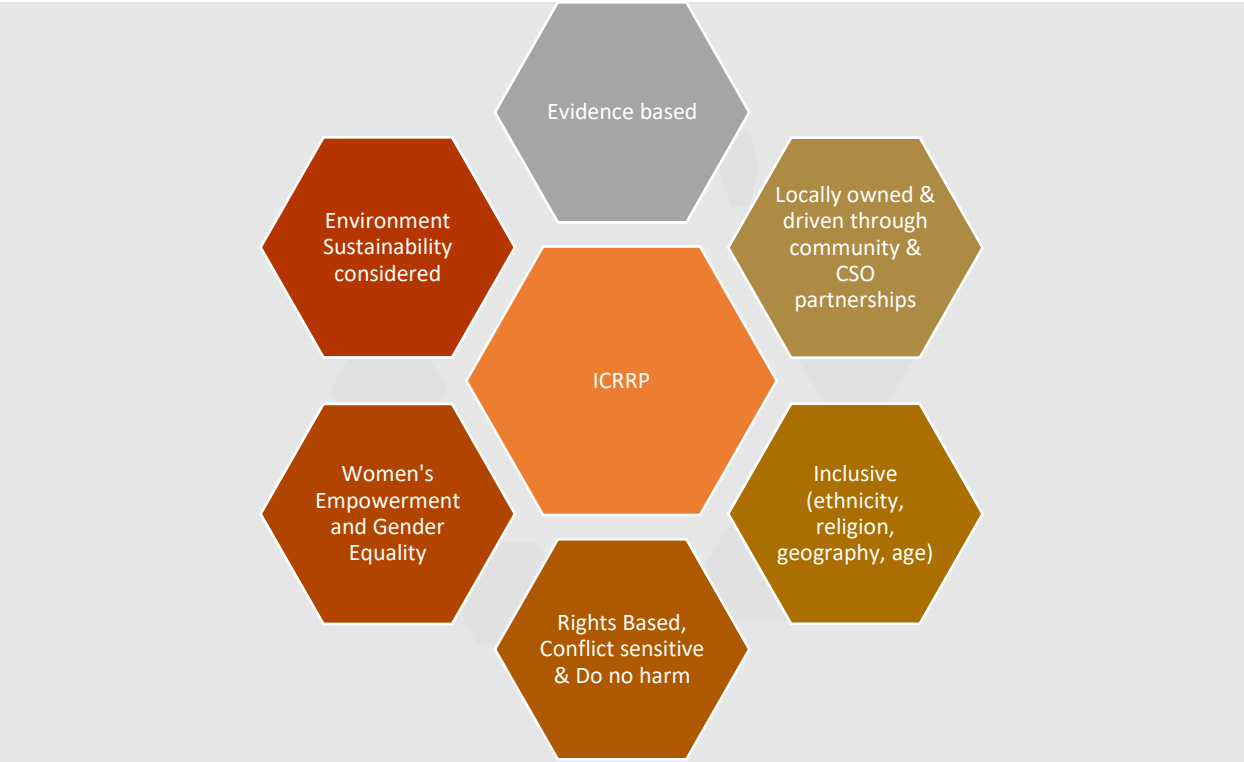

Gender and Youth

Women in Iraq have faced high levels of gender-based violence, including domestic violence, sexual harassment, honour killings, female genital mutilation, forced and early marriage, and human trafficking. They are excluded from accessing jobs and services, particularly in poor rural areas, heading households and experiencing high levels of poverty. When it comes to conflict situations, Iraqi women have always been among the first to feel the impact of violence and conflict. SGBV has been also at a high level among IDPs and the Syrian refugees. As detailed in the context section, youth in Iraq, (and especially young women) feel disempowered for various reasons, including due to lack of freedom of expression, challenges in access to education, employment opportunities, and the wide-spread social restrictions due to traditional and religious practices. As a result, youth in Iraq have become an easy target for extremist ideologies.

Gender will be mainstreamed across ICRRP in line with UN Resolution 1325 and UN Seven Point Action Plan on women's participation in peacebuilding. The activities funded by the Project will be designed to improve institutional policies and systems to incorporate gender considerations (i.e., crisis management and response systems), develop women's capacity to have meaningful participation in recovery processes (which contribute to the country's path to development), focusing on bridging gaps, reducing gender inequality, improving wellbeing and creating economic opportunities. Engaging men and boys will be key to challenge cultural gender norms and to advance gender equality and women's empowerment.

In keeping with UN Resolution 2250, youth will also be a specific target group under ICRRP. Specific provisions will be made to ensure women and youth participation in the planning, implementation and monitoring activities. This will eventually ensure equal access to benefits and resources for men and women.

The Project will strive to improve gender equality and women's empowerment in the following ways:

- Undertaking a gender analysis when needed to identify gaps and inform programming with specific gender dynamics.
- Commitment to mainstreaming and promoting gender equality, and the empowerment of women and girls through the project design and implementation mechanisms.
- Upholding UNDP's zero-tolerance policy on sexual and gender-based violence and abuse of authority.
- Conducting sensitization sessions and trainings for the Project staff, including dedicated sessions for associated field and monitoring teams, for increased capacities in gender mainstreaming.
- Ensuring assessments and community engagement exercises are designed with a view to encourage equal representation of women in all consultative processes and the perspectives of women are given equal weight in decision making. Where relevant community consultations will adopt specific measures to engage women, including if required having separate consultations where they feel comfortable to express their views.
- Providing opportunities for qualified women to take more active role in the decision making, implementation (e.g., women engineers) and monitoring process of rehabilitation works while creating a safe working environment.
- Through gender sensitive assessment, actively identifying opportunities, and designing livelihood activities that will create a greater space for women's engagement.
- In implementing livelihood activities, to promote engagement of women, taking into consideration the times and locations where activities are implemented with consideration of social and familial norms in Iraq (i.e., looking after their children, preparation of food etc.,) and cultural considerations (i.e., ability to travel long distances by themselves etc.).
- Identify women influencers and engage them in community mobilization as a way of increasing women participation.
- Monitor progress using gender-disaggregated targets and data, to ensure evidence-based decision making and project management.

Environment and Natural Resources

Iraq faces numerous threats to its environment and natural resource base, which have serious implications for its social and economic development and political stability. In terms of natural resource base, the risks include, i) growing water scarcity, water salinity and water pollution, ii) severe heat waves, iii) land degradation and desertification, iv) loss of biodiversity, especially in the historic marshlands, and v) the consequential worsening situation of sandstorms, droughts and periodic flooding.[22]

Furthermore, pollution of land, water and air is worsening with the high population growth, urbanization and the expansion of industries. This includes the industrial, urban, and medical waste and chemicals flowing into water ways and landmines. There is a lack of urban waste management. Carcinogenic plastic materials are not treated.

As the country transitions from a humanitarian to a development context, policies on sustainable development and climate change action are taking a centre stage, ICRRP will aim to ensure compliance to national environmental priorities and will make sure interventions protect the environment and natural resources. This would include for example introducing the environmental concerns into the crisis management/response policy and planning discourse, introducing environmental impact assessments for proposed infrastructure and livelihood interventions, promoting environmentally friendly and climate smart livelihood solutions, raising awareness on the importance of the environmental dimension to ensure sustainability, building stakeholder capacities about environmental protection, and mapping tensions around natural resources (i.e. access to water and land) through a conflict analysis lens, and working to resolve these tensions through community led dialogue and negotiation.


[22] National Disaster Management Strategy in Iraq, November 2015

Conflict sensitivity

The highly dynamic context in Iraq calls for an age, gender and conflict-sensitive approach as well as regular reviews and adaptations to remain in sync with the rapidly changing reality in the selected project sectoral and geographic areas. Gender-sensitive context/conflict analyses will be a cornerstone for programming in ICRRP. This will help in understanding conflict dynamics and inform all interventions to contribute to an adaptive management practice. The conflict sensitivity approach requires UNDP and its implementing partners to analyse and understand the impact of national and local conflict dynamics on UNDP Iraq and partners´ ability to deliver resilience and reintegration programmes. This will include UNDP's political, reputational, organisational, operational and staff risk management approach and focus on security aspects and beyond.

The other aspect of conflict sensitivity considers the impact of UNDP Iraq's programmatic interventions on the various national and local conflicts. The focus on conflict will go beyond the do-no-harm approach by explicitly providing support to local actors to resolve conflicts. Stated differently, UNDP shall not work around conflict, but work on conflict. Integrating conflict sensitivity into its programmes will allow UNDP to provide ongoing conflict and political economy monitoring and analysis which in turn will allow for swift adaptation of existing programmes and projects.

Expected Results: ICRRP will be based on the following theory of change:

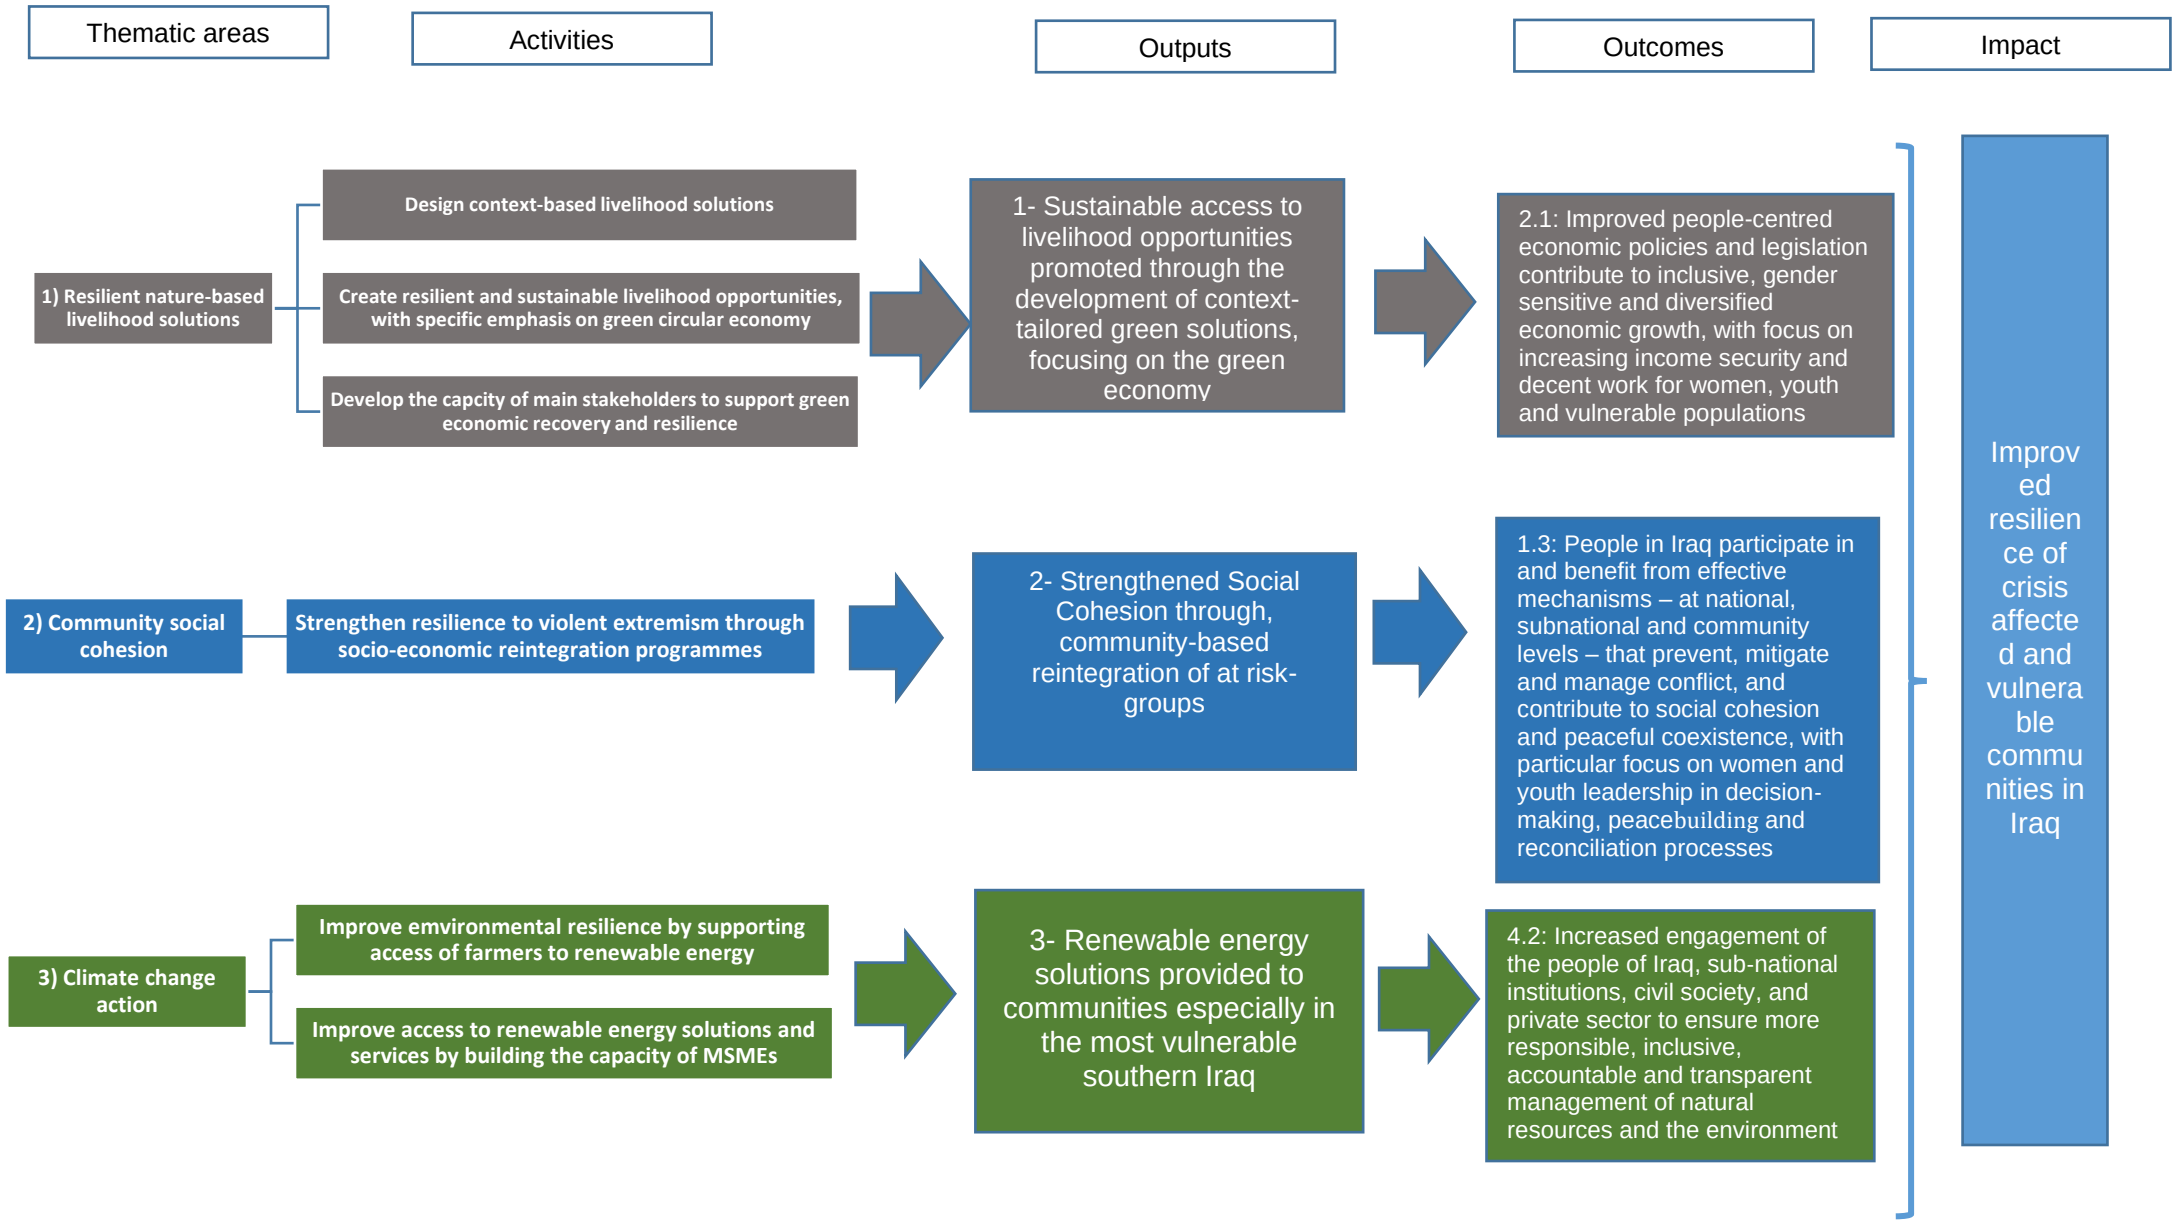

***Outcome*:**

ICRRP will contribute to outcome 1.3, 2.1, and 4.2 of the UNSDCF (2020-2024)

- 1.3: People in Iraq participate in and benefit from effective mechanisms – at national, subnational and community levels – that prevent, mitigate, and manage conflict, and contribute to social cohesion and peaceful coexistence, with particular focus on women and youth leadership in decision- making, peacebuilding and reconciliation processes.
- 2.1 Improved people-centered economic policies and legislation contribute to inclusive, gender sensitive and diversified economic growth, with focus on increasing income security and decent work for women, youth, and vulnerable populations.
- 4.2: Increased engagement of the people of Iraq, sub-national institutions, civil society, and private sector to ensure more responsible, inclusive, accountable, and transparent management of natural resources and the environment.

ICRRP is also aligned with the new **UNDP Strategic Plan (2022-2025)** and will contribute to the 6 signature solutions prioritized to guide people and planet beyond 2025:

1. **Poverty and inequality:** tacking inequality of opportunities by investing in the enhanced capabilities people need to move above the poverty line and keep moving forwards
2. **Gender equality:** confronting the structural obstacles to gender equality and strengthening women's economic empowerment and leadership
3. **Energy:** increasing energy access to those further left behind and accelerating the transition to renewable energy
4. **Environment:** putting nature and the environment at the heart of national economies and planning, helping government protect, manage, and value their natural assets
5. **Resilience:** supporting countries and communities in building resilience to diverse shocks and crises, including conflict, climate change, disasters, and epidemics
6. **Governance:** helping countries address emerging complexities by future-proofing governance systems through anticipatory approaches and better management

ICRRP will also contribute to the achievement of the National Development Plan (2018-2022), in particular:

- Priority (3): Recovery of communities affected by the displacement crisis and the loss of human security.
- Priority (4): Providing the requirements of an enabling environment for investment in all its forms and enhancing the role of the private sector
- Priority (5): Raising the economic growth rate in line with the Iraqi economy's potentials and requirements and
- Priority (7): Reducing unemployment and underemployment.

Furthermore, since the endorsement of the 2030 agenda for **Sustainable Development**, ICRRP contributed and will continue to contribute to several **Sustainable Development Goals**, of which the most important are Goal 1 (No Poverty), Goal 2 (Zero Hunger), Goal 5 (Gender equality), and Goal 16 (Peace, Justice, and Strong institutions). Starting 2022, ICRRP will also work to contribute to Goal 7 (Affordable and clean energy), Goal 8 (Decent work and economic growth), and Goal 12 (responsible consumption and production).

ICRRP will target three distinct, but interlinked outputs, which contribute to strengthening resilience and stability in Iraq.

Output 1: Sustainable access to livelihood opportunities is promoted through the development and implementation of context-tailored green solutions.

After the defeat of ISIL, ICRRP prioritized the creation of short-term, stabilization job creation interventions that aimed to provide a fast-track income generation for the most vulnerable through a community integrated engagement process. From 2014 till June 2022, ICRRP created 37,900 (31.1% for women) Cash for Work (CFW) opportunities[23] through the rehabilitation of core community assets. Impact assessments showed that the cash injected through CFW projects activated local economies and directly contributed to the households' food security of the most vulnerable. ICRRP has also implemented early recovery livelihood assistance that focused on waged and self-employment creation through a transition lens. It supported Iraqis (returnees, IDPs, women, and youth) to increase their skills and employability through vocational training and on the job-placement with the private sector. A total of 16,015 beneficiaries received start-up, asset replacement or scale-up grants to boost their businesses. ICRRP has developed an SMEs support methodology to structure SMEs' recovery process and has built the capacity of MOLSA staff to better design and monitor the support provided to their SMEs' grant program. A total of 14,630 beneficiaries received vocational training support to improve their skills and employability. ICRRP has piloted private sector engagement with Toyota- Iraq to provide a real example of how the private sector and the international community can work together to address Iraqis' socio-economic needs. Around 70 trainees graduated and 70% of them were employed directly by Toyota or their dealers across Iraq.

Going forward, ICRRP will focus more on advanced transition and sustainable interventions to strengthen economic recovery and resilience, while ensuring conflict sensitive and climate smart livelihoods are prioritized. ICRRP will select at the district level viable economic sectors and support their recovery and resilience by creating clusters as social capital, building the capacity of actors, rehabilitating, and supplying necessary assets to upgrade the selected sectors/value chains, providing scale-up and growth grants to diversify products/services, and providing start-up grants for the most vulnerable to support their inclusion in the selected sectors/value chains. The size of the grant will be tailored according to the business ability to create employment and the potential return on investment on the short and medium terms.

Sectoral and value chain interventions will be prioritized to prepare the ground for solid recovery and resilience solutions supporting Iraqis to adopt sustainable pathways in the long term.

In parallel, wage employment will be supported by additional engagement of the private sector as a receiver of skilled labour and the public sector as a facilitator of skilled labour through vocational training schools.

ICRRP will leverage the lessons learned from UNDP livelihoods interventions implemented between 2018-2022 to design medium- and long-term livelihoods solutions incorporating the 2 principles – ownership and sustainability- of 3x6 approach within 3 enablers (digital transformation, access to finance, and climate smart) that ensure Iraqis are structurally supported to lay the foundation for a sustainable and diversified livelihoods recovery.

Where rehabilitation of livelihoods' physical assets is necessary to upgrade the selected value chains, ICRRP will continue using the CFW modality to create short-term job opportunities for the most vulnerable. Under this component, ICRRP will incorporate the lessons learned gained from the Employment Intensive Investment Program (EIIP) that was piloted in 2021-2022 with ILO to design CFW projects in a more responsive and inclusive manner with a wider impact on the community.

As cross-cutting themes for all interventions, ICRRP will promote evidence-based design and implementation of activities that support circular and green economy, the use of alternative energy,

[23] At least 40 working days for each beneficiary

climate smart interventions, the use of digital transformation, promotion of social cohesion, women inclusion, and human rights-based approach, and the reintegration of returnees and former fighters. A conflict sensitive approach will be streamlined in activities where needed to reduce tension and increase inclusion.

ICRRP will consider agriculture and non-agriculture economic sectors that are both crucial to address the increasing level of food insecurity and the creation of livelihoods opportunities. Line ministries, development offices, business associations, chamber of commerce, cooperatives, SMEs, research centres, academic institutions, vocational training centres are examples of potential partners.

Output 2: Strengthened Social Cohesion through, community-based reintegration of at risk-groups.

In the context of Iraq, ICRRP has defined social cohesion as a general condition of stable co-existence within communities, when community members accept socio-ethnic differences, have equitable access to socio-economic and other community resources, and feel safe and secure in their homes.

ICRRP recognizes that building peace and social cohesion in Iraq will require a sustained and considerable effort, and one that is underpinned by political commitment, an inclusive and clear vision, and sustained and coherent external support. It requires addressing Iraq's conflict impacts including ensuring the safe and durable return and reintegration of IDPs and other vulnerable groups such as disengaged volunteer fighters creating conditions for social and economic development that benefit all segments of the Iraqi population; putting in place mechanisms and processes at multi-levels that are able to deal with conflicts constructively and non-violently; and strengthening conditions for co-existence between groups to prevent or withstand the re-emergence of violence. Further, longer-term strategic partnerships between the GoI and the international community are required to cultivate an environment enabling an inclusive national approach to social cohesion, and a strategic approach covering all parts of the country.

UNDP Iraq adopts an integrated approach to establishing foundations for peace and creating safe and habitable conditions for dignified returns while supporting prevention of violent extremism and strengthening justice, security, and the rule of law. The overall goal is to enhance resilience amongst communities/groups vulnerable to marginalization and violent extremism by advancing improved citizens' peaceful co-existence, perceptions of justice, inclusion and equality, community safety and security, and better socio-economic conditions in the target locations. The integrated approach of stabilization, security sector reform and social cohesion and building on each programme's mechanisms, partners and expertise positioned UNDP highly at the policy and implementation level as the key stabilization supporting agency with local and national partners.

ICRRP will target conflict-sensitive responses to specific groups at risk to ensure sustainable community reintegration and peaceful coexistence, especially for men, women and youth at-risk, disengaged volunteer fighters in targeted communities.

This will be done through an integrated and comprehensive package that includes livelihoods integration (vocational and business development training, and business start-up grants), psychosocial support, and community-resilience for the prevention of violent extremism.

- A target high risk group under this component of ICRRP are the disengaged former fighters in Iraq. The beneficiary selection under this programme will be subject to a rigorous vetting process based on a pre-determined set of selection criteria to ensure that support is provided to those who are most vulnerable and at risk of exclusion and or violent extremism. Another main selection criterion is that beneficiaries of this program must have been disengaged since at least three years, and are security cleared by the Iraqi authorities. Scoping assessment inclusive of market research will be conducted to determine the vocational training sectors and start-ups profiles. This goes in parallel to output one and includes targeted research for gender mainstreaming to

strategically support the economic empowerment of women as an integral part of the project's beneficiary group. All activities will be trauma-informed, and a series of mental and psychosocial support services will be provided (MHPSS) to enhance the resilience and healing process of the targeted groups to be able to better integrate in their communities. To this end, ICRRP will ensure: trauma-informed, and community-based reintegration services designed and implemented to target vulnerable and at-risk groups including disengaged fighters through psychosocial/mental health, catch-up education/vocational training, job placement/start-your-own business in the targeted locations.

- community security interventions implemented
- community stability support schemes (rehabilitation of community infrastructure, i.e., health clinics, vocational training centres, and markets) implemented as collective reparation and/or peace dividend at the community level and to foster local-level institutional strengthening.
- One-Stop Information Centres (OSIC) established in the target locations, with trained focal points to provide necessary referral services to all beneficiaries with special focus on women and girls
- Best practice and lesson learned documents and policy briefings elaborated and shared.
- Beneficiary satisfactory surveys conducted to gauge the level of satisfaction and quality of services provided to targeted groups including disengaged fighters
- Local and community structures strengthened to be effective, social cohesion, reintegration, and prevention of violent extremism

Output 3: Environmental resilience and response to climate change improved through promoting renewable energy/services among vulnerable communities.

Iraq suffers from a chronic lack of energy access, which in recent years has contributed to social and economic instability, and in some cases even triggered violent civil protests. Power outages remain a daily occurrence for most households. Power generating capacity has been outrun by the growing demand spurred by greater cooling needs in the peak summer months. Over the past five years, the gap between peak electricity demand and maximum grid supply has expanded despite the increase of available supply by one-third.

ICRRP will support pilot activities for renewable energy solutions that are reliable, tangible, scalable and cost-effective for communities exposed to rising temperatures and water shortages. It will focus on enhancing public exposure to the utility of clean energy solutions and will support market-based services through MSMEs.

Being the primary source of livelihoods for the most vulnerable, the agriculture sector will be targeted by ICRRP through the promotion of renewable energy solutions. Usage of solar energy will be promoted across agriculture value chains to help farmers/producers and processors decrease their cost of production and increase their resilience. ICRRP will work to provide renewable energy solutions to farmers in remote areas, who have no access to power from the state network. In the absence of grid connectivity, farmers usually resort to use of diesel generators for irrigation and other purposes. This increases their overall cost of production. With solar energy, farmers could have access to a sustainable source of energy which will reduce their cost of production and assets' maintenance. The productivity of solar energy is very high all over Iraq. ICRRP has piloted the use of solar energy for water pumping and results were very promising. The expansion of solar energy supply however faces multiple challenges including the low awareness of users, high upfront cost, and limited supply and knowledge of the technology. ICRRP will work to subsidize pilot solar energy solutions for the agriculture sector, raise awareness among farmers on the potential of solar energy, promote most successful solar technologies, as well as build capacity within the private sector for high quality solar energy solutions. The Project will focus on strengthening the role of MSMEs in the solar energy sector, which would also create job opportunities for youth. The training will be conducted on following subjects

A) Basic training workshops

- Cost effective design of long life and safe solar energy installations for small scale distributed off-grid irrigation
- Determine the quality of components (PV panels, inverters, batteries, pumps etc.)
- Marketing of solar energy units
- Identification of potential buyers
- Global market trends and technologies
- On-site training for staff

B) Advanced training workshops

- Diagnose solar installation problem
- Main parts software and hardware reparation of solar installations
- Cost effective design of after sale service

Through coordination with the local agriculture departments and farmer's associations, the geographic areas and individual farmer beneficiaries will be identified for supply of solar energy solutions. The criteria will be designed in consultation with the farmer associations, the agriculture department and other stakeholders to select individual beneficiaries. The criteria may be guided by considerations of remoteness, affordability, vulnerability, connectivity to grid/or lack of it, minority and marginalized groups, among others.

UNDP (through selected suppliers - MSMEs) will procure the solar equipment and facilitate its installation at the farm, storage and market facilities. Awareness, training and capacity building activities for the beneficiary farmers and the MSMEs will be carried out in parallel. The intervention would contribute to following direct impacts:

- Support livelihoods of the most vulnerable communities
- Reduce vulnerability
- Raise awareness of communities about benefits of solar energy
- Develop-capacity of the MSMEs on new technologies, maintenance and market development
- Promote climate change mitigation solutions

The activity will directly benefit 1200 farmers in three years with supply of solar panels and awareness-raising activities, while 200 staff of the MSMEs with training.

Partnerships and Stakeholder Engagement

The Project overall works in close consultation and partnership with the GoI, at national, governorate and local levels, and with the Kurdistan Regional Government. ICRRP/UNDP has been providing technical Assistance to the Ministry of Labour and Social Affairs (MoLSA) on Support to SMEs and Labour Market. The support aimed to improve corporate and staff capacity to effectively support and monitor small enterprises that received loans, incubation services from the ministry, and develop labour market indicators.

ICRRP beneficiaries, both individual and institutional are critical stakeholders, and regular engagement is therefore crucial for ensuring the project meets the priority needs of target communities and the strategies/plans of the Government. Regular interaction, starting from initial consultations with the communities, local, national and international partners to inform project prioritization will be ensured, including development partners and the main financial contributors to the Project as the key policy advocates with the GoI.

ICRRP also capitalizes on strategic partnerships to achieve quality results. Interventions will be implemented directly by UNDP and in close coordination with the Federal, Provincial and Local Governments, and other stakeholders who will serve as Responsible Parties.

Where required, ICRRP will leverage the comparative expertise and experience of sister UN Agencies on the ground in Iraq, such as IOM, FAO, UNIICEF and ILO, in implementing specialized activities (i.e., reintegration, livelihoods etc.).

To ensure coordination and information sharing with the relevant UN Agencies, UNDP will utilize UN coordination forums and mechanisms including the social cohesion, durable solutions, economic growth, and environment priority working groups of the United Nations Sustainable Development Cooperation Framework (UNSDCF), the Durable Solutions Technical Working Group (DSTWG), and the Prevention of Violent Extremism (PREV) technical working group.

A key feature of ICRRP has been engagement with civil society. As it moves forward, ICRRP will see an expansion of its partnership base, to invest in strengthening and empowering the local civil society, to play an active and constructive role in Iraq's path to achieve stability, and sustained peace. ICRRP aims to identify strategic linkages with private sector in addition to international academic and research institutions to support its efforts under the three thematic areas.

ICRRP will leverage the comparative experience and expertise of the relevant complementary projects and programmes such as Funding Facility of Stabilization (FFS), Social Cohesion, and others to ensure synergy through complementarity and continuity.

Risks and Assumptions

The Project is based on the following key assumptions:

- Policy makers/ key government officials and institutions, continue to be willing to engage with UNDP and ICRRP, and are receptive to the resilience support provided.
- Stakeholders, in particular beneficiaries are receptive to the support provided.
- Sufficient levels of security and political stability exist, enabling access to the target areas, to design, implement and monitor the project activities.
- Sufficient resources for the project are available, and on time.

The rapid changes in social, political, economic, operational and security situation at national and local levels are broadly the main anticipated categories of risks. The specific risks are detailed, together with the mitigation measures in the Annex to the Project Document.

Knowledge

ICRRP being one of the larger crisis response and recovery support Projects in the MENA region will aim to document and disseminate its learning, both on programmatic and operational matters. Given the current trend of intense fragility and conflict in the Arab region, the project will actively contribute to regional level learning programme design and management. The Project will also share its experiences, both positive and negative, with the Government, civil society and other partners. The Analysis (i.e., conflict, context and development analysis) and Assessments (i.e., Institutional Capacity Assessments, Livelihood Market Assessments, Needs Assessments, value chain assessment, sectoral assessments, etc.) undertaken through the Project, will be disseminated among partners/stakeholders, with a view to sharing knowledge and informing required mitigation and adaptation measure.

Sustainability

The Project's sustainability and exit strategy is built into the Project's approaches and activities. Before the final year of implementation, the Project will undertake a review of its overall strategy, with a view to developing a detailed plan for transition and exist. The exit strategy will also be informed by the findings of the Project evaluation proposed for 2023. The key elements of sustainability and exist strategy include the following:

a) The Project invests in creating/strengthening institutional capacities across the different components that would take the areas of work forward.

b) Engagement of civil society organizations, as Responsible Parties and as beneficiaries, would enable the Project to support capacity building of local and national civil society organizations and to respond to the fast-evolving needs of the vulnerable and at-risk groups in the communities.
c) The capacity building support for direct community beneficiaries (i.e., vocational training, job-placement, business development support, mentorship etc.) would help to develop their practical skills and knowledge to enable them to create income generating opportunities in the medium term.
d) Close engagement with relevant institutions at local and national level will be factored to ensure ownership and continuity of work initiated by the Project and later scaled up.
e) Venues and assets rehabilitated or supported by the project will be handed over to the respective National/ Local Authority/civil society partner. Capacity building provided to end users and stakeholders will ensure the assets delivered by the projects are maintained and continue supplying socio-economic benefits for the most vulnerable.

Project Management

The Project will be managed through the direct implementation modality (DIM) by UNDP Iraq, which is accountable for the overall achievement of results and management of resources.

UNDP will identify the required and qualified service providers and/or Responsible Parties, to support implementation of activities. Service providers and Responsible Parties will be selected according to UNDP's established Programme and Operations Policies and Procedures following as required procurement or programmatic selection processes, to achieve high quality results, to mitigate risks and to strengthen administrative efficiencies. Service providers and Responsible Parties will be directly accountable to UNDP in accordance with the terms of each agreement. Service Providers and Responsible Parties can be qualified entities from private sector, civil society, academia and/or government as deemed necessary to meet the requirements of the Project.

Financial contributions will be received by ICRRP, as both earmarked and un-earmarked contributions from donor countries. Funds will be managed by adhering to UNDP's Financial Rules and Regulations and with alignment with the Donor Contribution requirements.

The Project will be audited within the framework of the Direct Implementation Modality (DIM) as determined by UNDP's Office of Audit and Investigation (OAI). Additionally, any Responsible Party engagements that are guided by the Harmonized Approach to Cash Transfer (HACT), would be subject to spot-checks and audits in keeping with the requirements of the HACT Framework. The Project will also be evaluated in keeping with UNDP's Evaluation Guidelines both at mid-point and at the end of the Project.

Governance and management arrangements

ICRRP Project Board serves as the overall project governance structure. The Project Board provides the strategic directions and oversight of ICRRP and ensures that the interventions funded through ICRRP are in line with the Government priorities.

The Project Board will be chaired by UNDP, with the participation of the Ministry of Planning of the Kurdistan Regional Government (KRG) and the Ministry of Labor and Social Affairs (MOLSA) (Board decision on Feb 11, 2021) in Federal Iraq, and international partners to this program. The composition of the Project Board may be adjusted upon the decision of the Chair.

UNDP will serve as secretariat to the Project Board and will present regular updates on assessments, contracting, implementation, results, and contributions.

In principle, the Project Board will convene annually, although the Chair may decide to hold meetings at any time. The Project Board is expected to play a facilitating role and serve as an agile mechanism providing timely guidance in a rapidly changing context. Every effort will be made to achieve consensus on key issues. Where this is not possible, decisions will be guided by the Chair.

The Project Board is responsible for making, management decisions for ICRRP when guidance is required by UNDP, including recommendation for UNDP/Implementing Partner approval of project plans and revisions. To ensure UNDP's ultimate accountability, Project Board's decisions should be made in accordance with standards that shall ensure management for development results, best value money, fairness, integrity, transparency, and effective international competition.

Any member of the Project Board can propose to establish a sub-committee or task force group to discuss specific thematic or strategic matters related to ICRRP. Establishment of such a group will be endorsed by the Chair and approved by the Board.

The responsibilities of the Project Board include:

- Endorsing proposed ICRRP interventions, ensuring that these are in line with the strategic priorities of the Government and complementary to other efforts undertaken in relevant areas.
- Reviewing the priorities and appropriateness of ICRRP interventions.
- Providing policy guidance where required.
- Identifying obstacles to implementation and impact and agreeing on steps to address these.
- Reviewing periodic progress and financial reports.
- Reviewing risk mitigation measures.

Government of Iraq and Kurdistan Regional Government

The Government of Iraq (through MOLSA) and the Kurdistan Regional Government (KRG) are represented in the Project Board as the Senior Beneficiaries.

The UNDP Resident Representative

The UNDP Resident Representative will serve as the Executive and Chair of the Project Board. S/he will ensure full compliance of the Project with UNDP's Rules and Regulations, alignment with the UNDP Country Programme 2020-2024, and coordination and complementarity with the other UNDP Projects implemented in Iraq.

Head of Stabilization

The Head of Stabilization (HoS) is the Portfolio Manager in UNDP Iraq for Stabilization and Recovery support. The HoS provides guidance regarding the technical feasibility of the project. Moreover, the HoS provides advice on the identification of strategies, design and methods to carry out Project actions. Both roles help to ensure the needs and expectations of the beneficiaries are met.

The HoS reports to the UNDP Resident Representative for all strategic priorities and operational matters related to programming for Stabilization and Recovery. HoS coordinates with UNDP's Deputy Resident Representative (Programme) to ensure coherence with UNDP's country overall programme.

Project Management Team


ICRRP is managed by UNDP in line with UNDP corporate rules and regulations. The Project Management Team is responsible for the successful management of Project outputs and contribution to the achievement of Project outcomes. The Programme Manager (PM) has the responsibility to run the Project on a day-to-day basis on behalf of UNDP, and within the framework outlined by the Project Document and the guidance of the Project Board. The PM is responsible for working in coordination with

the respective Senior Beneficiary/ies, and service providers and Responsible Parties of the Project to ensure project implementation, financial management, administration, monitoring and reporting takes place in a timely manner. The Project Management Team also comprises of relevant technical, coordination, administration, finance, reporting, monitoring and evaluation expertise, both international and national. The Project Management Team comes directly under the oversight and purview of the HoS.

Project Assurance

The Project Assurance role provided by UNDP supports independent project oversight and monitoring functions. This role ensures appropriate project management milestones are managed and completed. The Project Assurance role needs to be engaged throughout the Project to ensure that the Project remains relevant, follows the approved plans and continues to meet the planned targets with quality. Project Assurance is required to ensure beneficiary needs and expectations are being met and/or managed; risks are being controlled; the project remains viable; applicable UNDP rules and regulations, and donor requirements, are being observed.

ICRRP Project Governance and Management Structure

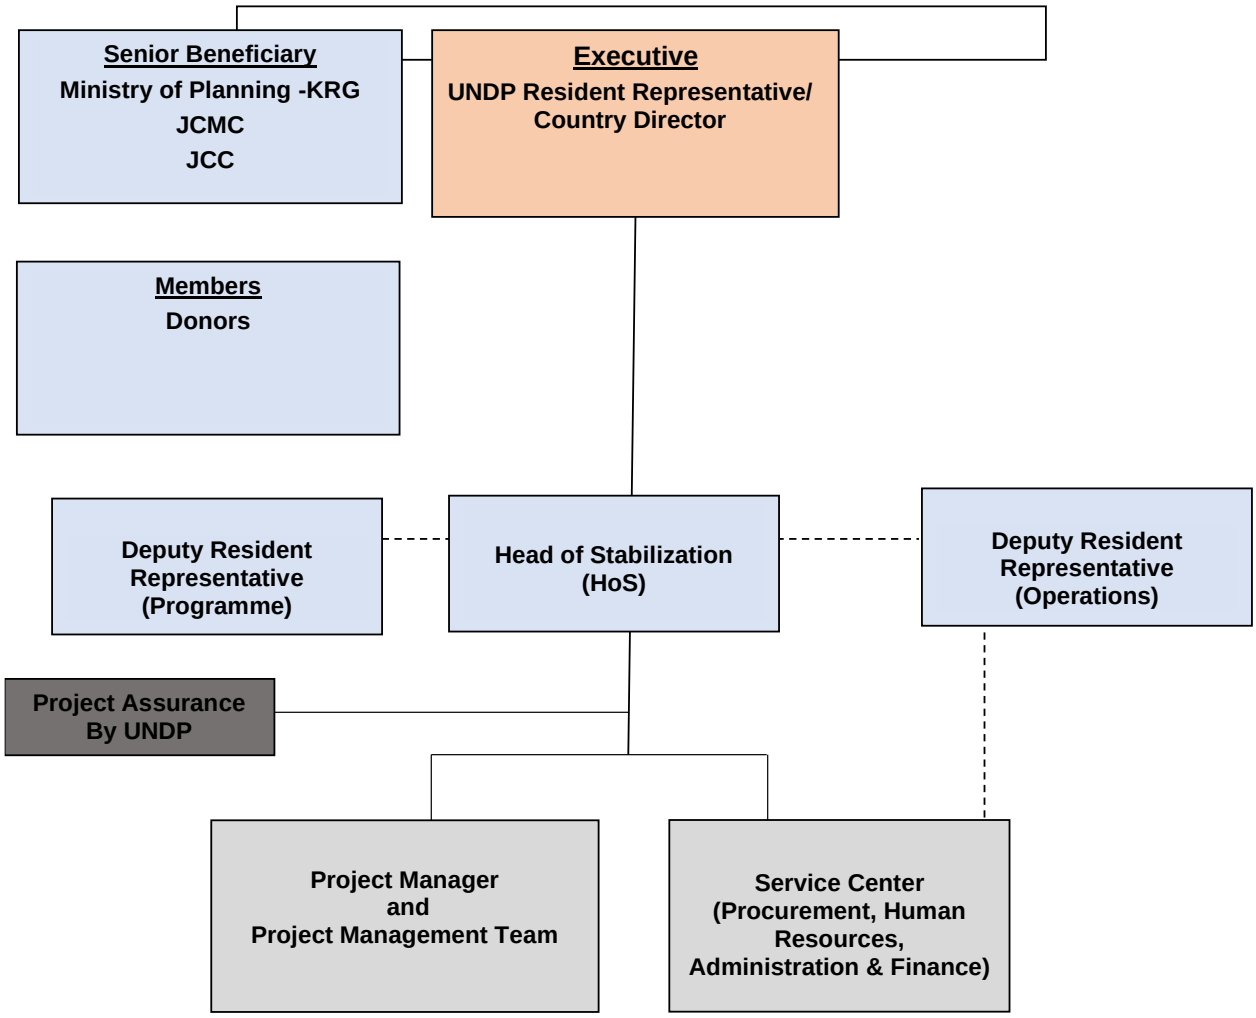

LEGAL CONTEXT

*[NOTE: Please choose **one** of the following options, as applicable. Delete all other options from the document]*

Option a. Where the country has signed the Standard Basic Assistance Agreement (SBAA)

This project document shall be the instrument referred to as such in Article 1 of the Standard Basic Assistance Agreement between the Government of (country) and UNDP, signed on (date). All references in the SBAA to "Executing Agency" shall be deemed to refer to "Implementing Partner."

This project will be implemented by [name of entity] ("Implementing Partner") in accordance with its financial regulations, rules, practices and procedures only to the extent that they do not contravene the principles of the Financial Regulations and Rules of UNDP. Where the financial governance of an Implementing Partner does not provide the required guidance to ensure best value for money, fairness, integrity, transparency, and effective international competition, the financial governance of UNDP shall apply.

RISK MANAGEMENT

UNDP (DIM)

1. UNDP as the Implementing Partner will comply with the policies, procedures, and practices of the United Nations Security Management System (UNSMS.)

2. UNDP as the Implementing Partner will undertake all reasonable efforts to ensure that none of the [project funds][24] [UNDP funds received pursuant to the Project Document][25] are used to provide support to individuals or entities associated with terrorism and that the recipients of any amounts provided by UNDP hereunder do not appear on the list maintained by the Security Council Committee established pursuant to resolution 1267 (1999). The list can be accessed via http://www.un.org/sc/committees/1267/aq_sanctions_list.shtml. This provision must be included in all sub-contracts or sub-agreements entered under this Project Document.

3. Social and environmental sustainability will be enhanced through application of the UNDP Social and Environmental Standards (http://www.undp.org/ses) and related Accountability Mechanism (http://www.undp.org/secu-srm).

4. UNDP as the Implementing Partner will: (a) conduct project and programme-related activities in a manner consistent with the UNDP Social and Environmental Standards, (b) implement any management or mitigation plan prepared for the project or programme to comply with such standards, and (c) engage in a constructive and timely manner to address any concerns and complaints raised through the Accountability Mechanism. UNDP will seek to ensure that communities and other project stakeholders are informed of and have access to the Accountability Mechanism.

5. All signatories to the Project Document shall cooperate in good faith with any exercise to evaluate any programme or project-related commitments or compliance with the UNDP Social and Environmental Standards. This includes providing access to project sites, relevant personnel, information, and documentation.

6. UNDP as the Implementing Partner will ensure that the following obligations are binding on each responsible party, subcontractor, and sub-recipient:

    a. Consistent with the Article III of the SBAA *[or the Supplemental Provisions to the Project Document]*, the responsibility for the safety and security of each responsible party, subcontractor and sub-recipient and its personnel and property, and of UNDP's property in such responsible parties, subcontractor's and sub-recipient's custody, rests with such responsible party, subcontractor and sub-recipient. To this end, each responsible party, subcontractor and sub-recipient shall:

[24] To be used where UNDP is the Implementing Partner

[25] To be used where the UN, a UN fund/programme or a specialized agency is the Implementing Partner

i. put in place an appropriate security plan and maintain the security plan, considering the security situation in the country where the project is being carried.
ii. assume all risks and liabilities related to such responsible parties, subcontractor's and sub-recipient's security, and the full implementation of the security plan.

b. UNDP reserves the right to verify whether such a plan is in place, and to suggest modifications to the plan when necessary. Failure to maintain and implement an appropriate security plan as required hereunder shall be deemed a breach of the responsible party's, subcontractor's and sub-recipient's obligations under this Project Document.

c. Each responsible party, subcontractor and sub-recipient will take appropriate steps to prevent misuse of funds, fraud or corruption, by its officials, consultants, subcontractors and sub-recipients in implementing the project or programme or using the UNDP funds. It will ensure that its financial management, anti-corruption, and anti-fraud policies are in place and enforced for all funding received from or through UNDP.

d. The requirements of the following documents, then in force at the time of signature of the Project Document, apply to each responsible party, subcontractor, and sub-recipient: (a) UNDP Policy on Fraud and other Corrupt Practices and (b) UNDP Office of Audit and Investigations Investigation Guidelines. Each responsible party, subcontractor and sub-recipient agrees to the requirements of the above documents, which are an integral part of this Project Document and are available online at www.undp.org.

e. If an investigation is required, UNDP will conduct investigations relating to any aspect of UNDP programmes and projects. Each responsible party, subcontractor and sub-recipient will provide its full cooperation, including making available personnel, relevant documentation, and granting access to its (and its consultants', subcontractors' and sub-recipients') premises, for such purposes at reasonable times and on reasonable conditions as may be required for the purpose of an investigation. Should there be a limitation in meeting this obligation, UNDP shall consult with it to find a solution.

f. Each responsible party, subcontractor and sub-recipient will promptly inform UNDP as the Implementing Partner in case of any incidence of inappropriate use of funds, or credible allegation of fraud or corruption with due confidentiality.

Where it becomes aware that a UNDP project or activity, in whole or in part, is the focus of investigation for alleged fraud/corruption, each responsible party, subcontractor and sub-recipient will inform the UNDP Resident Representative/Head of Office, who will promptly inform UNDP's Office of Audit and Investigations (OAI). It will provide regular updates to the head of UNDP in the country and OAI of the status of, and actions relating to, such investigation.

g. Choose one of the three following options:

Option 1: UNDP will be entitled to a refund from the responsible party, subcontractor or sub-recipient of any funds provided that have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of this Project Document. Such amount may be deducted by UNDP from any payment due to the responsible party, subcontractor or sub-recipient under this or any other agreement. Recovery of such amount by UNDP shall not diminish or curtail any responsible party's, subcontractor's or sub-recipient's obligations under this Project Document.

Option 2: Each responsible party, subcontractor or sub-recipient agrees that, where applicable, donors to UNDP (including the Government) whose funding is the source, in whole or in part, of the funds for the activities which are the subject of the Project Document, may seek recourse to such responsible party, subcontractor or sub-recipient for the recovery of any funds determined by UNDP to have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of the Project Document.

Option 3: UNDP will be entitled to a refund from the responsible party, subcontractor or sub-recipient of any funds provided that have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of the

Project Document. Such amount may be deducted by UNDP from any payment due to the responsible party, subcontractor or sub-recipient under this or any other agreement.

Where such funds have not been refunded to UNDP, the responsible party, subcontractor or sub-recipient agrees that donors to UNDP (including the Government) whose funding is the source, in whole or in part, of the funds for the activities under this Project Document, may seek recourse to such responsible party, subcontractor or sub-recipient for the recovery of any funds determined by UNDP to have been used inappropriately, including through fraud or corruption, or otherwise paid other than in accordance with the terms and conditions of the Project Document.

Note: The term "Project Document" as used in this clause shall be deemed to include any relevant subsidiary agreement further to the Project Document, including those with responsible parties, subcontractors and sub-recipients.

h. Each contract issued by the responsible party, subcontractor or sub-recipient in connection with this Project Document shall include a provision representing that no fees, gratuities, rebates, gifts, commissions or other payments, other than those shown in the proposal, have been given, received, or promised in connection with the selection process or in contract execution, and that the recipient of funds from it shall cooperate with any and all investigations and post-payment audits.

i. Should UNDP refer to the relevant national authorities for appropriate legal action any alleged wrongdoing relating to the project or programme, the Government will ensure that the relevant national authorities shall actively investigate the same and take appropriate legal action against all individuals found to have participated in the wrongdoing, recover and return any recovered funds to UNDP.

j. Each responsible party, subcontractor and sub-recipient shall ensure that all of its obligations set forth under this section entitled "Risk Management" are passed on to its subcontractors and sub-recipients and that all the clauses under this section entitled "Risk Management Standard Clauses" are adequately reflected, *mutatis mutandis*, in all its sub-contracts or sub-agreements entered into further to this Project Document.

Results and Resources Framework (RRF)- Iraq Crisis Response and Resilience Programme
RRF: 1 October 2014 – 31 December 2022 is annexed to this project document

Intended Outcome as stated in the UNSDCF/Country Programme (2020-2024) Results and Resource Framework:

- 1.3: People in Iraq participate in and benefit from effective mechanisms – at national, subnational and community levels – that prevent, mitigate, and manage conflict, and contribute to social cohesion and peaceful coexistence, with particular focus on women and youth leadership in decision- making, peacebuilding and reconciliation processes.
- 2.1 Improved people-centered economic policies and legislation contribute to inclusive, gender sensitive and diversified economic growth, with focus on increasing income security and decent work for women, youth, and vulnerable populations.
- 4.2: Increased engagement of the people of Iraq, sub-national institutions, civil society, and private sector to ensure more responsible, inclusive, accountable, and transparent management of natural resources and the environment.

Contribute to the six signature solutions of UNDP strategic plan 2022-2025:

1. **Poverty and inequality:** tacking inequality of opportunities by investing in the enhanced capabilities people need to move above the poverty line and keep moving forwards
2. **Gender equality:** confronting the structural obstacles to gender equality and strengthening women's economic empowerment and leadership
3. **Energy:** increasing energy access to those further left behind and accelerating the transition to renewable energy
4. **Environment:** putting nature and the environment at the heart of national economies and planning, helping government protect, manage, and value their natural assets
5. **Resilience:** supporting countries and communities in building resilience to diverse shocks and crises, including conflict, climate change, disasters, and epidemics
6. **Governance:** helping countries address emerging complexities by future-proofing governance systems through anticipatory approaches and better management

Outcome indicators and outputs as stated in the Country Programme (2020-2024) Results and Resources Framework, including baseline and targets:

- Indicator 1.1. Number of governorates with direct participation mechanisms for civil society engagement in all facets of development plans for the delivery of equitable and responsive services that operate regularly and transparently.
    - Output 1.2. civil society and academic institutions strengthened to promote social cohesion, prevention of violent extremism and sustainable development
        - Indicator 1.2.1. Number of civil society organizations supported to engage in sustainable development, conflict prevention and mitigation processes
        - Indicator 1.2.3. number of community-level mechanisms for conflict resolution and consensus-building that are operational with the engagement of youth and women
- Indicator 2.1. Number of jobs created in productive non-oil sectors out of total jobs by sex and age and persons with disabilities.
    - Output 2.2. access to livelihoods and employment creation opportunities increased in locations affected by and vulnerable to conflict
        - Indicator 2.2.1 number of people benefiting from emergency livelihoods support, disaggregated by gender
        - Indicator 2.2.2. number of people supported to access sustainable livelihoods and employment opportunities, disaggregated by gender
- Indicator 4.1. Adopted and implemented national disaster risk reduction (DRR) strategies in line with sendai framework for DRR, 2015-20230
    - Output 4.1. Number of renewable energy solutions provided to vulnerable communities

Project title and Atlas Project Number:
Iraq Crisis Response and Resilience Programme (ICRRP) /**00085156**

EXPECTED OUTPUTS	OUTPUT INDICATORS	DATA SOURCE	BASELINE		TARGETS (Targets set from 2022-2024)			DATA COLLECTION METHODS
			Value	Year	2022	2023	2024	
Output 1: Sustainable access to livelihood opportunities promoted through the development of context-tailored green solutions, focusing on the green economy	1.1. **Design context-based livelihood solutions**							
	(a) # of livelihoods strategies developed at district/governorate level Overall target: 15	(i) list of assessments conducted (ii) list of stakeholders who participated	Zero	2022	1 strategy	10 strategies	4 strategies	UNDP monitoring reports
	(b) # of value chain/market assessment conducted Overall target: 25	(i) list of assessments conducted (ii) list of stakeholders who participated	Zero	2022	2 assessments	13 assessments	10 assessments	UNDP monitoring reports
	1.2. **Create resilient and sustainable livelihood opportunities**							
	(a) # of MSMEs supported with start-up or scale-up grants Overall target: 22,015	(i) list of businesses supported	16,015	2022	500 businesses	2,500 businesses	2,500 businesses	UNDP monitoring reports
	(b) # of MSMEs with improved business management skills Overall target: 22,015	(i) list of businesses supported	16,015	2022	500 businesses	2,500 businesses	2,500 businesses	UNDP monitoring reports
	(c) # of CFW short-term opportunities created to rehabilitate physical livelihoods productive infrastructure Overall target: 42,900	(i) list of CFW BNFs (ii) List of projects	37,900	2022	1,100 CFW	3,000 CFW	900 CFW	UNDP monitoring reports
	(d) # of partnership developed with the private sector Overall target: 17	(i) list of partnerships developed	2	2022	0 partnership	7 partnerships	8 partnerships	UNDP monitoring reports
	(e) # of Beneficiaries offered Vocational Training Overall target: 17,400	(i) list of Beneficiaries	14,630	2022	370 BNFs	1,200 BNFs	1,200 BNFs	UNDP monitoring reports

	(f) # of value chain cluster initiated Overall target: 10	(i) list of members/stakeholders	Zero	2022	0	5 clusters	5 clusters	UNDP monitoring reports
	(g) # of community led local initiatives upgrading targeted value chains Overall target: 25	(i) list of projects and BNFs	Zero	2022	0	12 projects	13 projects	UNDP monitoring reports
	(h) Percentage increase in income generated among target beneficiaries Overall target: minimum 10%	i) Baseline/Endline reports	Zero	2022	10%	10%	10%	Baseline and Endline survey
	1.3. **Develop the capacity of main stakeholders to support economic recovery and resilience**							
	(a) # of public/private institutions benefiting from capacity building Overall target: 15 institutions	i)Monthly progress report. and/or Quarterly reports	1	2022	1 institution	7 institutions	7 institutions	UNDP monitoring reports
Output 2: Strengthened Social Cohesion through, community-based reintegration of at risk-groups	2.1 **Strengthen resilience to violent extremism through socio-economic reintegration including psychosocial support targeting men and women, youth at-risk, disengaged fighters**							
	(a) # of gender-sensitive assessments, studies and lessons learned products on the community security initiative carried out Overall target: 11	assessments, studies and lessons learned report	3 assessments conducted	2022	2 assessment and lessons learnt product	3 assessment and lessons learnt product	3 assessment and lessons learnt product	Assessment Reports Community consultation reports/Monitoring visit reports
	(b) % Women and girls targeted with specific activities in the target location	Project progress report Field monitoring reports Project Data base	TBD	2022	35%	35%	35%	Project site monitoring reports UNDP Staff Progress and monitoring reports by responsible Parties

	(c) # of vulnerable and at-risk groups including disengaged fighters from target location that receive reintegrating support by type (disaggregated by age/at-risk youth and gender where relevant) Overall target: 3,900	Perception survey Project Data base Project progress report Field monitoring reports	300	2022	900 vulnerable and at-risk groups including disengaged fighters from target location that receive reintegrating support	1,350 vulnerable and at-risk groups including disengaged fighters from target location that receive reintegrating support	1,350 vulnerable and at-risk groups including disengaged fighters from target location that receive reintegrating support	Project site monitoring reports UNDP Staff Progress and monitoring reports by responsible Parties
	(d) # of LPCs and local structures supported to facilitate reintegration of returnees and vulnerable groups including disengaged fighters Overall target: 50	Field monitoring reports and progress reports from LPCs and Responsible Parties/Service Providers	28	2022	6	8	8	Project field visits and Regular monitoring of database
Output 3: Environmental resilience and response to climate change improved through promoting renewable energy/services among vulnerable communities	**3.1. Improve environmental resilience by supporting access of farmers to renewable energy**							
	(a) # of farmers who received solar energy solutions Overall target: 1,200	(i) List of BNFs (ii) Signed receipt from farmers	Zero	2022	30 farmers	600 farmers	570 farmers	UNDP reports
	3.2. Improve access to renewable energy solutions and services by building the capacity of MSMEs							
	(a) # of MSME's personal trained on clean energy solutions Overall target: 200	(i) Training reports	Zero	2022	00	100 persons/MSMEs	100 persons/MSMEs	UNDP reports

Multi-Year Work Plan

Iraq Crisis Response and Resilience Programme -Project Document Revision

EXPECTED OUTPUTS	PLANNED ACTIVITIES- INDICATORS	Planned Implementation by Year			RESPONSIBLE PARTY	PLANNED BUDGET	
		Year 1- 2022	Year 2 - 2023	Year 3- 2024		Funding Source	Amount
Output 1: Sustainable access to livelihood opportunities promoted through the development of context-tailored green solutions, focusing on the green economy Sustainable *1.1* *Design context-based livelihood solutions* *1.2* *Create Resilient and sustainable livelihood opportunities* *1.3* *Develop the capacity of main stakeholders to support economic recovery and resilience*	Activity 1.1.a# of livelihoods strategies developed at district/governorate level Target: 15	x	x	x	UNDP, UN agencies, Civil Society Organizations , Government institutions		**1,600,000**
	Activity 1.1.b # of value chain assessment conducted Target: 25	x	x	x			
	Activity 1.2. (a) # of MSMEs supported with start-up or scale-up grants Overall target: 22,015	x	x	x			**57,025,000**
	Activity 1.2.(b) # of MSMEs with improved business management skills Overall target: 22,015	x	x	x			
	Activity 1.2.(c) # of CFW short-term opportunities created to rehabilitate physical livelihoods productive infrastructure Overall target: 42,900	x	x	x			
	Activity 1.2.(d) # of partnership developed with the private sector Overall target: 20	x	x	x			
	Activity 1.2.(e) # of Beneficiaries offered Vocational Training Overall target: 17,400	x	x	x			
	Activity 1.2.(f) # of value chain cluster initiated Overall target: 10	x	x	x			
	Activity 1.2.(g) # of community led local initiatives upgrading targeted value chains Overall target: 25	x	x	x			
	Activity 1.2.(h) Percentage increase in income generated among target BNFs Overall target: minimum 10%	x	x	x			
	Activity 1.3.a# and type of public/private institutions benefiting from capacity Target: 15 institutions	x	x	x			**600,000**

Gender marker:2	MONITORING						**1,184,500**
	Sub-Total for Output 1						**60,409,500**
Output 2: Strengthened Social Cohesion through, community-based reintegration of at risk-groups *2.1* *Strengthen resilience to violent extremism through socio-economic reintegration programs including psychosocial support targeting men and women, youth-at-risk, disengaged fighters and host communities*	Activity 2.1.(a) # of gender-sensitive assessments, studies and lessons learned products on the community security initiative carried out Activity 2.1.b % Women and girls targeted with specific activities in the target location	x	x	x	UNDP, UN agencies, Civil Society Organizations, Government institutions		**21,000,000**
	Activity 2.1. (b) # of vulnerable and at-risk groups including disengaged fighters from target location that receive reintegrating support by type (disaggregated by age/at-risk youth and gender where relevant)	x	x	x			
	Activity 2.1. (c) # of LPCs and local structures supported to facilitate reintegration of returnees and vulnerable groups including disengaged fighters	x	x	x			
Gender marker:2	MONITORING						**420,000**
	Sub-Total for Output 2						**21,420,000**
Output 3: Environmental resilience and response to climate change improved through promoting renewable energy/services among vulnerable communities 3.1. Improve environmental resilience by supporting access to farmers to renewable energy 3.2. Improve access to renewable energy solutions and services by building the capacity of MSMEs	Activity 3.1. (a) # # of farmers benefited from solar energy solutions Overall target: 1200 farmers	x	x	x			**8,000,000**
	Activity 3.2.(a) # of MSME's personal trained on clean energy solutions Overall target: 200						
Gender marker:2	MONITORING						**160,000**
	Sub-Total for Output 3						**8,160,000**

Program Management	Delivery Enabling Services (DES)						**3,599,580**
	Staffing & Management Cost						**5,399,370**
Evaluation *(as relevant)*	EVALUATION						**250,000**
General Management Support 8%							**7,939,076**
TOTAL							**107,177,526**

MONITORING AND EVALUATION

Monitoring Plan

Monitoring Activity	Purpose	Frequency	Expected Action	Partners (if joint)	Estimated Cost (if any)
Track results progress	a) Field level monitoring of progress of activity implementation, challenges and issues that negatively impact the pace and quality of project implementation. b) Progress data against the results indicators in the RRF collected and analysed to assess the progress of the project in achieving the agreed outputs.	a) Weekly or monthly or quarterly based on Component (additionally details provided in a multi-layered monitoring framework) b) Quarterly, and Annually where relevant in keeping with the frequency required for each indicator.	Slower than expected progress will be addressed by project management.		$1,235,150
Monitor and Manage Risks	Identify specific risks that may threaten achievement of intended results. Identify and monitor risk management actions using a risk log. This includes monitoring measures and plans that may have been required as per UNDP's Social and Environmental Standards. Audits will be conducted in accordance with UNDP's audit policy to manage financial risk.	Annually	Risks are identified by project management and actions are taken to manage risk. The risk log is maintained to keep track of identified risks and actions taken.		$176,450

Monitoring Activity	Purpose	Frequency	Expected Action	Partners (if joint)	Estimated Cost (if any)
Knowledge Management	Knowledge, good practices, and lessons will be captured regularly, as well as actively sourced from other projects and partners and integrated back into the project.	Annually	Relevant lessons are captured by the project team and used to inform management decisions.		$35,290
Project Review to Make Course Corrections	Internal review of data and evidence from all monitoring actions undertaken by the Project Team to inform decision making by the Project Board. This internal review will also include taking stock of exit/phase-out strategies adopted by the Project.	Annually	Performance data, risks, lessons and quality will be discussed by the project and used to make course corrections.		$35,290
Annual Project Quality Assurance	The quality of the project will be assessed against UNDP's quality standards to identify project strengths and weaknesses and to inform management decision making to improve the project. The Quality Assessment tool is used from 2016 onwards.	Annually	Areas of strength and weakness will be reviewed by project management and used to inform decisions to improve project performance.		$35,290
Project Report	A progress report is circulated to members of the Project Board and key stakeholders, consisting of progress data showing the results achieved during the reporting period, a summary of risks, and lessons learned, and any evaluation or review reports prepared over the period.	-Annual progress report -Final project report			$176,450
Project Review by the Project Board	The Project Board holds regular project reviews (a minimum annually) to assess the performance of the project. In the project's final year, the Project Board will hold an end-of project review to capture lessons learned and discuss opportunities for scaling up and to socialize project results and lessons learned with relevant audiences.	At-least Annually	The Project Board will discuss any quality concerns or slower than expected progress and agree on management actions to address the issues identified.		$35,290
Project Evaluation	To determine the lessons learned and successes of program activities to strengthen the implementation process.	Mid-Term and/or Final Evaluation	The Project Management Team and Steering Committee will review the findings of the Evaluation to identify ways to strengthen the implementation process and determine the need for and nature of a further phase of support.		$250,000
Project Closure Quality Assurance	The quality of the closure process of the project will be assessed against UNDP's quality standards to identify strengths and weaknesses and to inform management decision making to improve the process.	In the lead up to Closure of the Project	Areas of strength and weakness will be reviewed by project management and used to inform decisions to improve project performance.		$35,290

Monitoring Activity	Purpose	Frequency	Expected Action	Partners (if joint)	Estimated Cost (if any)

Annexes:

Annex 1: Risk Analysis

ANNEX 1: IRAQ CRISIS RESPONSE AND RESILIENCE PROGRAMME – RISK ANALYSIS

SL #	Description	Type	Probability(P)/ Impact (I) On a scale from 1 (low) to 5 (high)	Counter Measures / Management Response	Monitored by	Status (as of Q2-2022)
1	Fluid political environment causes high turnover of leadership negatively affects the pace of project implementation.	Political	P- 3 I- 3	UNDP to ensure strong relationships are maintained at the high political level, as well as with provincial command cells and municipal officials, and the required high-level decisions are minted through the Steering Committee meetings.	Head of Stabilization	No change
2	Challenges related to rotation of governments 'staff. Fluid political environment whereby changes in government positions could lead to invite changing opinions on priorities or leadership gaps.	Operational	Impact: 3 Probability: 3	Ensure strong relationships are maintained at high political level, and high-level decisions on ICRRP are documented through the Steering Committee.	Programme Manager	Unchanged.
3	Lack of programme ownership by national partners: a) Poor involvement of national counterparts would effectively impede or cease project activities as well as reduce the sustainability of project results. b) Different levels of ownership and commitment may occur	Strategic/operational.	P-4 I-4	Government partners (KRG and national authorities (MOLSA)) would be closely involved throughout the project preparation. The Project will build on key national strategic strategies, including the national reintegration strategy. Close cooperation will be ensured throughout the project implementation cycle and authorities will be accountable for the projects results and achievements.	Programme Manager UNDP Management	Unchanged.

	between KRG and Iraq national level counterpart (MOLSA).					
4.	Environmental safeguards not being incorporated, resulting in damage to the natural habitat in the target location because of project activities OR Project failing to promote environmentally sustainable practices across all activities, results in negative impact upon programme results, and environmental impacts.	Strategic Environmental	P-3 I-4	- Social and environmental screening assessment to be completed for each Component of ICRRP. - Environmental screening checklists and safeguards to be factored into all construction work that will be undertaken. Requirements will also be reflected from the BoQ development stage, through the procurement phase, right through to completion of activities. - ICRRP will also aim to design livelihood activities which support sustainable practices and protection of natural resources. - Social cohesion activities, including the conflict analyses will incorporate the triggers of conflict related to natural resources. - Small grants will incorporate the need to ensure environmentally friendly projects/initiatives are implemented.	Programme Manager Component Leads	Unchanged.
5	Corruption by various stakeholders (internal and external) during project planning and implementation.	Operational Financial	P- 4 I- 5	- A no-tolerance policy in terms of dealing with corruption, which is practiced transparently and without exception in all cases where corrupt or fraudulent activities are encountered. - Robust monitoring mechanisms on all projects, with additional measures employed for projects which present a greater risk for corruption. - UNDP Operational and Financial Rules and Regulations will be communicated regularly to partners. - A frequent pace of field level monitoring to be undertaken and increase the capacity of staff to detect fraud and corruption. - Spot-checks by third-party for Government and NGOs serving as Responsible Parties.	Programme Manager	Unchanged
6	Corruption during procurement processes.	Operational Financial	P- 4 I- 5	- All procurement actions will be managed in keeping with UNDP's Operational and Financial Rules and Regulations. - To prevent leakage of confidential bidding information, including cost estimates, UNDP procurement staff communicate with all other UNDP staff only through emails; (communication by phone on procurement issues is banned). - Every single document submitted by a potential bidder will be verified. Only six staff will have access to draft and the final bills of quantity with pricing, limiting the possibility that information will be leaked. UNDP will hire predominantly international procurement staff, to limit the risk of conflict of interest and shield UNDP/ from pressures exerted on national staff by local authorities and vendors. UNDP-contracted engineers will also be rotated between core functions. All bids will be submitted on-line using an e-tendering platform.	UNDP Senior Management Programme Manager	Unchanged
	ICRRP Output 1					

1	Poor performance by contractor/service provider, low quality of supplied goods, works and service.	Operational	P-3 I- 3	- Release the payments upon certification of satisfactory completion of all works or after successful delivery of supplied equipment/kits with required testing and inspection in place, certified by UNDP. - Quality and quantities of supplied equipment/kits/goods should be controlled by engineers from UNDP. - UNDP contracted engineer on the ground sufficiently monitors implementation of activities and inspect supplied goods to ensure compliance and quality of works. Ensure that any issues identified are brought to UNDP's attention in a timely manner. - Ensure the Performance Security in the amount of 10% of Contract price is in place, which shall be valid and activated from the date of substantial receiving of project. Consider the performance evaluation of the recommended bidder during the evaluation and procurement process, for the pervious works performed by the bidder with UNDP.	Component Lead- Basic Services Area Coordinators	Unchanged
2	Significant delay in receiving the project by the end-user government after completion of all works by UNDP contractor.	Operational	P-4 I-3	UNDP shall assign the focal point to work closely with end-user to ensure all documentation and process in place within the timeliness.	Component Lead- Basic Services Area Coordinators Project Manager	Unchanged
3.	Delay in completion of works or delivery of goods by the supplier by the contract end-date.	Operational	P-4 I- 3	- Ensure the payments per the contract terms to be released on time upon completion of the correspondence milestone with satisfactory. - Facilitate from Project side, an improved process of vendor creation and approval in UNDP internal system and find alternative ways to ensure international transfer of payments are processed smoothly and reach to beneficiary quicker. - In addition to the liquidated damage clause in the contractor, a pre-award meeting to be considered where possible to de-brief the selected bidder on the UNDP contract terms and special conditions. - Better coordination with relevant government Departments to facilitate the entry of UNDP's contractual equipment with all required shipping document in place to ensure smooth through the entry boarder	Component Lead- Basic Services Area Coordinators Programme Manager	Unchanged

4.	Security conditions where activities are implemented (i.e., Diyala), poses a challenge to implementation and monitoring of project activities.	Operational	P-2 I-2	- Regular monitoring of security situation in each implementation location. - Assess any implication on implementation and monitoring in a timely manner, and together with project management identify alternative options for continuing implementation. - UNDP focal point to regularly assess implementation progress, and any implications If required, identify the need for 3rd party monitors, to supplement monitoring efforts.	Component Lead- Basic Services Area Coordinators Programme Manager	Changed- lower risk.
5	Lack of coordination of livelihood programming efforts being undertaken, results in duplication of support provision.	Strategic Operational	P-3 I-4	There will be active engagement to secure information relating to the livelihood programming efforts being undertaken by UN Agencies and civil society organizations. This will provide an opportunity for the Project to also share information relating to its programming.	Component Lead- Livelihoods	Unchanged
6	Financial support (grants or CFW) doesn't reach the beneficiaries, due to the high levels of corruption.	Operational Financial	P-4 I-4	-Standard Operating Procedures on cash for work programming implemented. -Supporting documentation to confirm beneficiary identification and receipt of cash to be specified and verified during monitoring visits. -Selection of Responsible Parties consider experience of I/NGOs that have experience in conducting cash support activities in Iraq and have established monitoring systems and safeguards. -Follow up calls to randomly selected beneficiaries to verify receipt of cash. -Putting in place a complaints management system, that beneficiaries can access to raise concerns.	Component Lead- Livelihoods	Unchanged
	ICRRP Output 2					
SL #	**Description**	**Type**	**Probability(P)/ Impact (I)** **On a scale from 1 (low) to 5 (high)**	**Counter Measures / Management Response**	**Monitored by**	**Status** **Status (as of Q2-2022)**
1	Limited implementation time-frames negatively impact upon social cohesion programming which requires medium to longer term interventions.	Operational	P- 2 I-4	The project will plan for activities within Q4-2022, with early design of Terms of References, and early identification of Responsible Parties, providing as much time as possible for implementation of activities, in keeping with the validity timeframe of the donor contributions.	Component Lead- Social Cohesion Programme Manager	Unchanged
2	Declining donor funding for social cohesion activities, negatively	Financial Operational	P-3 I-4	The project will review the project closure phases for each of the social cohesion projects to take stock of transition and handover	Programme Manager	Unchanged.

	impacts upon the continuity of some of the social cohesion activities.			requirements, with a view to ensuring responsible closure of the Project.	Component Lead- Social Cohesion	
	ICRRP Output 3					
SL #	**Description**	**Type**	**Probability(P)/ Impact (I)** **On a scale from 1 (low) to 5 (high)**	**Counter Measures / Management Response**	**Monitored by**	**Status** **Status (as of Q2-2022)**
1	Poor performance by contractor/service provider, low quality of supplied goods, works and service.	Operational	P-3 I- 3	- Release the payments upon certification of satisfactory completion of all works or after successful delivery of supplied equipment/kits with required testing and inspection in place, certified by UNDP. - Quality and quantities of supplied equipment/kits/goods should be controlled by engineers from UNDP. - UNDP contracted engineer on the ground sufficiently monitors implementation of activities and inspect supplied goods to ensure compliance and quality of works. Ensure that any issues identified are brought to UNDP's attention in a timely manner. - Ensure the Performance Security in the amount of 10% of Contract price is in place, which shall be valid and activated from the date of substantial receiving of project. Consider the performance evaluation of the recommended bidder during the evaluation and procurement process, for the pervious works performed by the bidder with UNDP.	Component Lead- Basic Services Area Coordinators	Unchanged
2	Delay in completion of works or delivery of goods by the supplier by the contract end-date.	Operational	P-4 I- 3	- Ensure the payments per the contract terms to be released on time upon completion of the correspondence milestone with satisfactory. - Facilitate from Project side, an improved process of vendor creation and approval in UNDP internal system and find alternative ways to ensure international transfer of payments are processed smoothly and reach to beneficiary quicker. - In addition to the liquidated damage clause in the contractor, a pre-award meeting to be considered where possible to de-brief the selected bidder on the UNDP contract terms and special conditions. - Better coordination with relevant government Departments to facilitate the entry of UNDP's contractual equipment with all	Component Lead- Basic Services Area Coordinators Programme Manager	Unchanged

				required shipping document in place to ensure smooth through the entry boarder		
3	Financial support doesn't reach the beneficiaries, due to the high levels of corruption.	Operational Financial	P-4 I-4	-Standard Operating Procedures on cash for work programming implemented. -Supporting documentation to confirm beneficiary identification and receipt of cash to be specified and verified during monitoring visits. -Selection of Responsible Parties consider experience of I/NGOs that have experience in conducting cash support activities in Iraq and have established monitoring systems and safeguards. -Follow up calls to randomly selected beneficiaries to verify receipt of cash. - -Putting in place a complaints management system, that beneficiaries can access to raise concerns.	Component Lead-Livelihoods	Unchanged
